


Bridge_0150 MOT

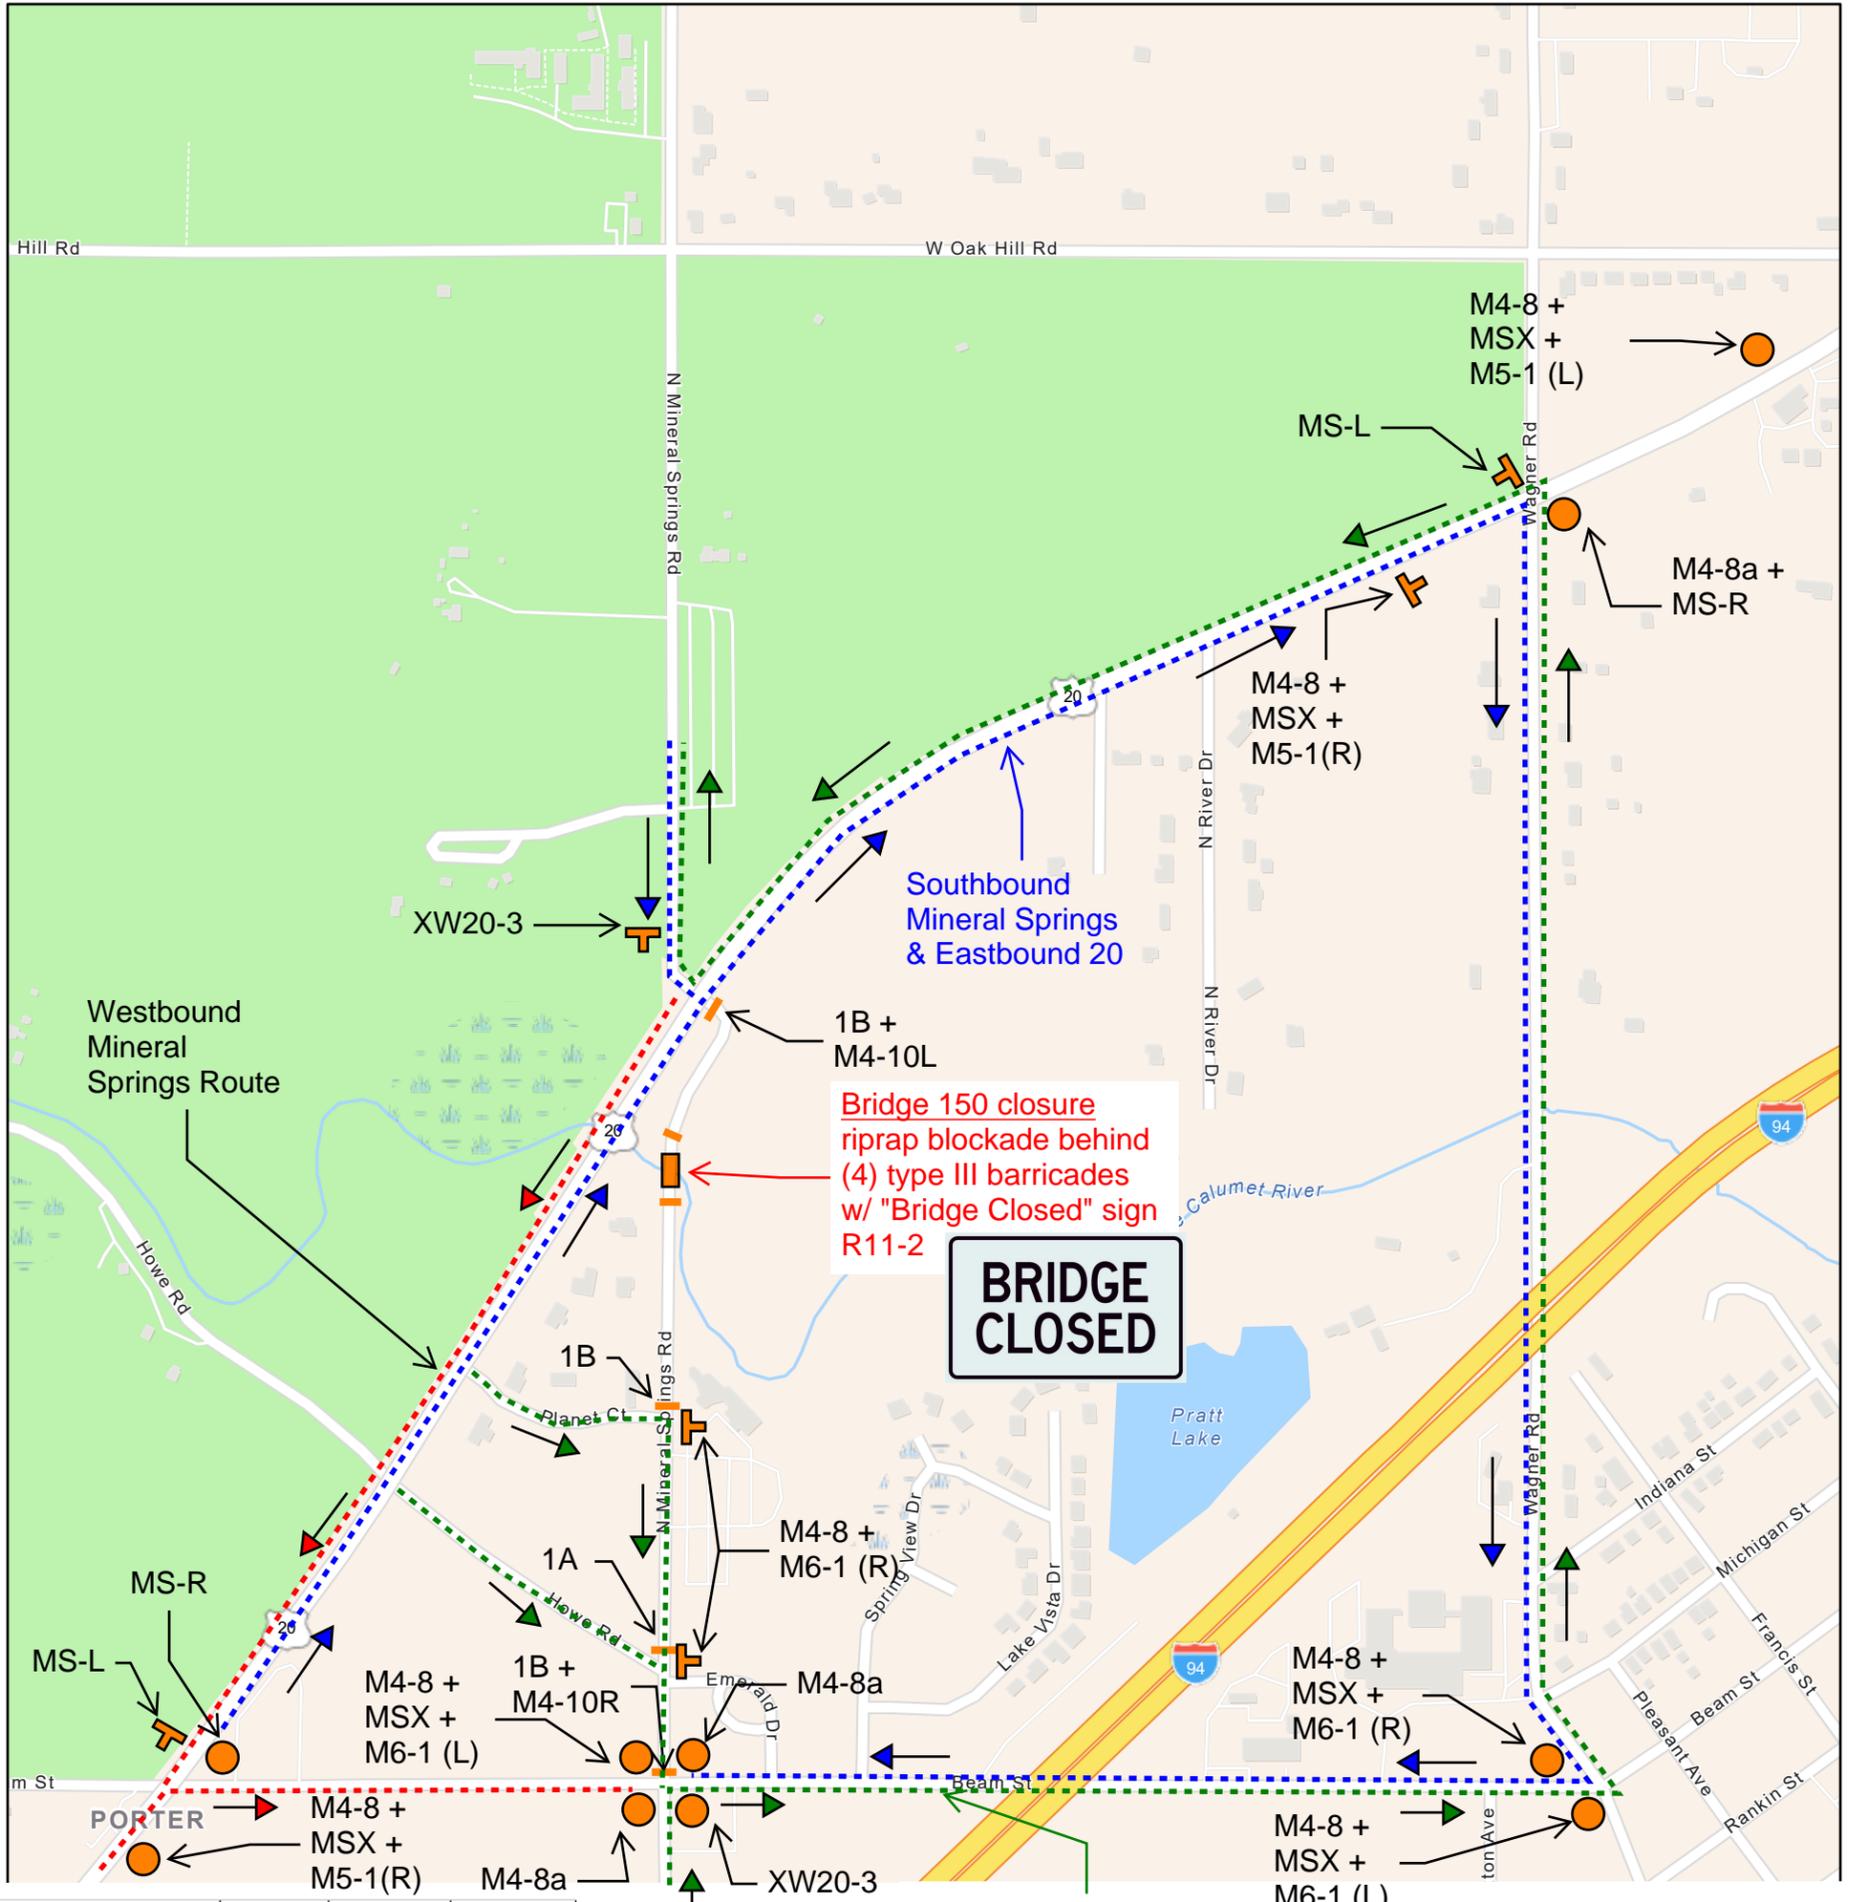

Bridge 150 closure
riprap blockade behind
(4) type III barricades
w/ "Bridge Closed" sign
R11-2


**BRIDGE
CLOSED**

	Sign Code	Size (INxIN)	Qty (each)
	M4-8a	24x24	3
	MS-R	30X30	2
	MS-L	30X30	2
	M4-10L	48x18	1
	M4-10R	48x18	1
	R11-4	60x30	2
	R11-2	60x30	2


	Sign Code	Size (INxIN)	Qty (each)
	XW20-3	36x36	2
	M4-8	24x12	8
	W16-8aP / "MSX"	30x15	6
	M5-1(L)	21x15	2
	M5-1(R)	21X15	2
	M6-1	24x18	5

- Temporary Driven Post
- On Existing Post

Signs to be installed on per INDOT Standard Drawings E-801-TCDV-05 or E-801-TCDV-06. Temporary sign supports will be provided until utility locates are provided for driven posts.

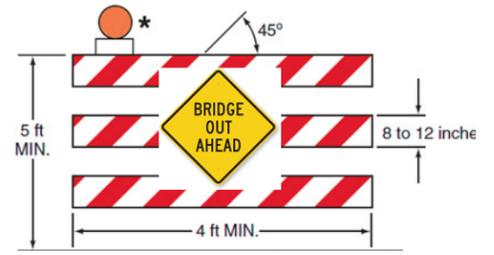


1A - Type 3 Barricade




1B - Type 3 Barricade w/ R11-4 (60x30)

NOTES:

1. Barricade lights, signs, and supports shall satisfy NCHRP 350 or MASH crash evaluation criteria.
- ② The detour arrow sign shall be used only when a detour route has been signed.
- ③ The sign assembly shall be above the Type III barricade.


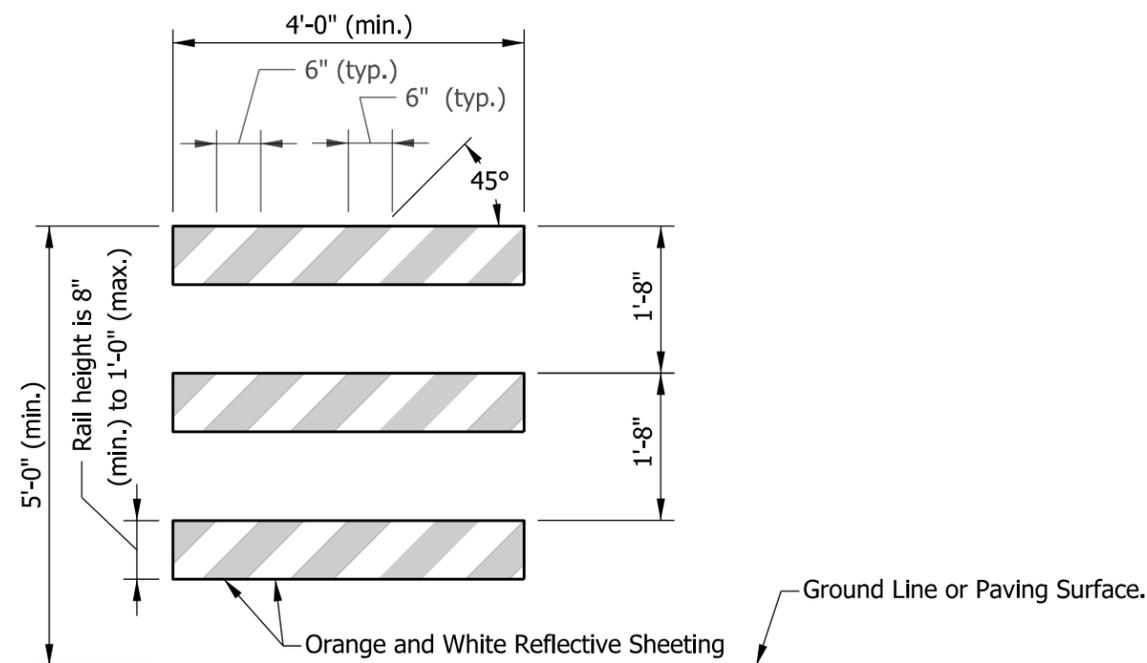


TYPE III BARRICADE


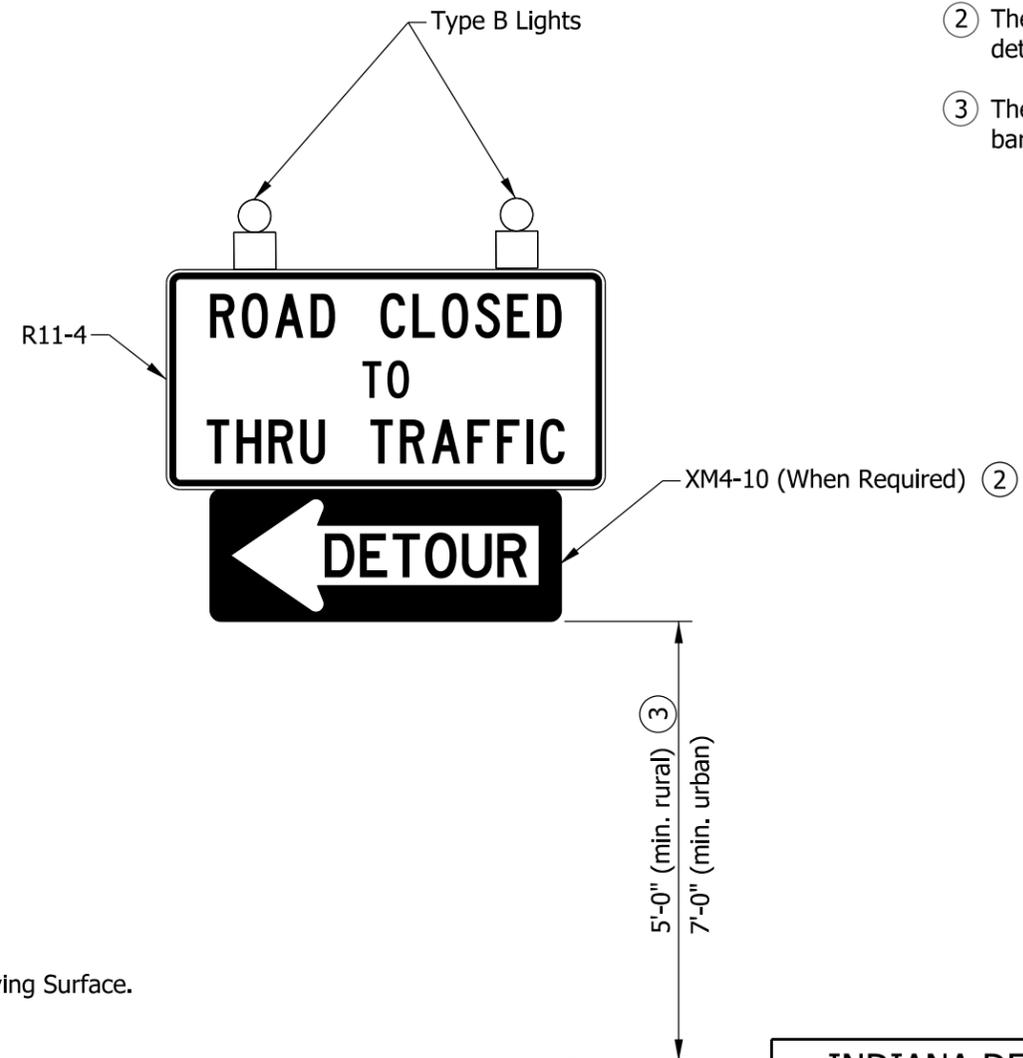


ROAD CLOSURE SIGN ASSEMBLY


INDIANA DEPARTMENT OF TRANSPORTATION	
TYPE III BARRICADE	
SEPTEMBER 2022	
STANDARD DRAWING NO. E 801-TCDV-05	
	<p style="text-align: right;"><i>David H. Boruff</i> 06/08/22 DESIGN STANDARDS ENGINEER DATE</p> <p style="text-align: right;"><i>[Signature]</i> 06/27/2022 CHIEF ENGINEER DATE</p>

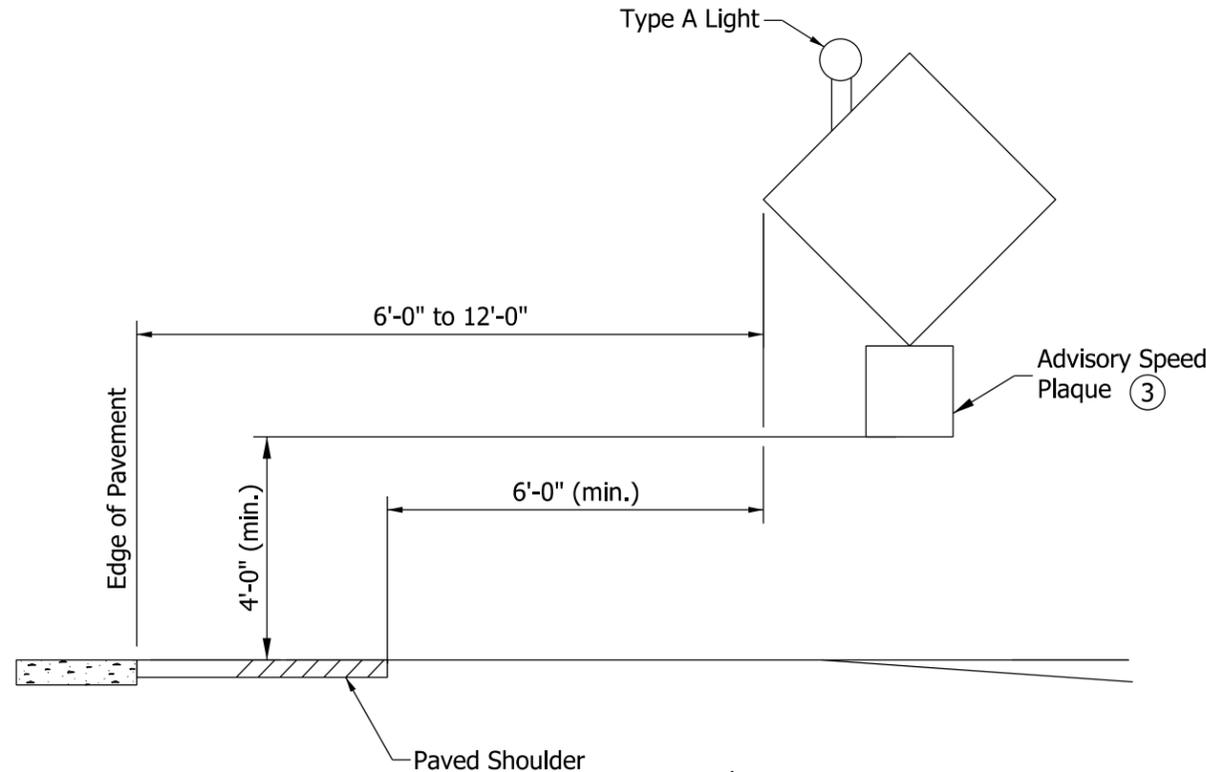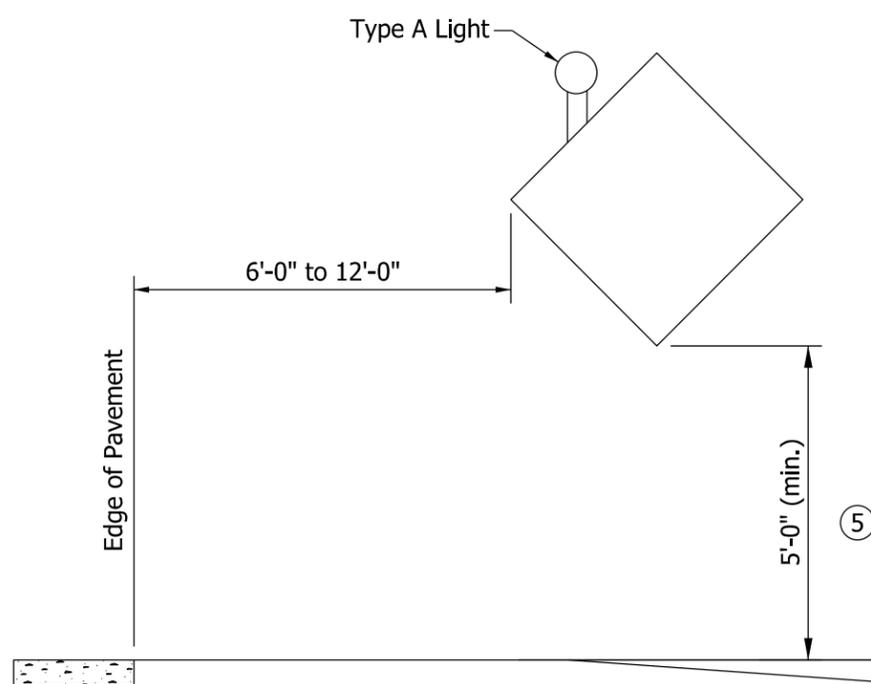

ROADWAY WITHOUT CURB

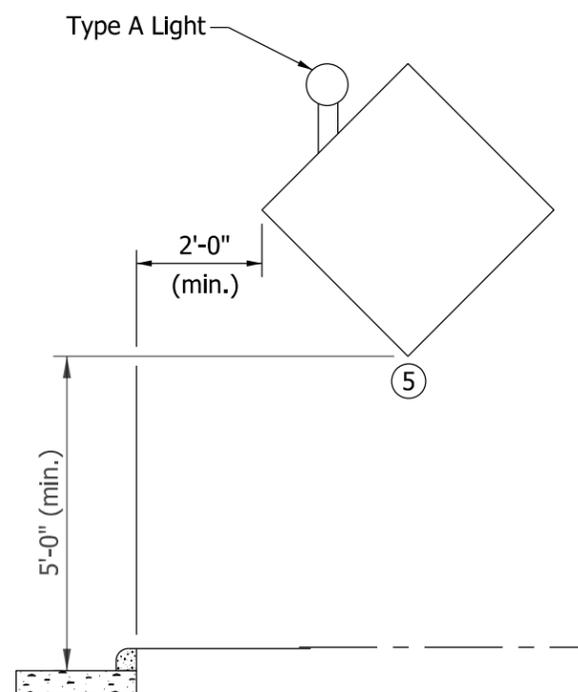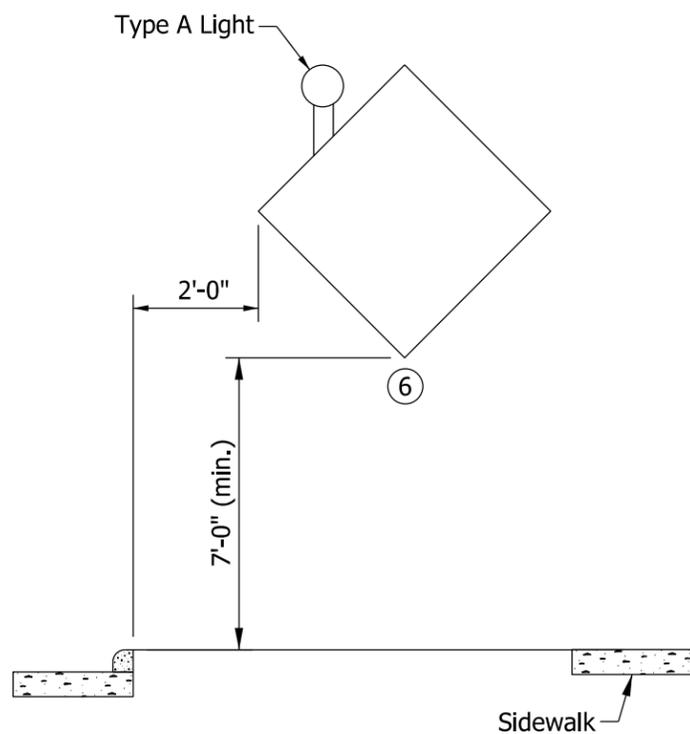

CURBED ROADWAY

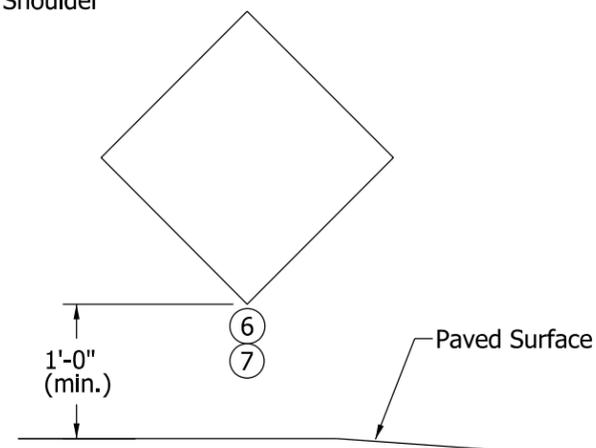

TEMPORARY MOUNTED CONSTRUCTION SIGN

NOTES:

1. See Standard Drawing E 801-TCSN-07 for additional notes.
2. Signs, lights, and supports shall satisfy NCHRP 350 or MASH crash evaluation criteria.
- ③ An advisory speed plaque, required to be placed with another construction sign, may be mounted on the post closest to the roadway at a height not less than 4 ft above the edge of pavement adjacent to the sign. The bottom of the construction warning sign shall not be lower than the top of the advisory speed plaque.
4. Type A warning light required on all construction signs.
- ⑤ In urban area or on Interstate route, mounting height shall not be less than 7 ft.
- ⑥ When signs are placed on sidewalk, a 4 ft useable width shall be maintained. No part of the sign or support that is less than 7 ft in height may protrude more than 4 in. into the 4 ft useable sidewalk width.
- ⑦ Temporary mounted construction sign for nighttime work or for operations which affect traffic lanes shall have a mounting height of 5 ft above the traveled way. On roadways where on-street parking is allowed, temporary mounted construction signs shall have a minimum sign mounting height of 7 ft above the traveled way.

INDIANA DEPARTMENT OF TRANSPORTATION	
TYPICAL CONSTRUCTION SIGN MOUNTING	
SEPTEMBER 2022	
STANDARD DRAWING NO. E 801-TCDV-06	
	 DESIGN STANDARDS ENGINEER 06/08/22 DATE
	 CHIEF ENGINEER 06/27/2022 DATE
