STATE OF INDIANA
DEPARTMENT OF ADMINISTRATION
PROCUREMENT DIVISION
402 W. WASHINGTON ST. W468
INDIANAPOLIS, IN 46204
317/232-3150

NOTICE OF ADDENDUM #1 TO SOLICITATION

REQUISITION NUMBER: ***ASA-10-40 Pre-Fab Boat Ramps***

OPENING DATE: July 7, 2010 3:00 PM Eastern Time

* * * * * * * * *

Please find attached a new Attachment A, the diagrams for the Boat Ramps.

Should you desire to submit a bid, please do so on the basis of information detailed above.

This acknowledgement should be signed and returned with your solicitation.

Procurement Division:

Approved: Susan Deaton-Reed

----------**ACKNOWLEDGEMENT**----------

Receipt of Notice of Addendum, for Solicitation # _____

Vendor Name:_____

Signed:_____

Title:_____

Date:_____

Handicap Transfer Vault Lid: • Railing & Swingarm Stub Detail
(Not to scale) Drawing 1 of 2 • Lifting Lug Detail
Public Access South, Feb. 2007 • Rebar Grid in Lid
(812) 644-7731

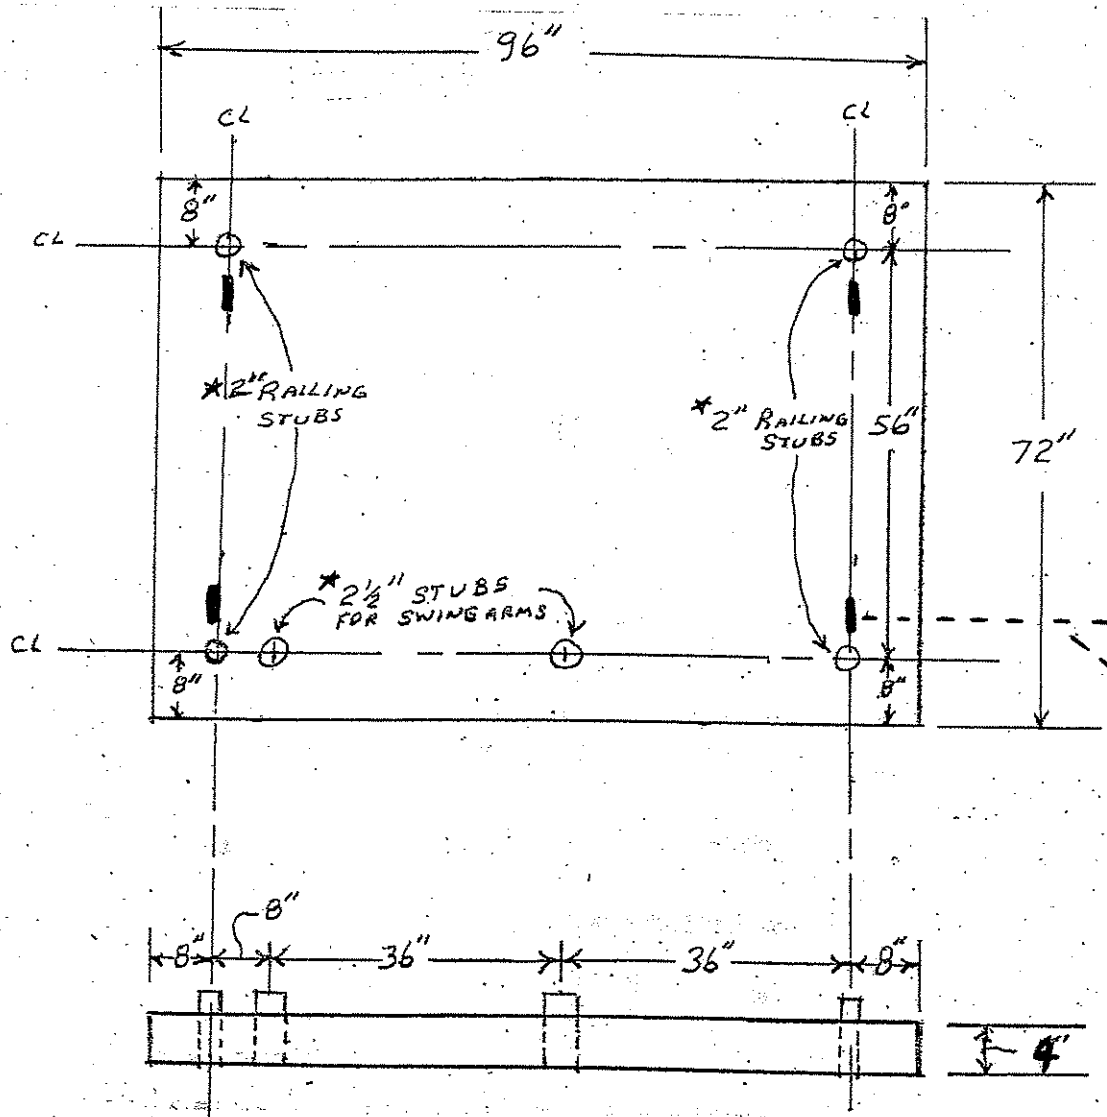

Rebar Grid For Lid & Bottom of Vault
½" rebar – Tack welded at intersections.

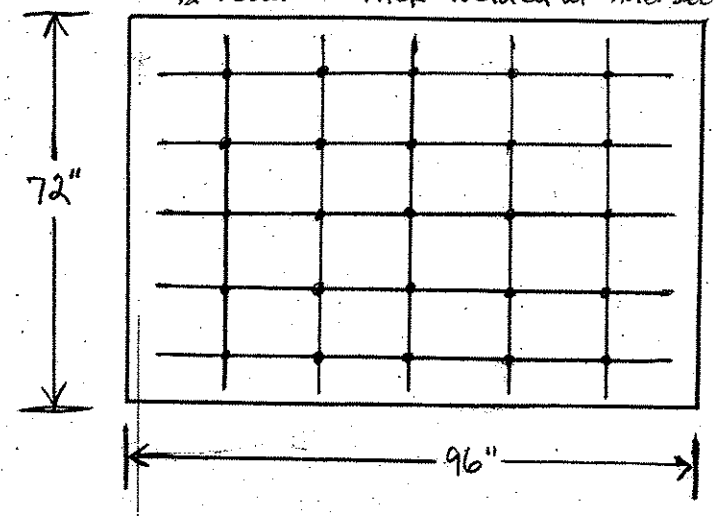

Lifting Lugs (4) – to run parallel to handrails.
– ½" rebar

Side View:



* Top of Lifting Lug must be same height as top of handrail stubs.

- All sides & Lid to be poured from continuous batch of 6500 psi ready-mix concrete.
- Top side of Lid to be a broom finish.
- Lid & bottom of vault to have a ½" rebar grid tack welded at intersections.
- Pipe Stubs (schedule 80 pipe) to stick up 2" above top of Lid & flush on bottom of Lid (6" Long)

Diagram 1

Handicap Transfer Vault (Not to Scale)
Drawing 2 of 2
Public Access South, Feb. 2007
(812) 644-7731

* All sides & Lid to be poured from continuous batch of 6,500 psi ready mix concrete.

* All sides to be reinforced with 12.5 4" Mesh center-right reinforcing wire with a minimum of 3-½" rebar rods in the center-right slots.

Bottom

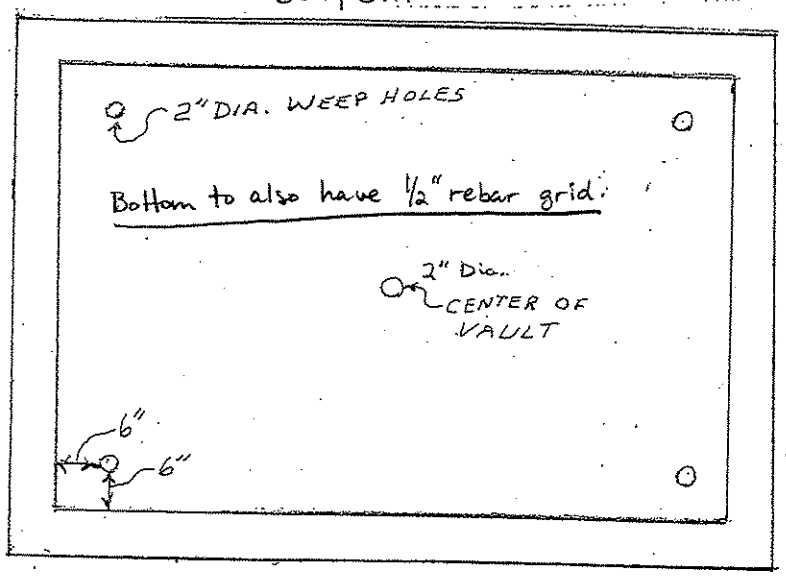

SIDE

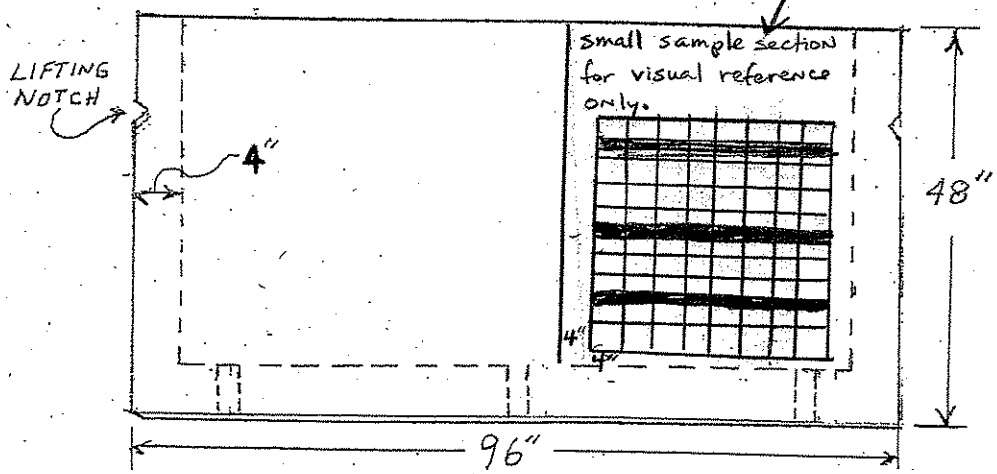

END

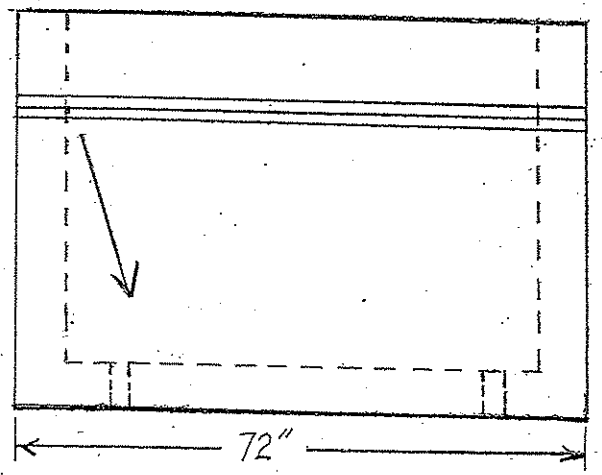

Diagram 2
