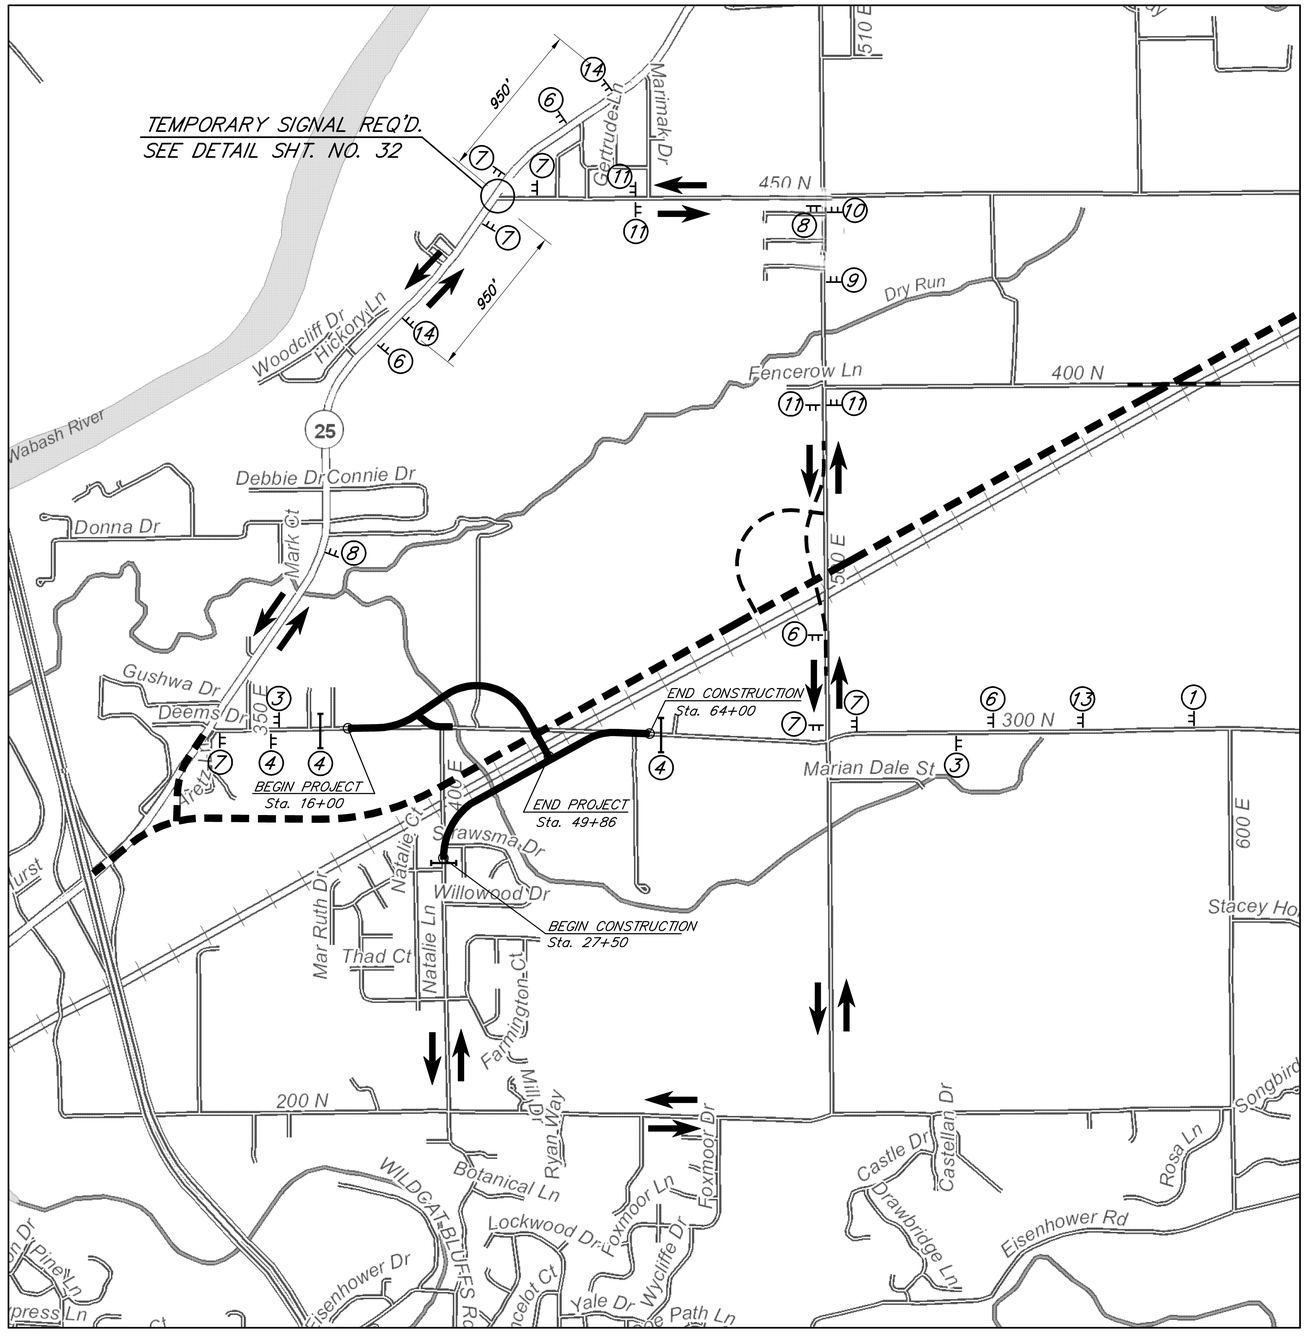

THE CONTRACTOR SHALL BE RESPONSIBLE TO PROVIDE SIGNS AND PLACEMENT OF SAID SIGNS IN COMPLIANCE WITH THE IMUTCD (LATEST EDITION) AND THE CURRENT INDOT STANDARDS.

NOTE:
Construction & Detour Signage to be Completed Upon Concurrence of Detour Routes & Phasing.

SYMBOL	MESSAGE	CODE	TYPE	QUANTITY
(1)	ROAD CLOSED AHEAD	XW20-3	A	1
(3)	END CONSTRUCTION	XG20-2	A	2
(4)	ROAD CLOSURE SIGN ASSEMBLY W/SIGN "ROAD CLOSED TO THRU TRAFFIC"	R11-4	A	3
(6)	ADVANCE TURN DETOUR ROUTE MARKER ASSEMBLY	XM4-8 M1-6 M5-1(R or L)S		4
(7)	DIRECTIONAL DETOUR ROUTE MARKER ASSEMBLY	XM4-8 M1-6 M6-1S		6
(8)	CONFIRMING DETOUR ROUTE MARKER ASSEMBLY	XM4-8 M1-6 M6-3S		2
(9)	ADVANCE TURN DETOUR ROUTE MARKER ASSEMBLY	XM4-8 M1-6 M1-6 M5-1(R or L)S		1
(10)	DIRECTIONAL DETOUR ROUTE MARKER ASSEMBLY	XM4-8 M1-6 M1-6 M6-1S		1
(11)	CONFIRMING DETOUR ROUTE MARKER ASSEMBLY	XM4-8 M1-6 M1-6 M6-3S		4
(12)	ROAD CONSTRUCTION AHEAD	XW20-1	A	–
(13)	ROAD CLOSED 1 MILE AHEAD	R11-3	A	1
(14)	SIGNAL AHEAD	W3-3	A	2

(6)



ADVANCE TURN DETOUR ROUTE MARKER ASSEMBLY
SCALE: NONE

(7)



DIRECTIONAL DETOUR ROUTE MARKER ASSEMBLY
SCALE: NONE

(8)



CONFIRMING DETOUR ROUTE MARKER ASSEMBLY
SCALE: NONE

(9)



ADVANCE TURN DETOUR ROUTE MARKER ASSEMBLY
SCALE: NONE

(10)



DIRECTIONAL DETOUR ROUTE MARKER ASSEMBLY
SCALE: NONE

(11)



CONFIRMING DETOUR ROUTE MARKER ASSEMBLY
SCALE: NONE

LEGEND

UNDER CONSTRUCTION
FUTURE CONSTRUCTION
TYPE III -B BARRICADE
TRAFFIC SIGN
DETOUR ROUTE
CLOSE

BF&S
Butler Fairman Seufert
CIVIL ENGINEERS
8450 WESTFIELD BLVD., SUITE 300
INDIANAPOLIS, IN. 46240
317 713-4615
FAX 317 713-4616
509 WEST 84TH DRIVE, SUITE G
MERRILLVILLE, IN. 46410
219 769-2333
FAX 219 769-2377

RECOMMENDED FOR APPROVAL: _____ DESIGN ENGINEER DATE

DESIGNED: B.Z. DRAWN: J.M.
CHECKED: D.I. CHECKED: B.Z.

INDIANA
DEPARTMENT OF TRANSPORTATION

C.R. 300 N. & 400 E.
DETOUR ROUTE

HORIZONTAL SCALE	FILE
1" = 1000'	4265
VERTICAL SCALE	DESIGNATION
1" = 1000'	0500648
SURVEY BOOK	SHEET
17222	07 OF 123
CONTRACT	PROJECT
IB-30837	NH-071-5(010)

BFS NO. 4265.07

R: \4265\AUTOCAD\ROAD\CR300NLSR-1\4265R302.dwg 11-24-08 AT 07:10 1 BKM
