




























ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21			
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	
1			State of Indiana Genesys Cloud Project	310.38 days																			
2			All Contracts Signed & Purchase Orders Provided	1 day	SOI																		
3			Initiate & Define Phase	299.38 days																			
4			Project Planning	10 days																			
5			Determine Priority/Complexity/Size of Each of 18 Departmens	2 days	Avtex,SOI																		
6			Determine Number of Genesys Cloud Organizations Needed (Dev & Prod)	2 days	Avtex,SOI																		
7			Determine if Some Departments Are Similar to Others	3 days	Avtex,SOI																		
8			Determine How Many Training Sessions Needed For Each Department	3 days	Avtex,SOI																		
9			Determine Which Department Uses Speech - What Flavor of Speech	1 day																			
10			Prepare 1st Draft Project Plan	5 days	Avtex																		
11			Initiation	14.38 days																			
12			Send Genesys Cloud Welcome Letter for Each Needed Genesys Cloud Org	2 hrs	Avtex																		
13			Order Licenses	2 hrs	Avtex																		
14			Order Any Needed Hardware	2 hrs	Avtex																		
15			Provide Any Other Needed Hardware	1 day	SOI																		
16			Complete Tasks from Each Welcome Let	4 hrs	SOI																		
17			Create Org Name for Each Org	1 hr	Avtex																		

Project: Sample PureCloud Imp

Date: Fri 9/17/21

Task

Split


Milestone


Summary


Project Summary


Inactive Task


Inactive Milestone

















Inactive Summary

Manual Task


Duration-only


Manual Summary Rollup


Manual Summary


Start-only


Finish-only


















External Tasks


External Milestone


Deadline


Progress


Manual Progress

































































































ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21			
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	
18			Set Up Each Genesys Cloud Org	1 day	Genesys																		
19			Avtex Planning Meeting	1 hr	Avtex																		
20			Kickoff Meeting	2 hrs	Avtex,SOI																		
21			Order 3 Test Numbers from Genesys Clo	1 hr	SOI																		
22			Prepare Facility, Network, Firewall, Servers, Hardware	4 days	SOI																		
23			Perform Network Assessment & Web RTC Test - Results to Avtex	4 days	SOI																		
24			Design	174 days																			
25			Department 1	19 days																			
26			Review of Current PureConnect Environment(s)	9 days	Avtex,SOI																		
27			Call Flows	9 days	Avtex,SOI																		
28			Gather & Document Configuration Information	9 days	Avtex,SOI																		
29			Integrations	9 days	Avtex,SOI																		
30			Discuss Test Data	9 days	Avtex,SOI																		
31			Complete Prompt Worksheet	9 days	SOI																		
32			Identify Voice Talent	9 days	SOI																		
33			Review Design Documents	4 days	SOI																		
34			Revise Design Documents	5 days	Avtex																		
35			Sign Off on Design Documents	1 day	SOI																		
36			Department 2	19 days																			

Project: Sample PureCloud Imp

Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21					
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W			
37			Review of Current PureConnect Environment(s)	10 days	Avtex,SOI																				
38			Call Flows	10 days	Avtex,SOI																				
39			Gather & Document Configuration Information	10 days	Avtex,SOI																				
40			Integrations	10 days	Avtex,SOI																				
41			Discuss Test Data	10 days	Avtex,SOI																				
42			Complete Prompt Worksheet	10 days	SOI																				
43			Identify Voice Talent	10 days	SOI																				
44			Review Design Documents	4 days	SOI																				
45			Revise Design Documents	4 days	Avtex																				
46			Sign Off on Design Documents	1 day	SOI																				
47			Department 3	16 days																					
58			Department 4	16 days																					
69			Department 5	19 days																					
80			Department 6	19 days																					
91			Department 7	19 days																					
102			Department 8	19 days																					
113			Department 9	19 days																					
124			Department 10	19 days																					
135			Department 11	19 days																					
146			Department 12	19 days																					
157			Department 13	18 days																					
168			Department 14	18 days																					

Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task

Split


Milestone


Summary


Project Summary


Inactive Task


Inactive Milestone

















Inactive Summary

Manual Task


Duration-only


Manual Summary Rollup


Manual Summary


Start-only


Finish-only


















External Tasks


External Milestone


Deadline


Progress


Manual Progress
































































































ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21				
						M	T	W	T	F	S		S	M	T	W	T	F	S	S	M	T	W	
179			Department 15	19 days																				
190			Department 16	19 days																				
201			Department 17	18 days																				
212			Department 18	18 days																				
223			Build	175 days																				
224			Department 1	21 days																				
225			Configuration	11 days	Avtex																			
226			Development	11 days	Avtex																			
227			Voice Recordings	11 days	SOI																			
228			Prepare Test Plans	11 days	SOI,Avtex																			
229			Prepare Training	11 days	Avtex																			
230			Unit Testing	9 days	Avtex																			
231			Department 2	21 days																				
232			Configuration	11 days	Avtex																			
233			Development	11 days	Avtex																			
234			Voice Recordings	11 days	SOI																			
235			Prepare Test Plans	11 days	SOI,Avtex																			
236			Prepare Training	11 days	Avtex																			
237			Unit Testing	9 days	Avtex																			
238			Department 3	19 days																				
245			Department 4	19 days																				
252			Department 5	19 days																				
259			Department 6	19 days																				

Project: Sample PureCloud Imp

Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21				
						M	T	W	T	F	S		S	M	T	W	T	F	S	S	M	T	W	
266			Department 7	19 days																				
273			Department 8	19 days																				
280			Department 9	19 days																				
287			Department 10	19 days																				
294			Department 11	19 days																				
301			Department 12	19 days																				
308			Department 13	18 days																				
315			Department 14	18 days																				
322			Department 15	19 days																				
329			Department 16	19 days																				
336			Department 17	18 days																				
343			Department 18	18 days																				
350			Test & Train	92 days																				
351			Department 1	32 days																				
352			Quality Assurance Testing	14 days	Avtex																			
353			Training	5 days	Avtex,SOI																			
354			User Acceptance Testing	12 days	Avtex,SOI																			
355			Department 2	32 days																				
356			Quality Assurance Testing	14 days	Avtex																			
357			Training	5 days	Avtex,SOI																			
358			User Acceptance Testing	12 days	Avtex,SOI																			
359			Department 3	32 days																				
363			Department 4	32 days																				

Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks
































External Milestone

Deadline

Progress

Manual Progress

Page 5

ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21				
						M	T	W	T	F	S		S	M	T	W	T	F	S	S	M	T	W	
367			Department 5	33 days																				
371			Department 6	33 days																				
375			Department 7	33 days																				
379			Department 8	33 days																				
380			Quality Assurance Testing	14 days	Avtex																			
381			Training	4 days	Avtex,SOI																			
382			User Acceptance Testing	13 days	Avtex,SOI																			
383			Department 9	33 days																				
384			Quality Assurance Testing	14 days	Avtex																			
385			Training	4 days	Avtex,SOI																			
386			User Acceptance Testing	13 days	Avtex,SOI																			
387			Department 10	33 days																				
391			Department 11	33 days																				
395			Department 12	33 days																				
399			Department 13	33 days																				
403			Department 14	33 days																				
407			Department 15	33 days																				
411			Department 16	33 days																				
415			Department 17	33 days																				
419			Department 18	33 days																				
423			Deploy	110 days																				
424			Department 1	5 days																				
425			Deploy & Test	5 days	Avtex,SOI																			

Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task

Split


Milestone


Summary


Project Summary


Inactive Task


Inactive Milestone

















Inactive Summary

Manual Task


Duration-only


Manual Summary Rollup


Manual Summary


Start-only


Finish-only


















External Tasks


External Milestone


Deadline


Progress


Manual Progress






































ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21			
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	
426			Department 2	5 days																			
427			Deploy & Test	5 days	Avtex,SOI																		
428			Department 3	5 days																			
430			Department 4	4 days																			
432			Department 5	5 days																			
434			Department 6	5 days																			
436			Department 7	5 days																			
438			Department 8	5 days																			
440			Department 9	5 days																			
442			Department 10	3 days																			
444			Department 11	5 days																			
446			Department 12	3 days																			
448			Department 13	5 days																			
450			Department 14	5 days																			
452			Department 15	5 days																			
454			Department 16	5 days																			
456			Department 17	5 days																			
458			Department 18	1 day																			
460			Transition & Accept	109 days																			
461			Department 1	4 days																			
462			Post Deployment Support	4 days	Avtex,SOI																		
463			Department 2	4 days																			
464			Post Deployment Support	4 days	Avtex,SOI																		

Project: Sample PureCloud Imp

Date: Fri 9/17/21

Task

Split


Milestone


Summary


Project Summary


Inactive Task


Inactive Milestone

















Inactive Summary

Manual Task


Duration-only


Manual Summary Rollup


Manual Summary


Start-only


Finish-only


















External Tasks


External Milestone


Deadline


Progress


Manual Progress














































ID		Task Mode	Task Name	Duration	Resource Names	12, '21							Sep 19, '21							Sep 26, '21			
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	
465			Department 3	4 days																			
467			Department 4	4 days																			
469			Department 5	4 days																			
471			Department 6	4 days																			
473			Department 7	4 days																			
475			Department 8	4 days																			
477			Department 9	4 days																			
479			Department 10	4 days																			
481			Department 11	4 days																			
483			Department 12	4 days																			
485			Department 13	4 days																			
487			Department 14	4 days																			
489			Department 15	4 days																			
491			Department 16	4 days																			
493			Department 17	4 days																			
495			Department 18	4 days																			


--

<div>Project: Sample PureCloud Imp</div> <div>Date: Fri 9/17/21</div>	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

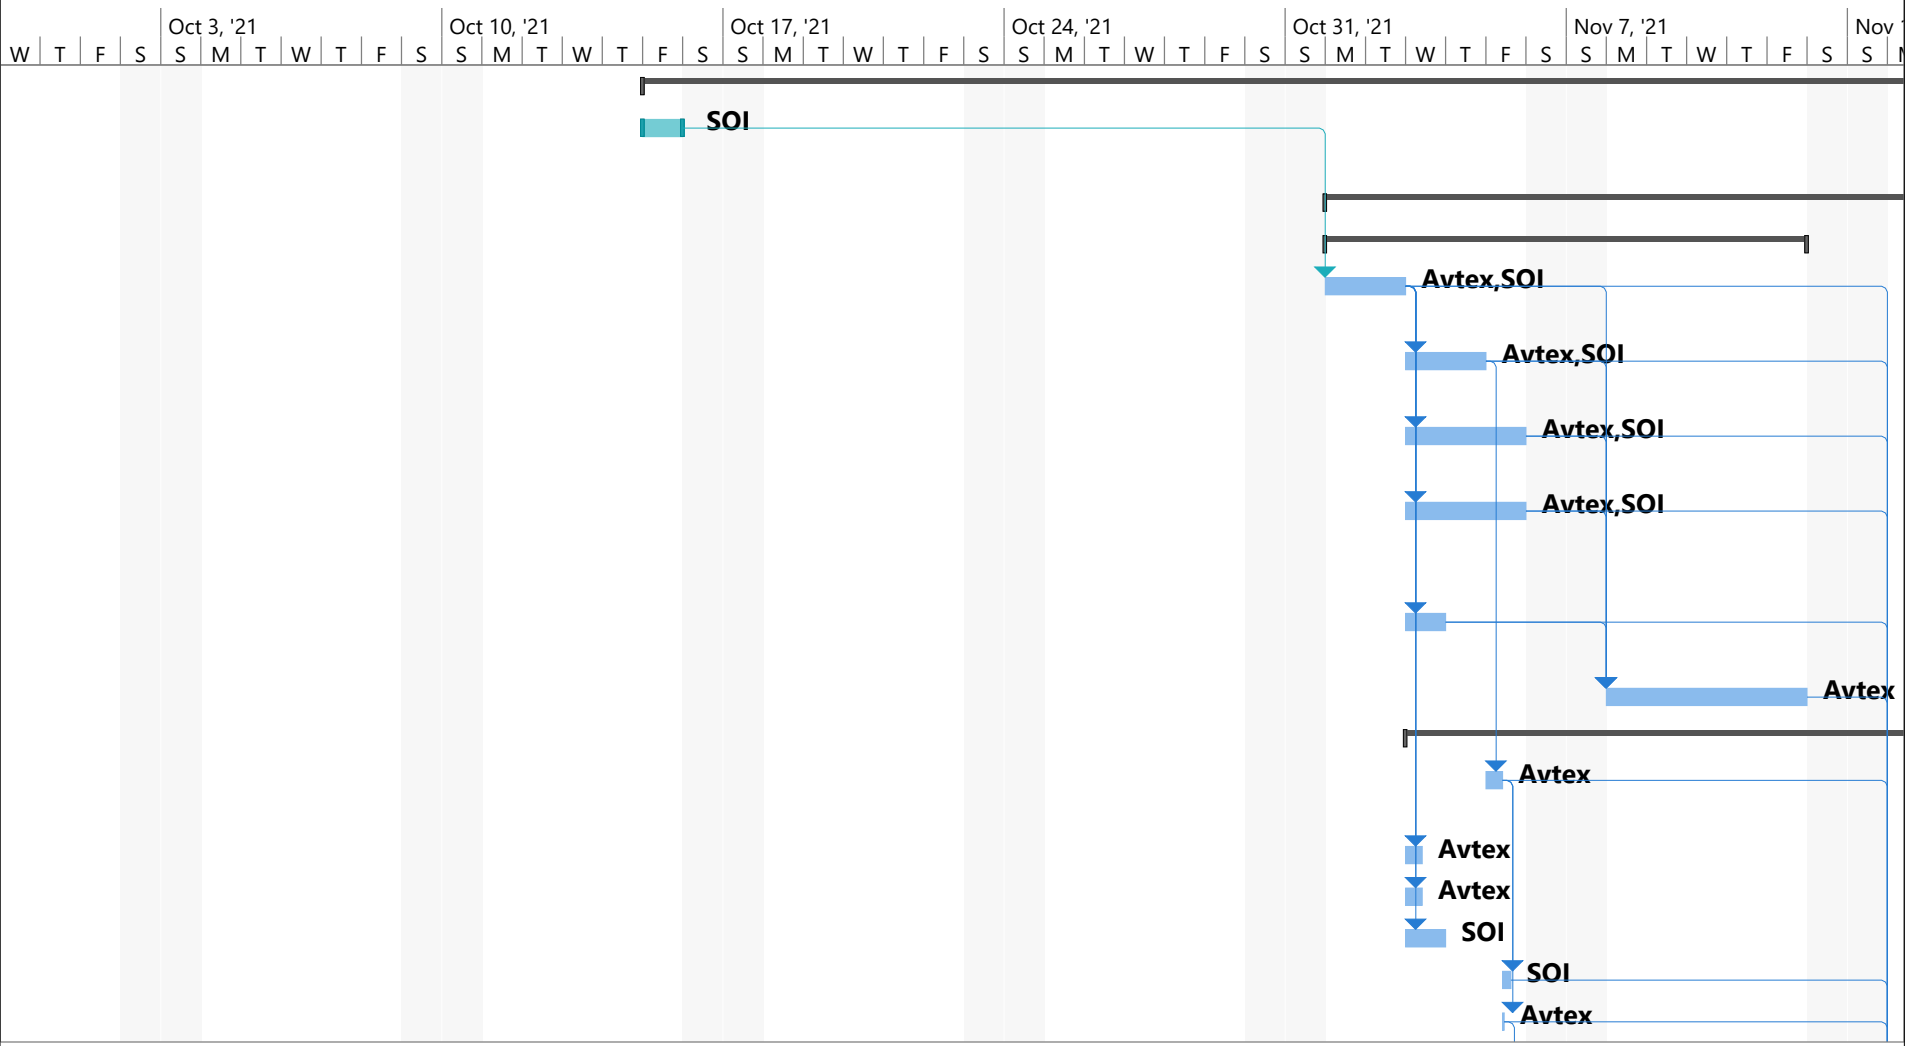








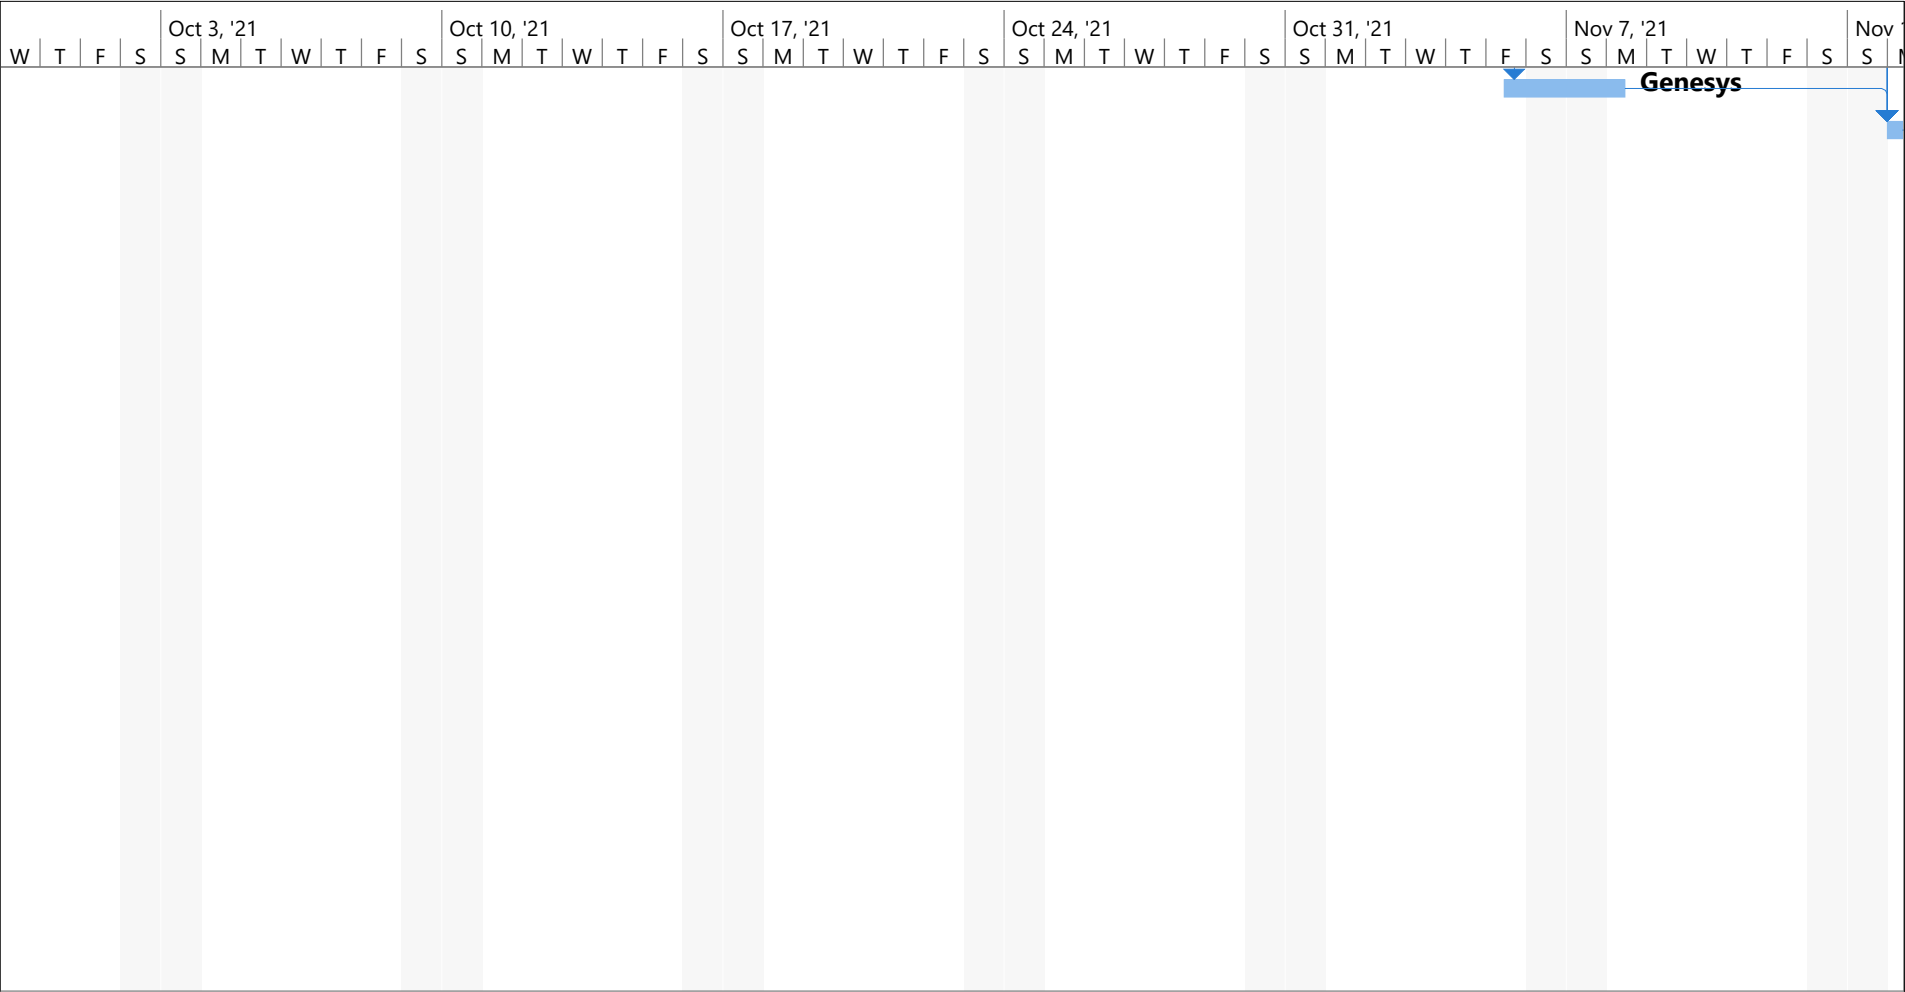












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			










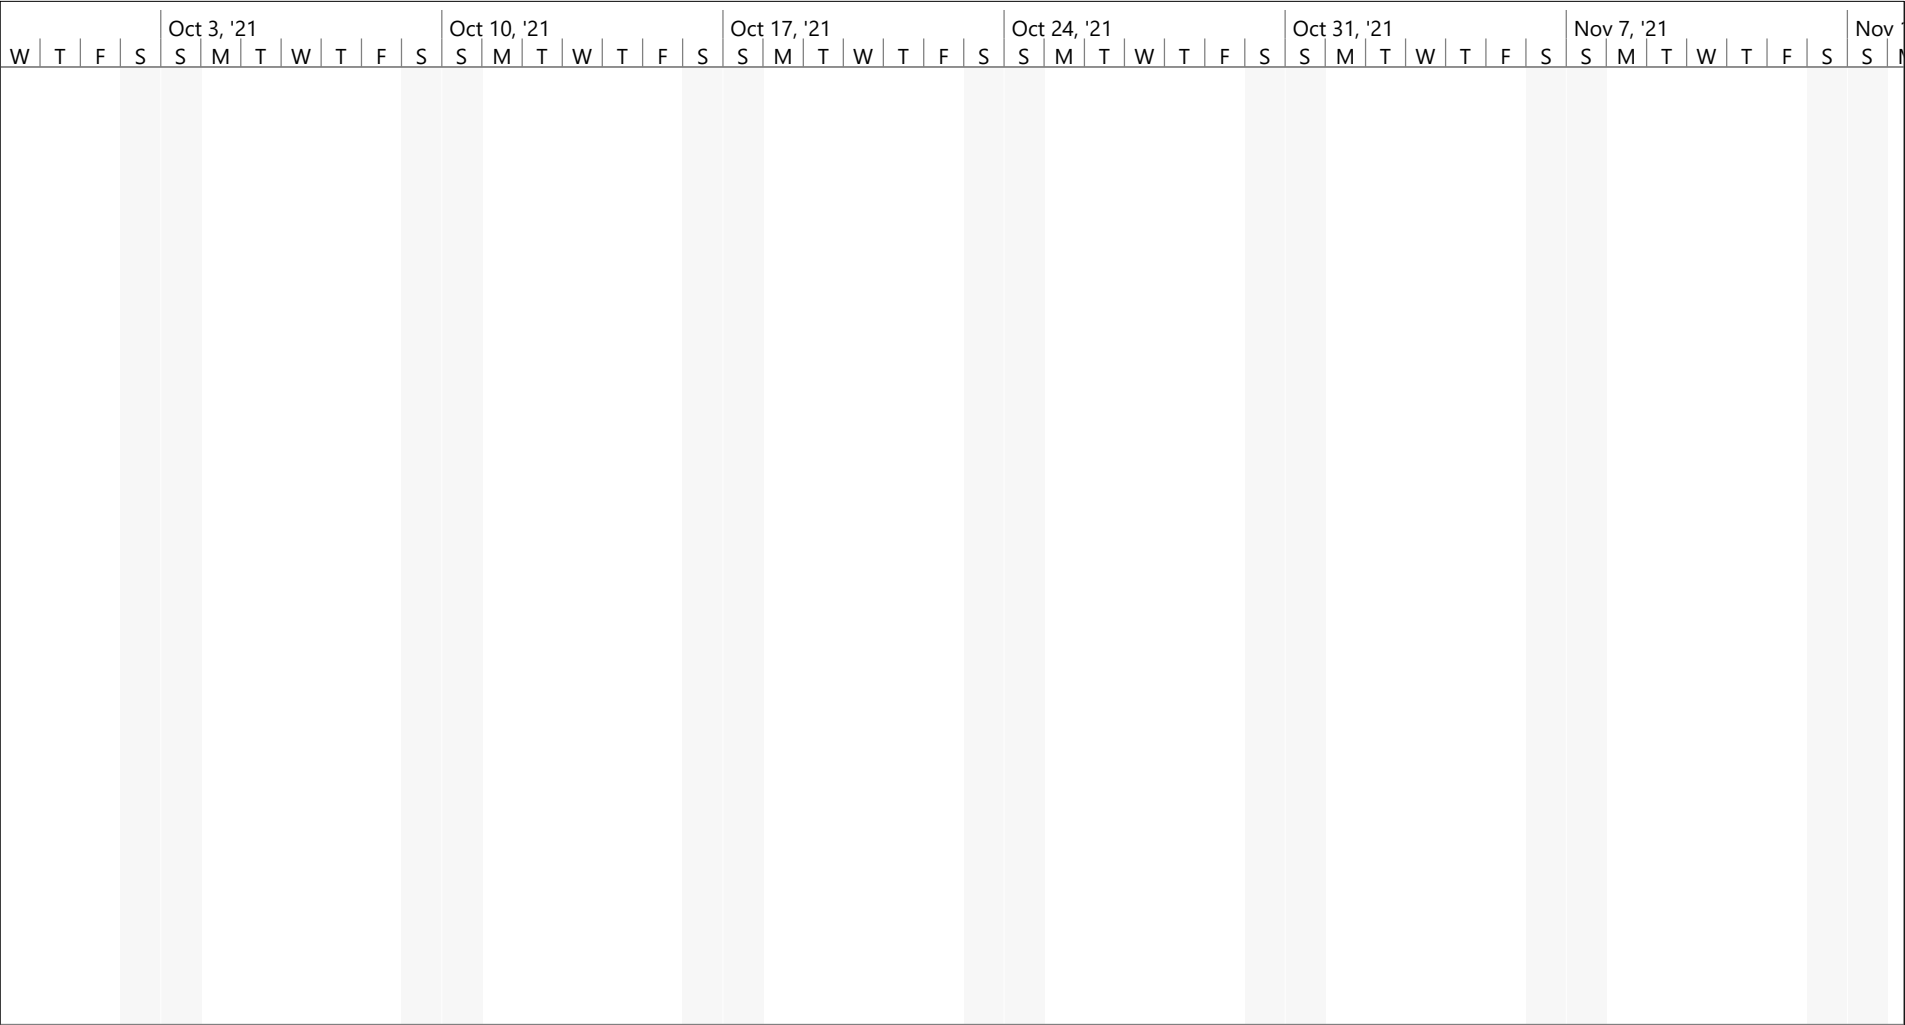












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			










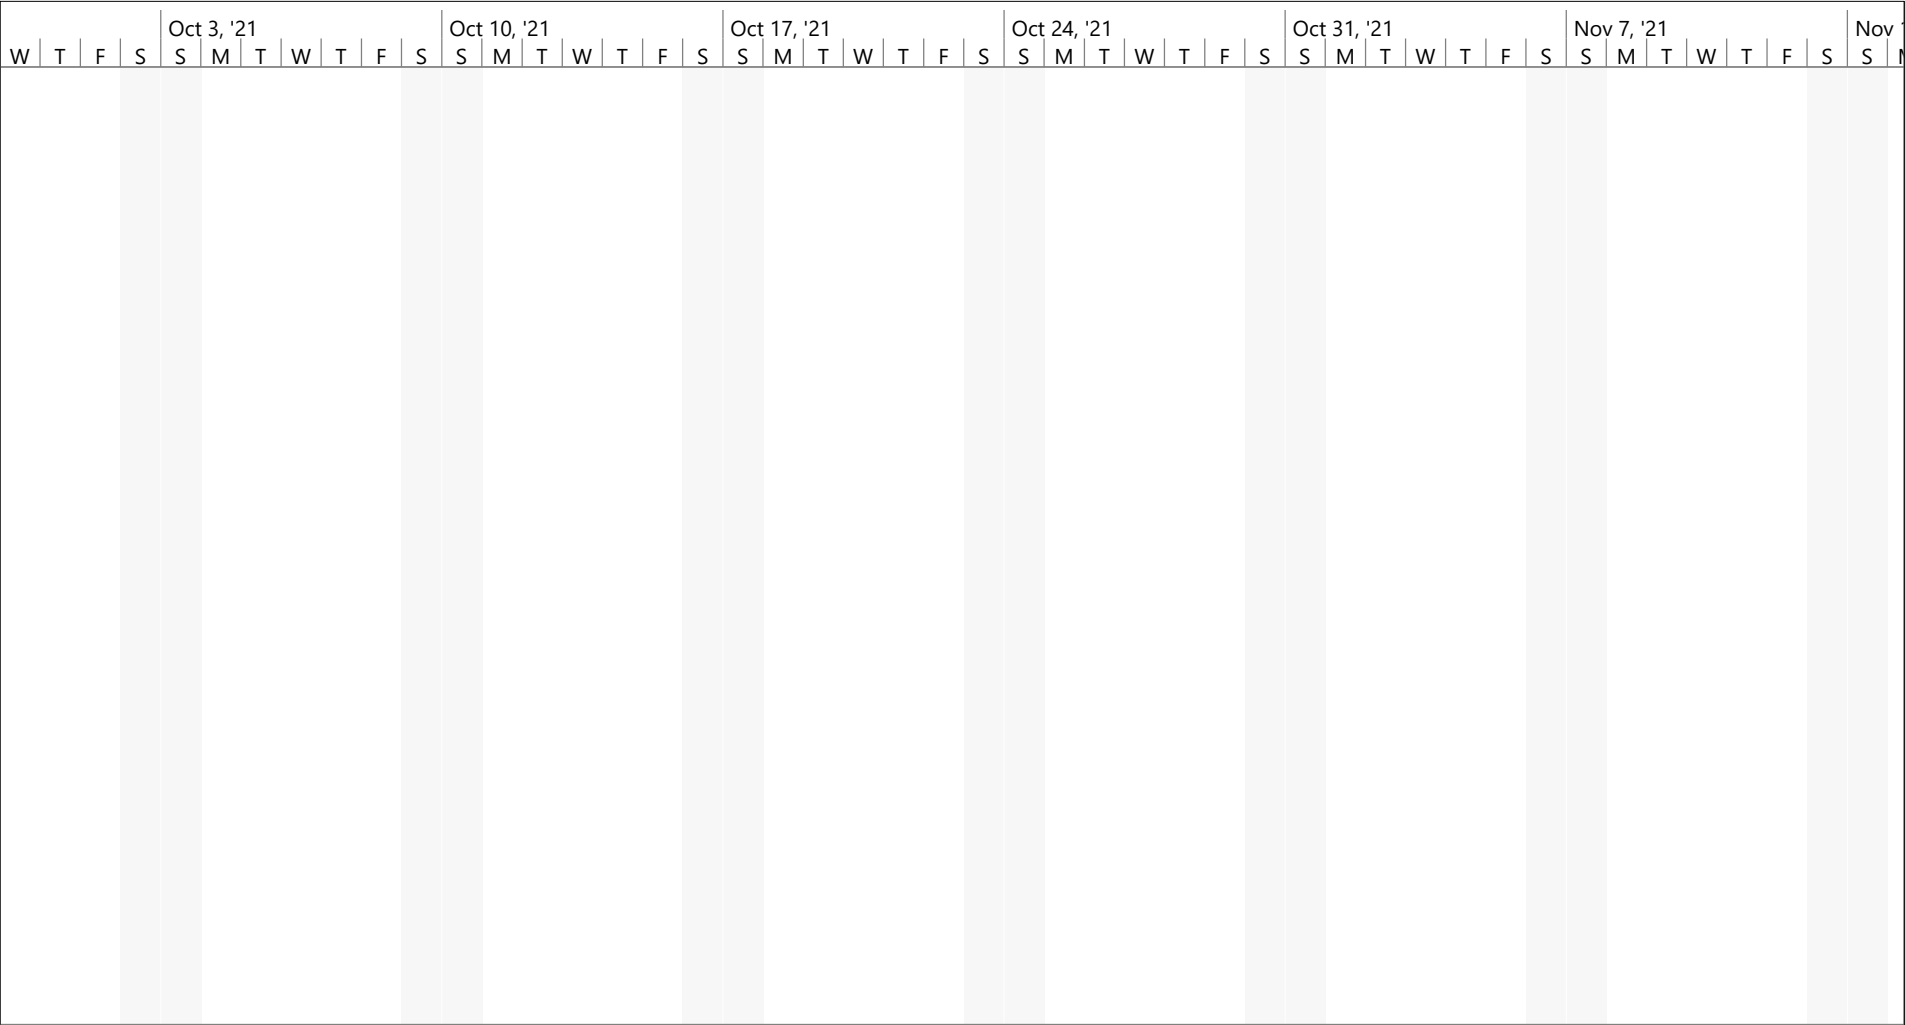












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			























Project: Sample PureCloud Imp
Date: Fri 9/17/21












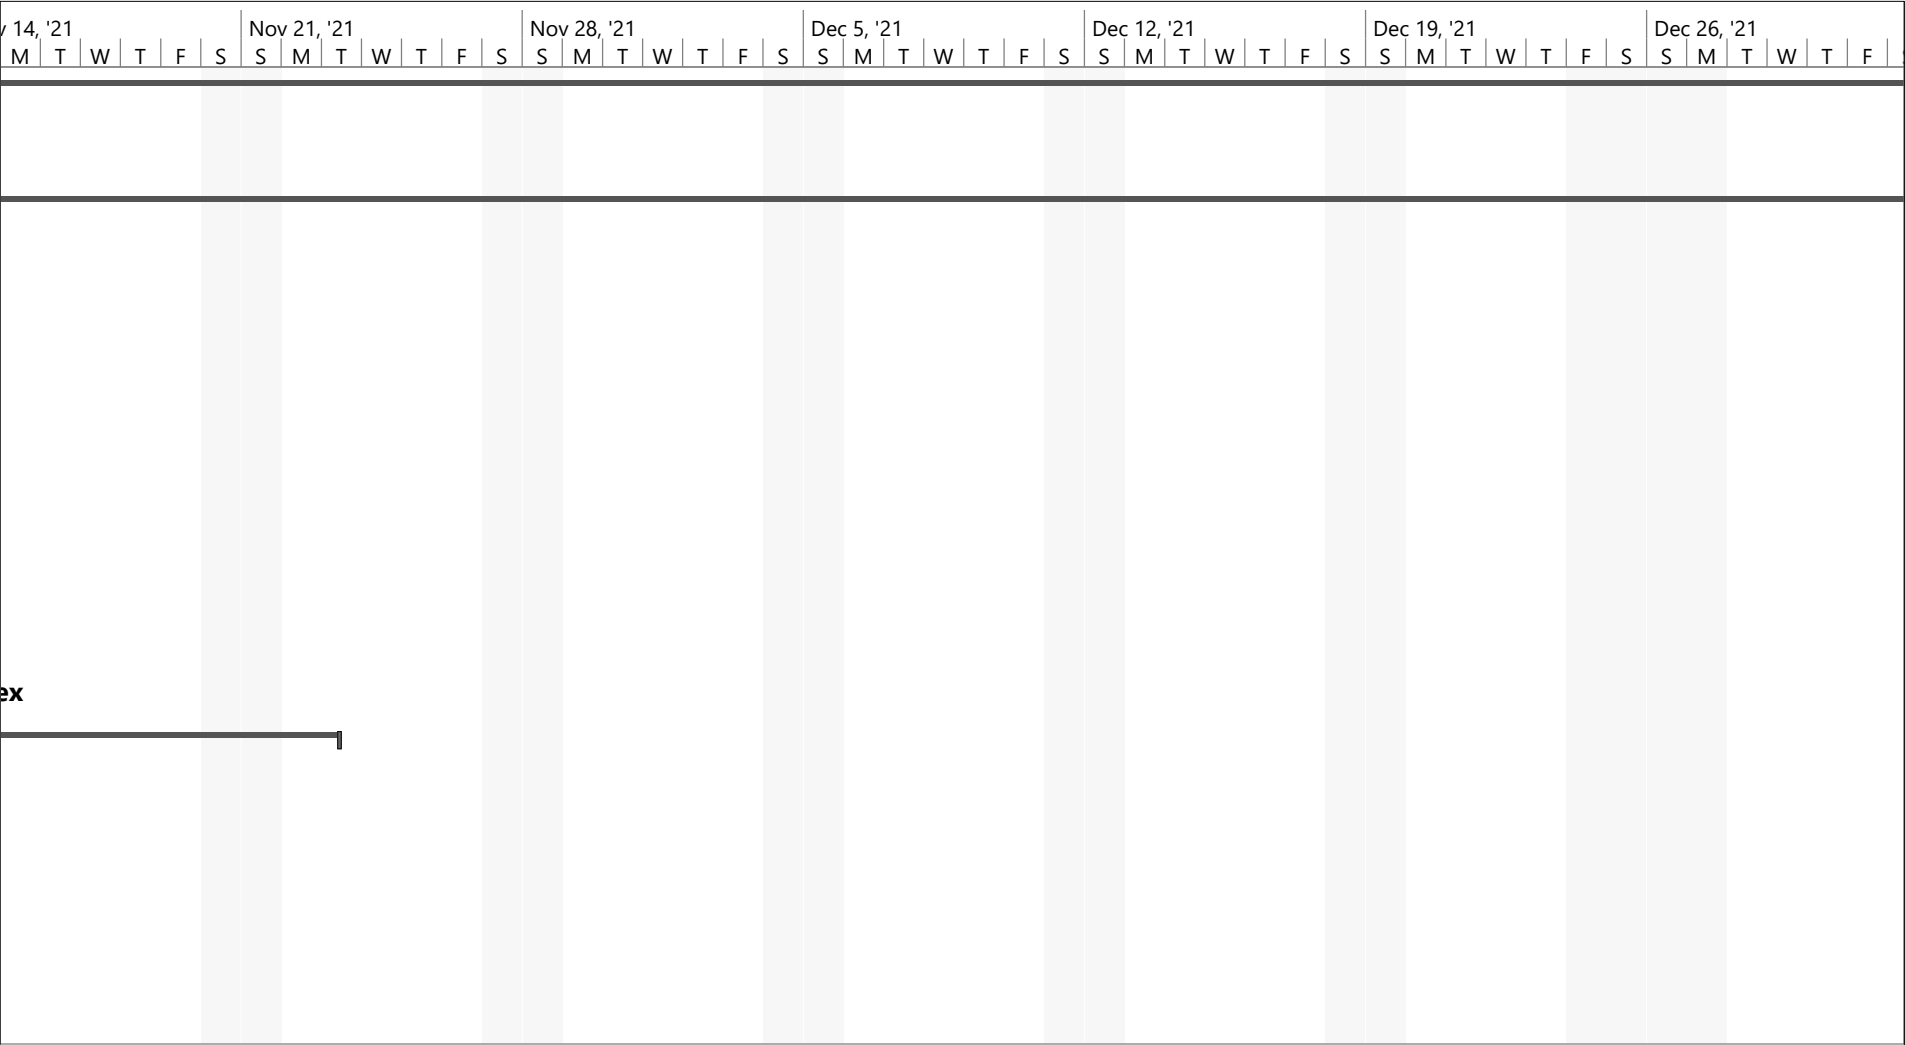







Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

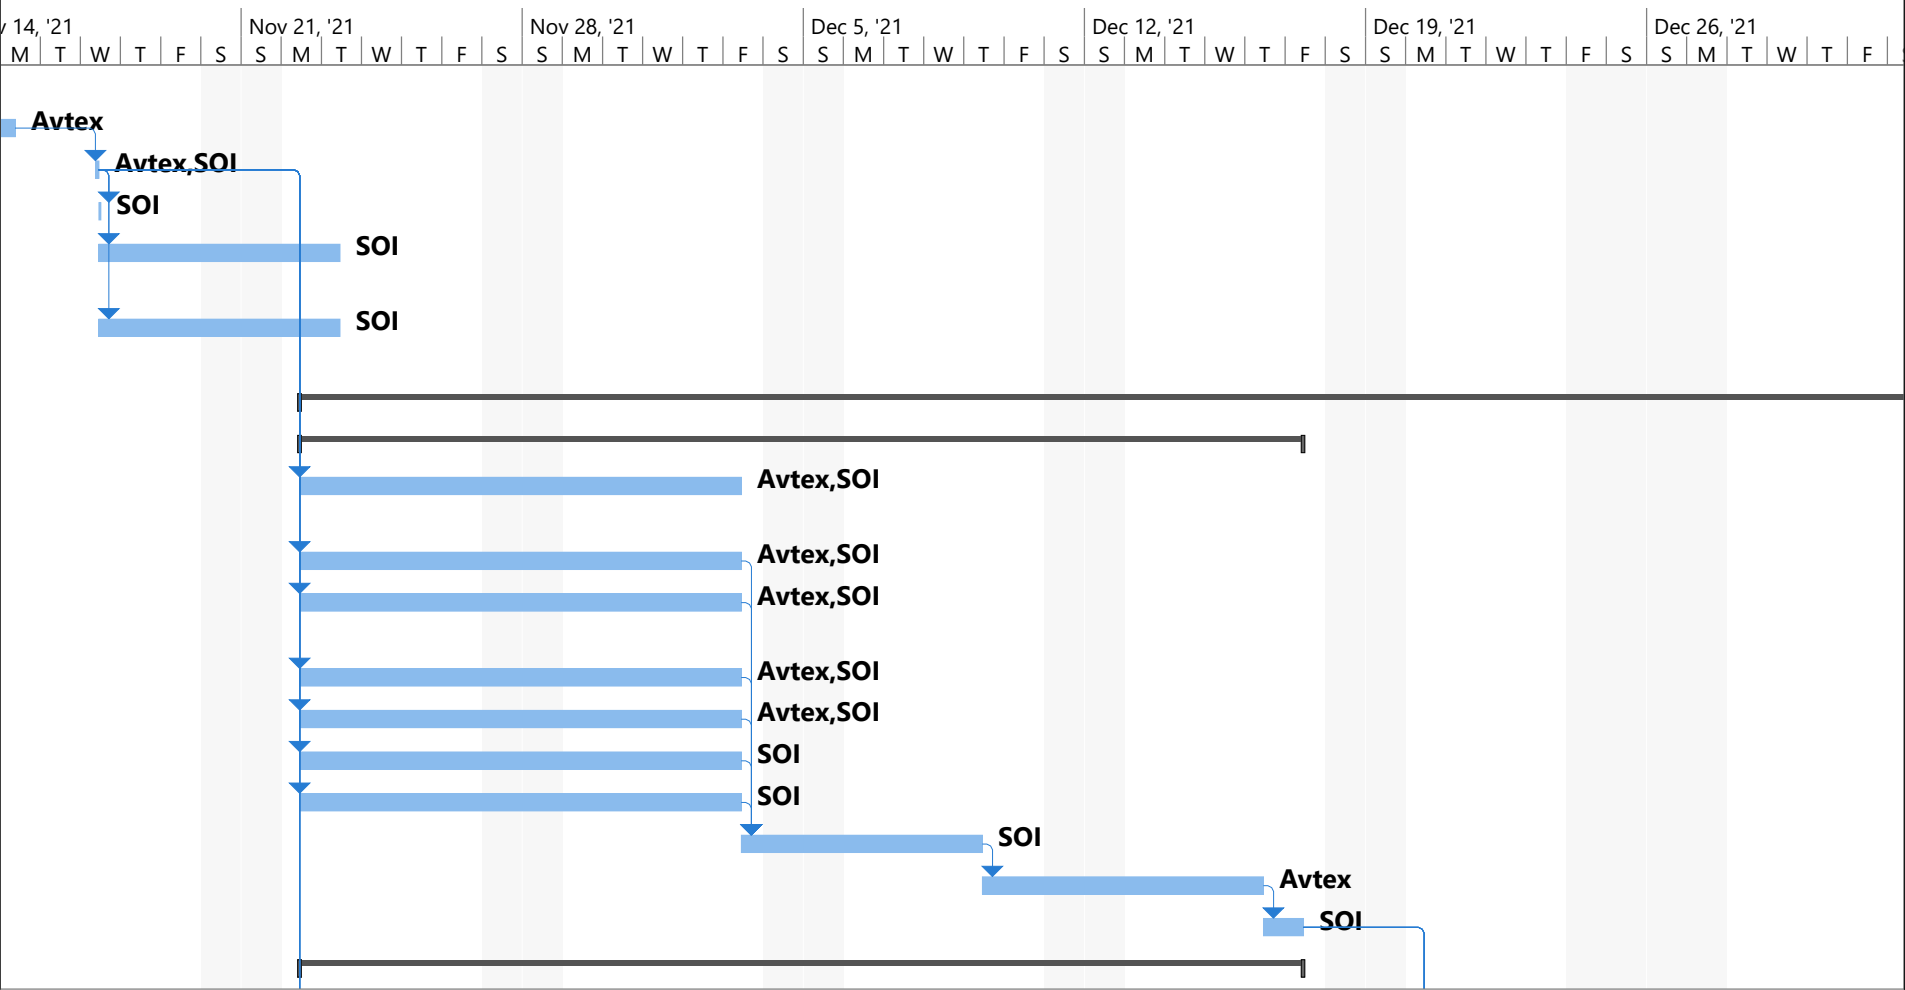


Project: Sample PureCloud Imp
Date: Fri 9/17/21




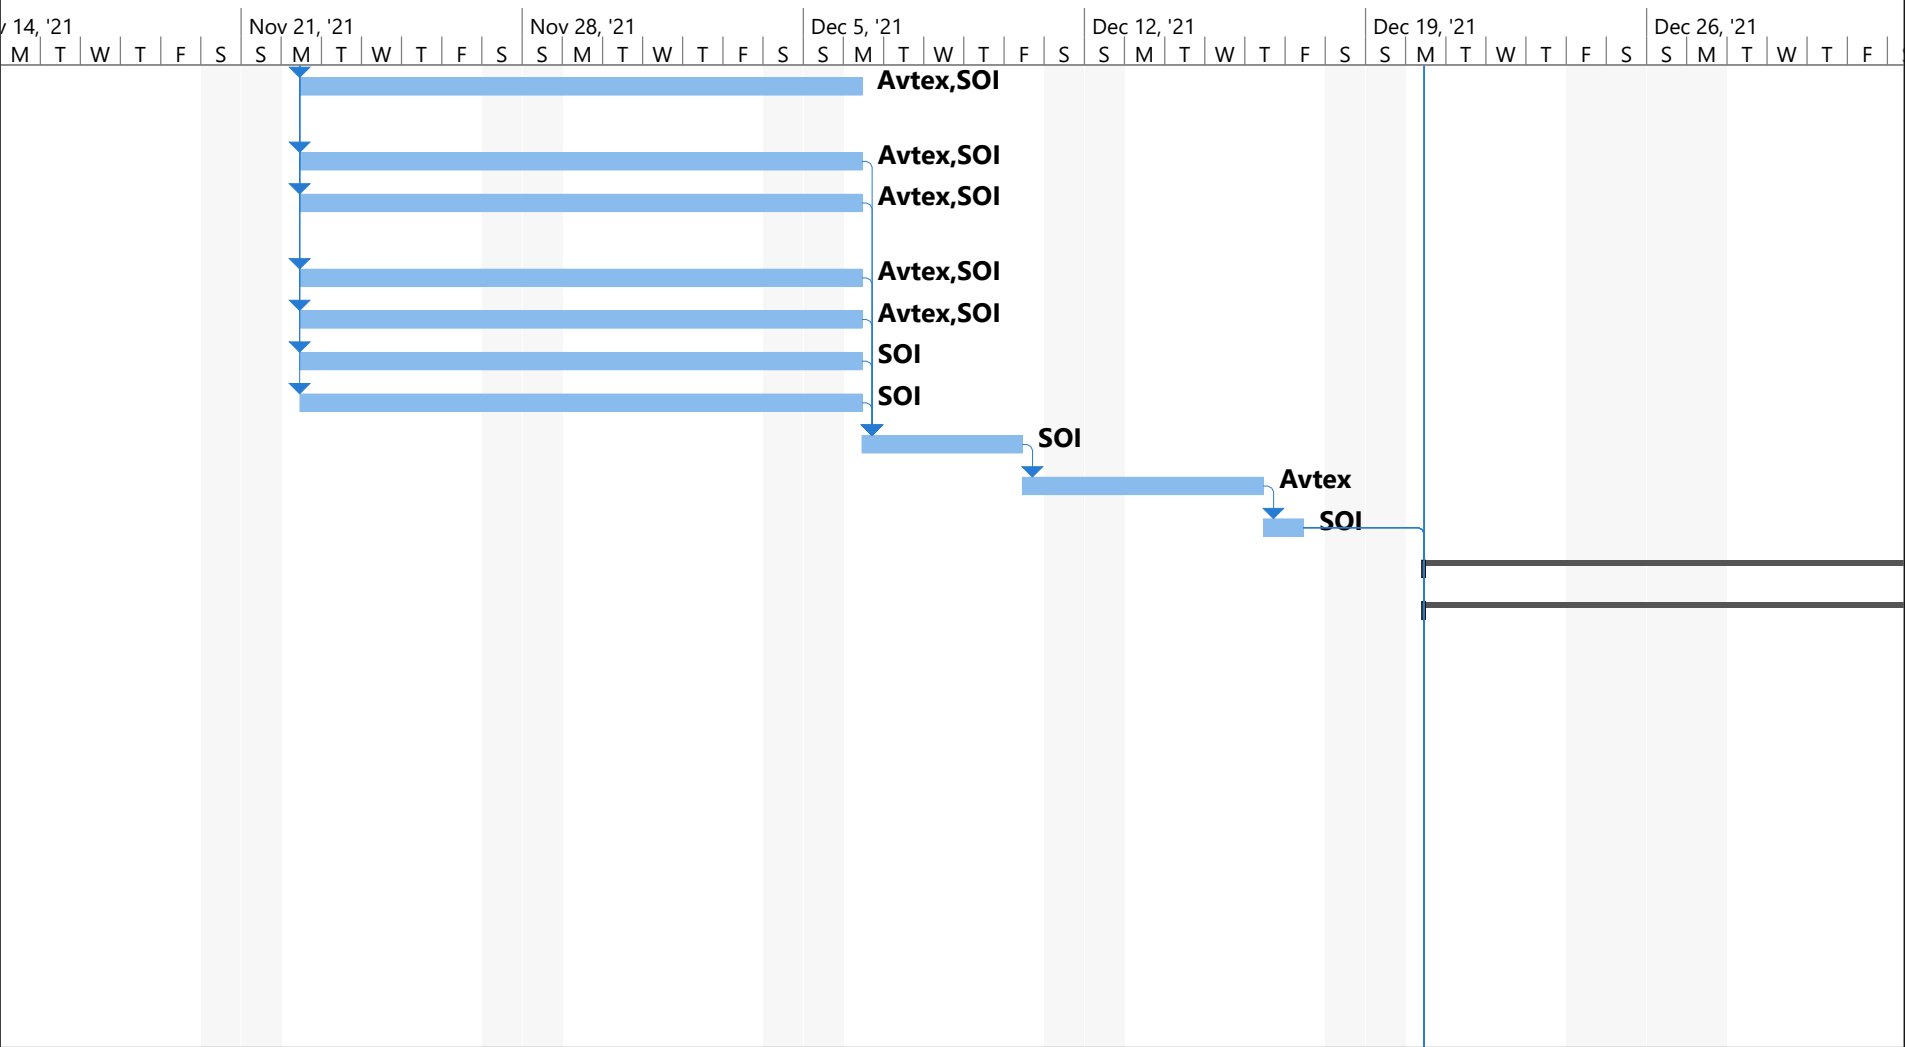



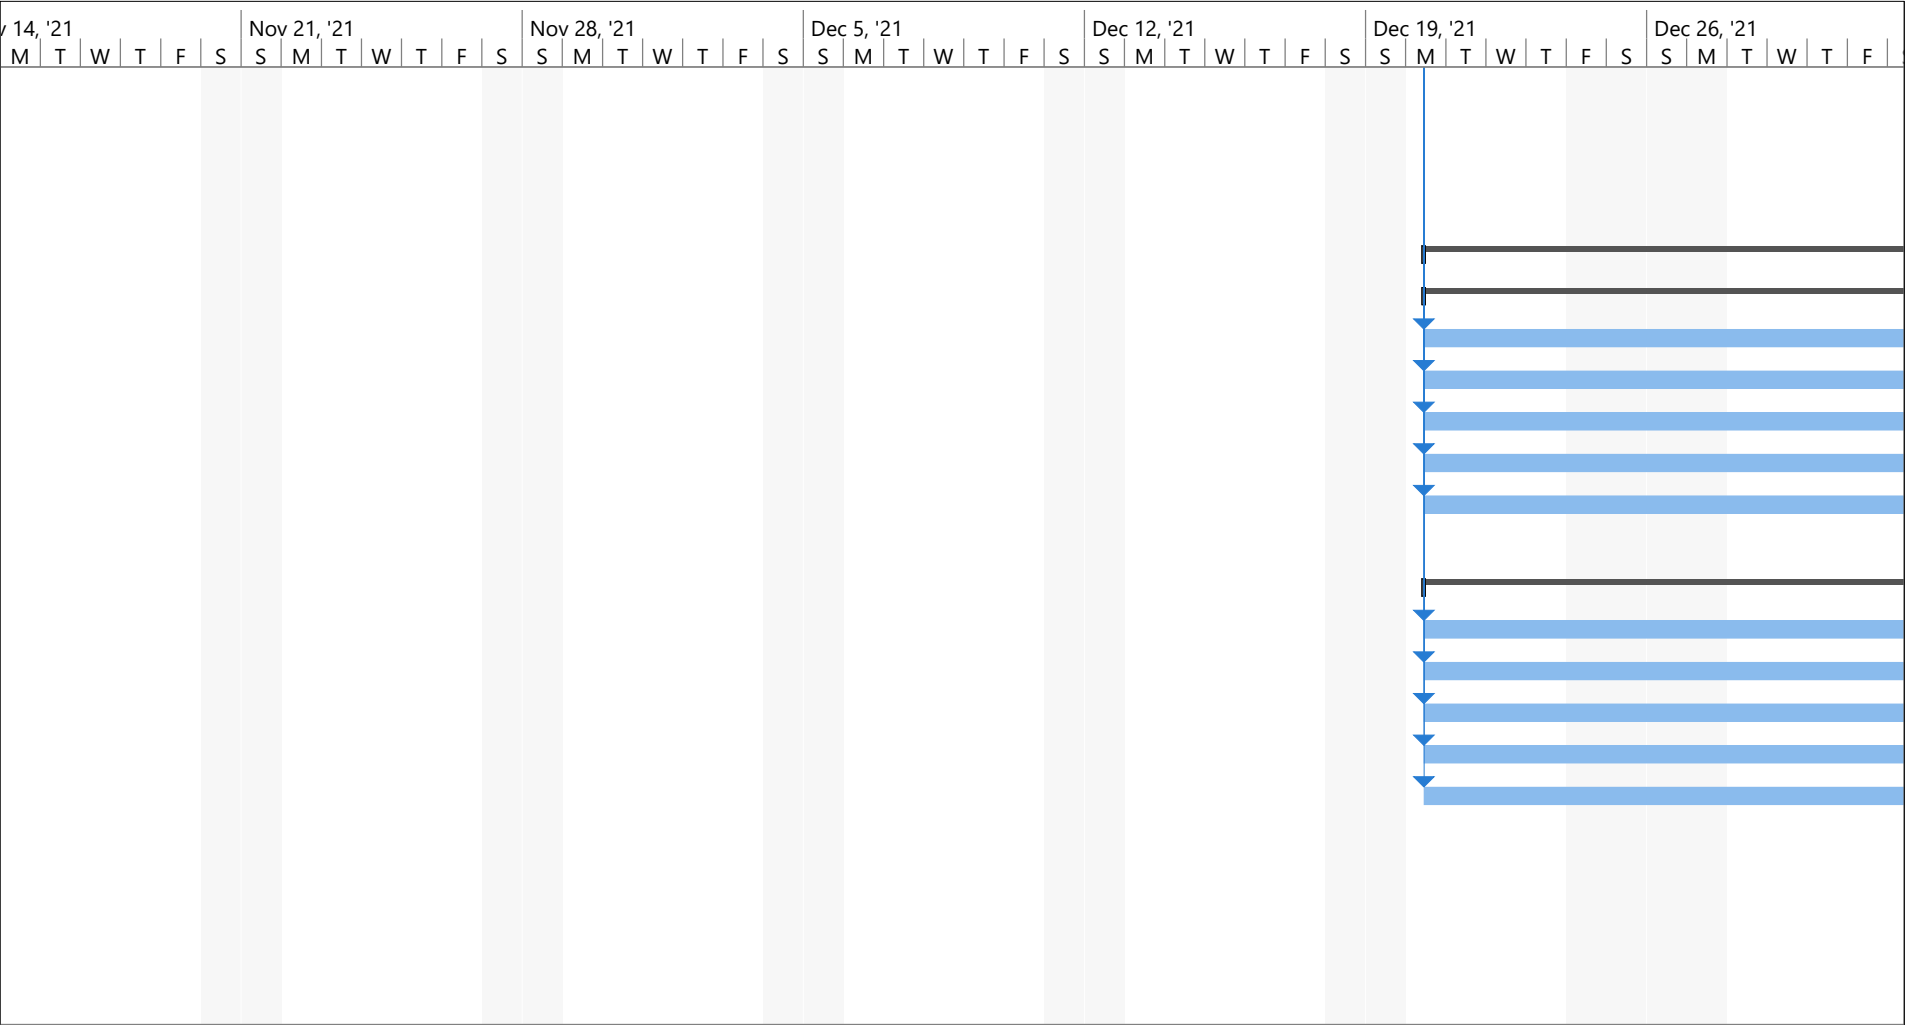











Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			










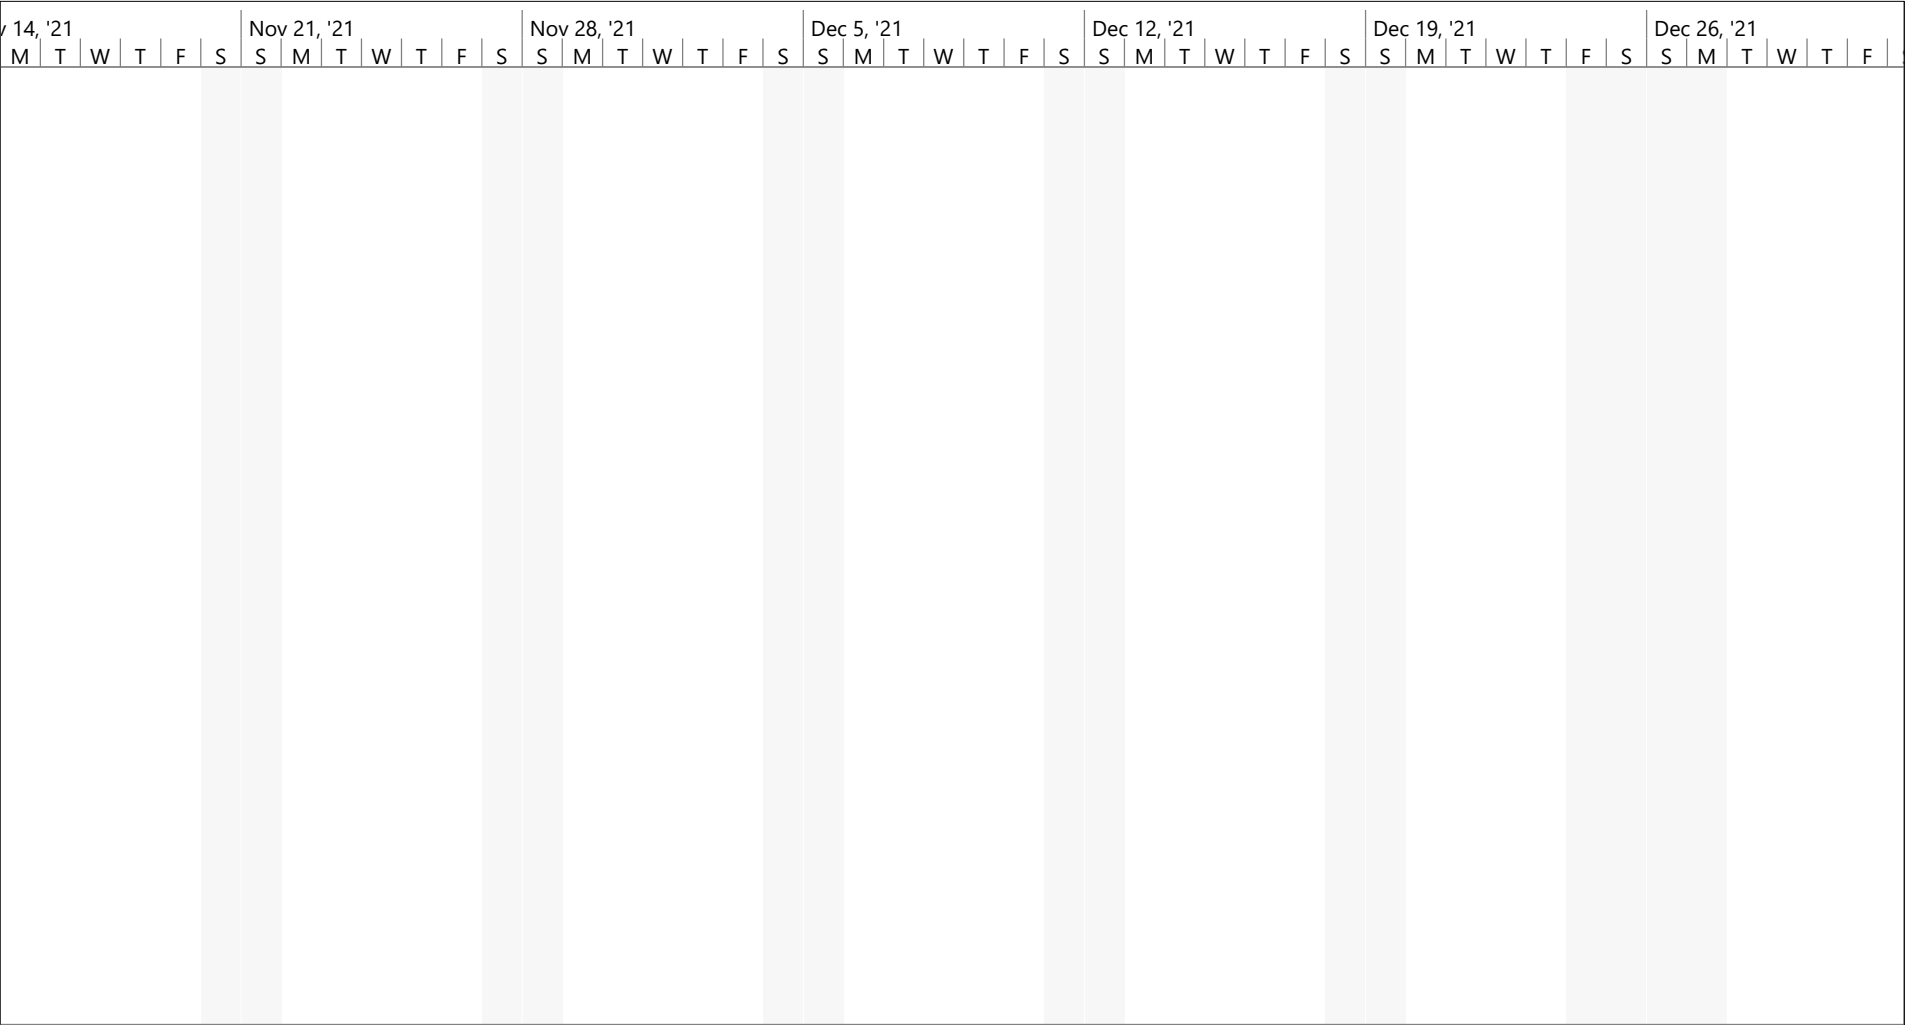












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			










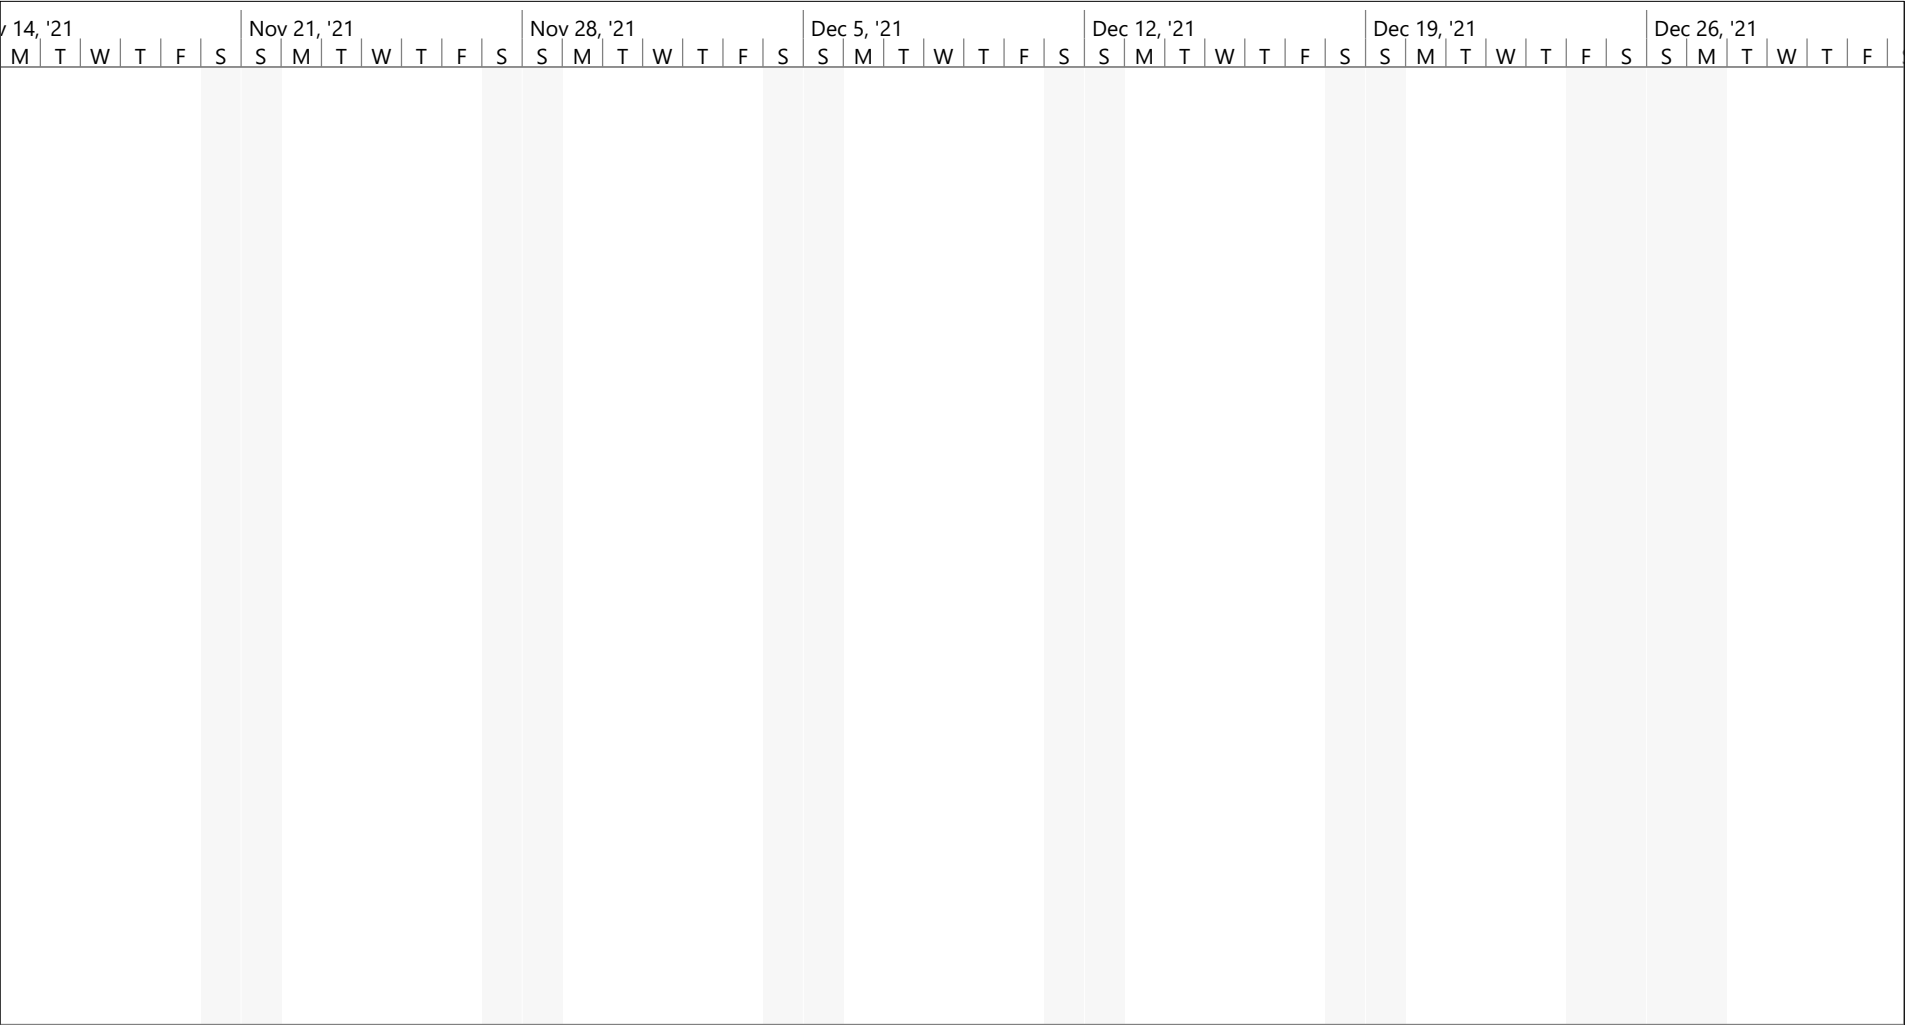












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			







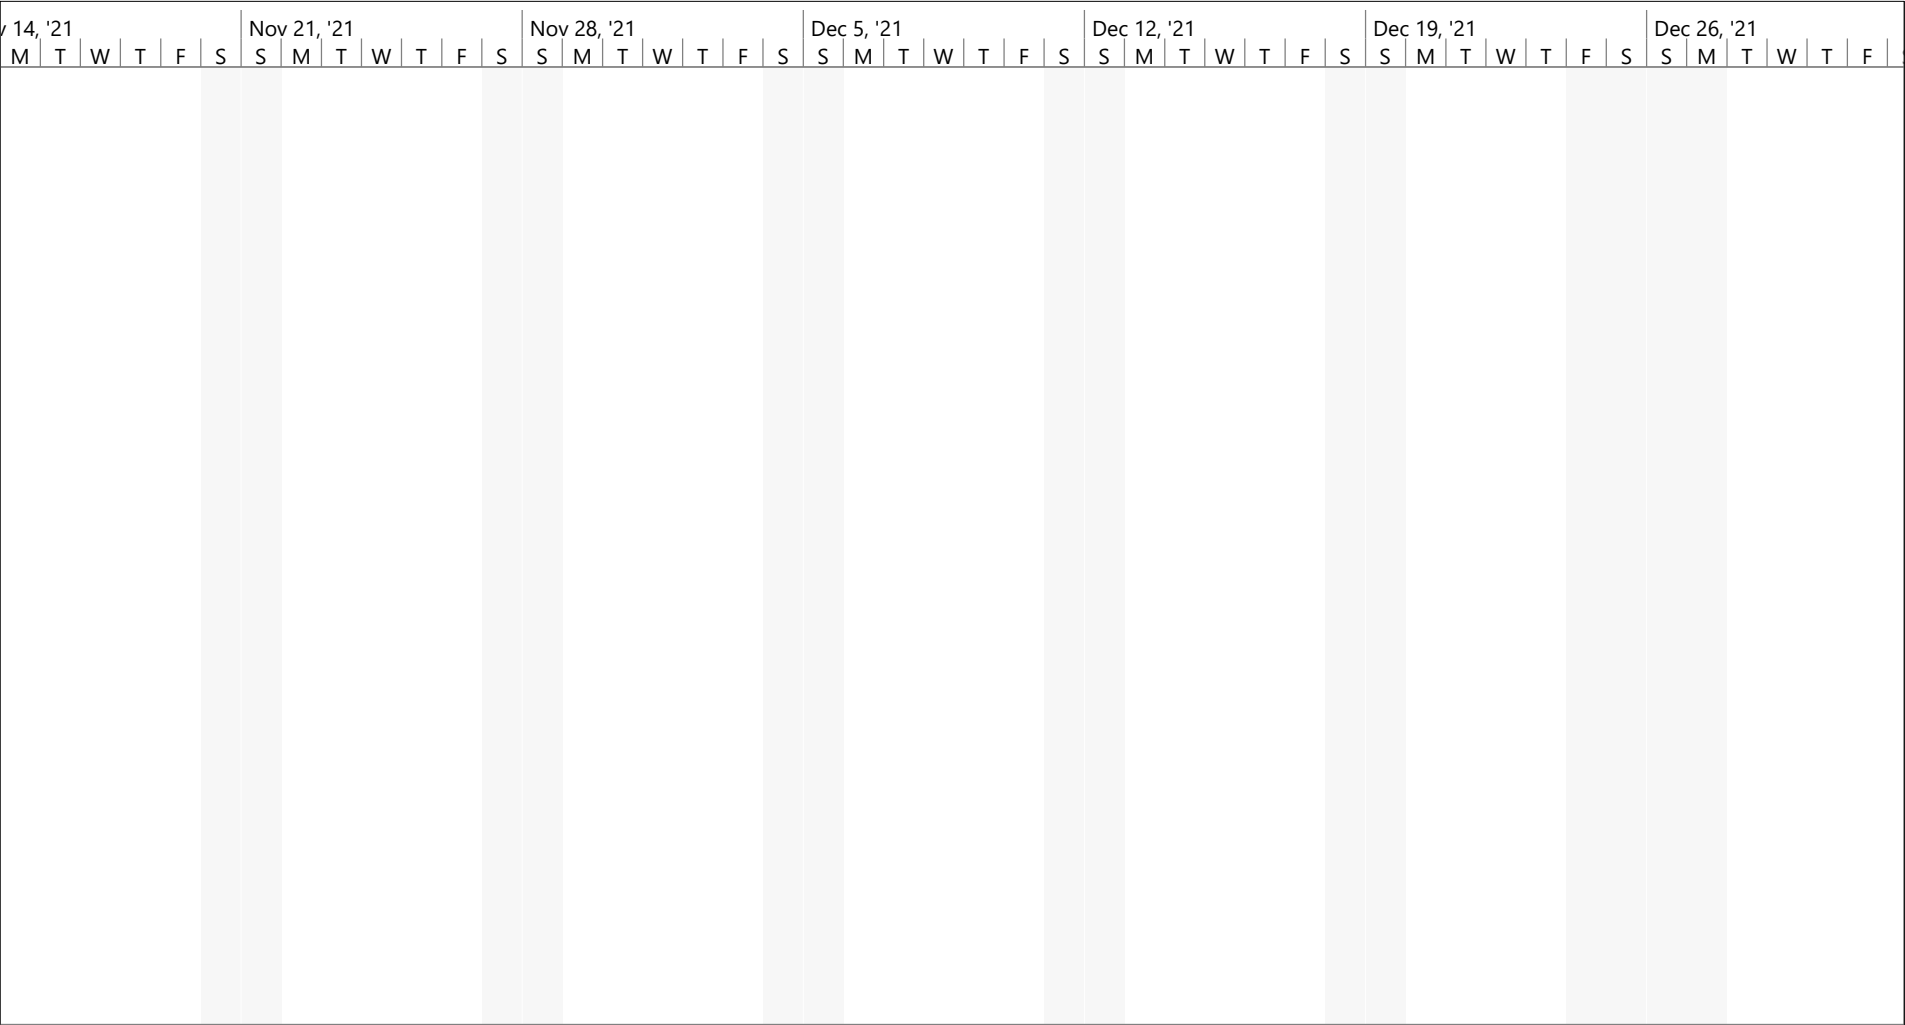















Project: Sample PureCloud Imp
Date: Fri 9/17/21




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

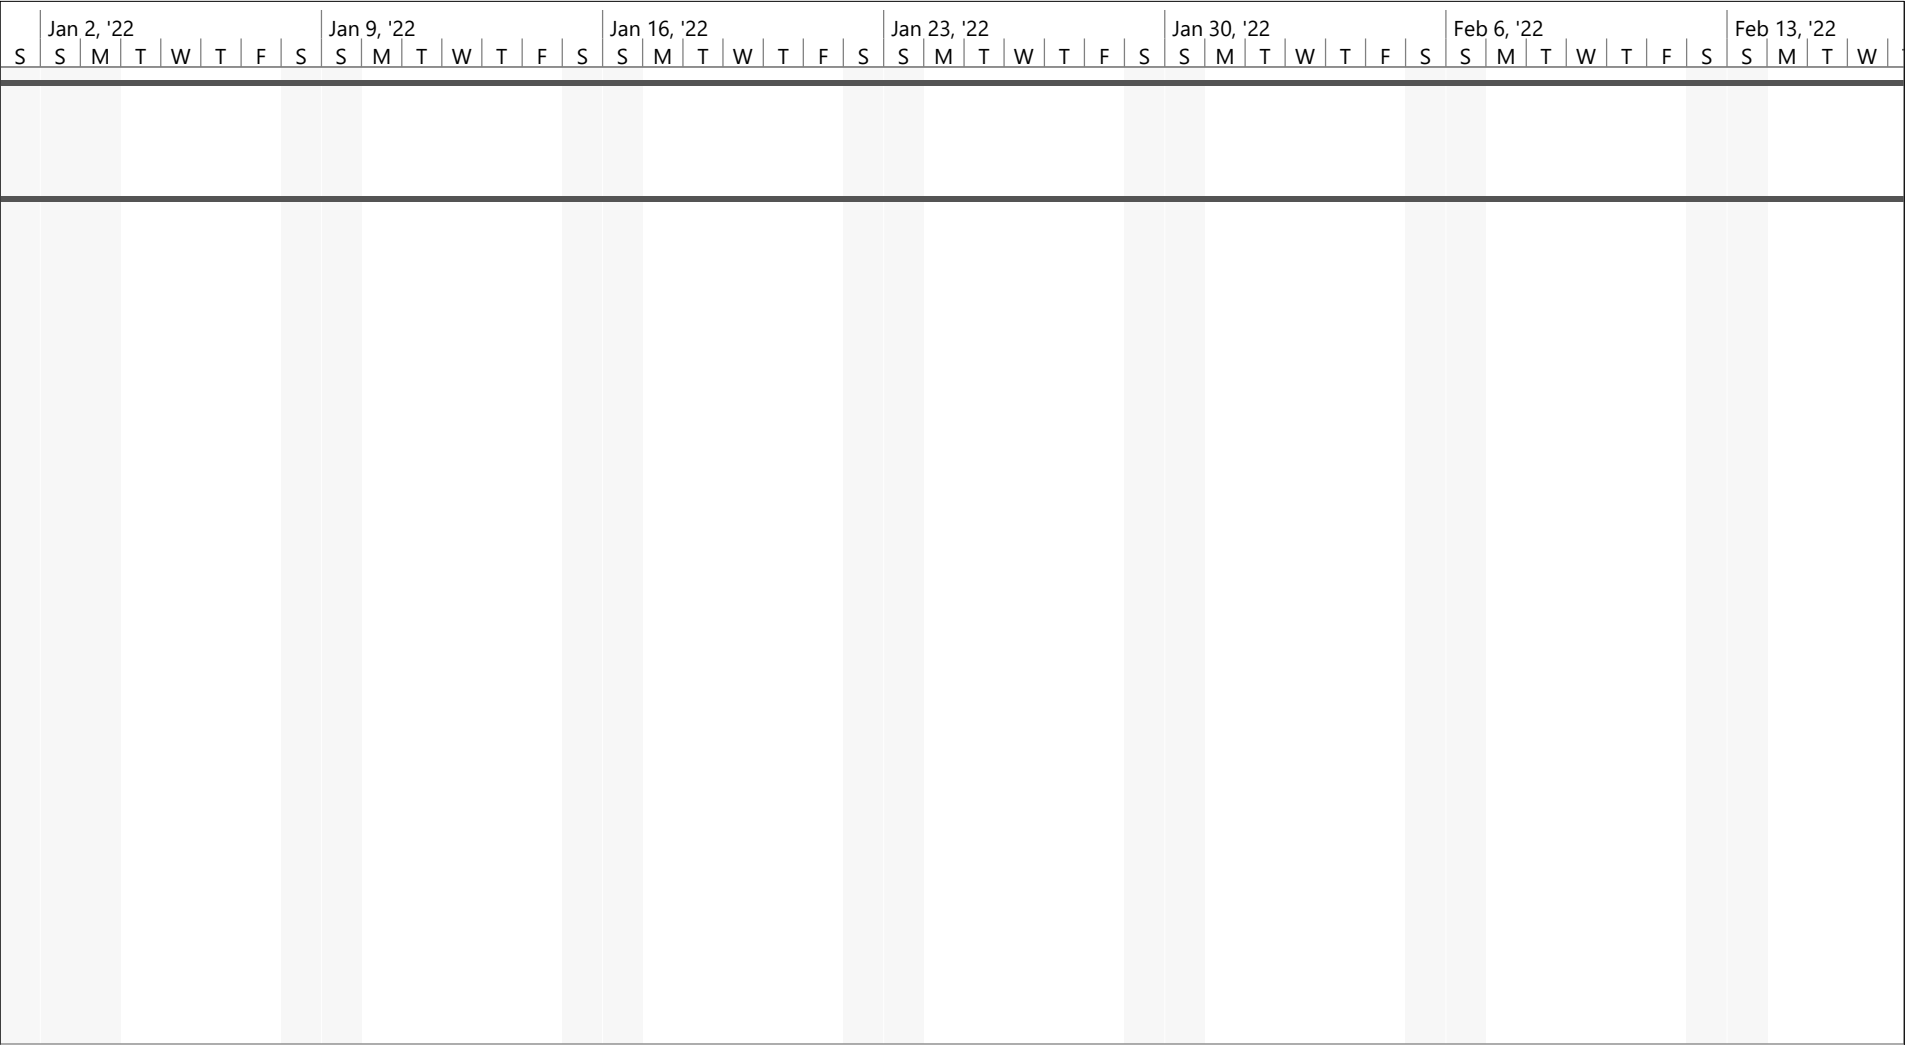


Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

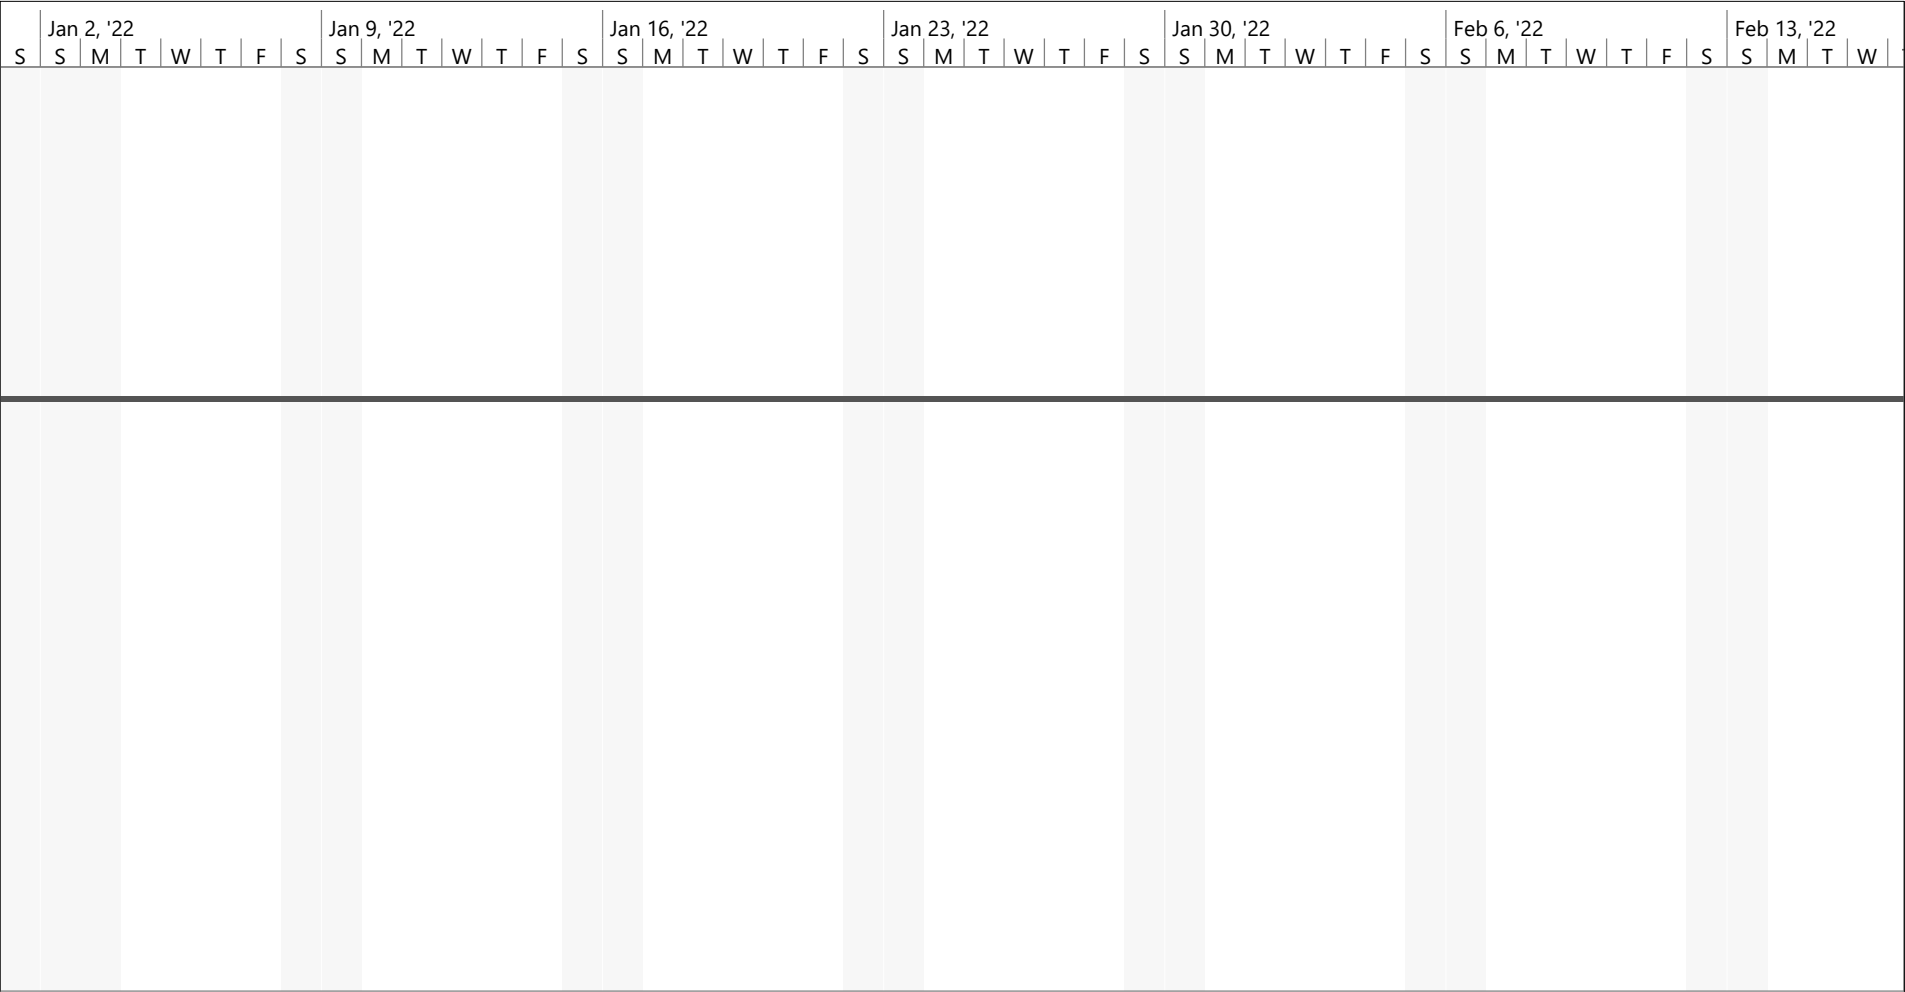

Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

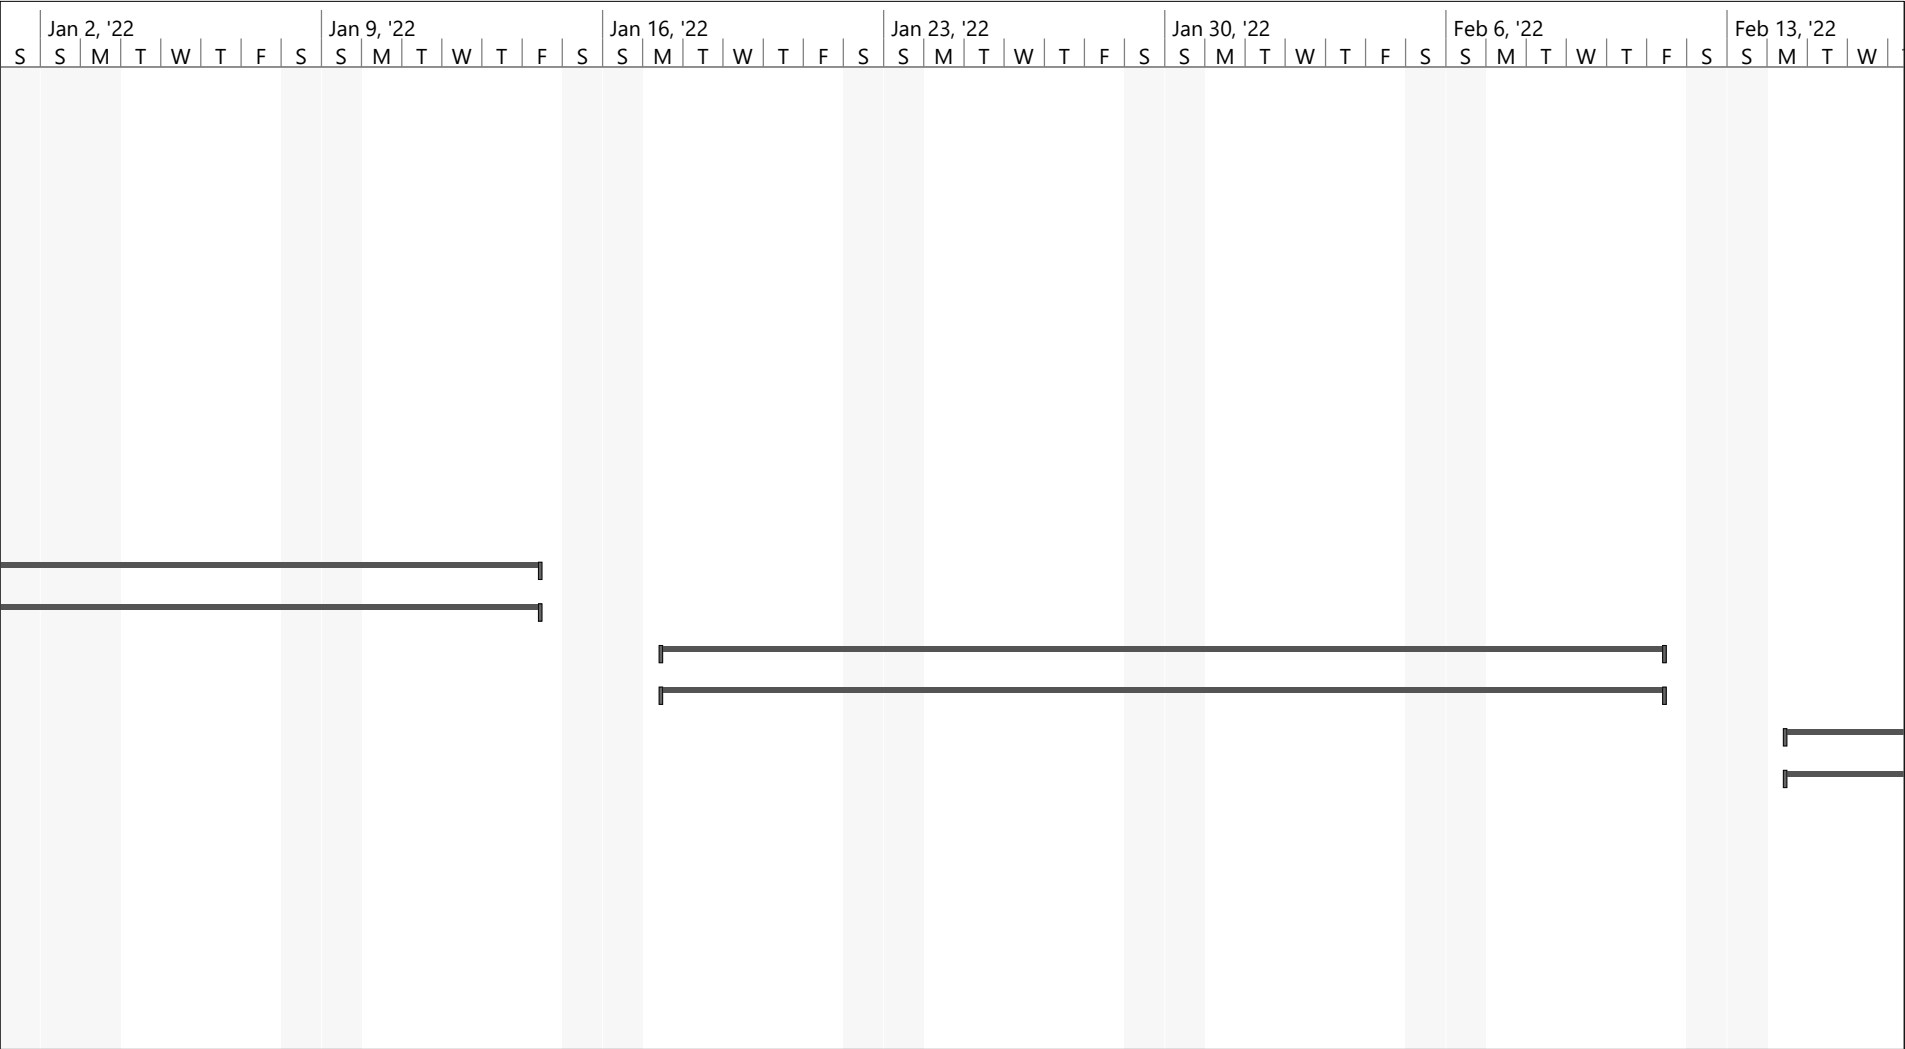




















Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















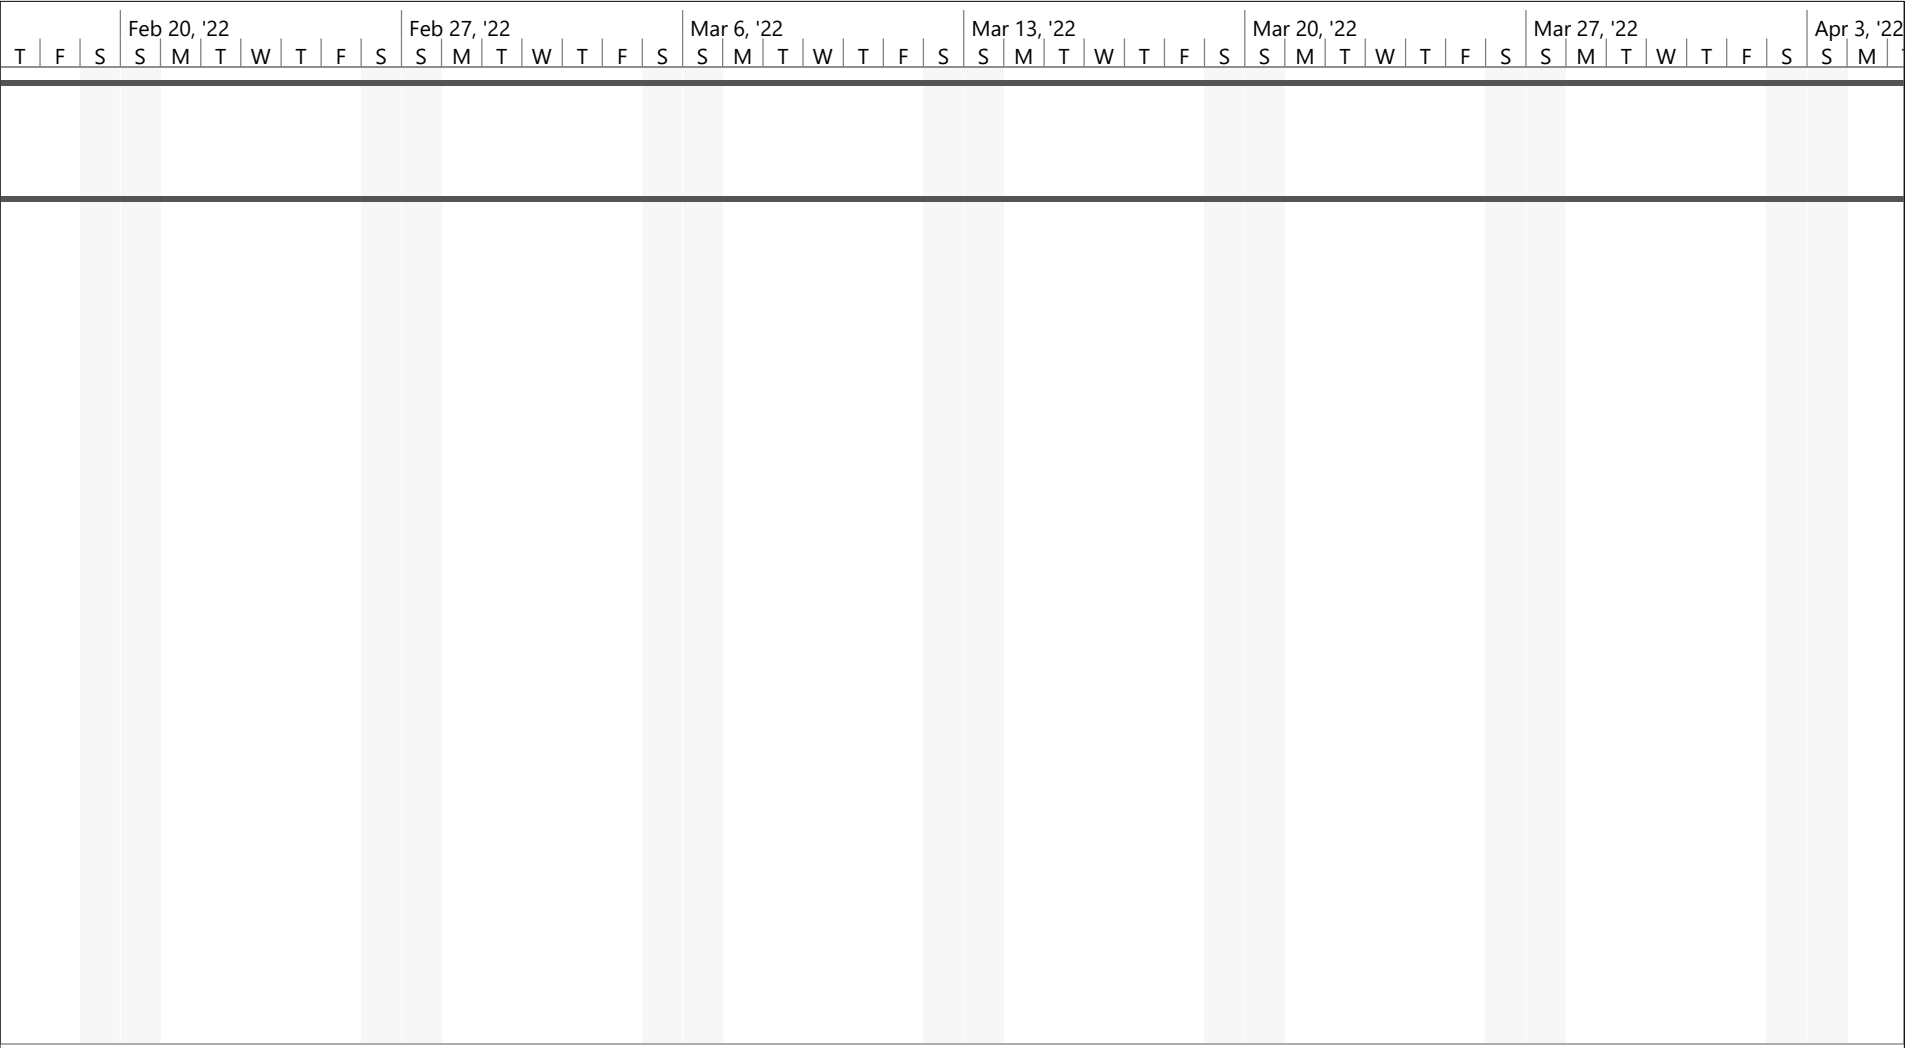
Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

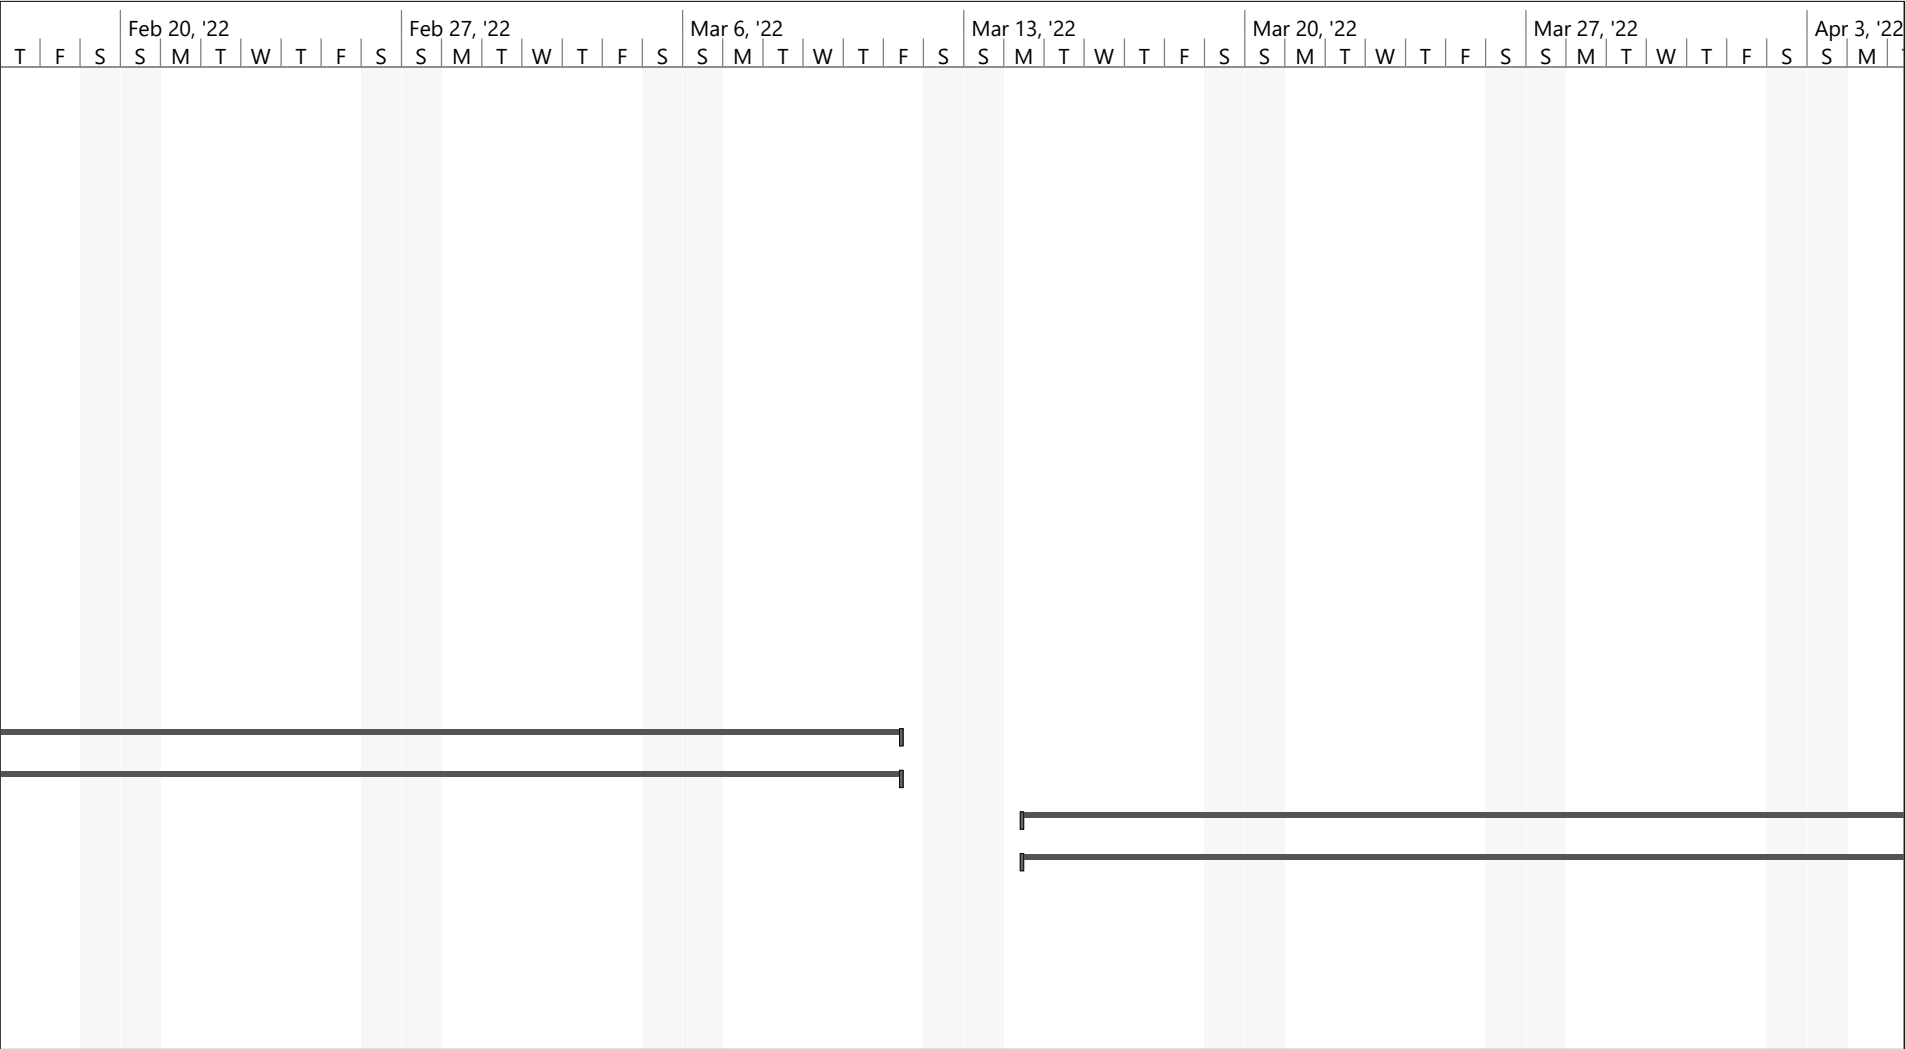





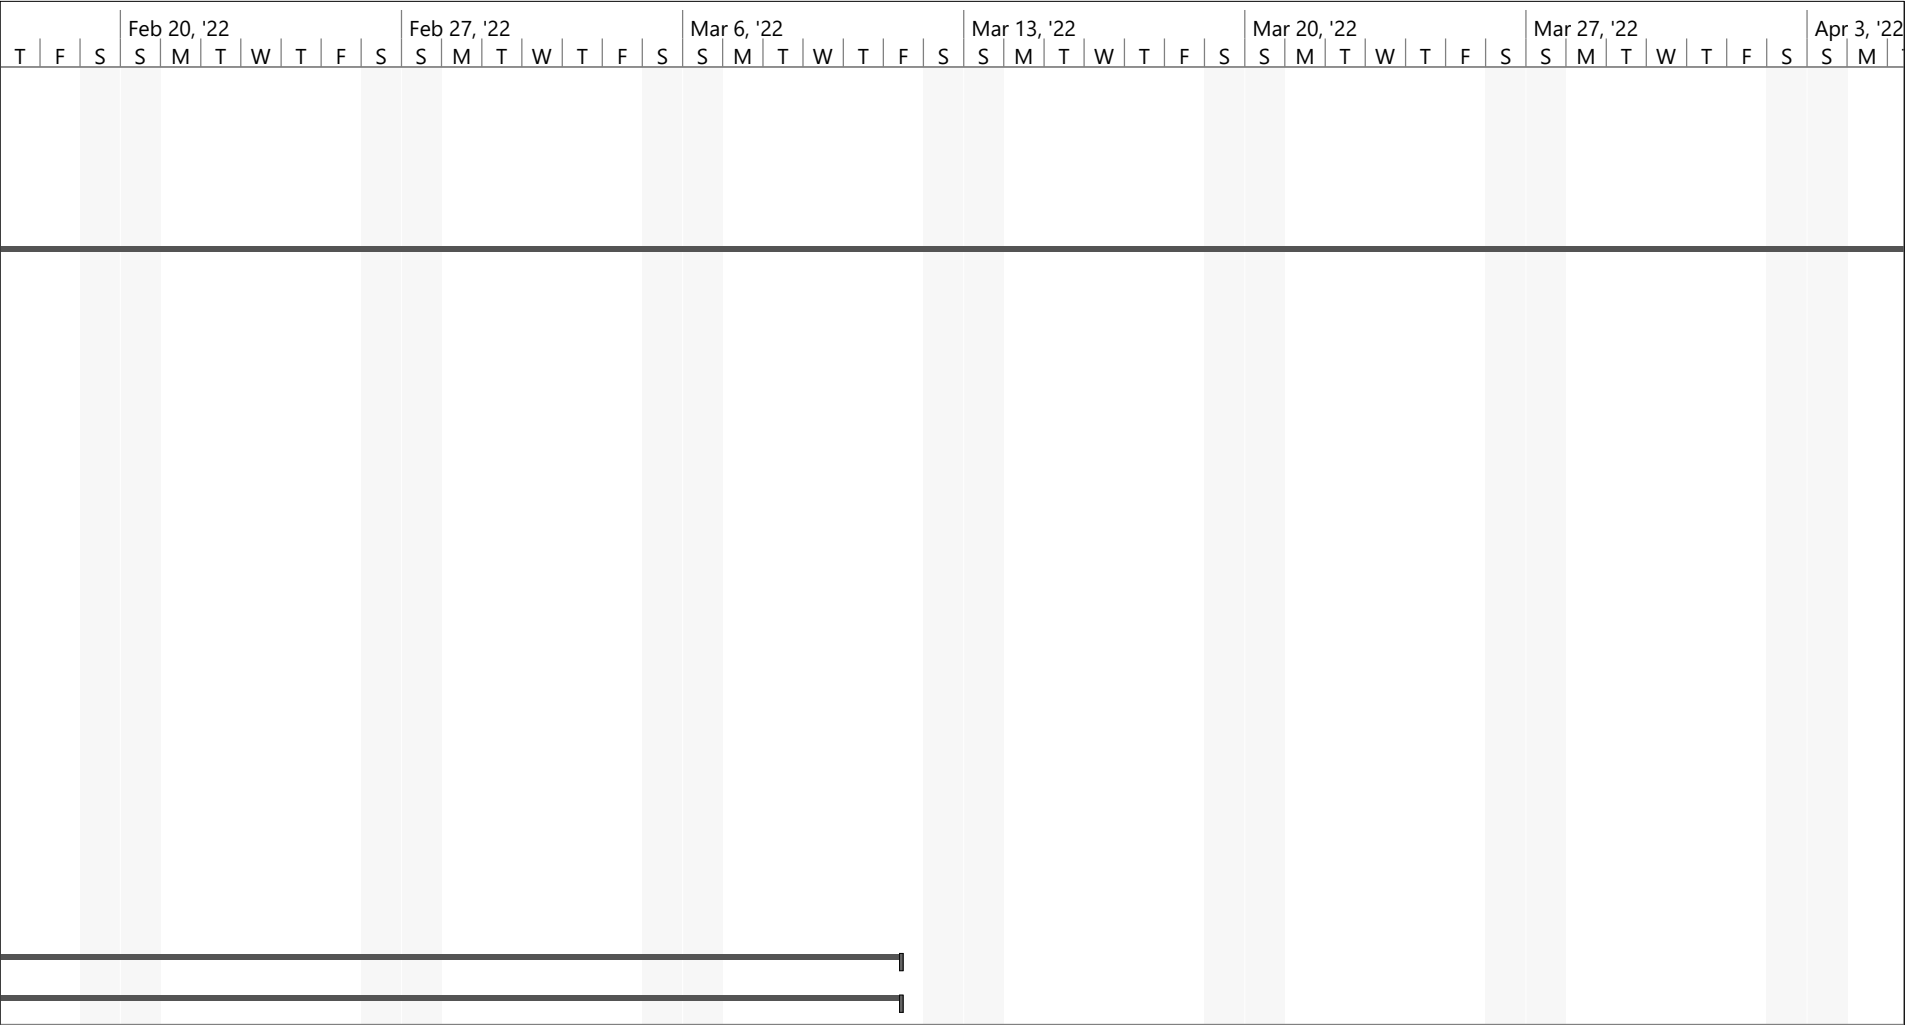














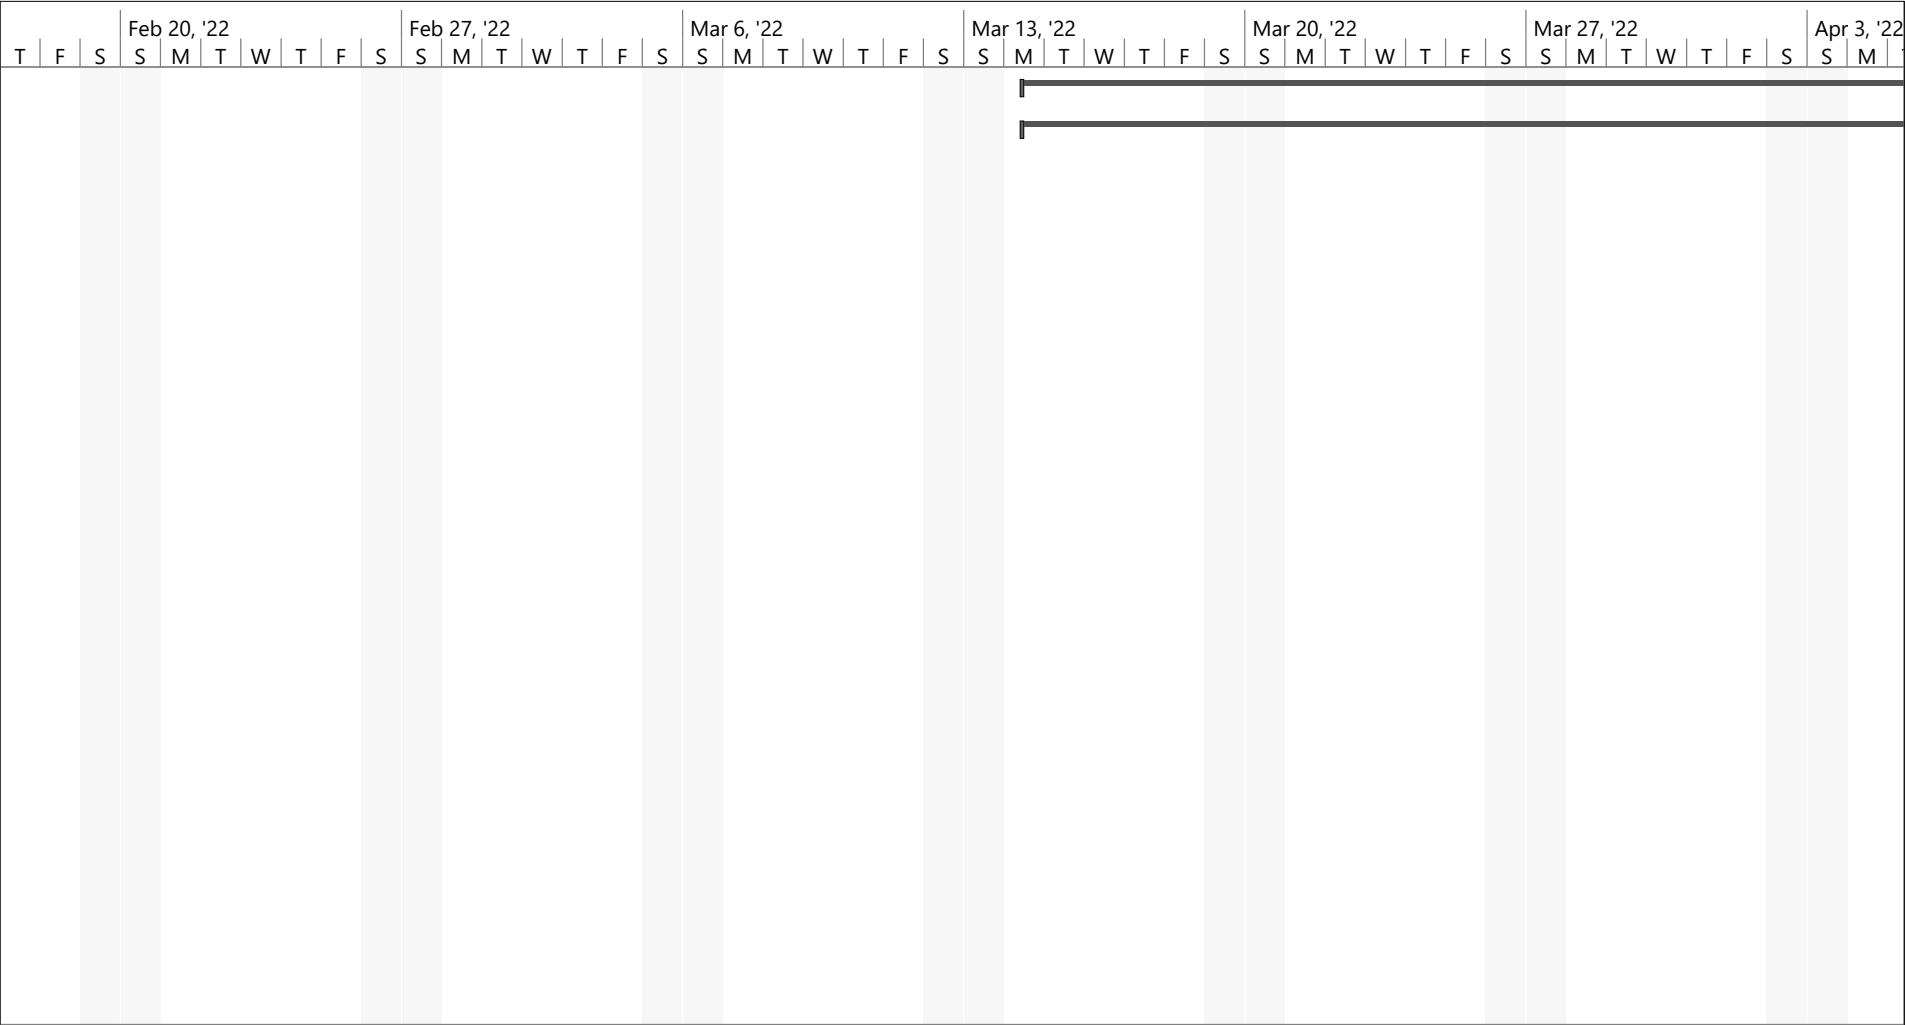
Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			























Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			








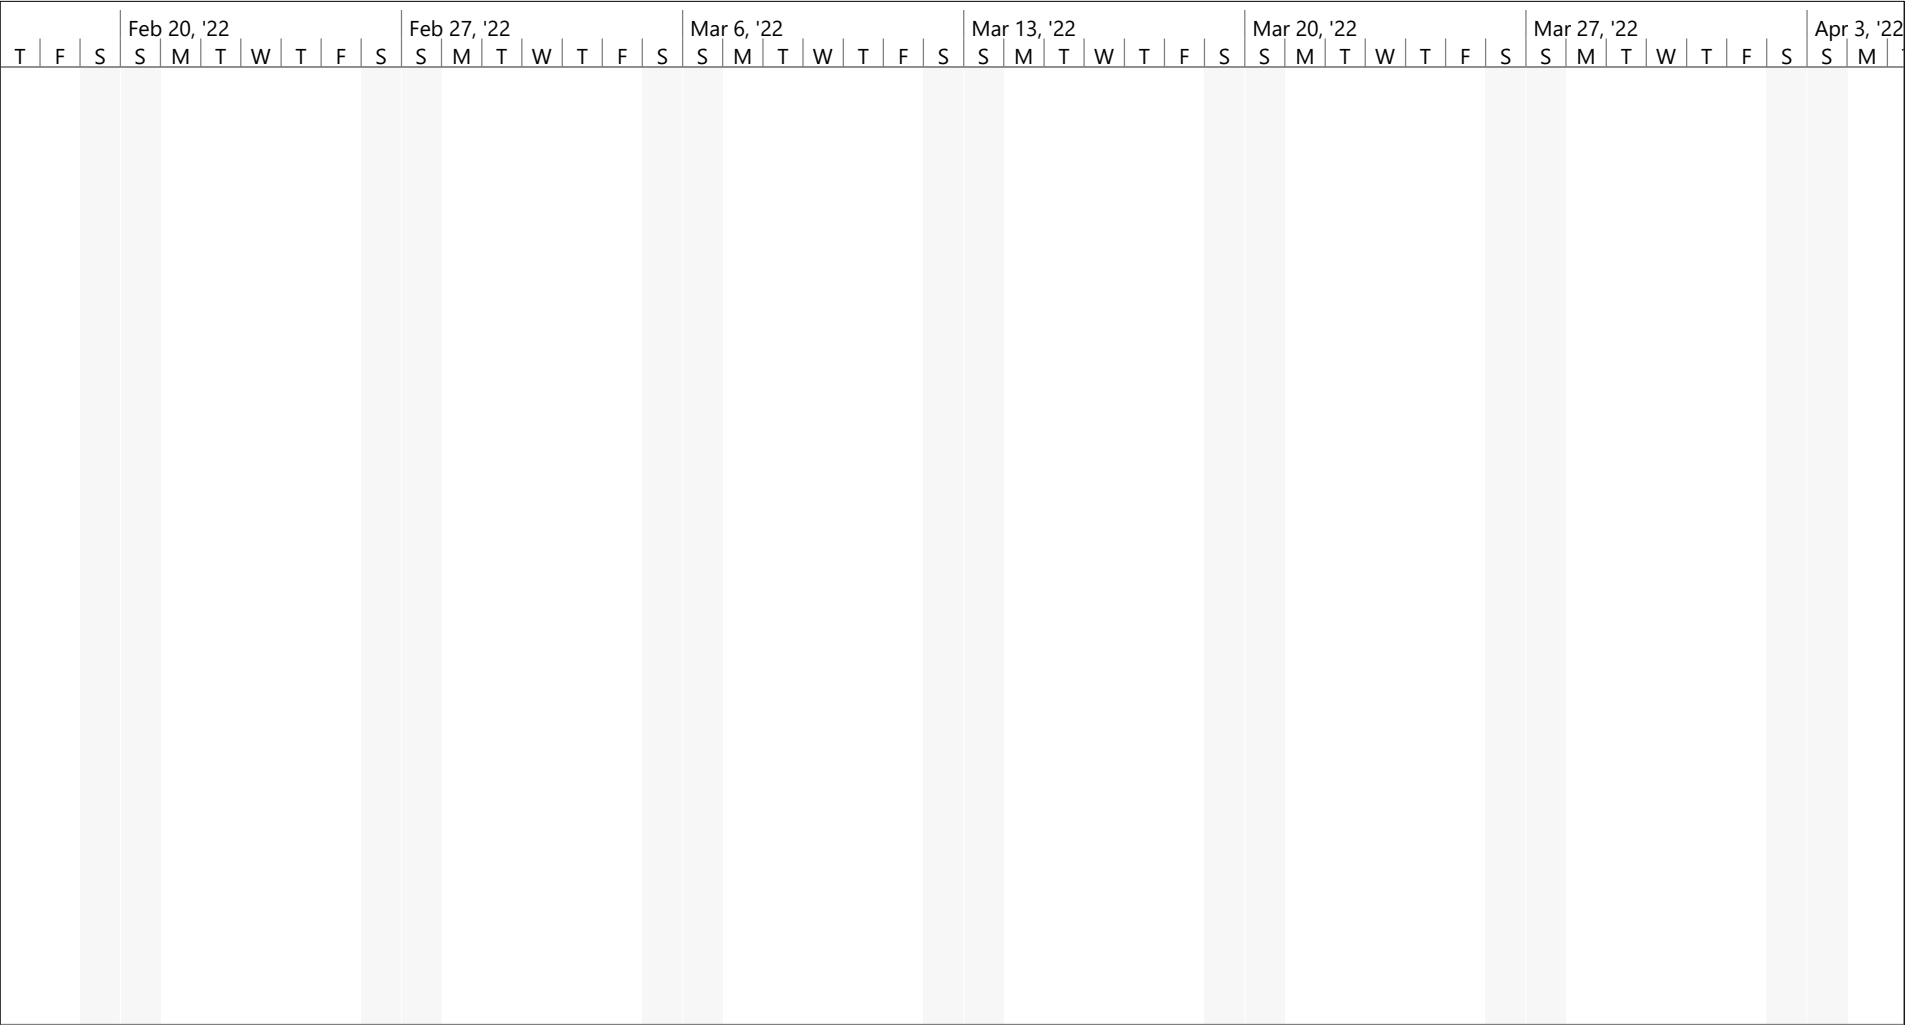














Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			










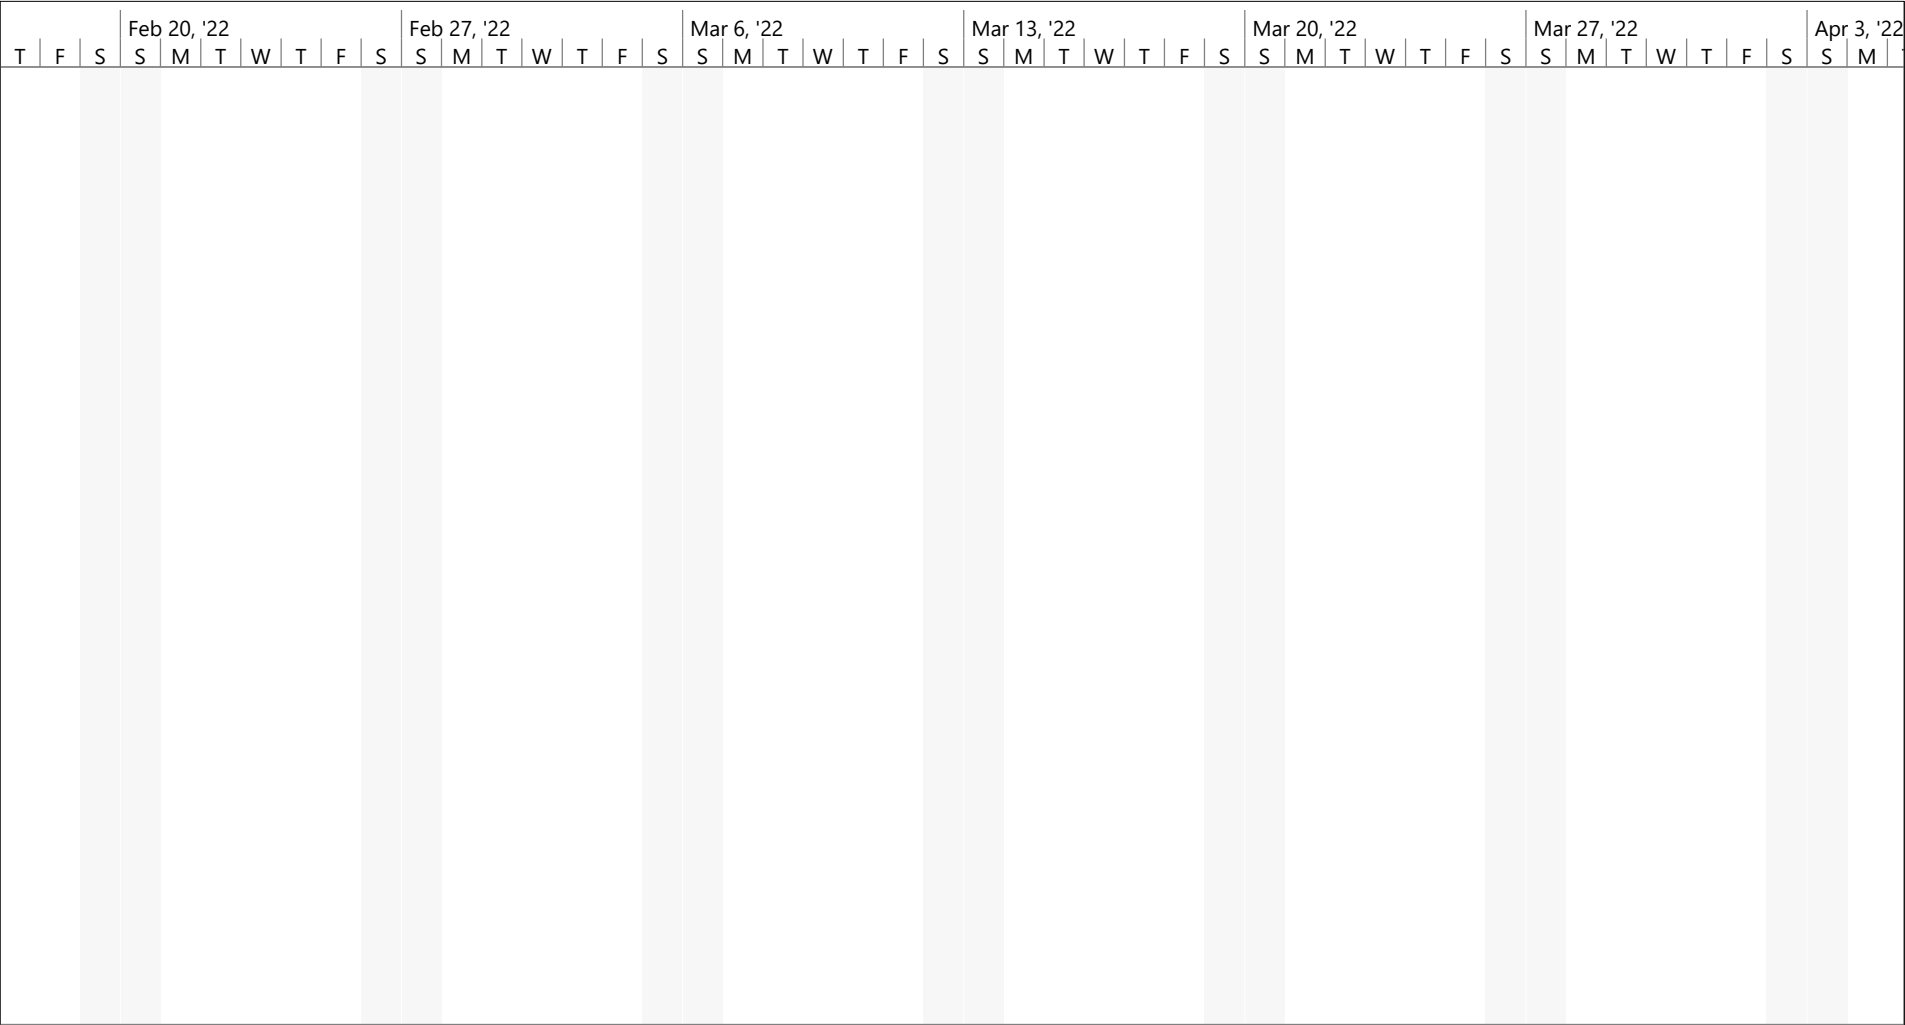












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			










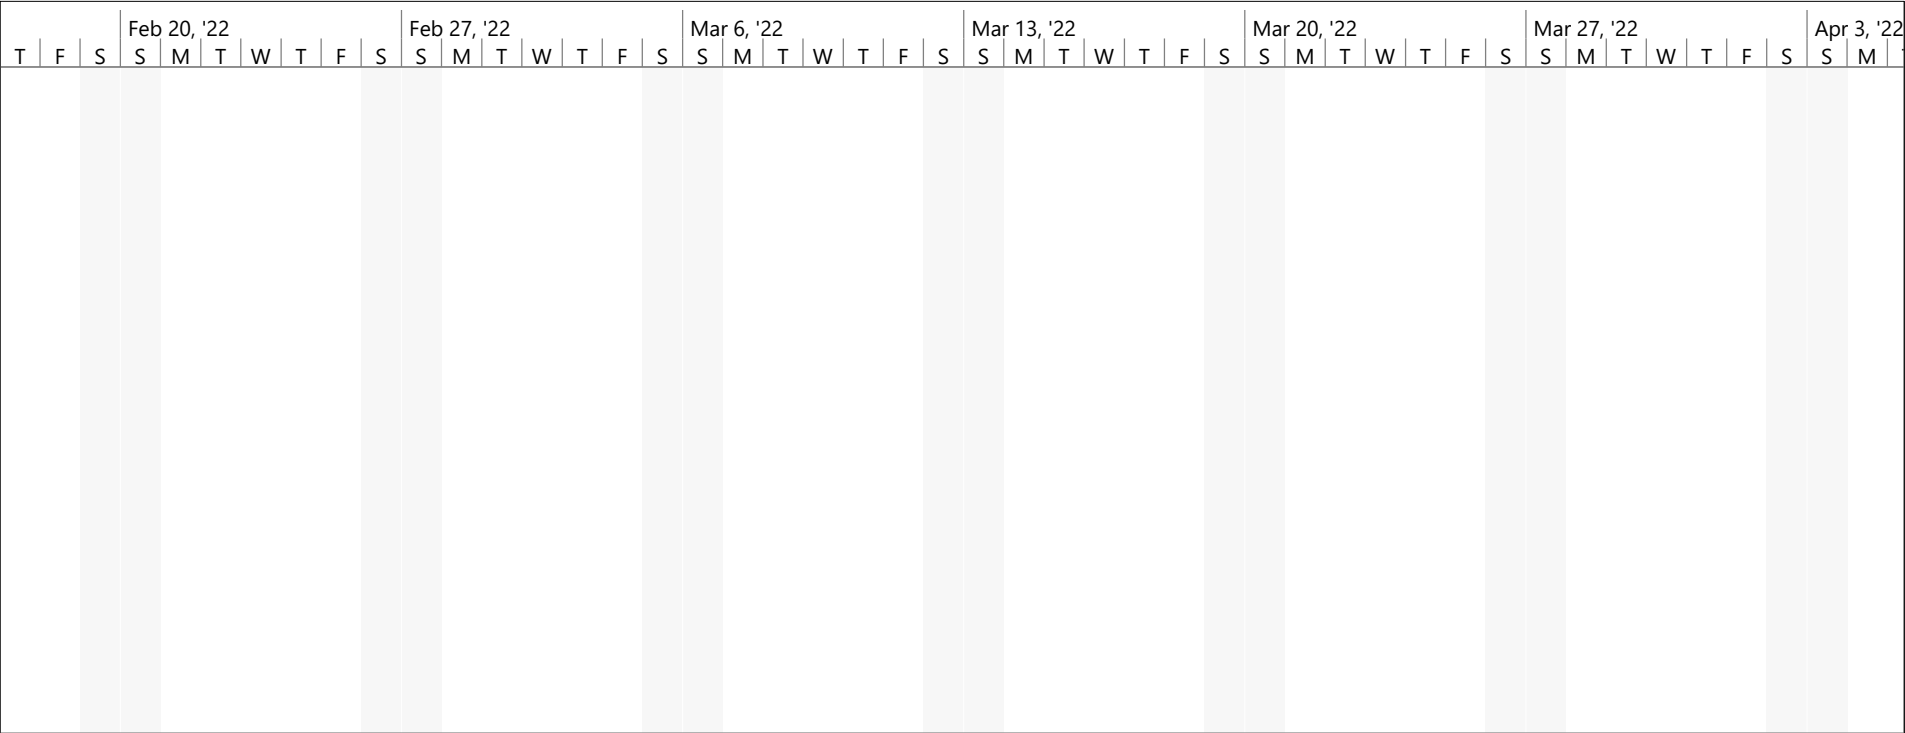












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

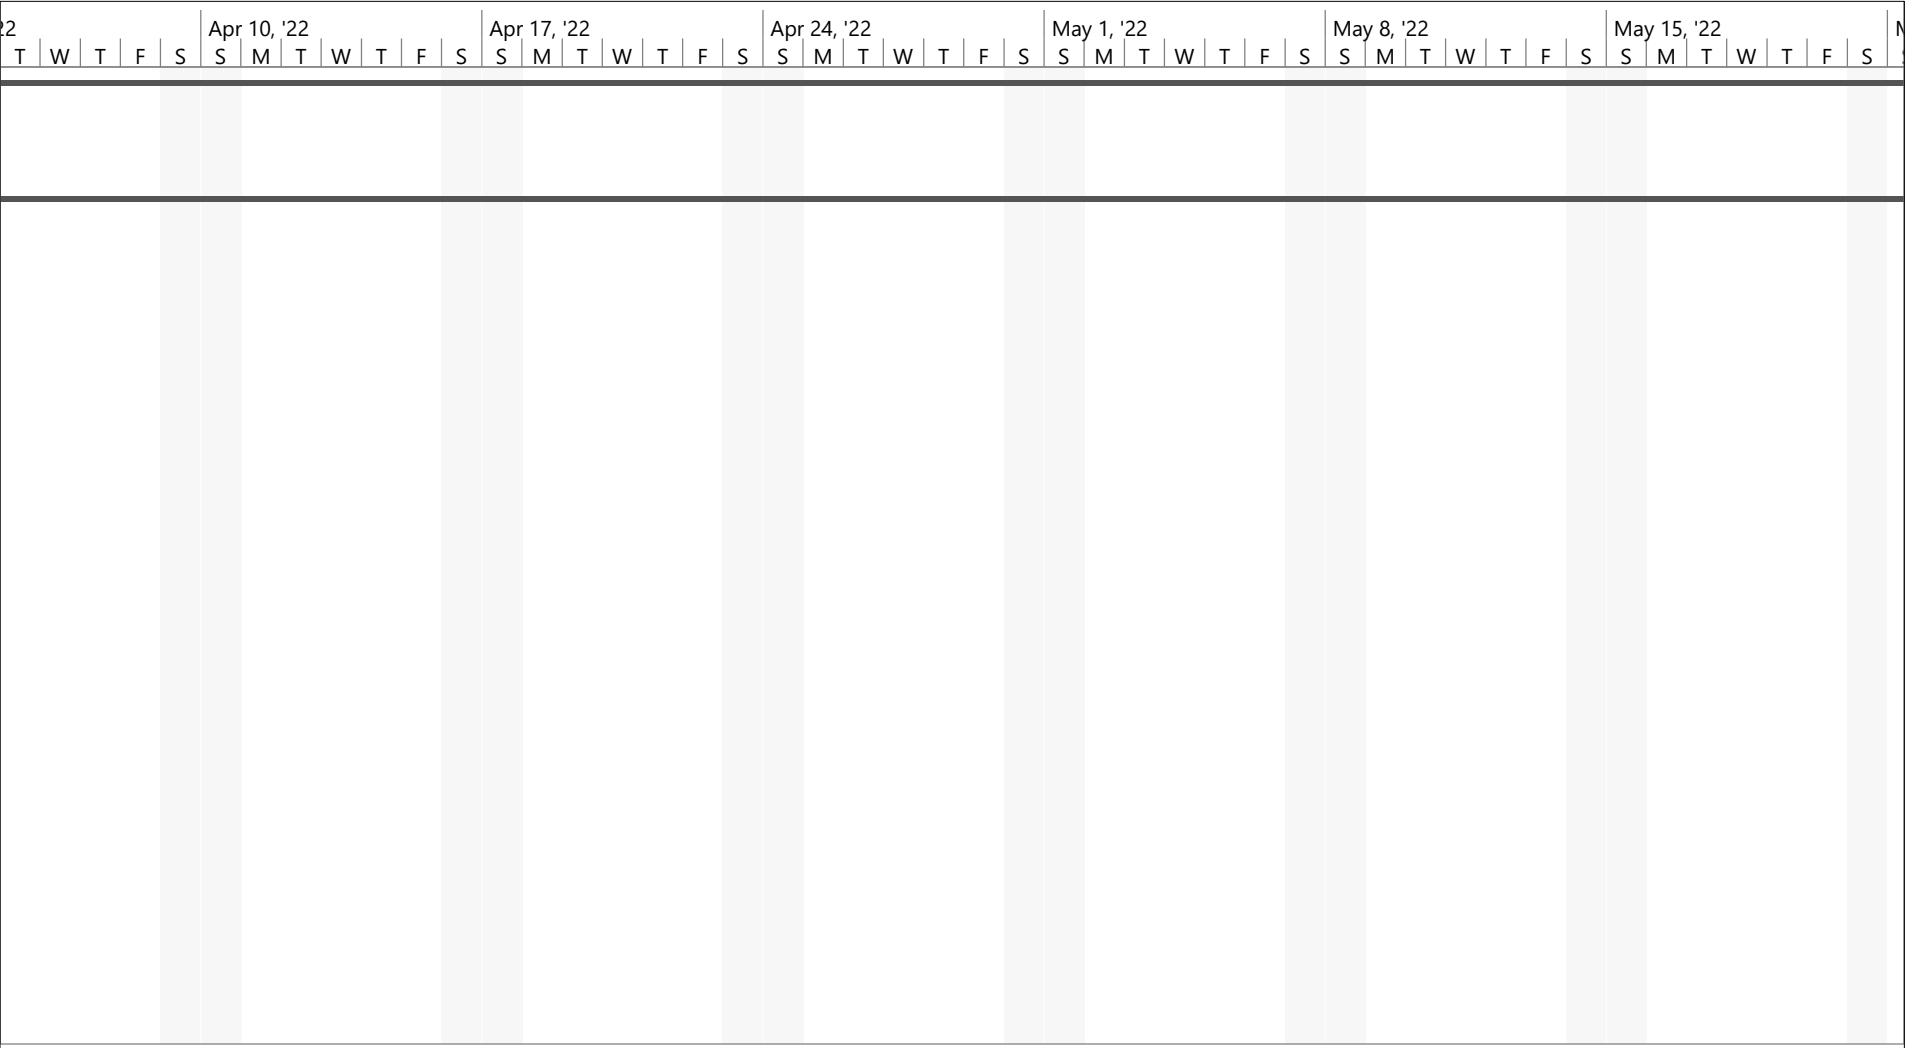


Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

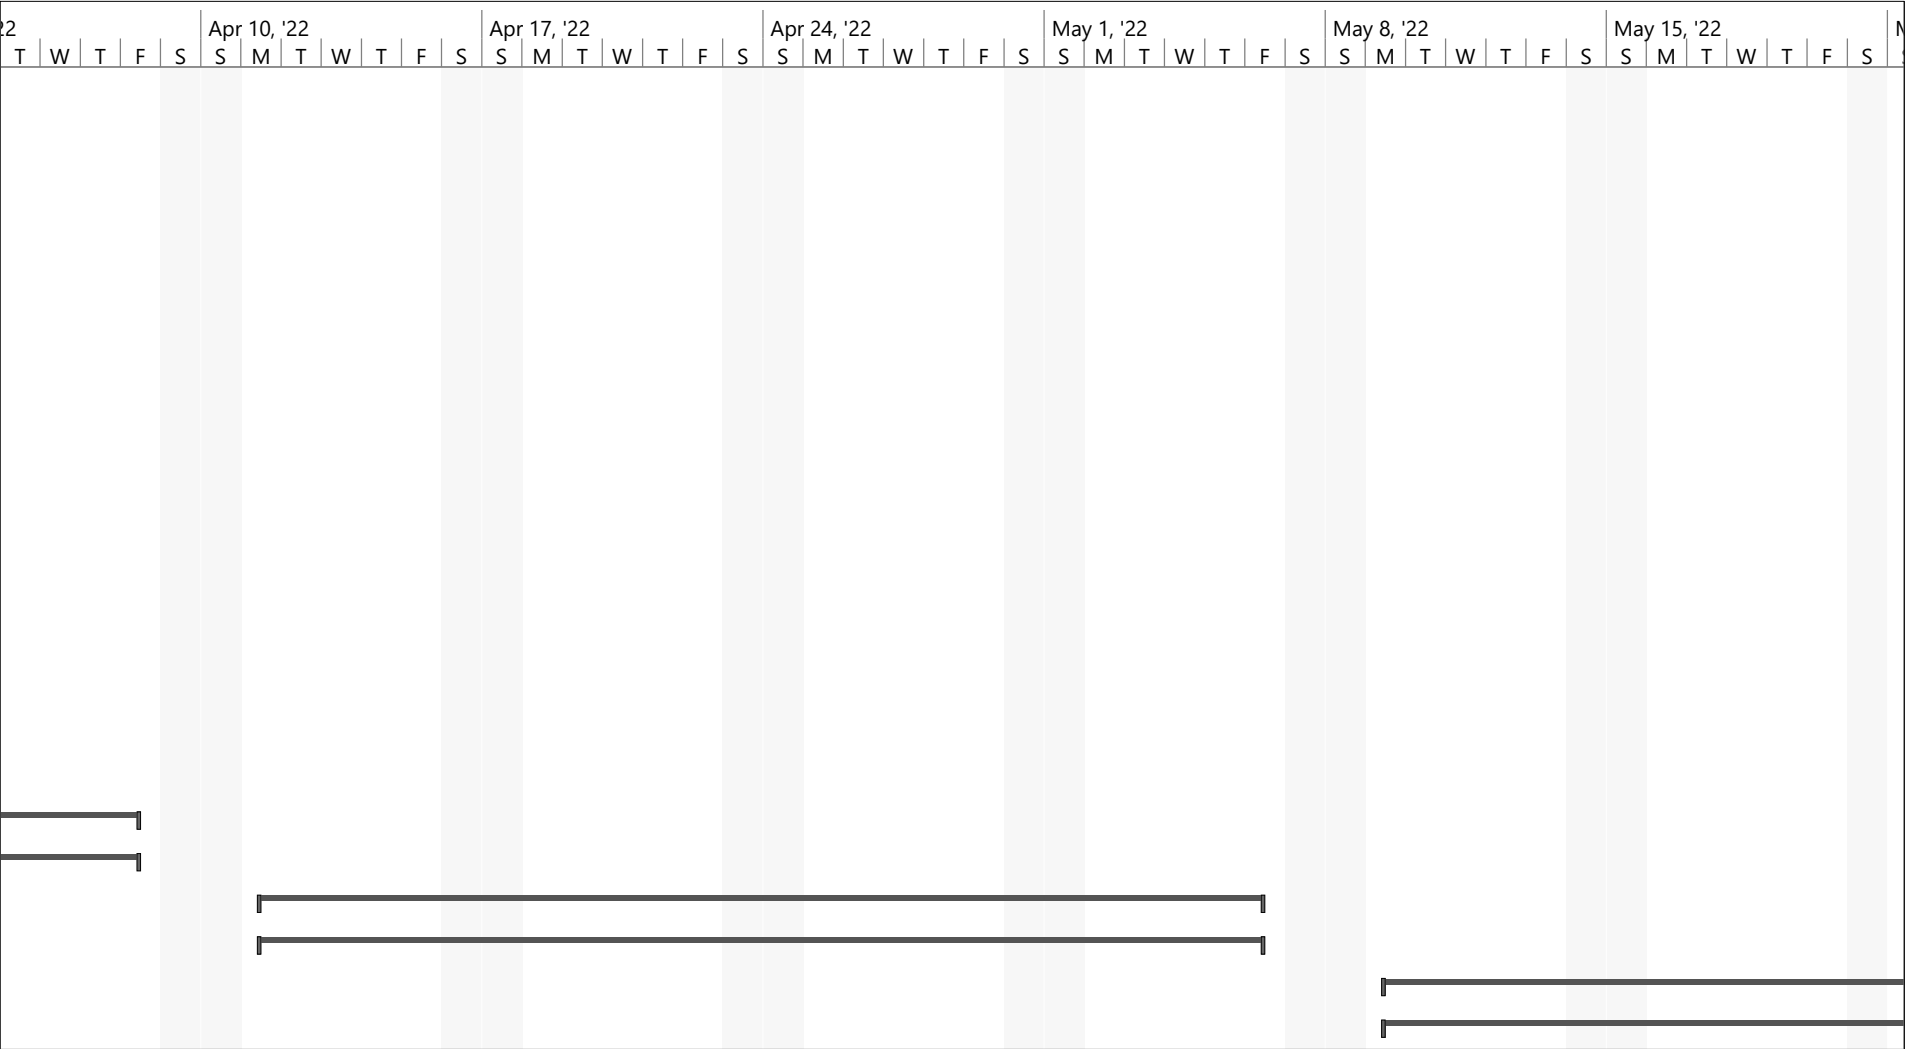


Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

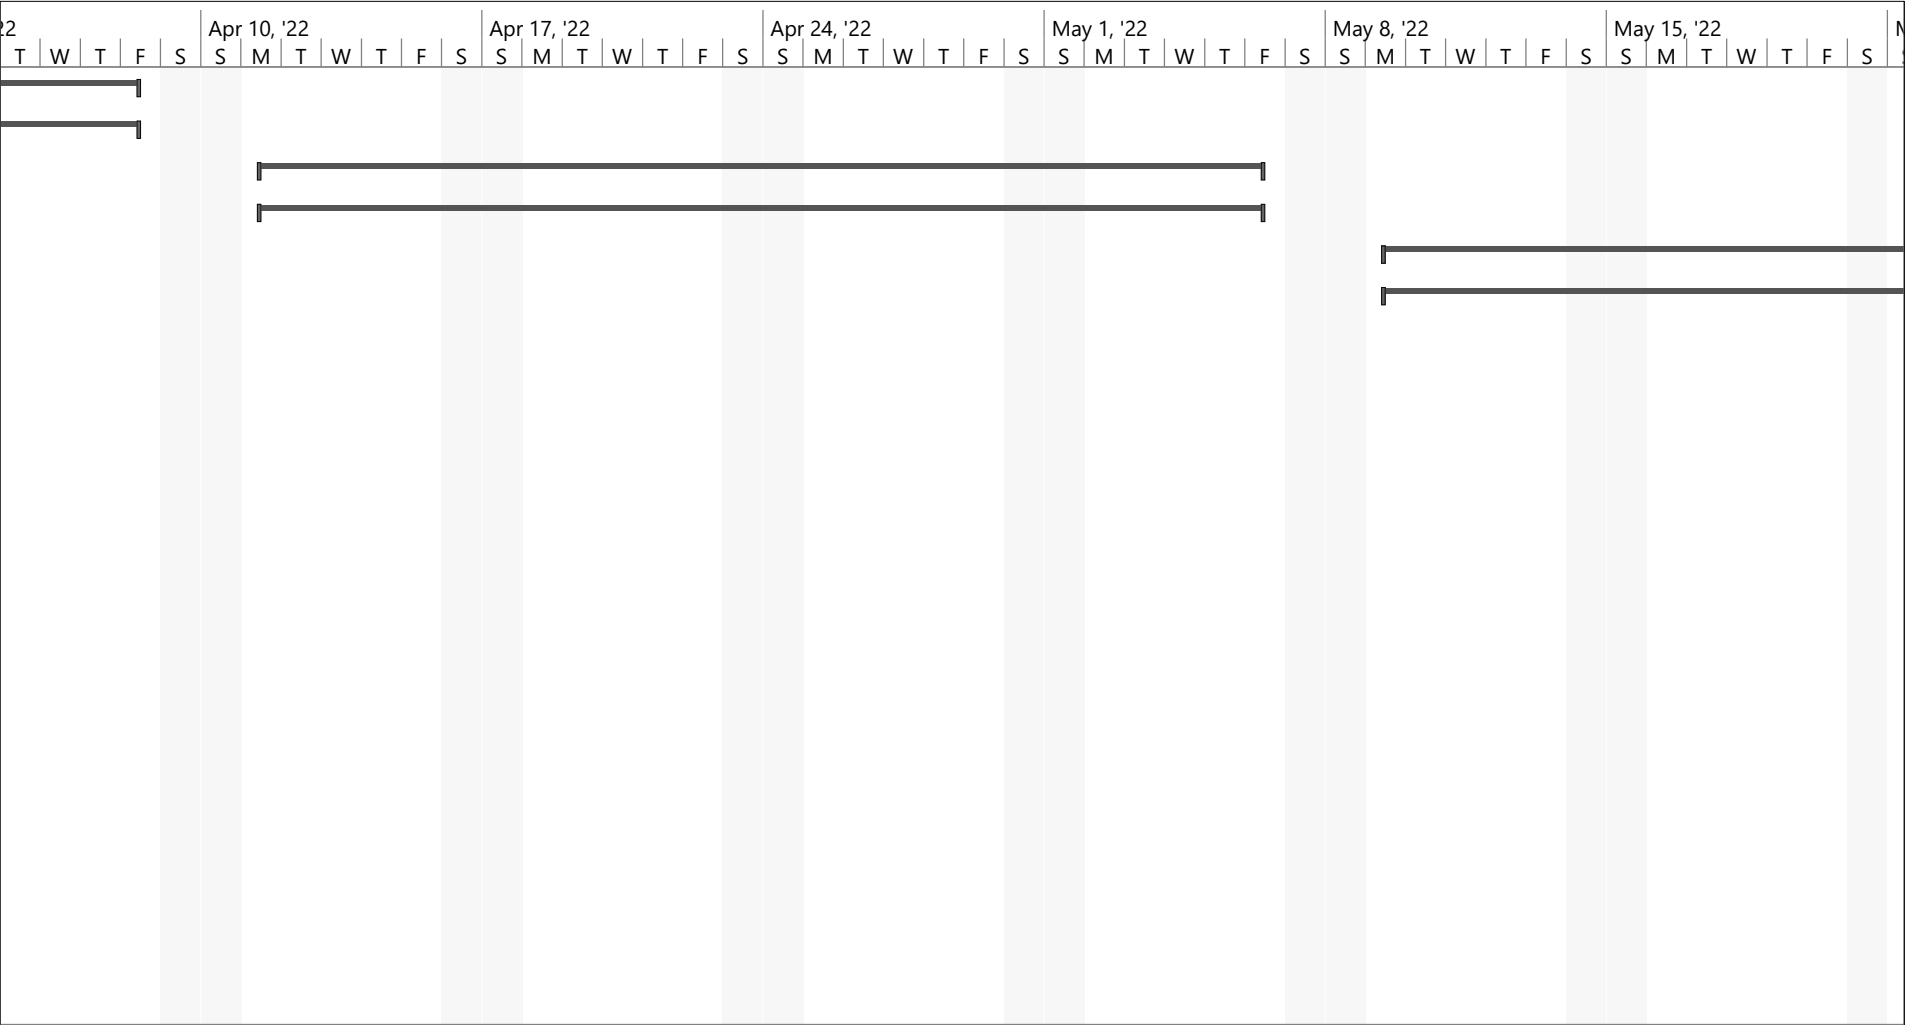








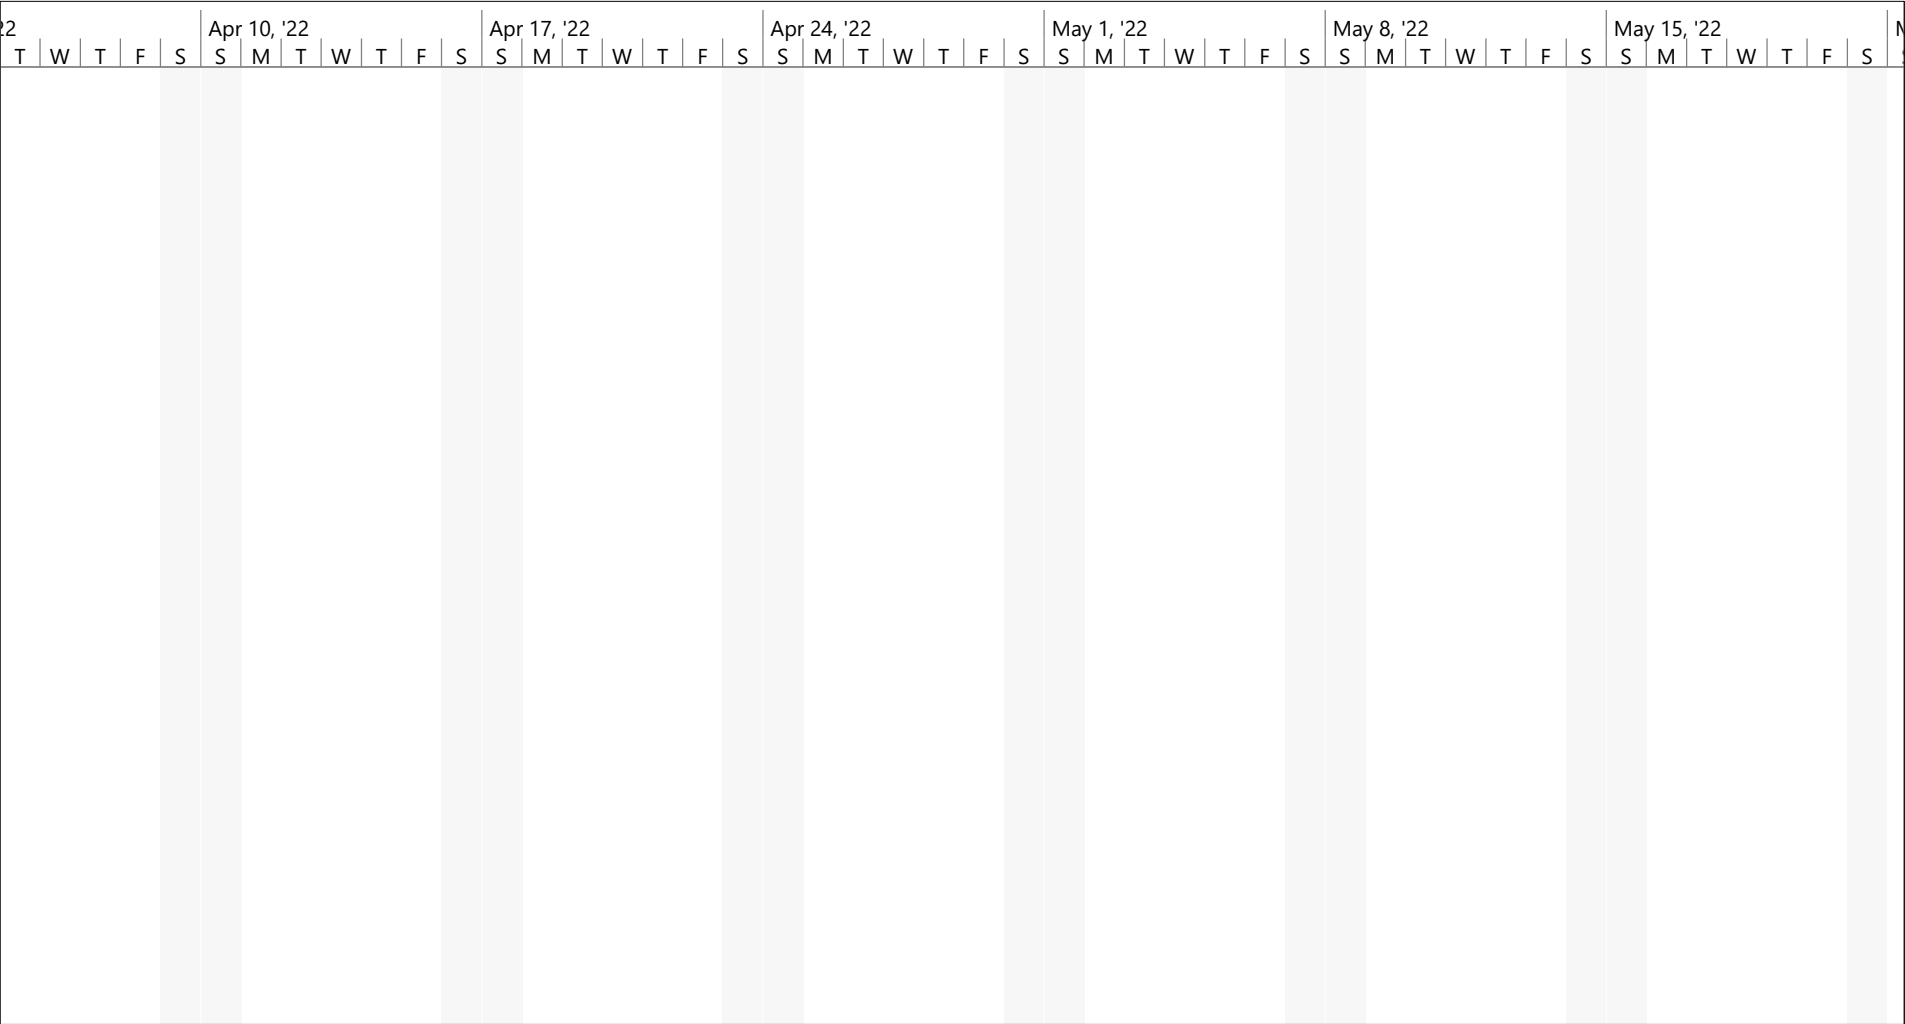












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

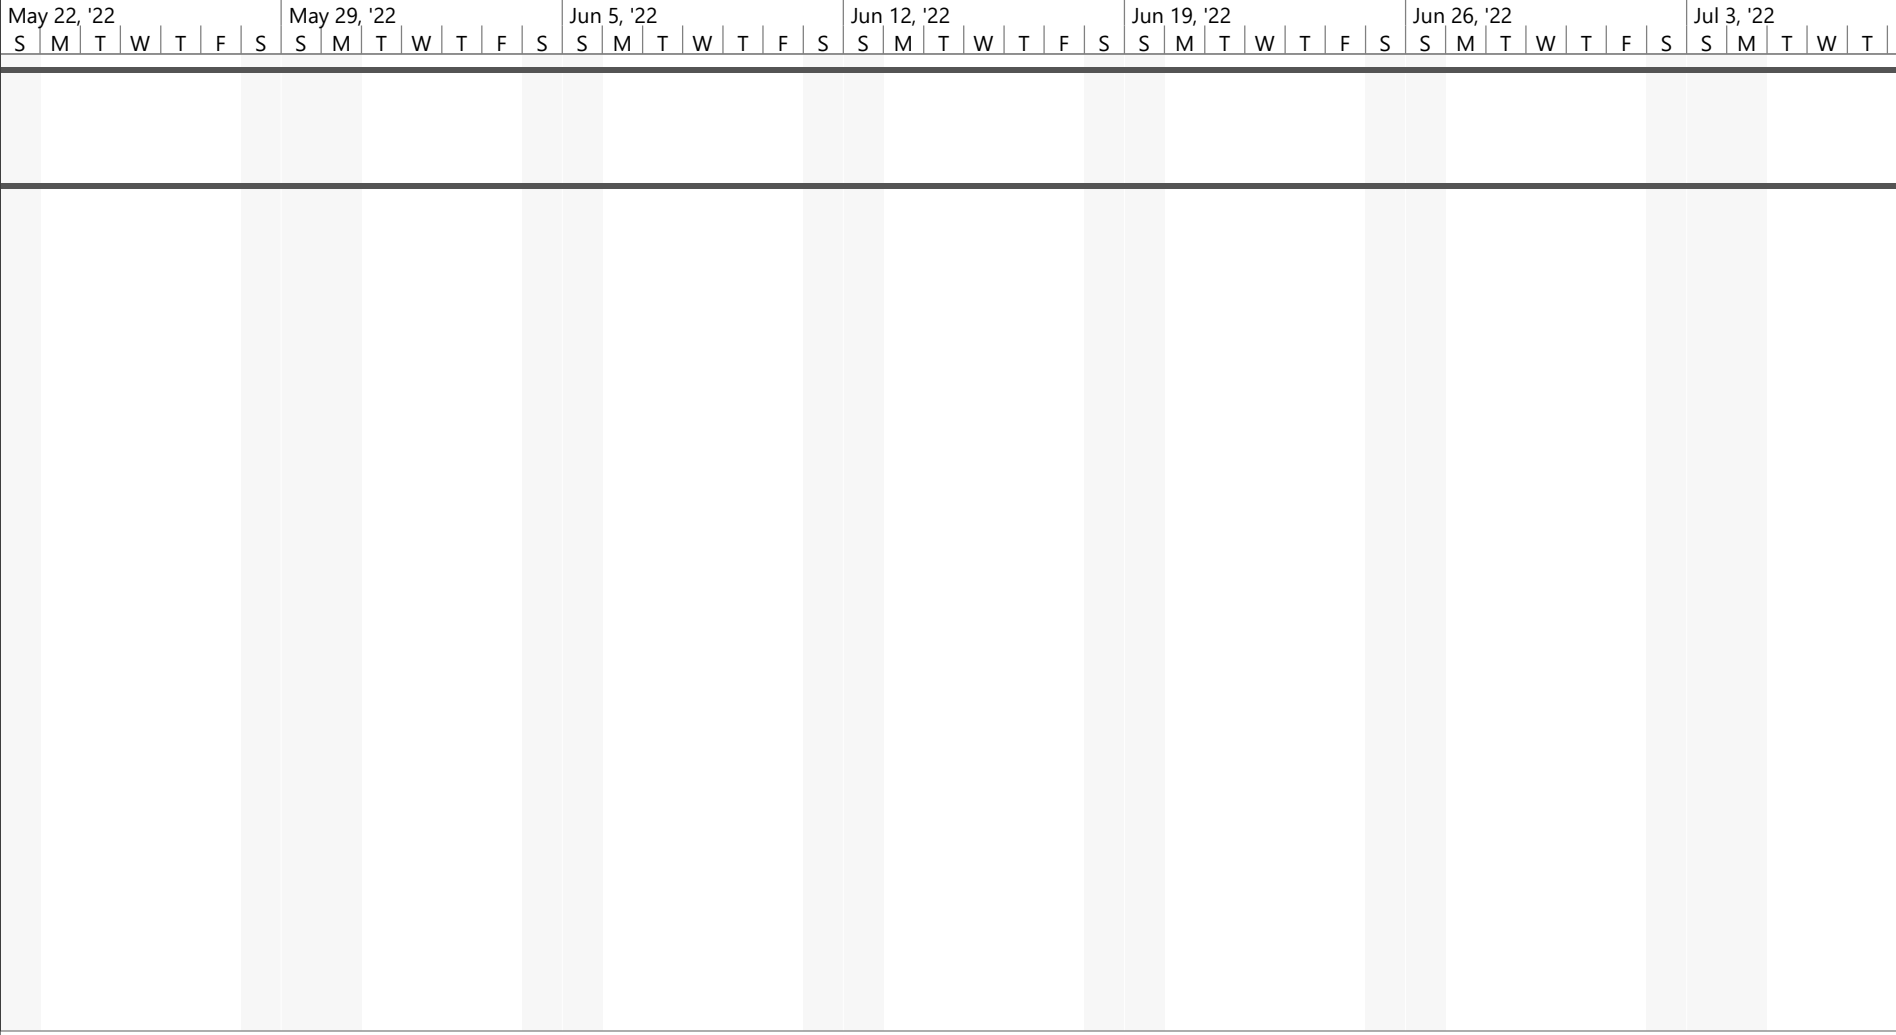


Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

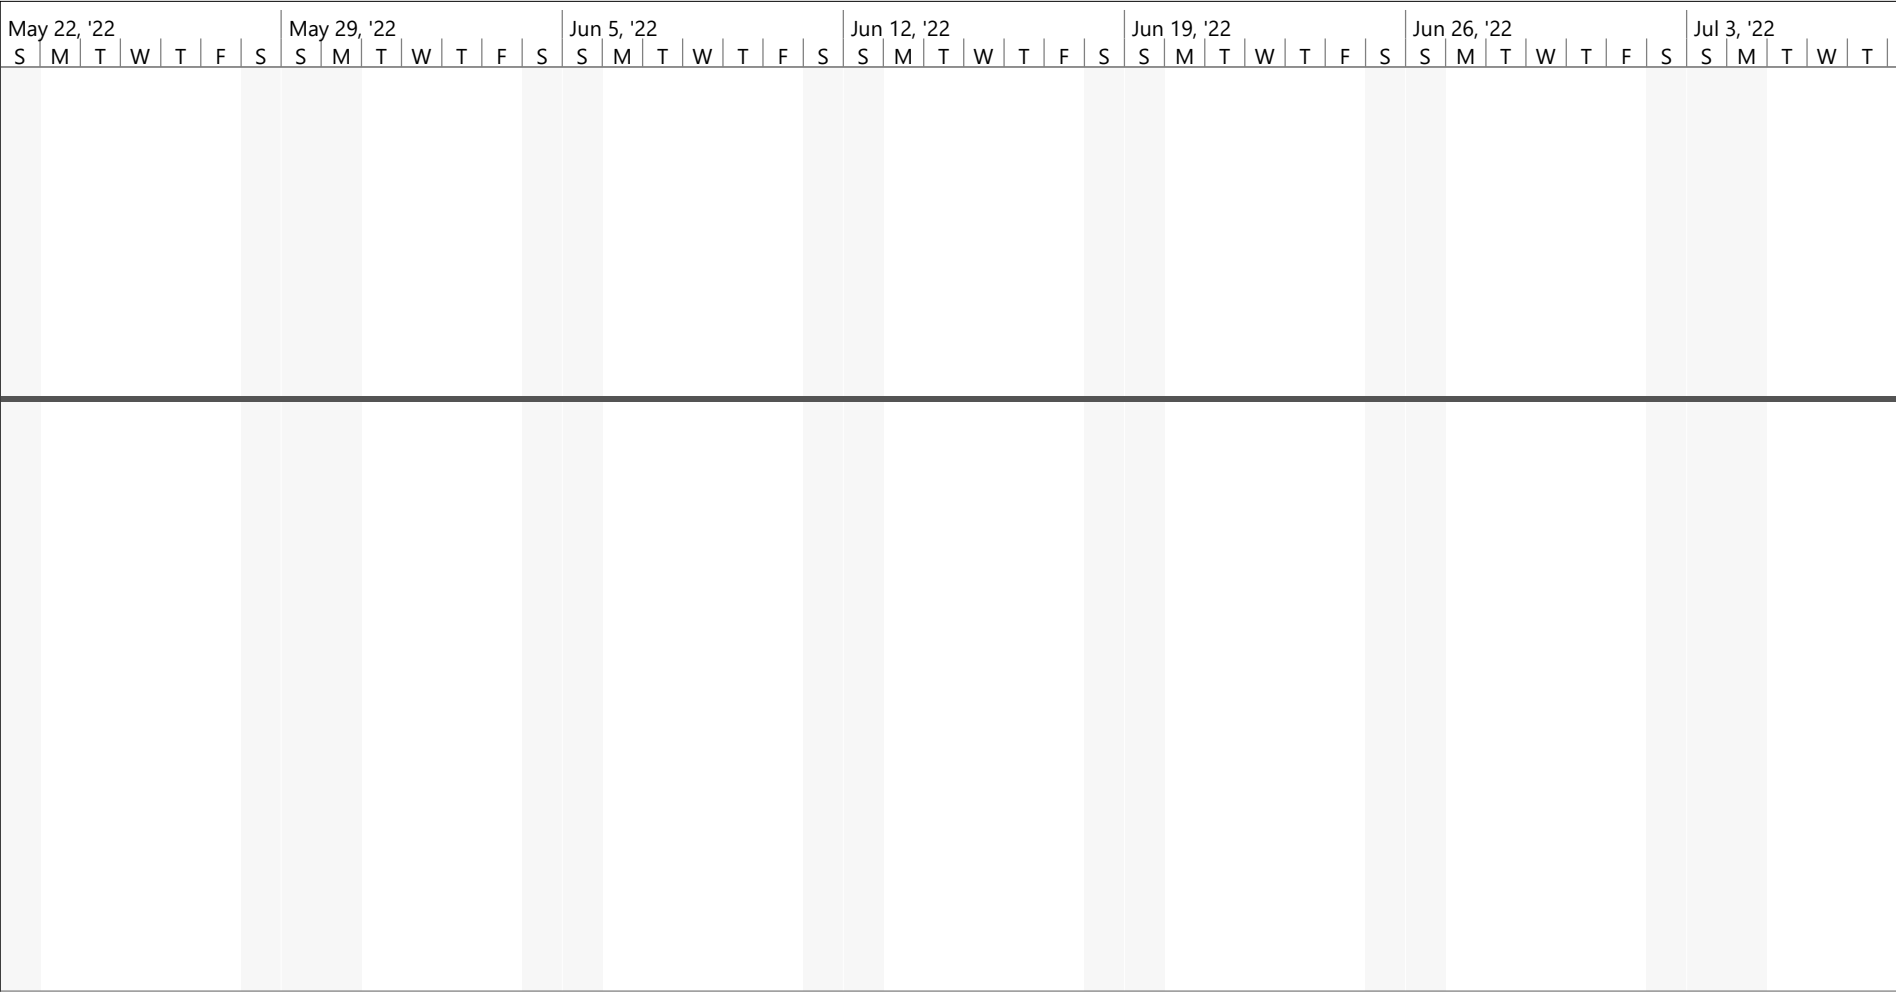


Project: Sample PureCloud Imp
Date: Fri 9/17/21




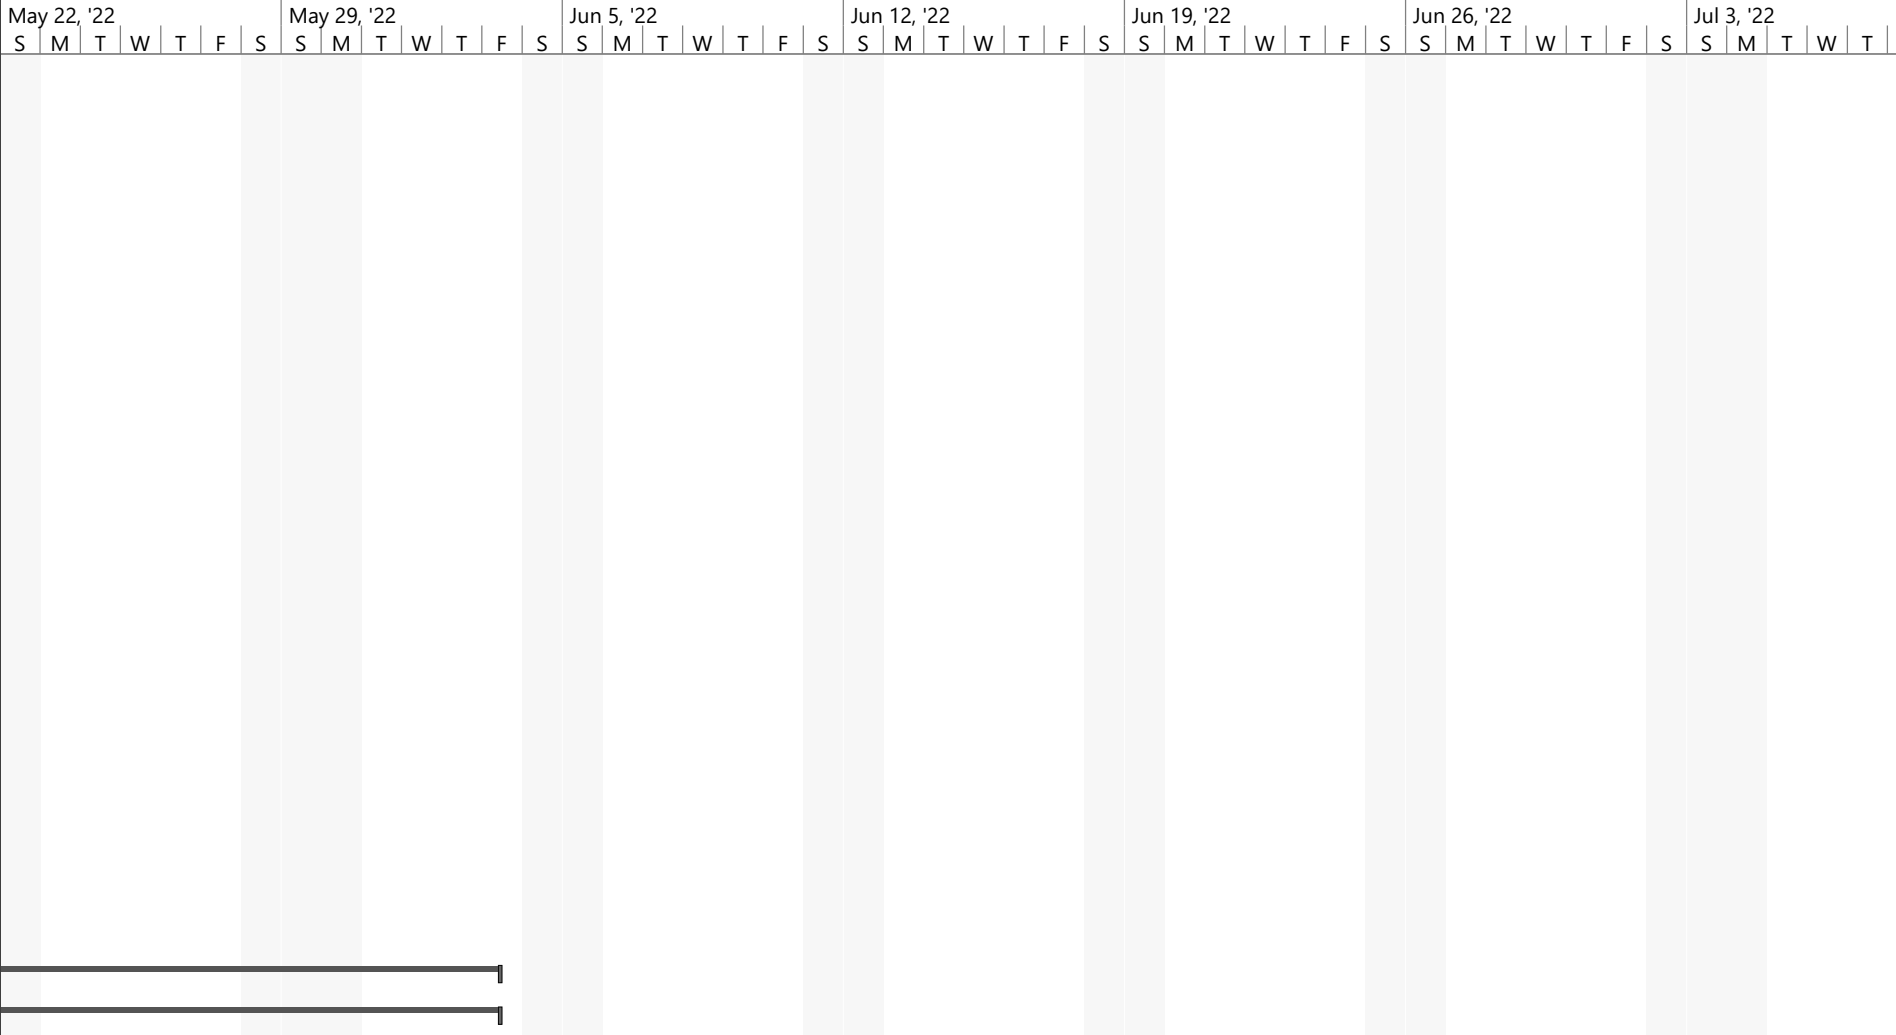



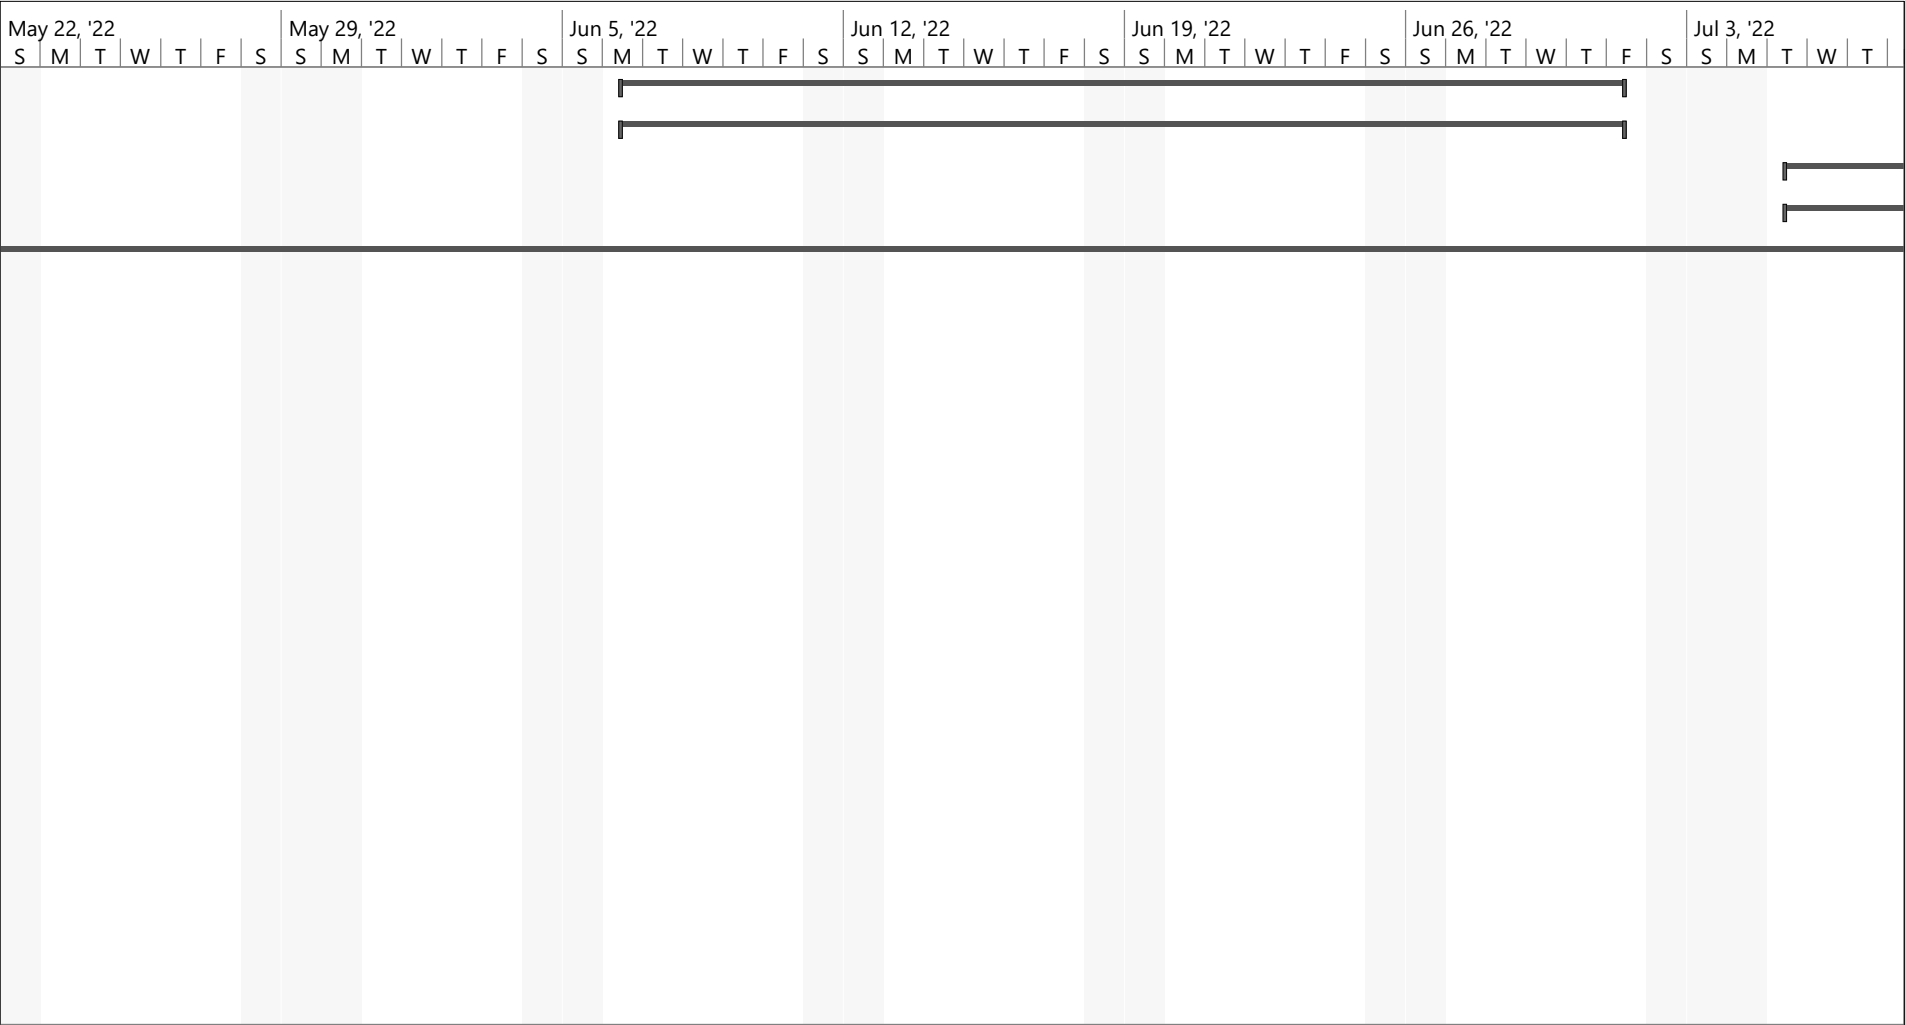











Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

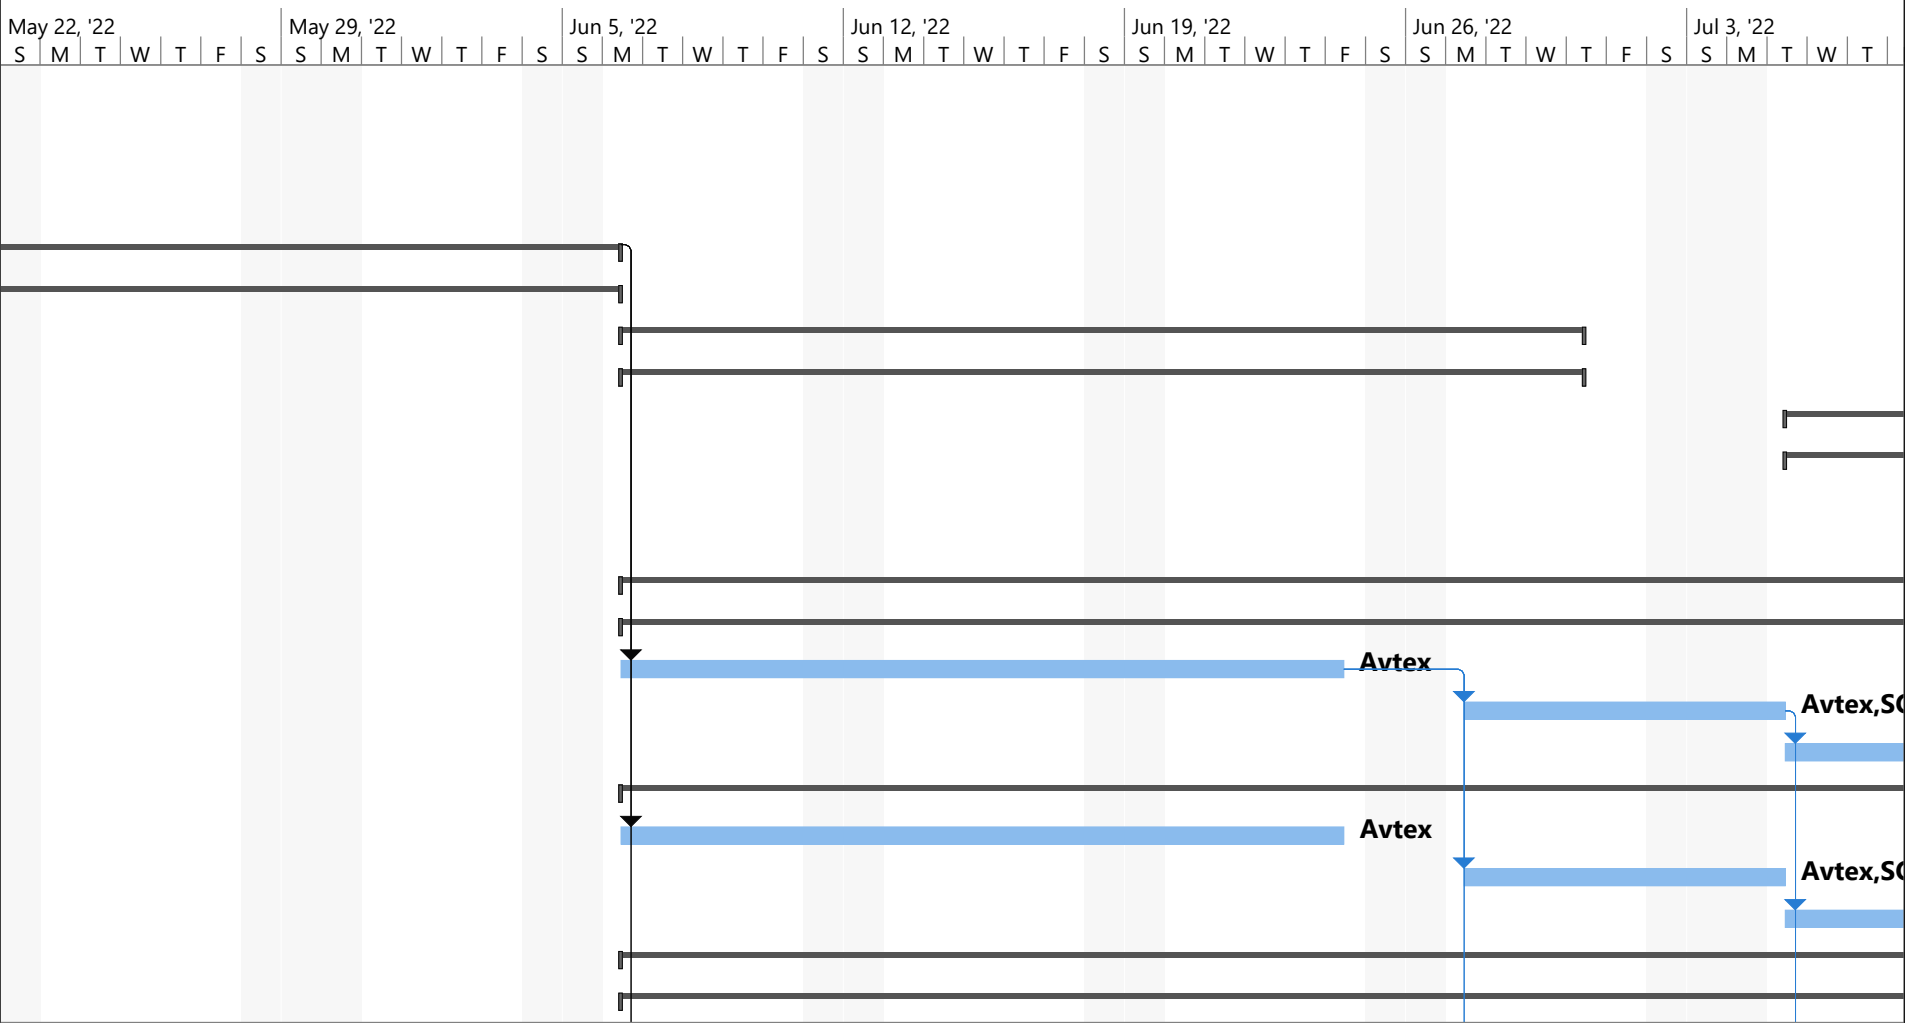




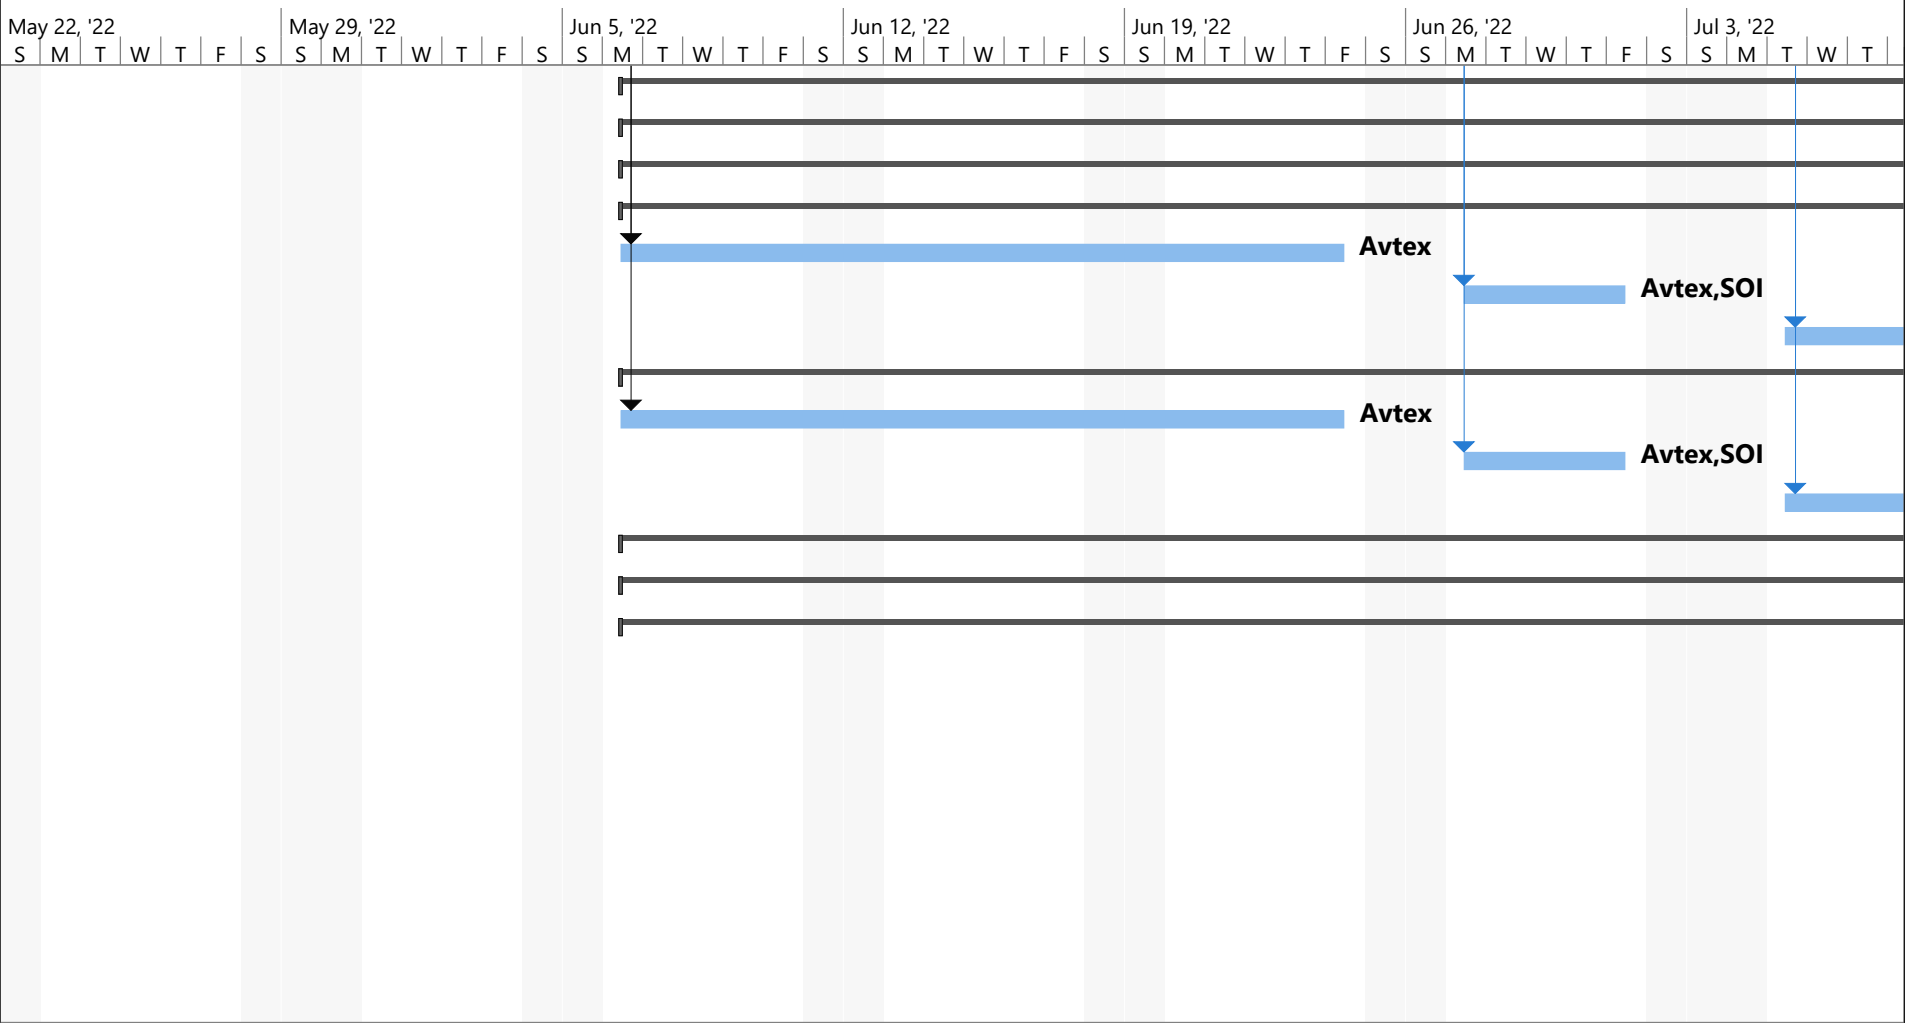















Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			













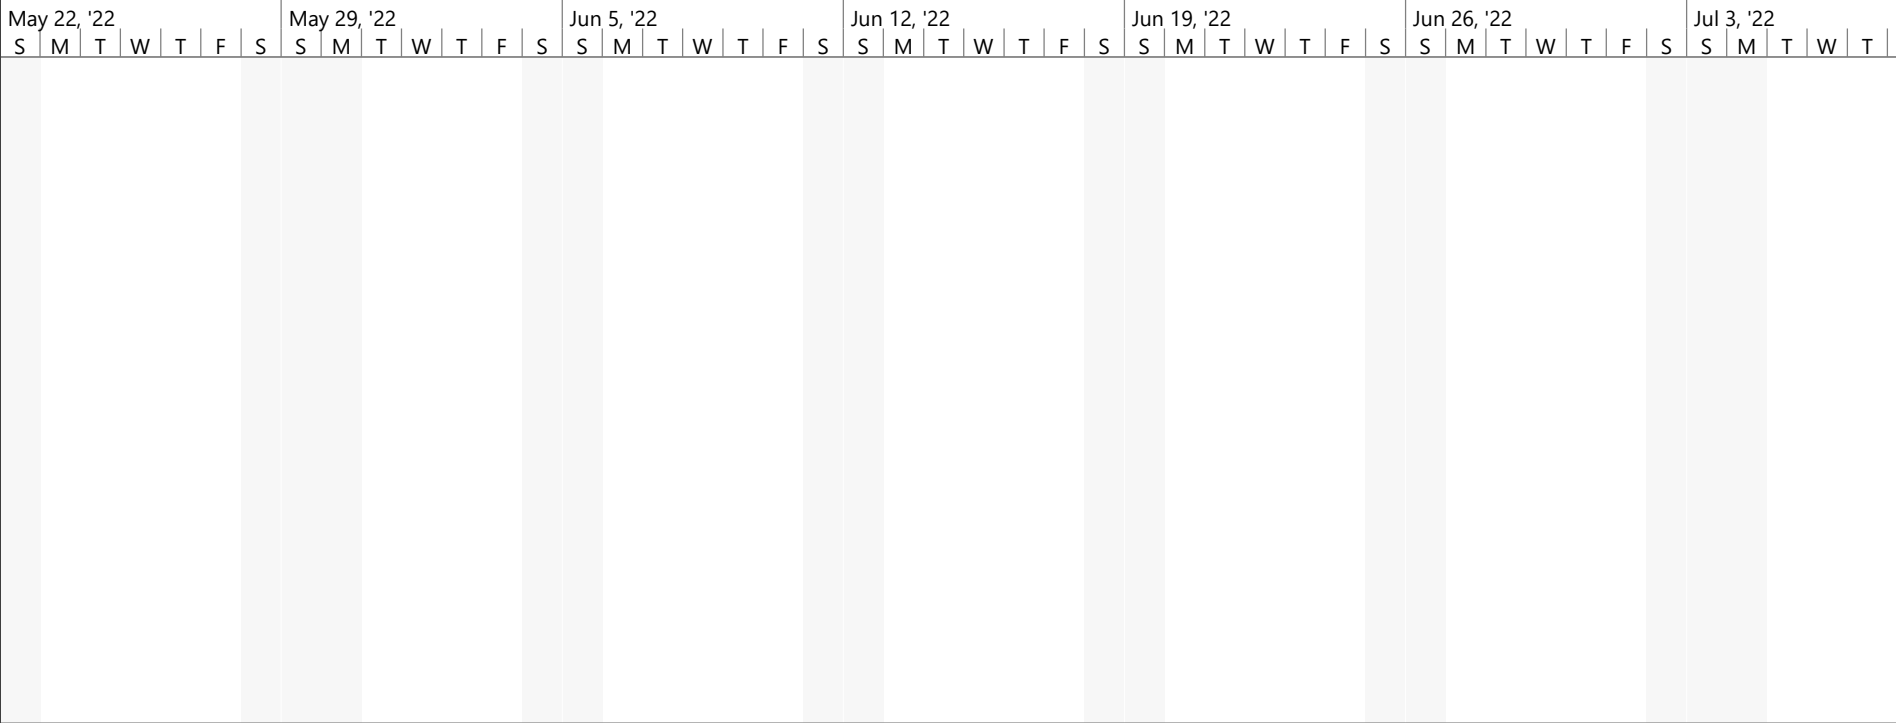









Project: Sample PureCloud Imp
Date: Fri 9/17/21


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

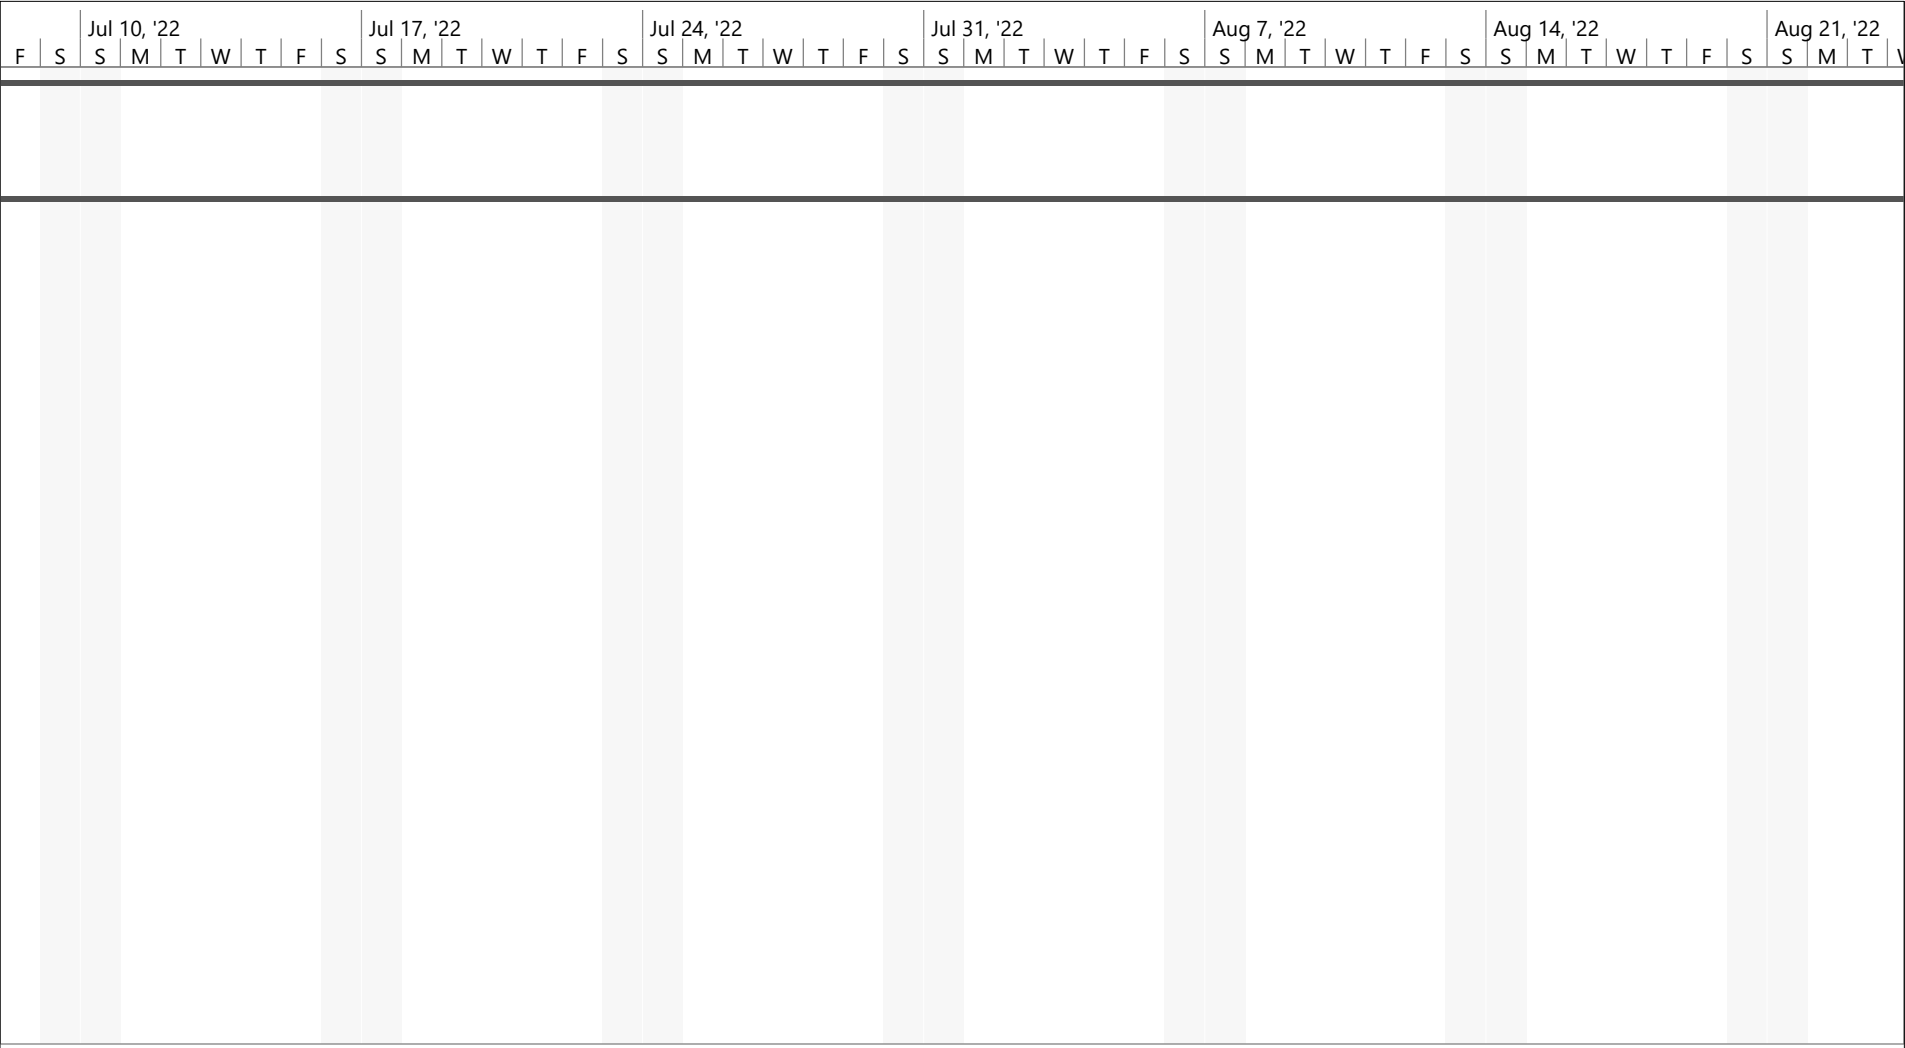





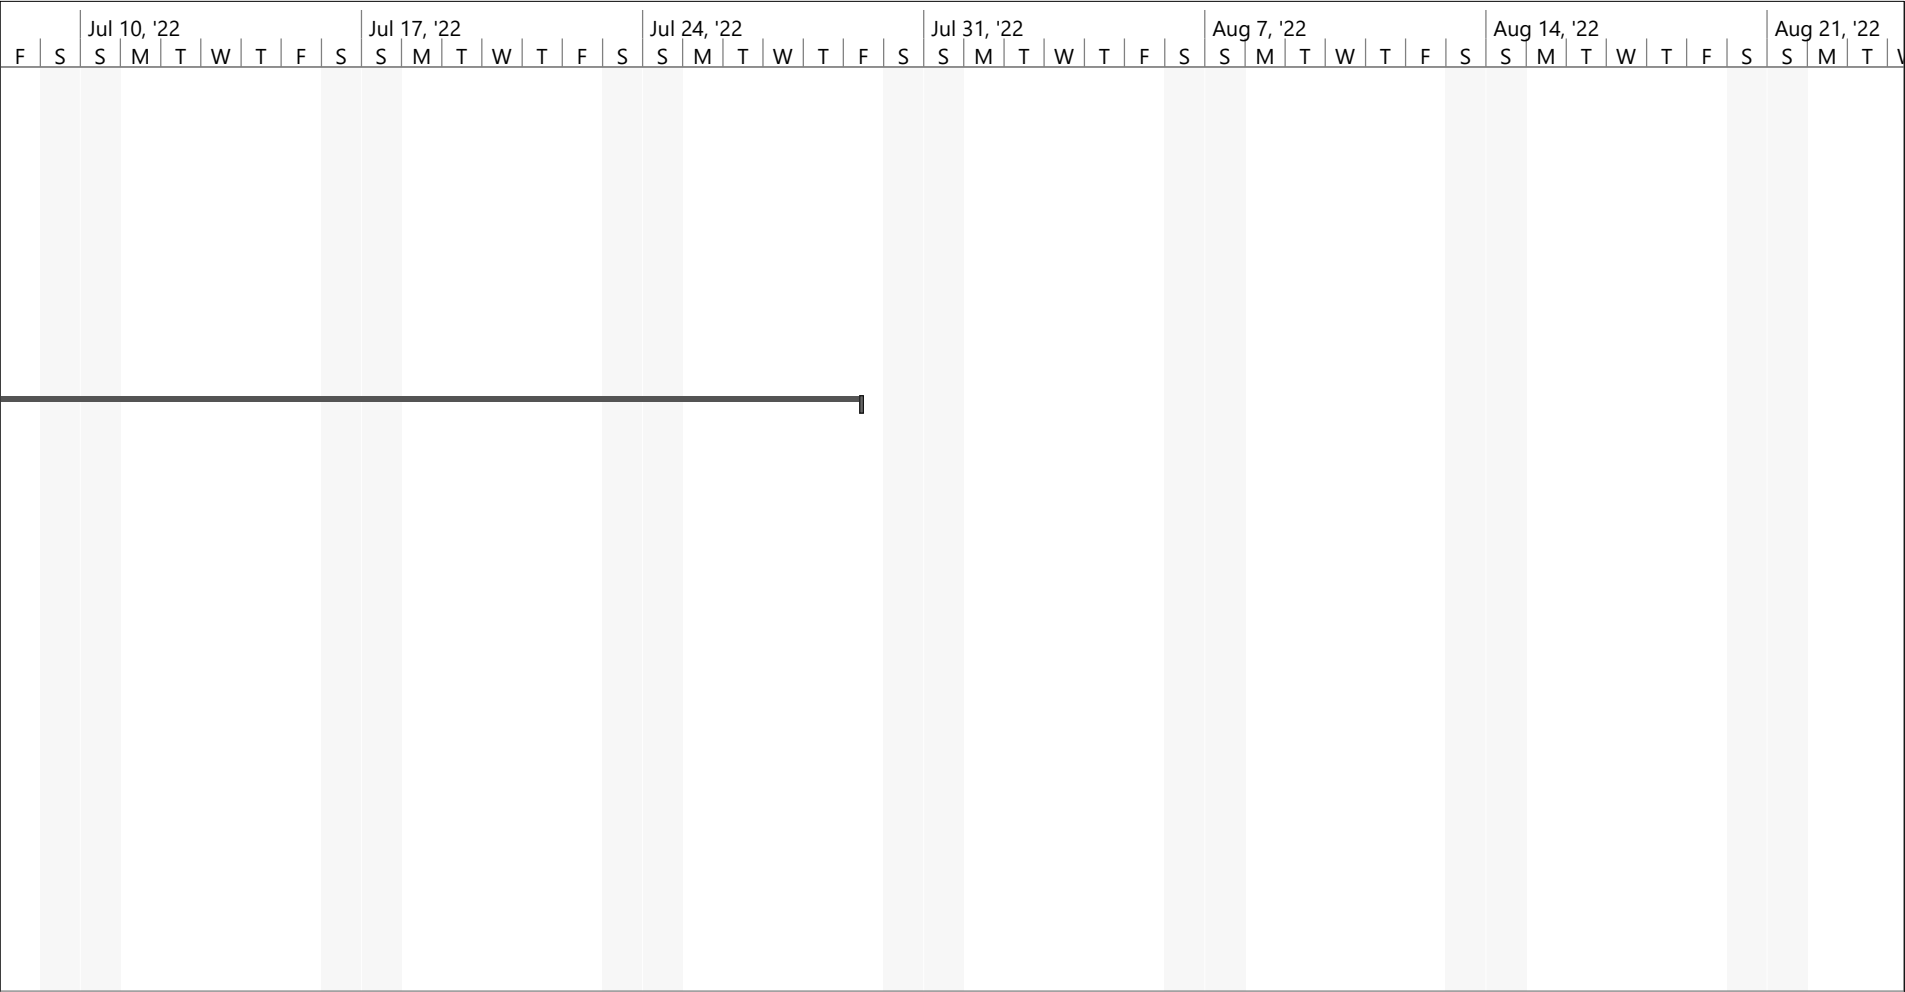














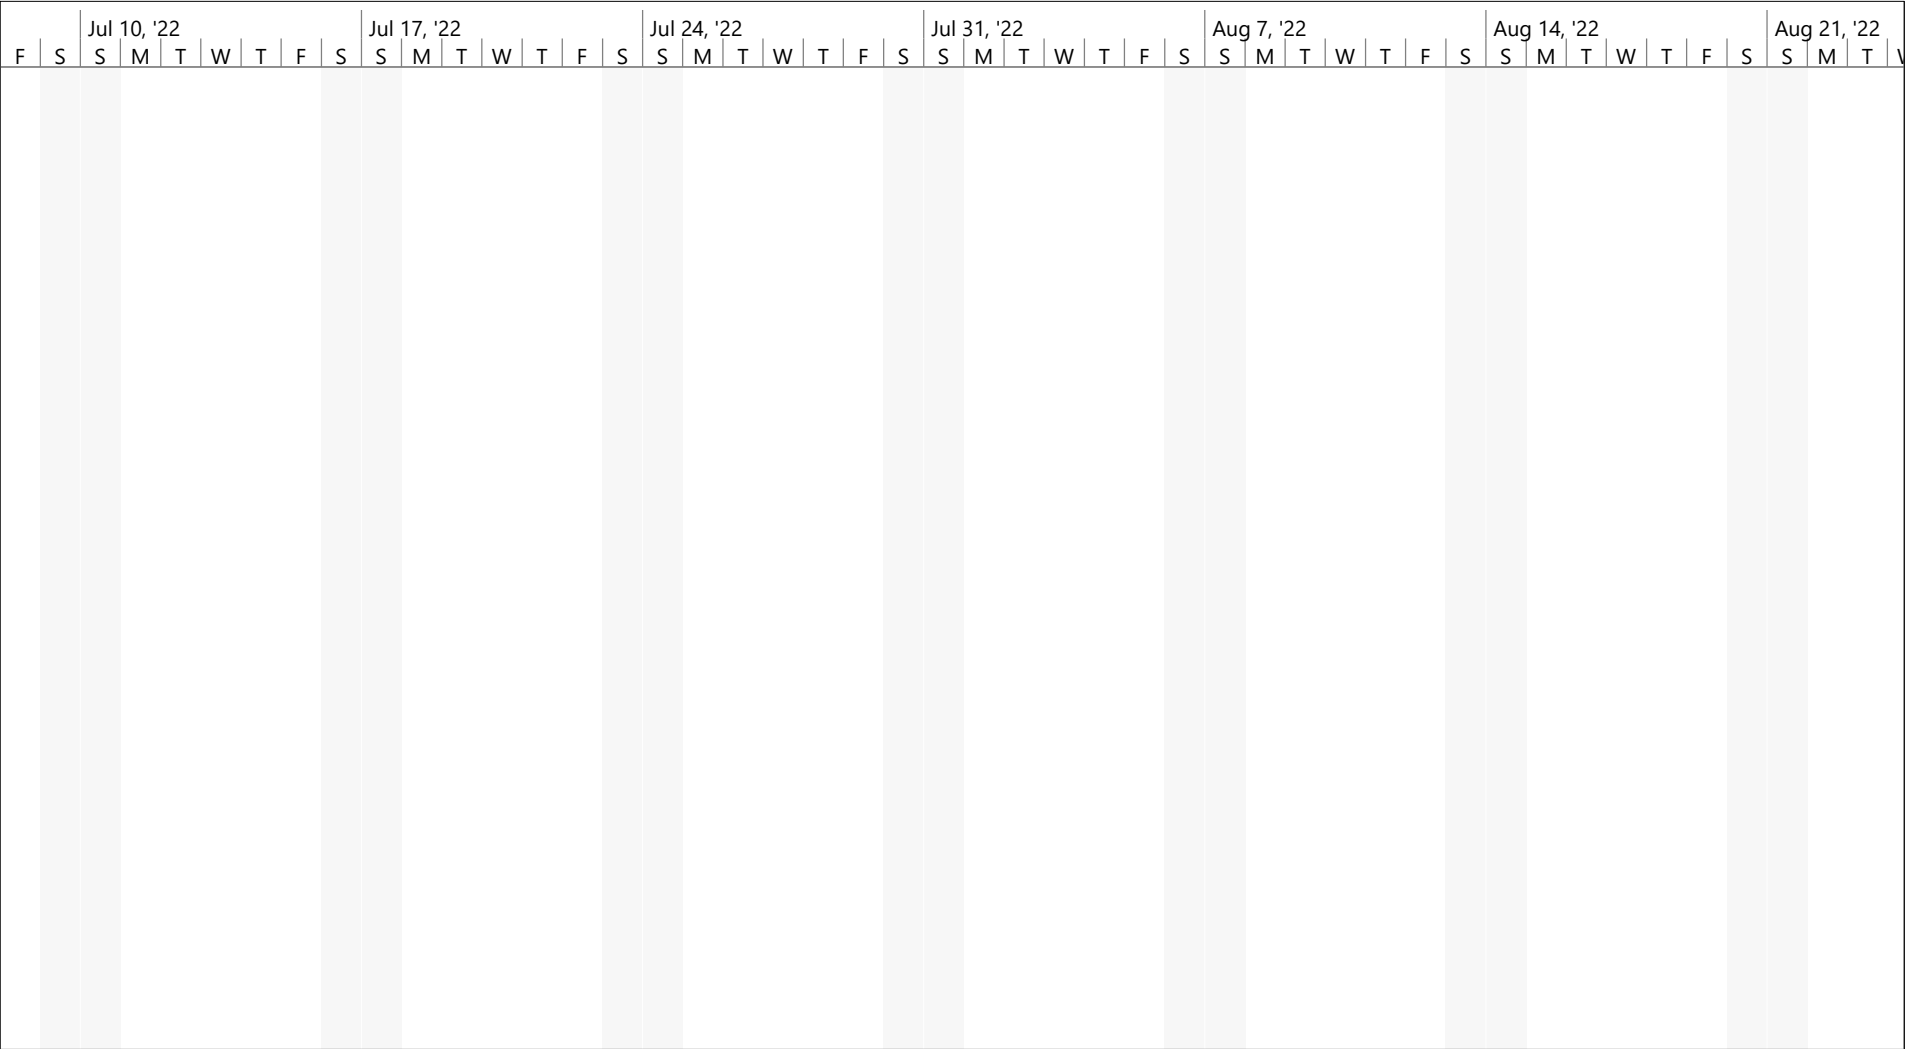
Project: Sample PureCloud Imp
Date: Fri 9/17/21




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21








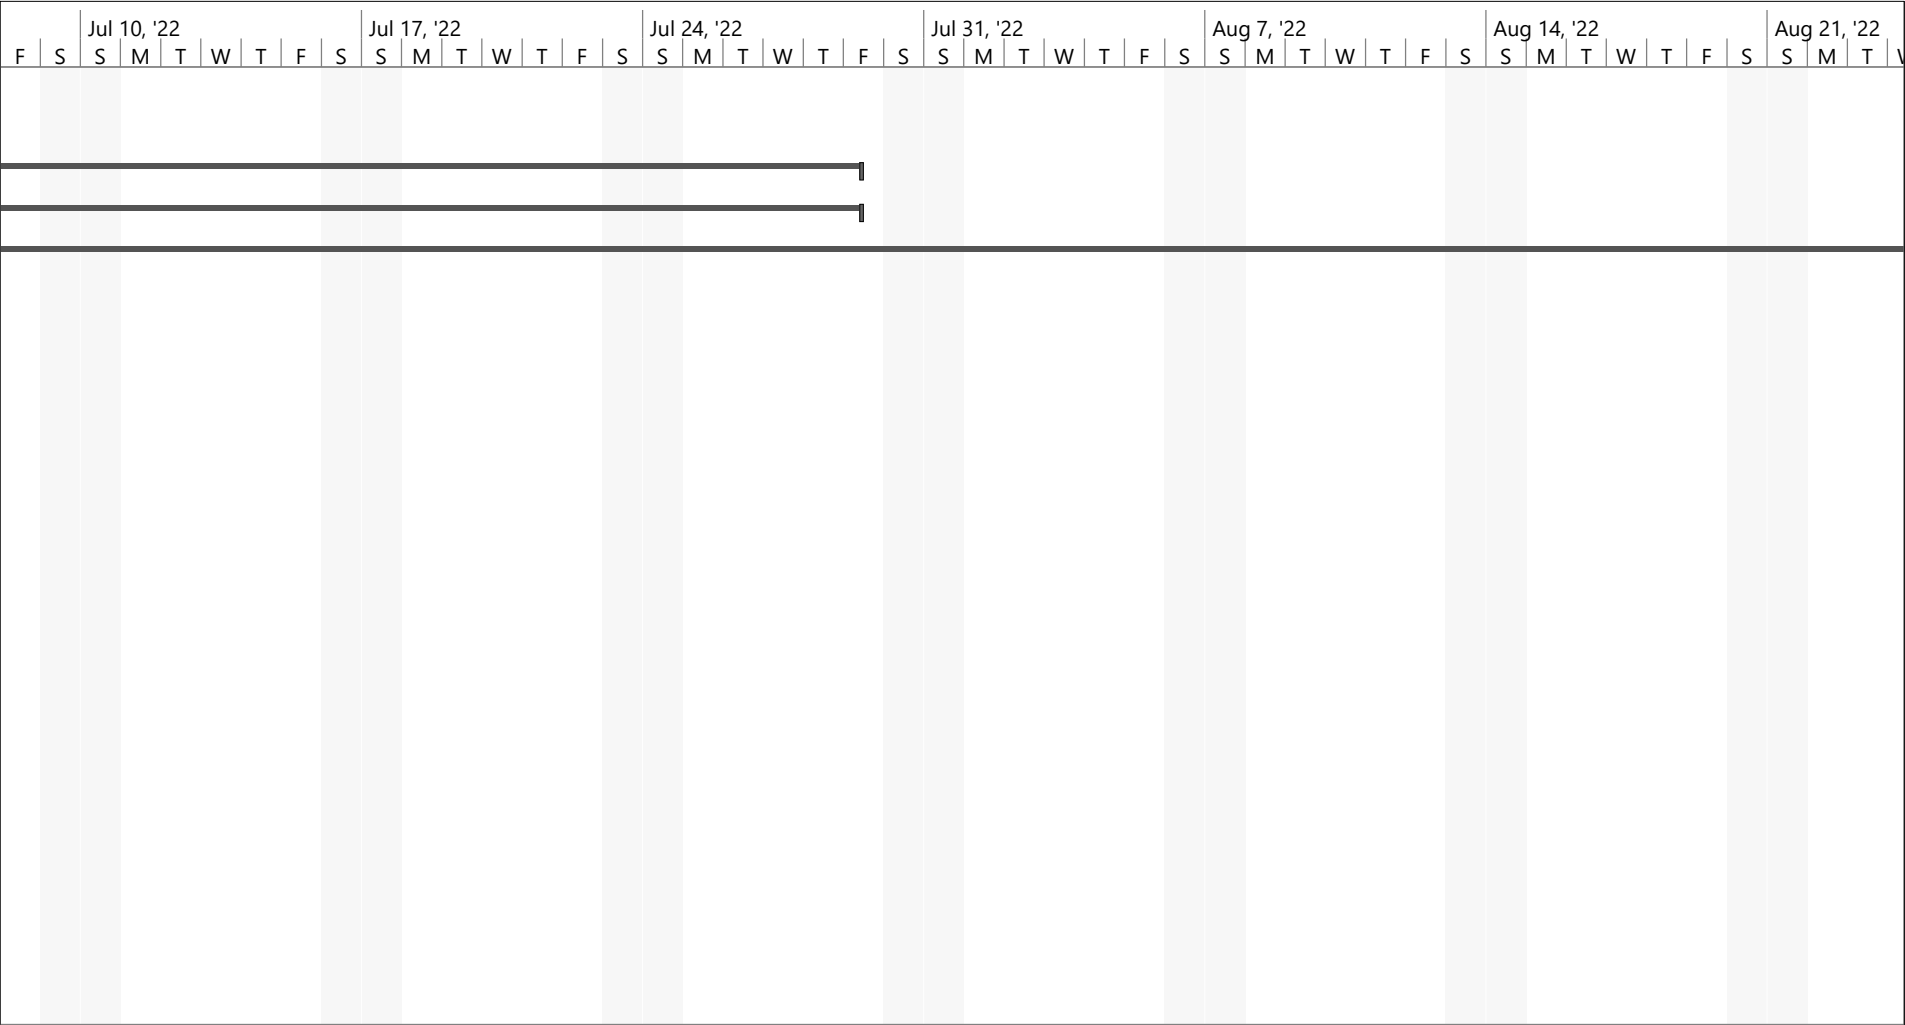











Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

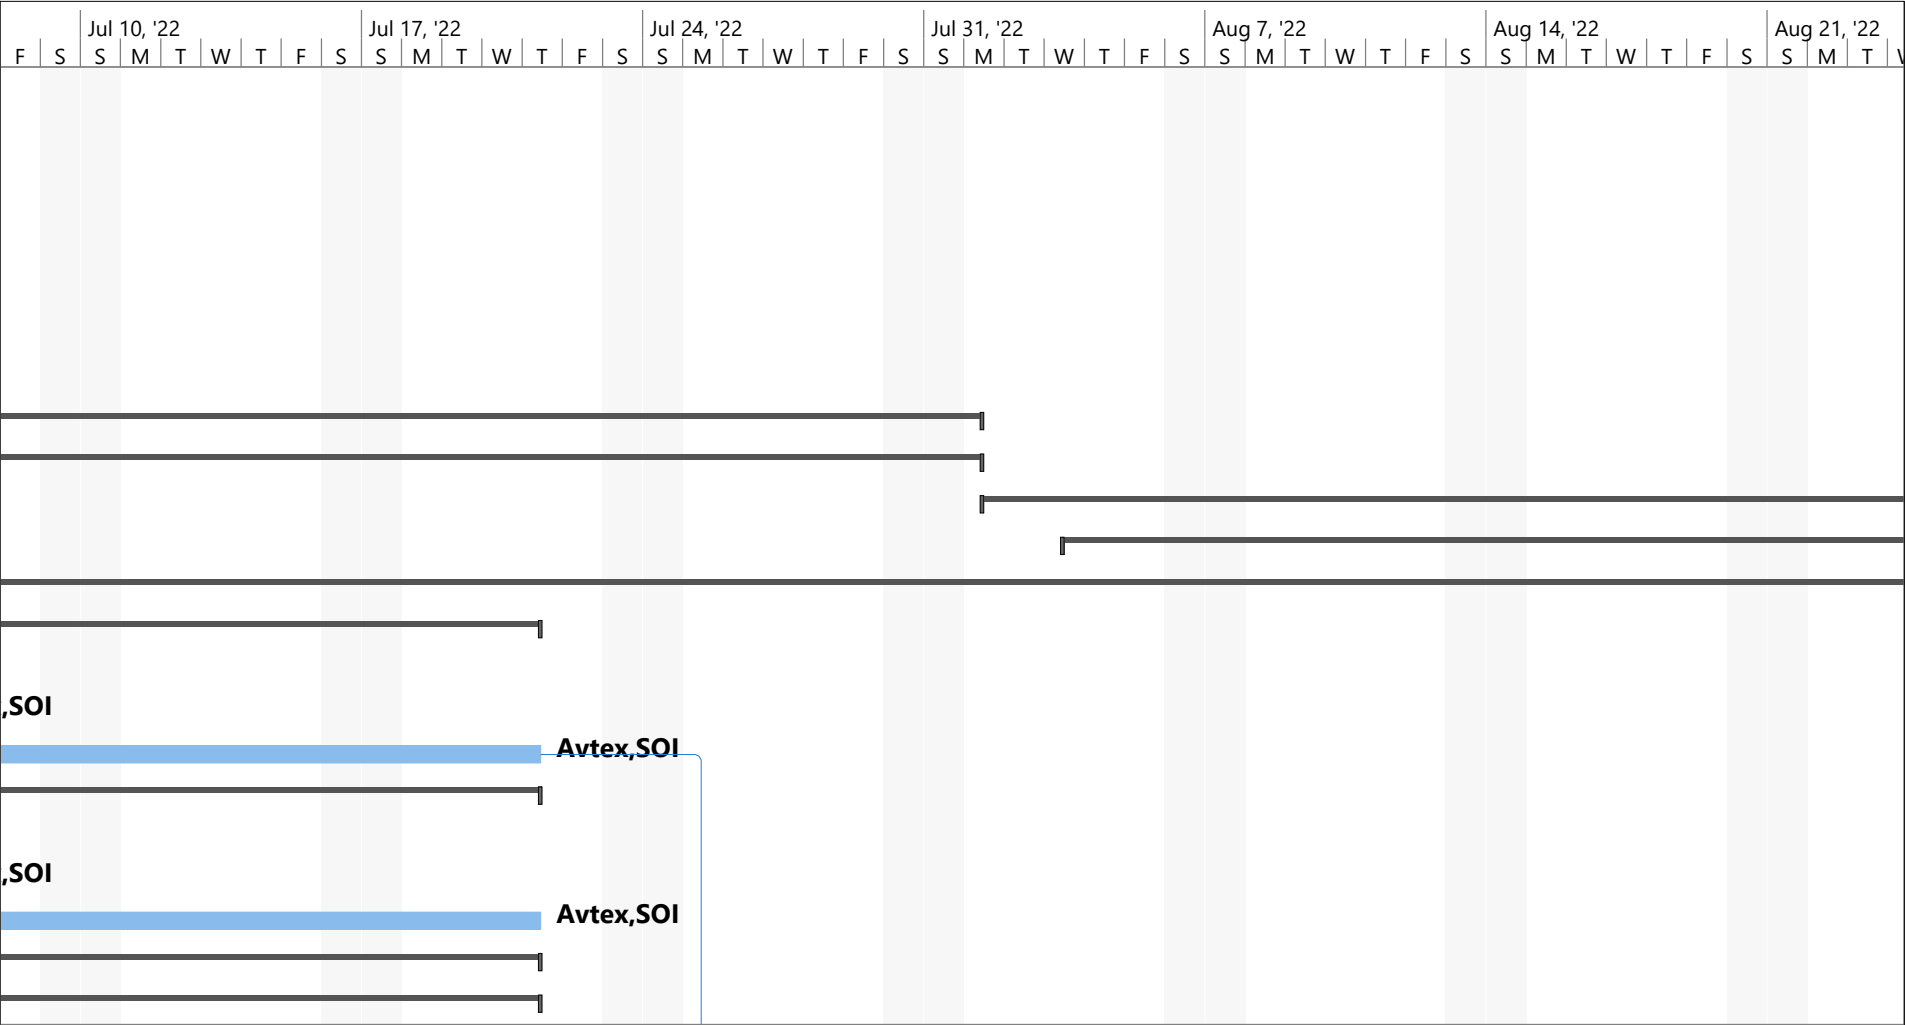


Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

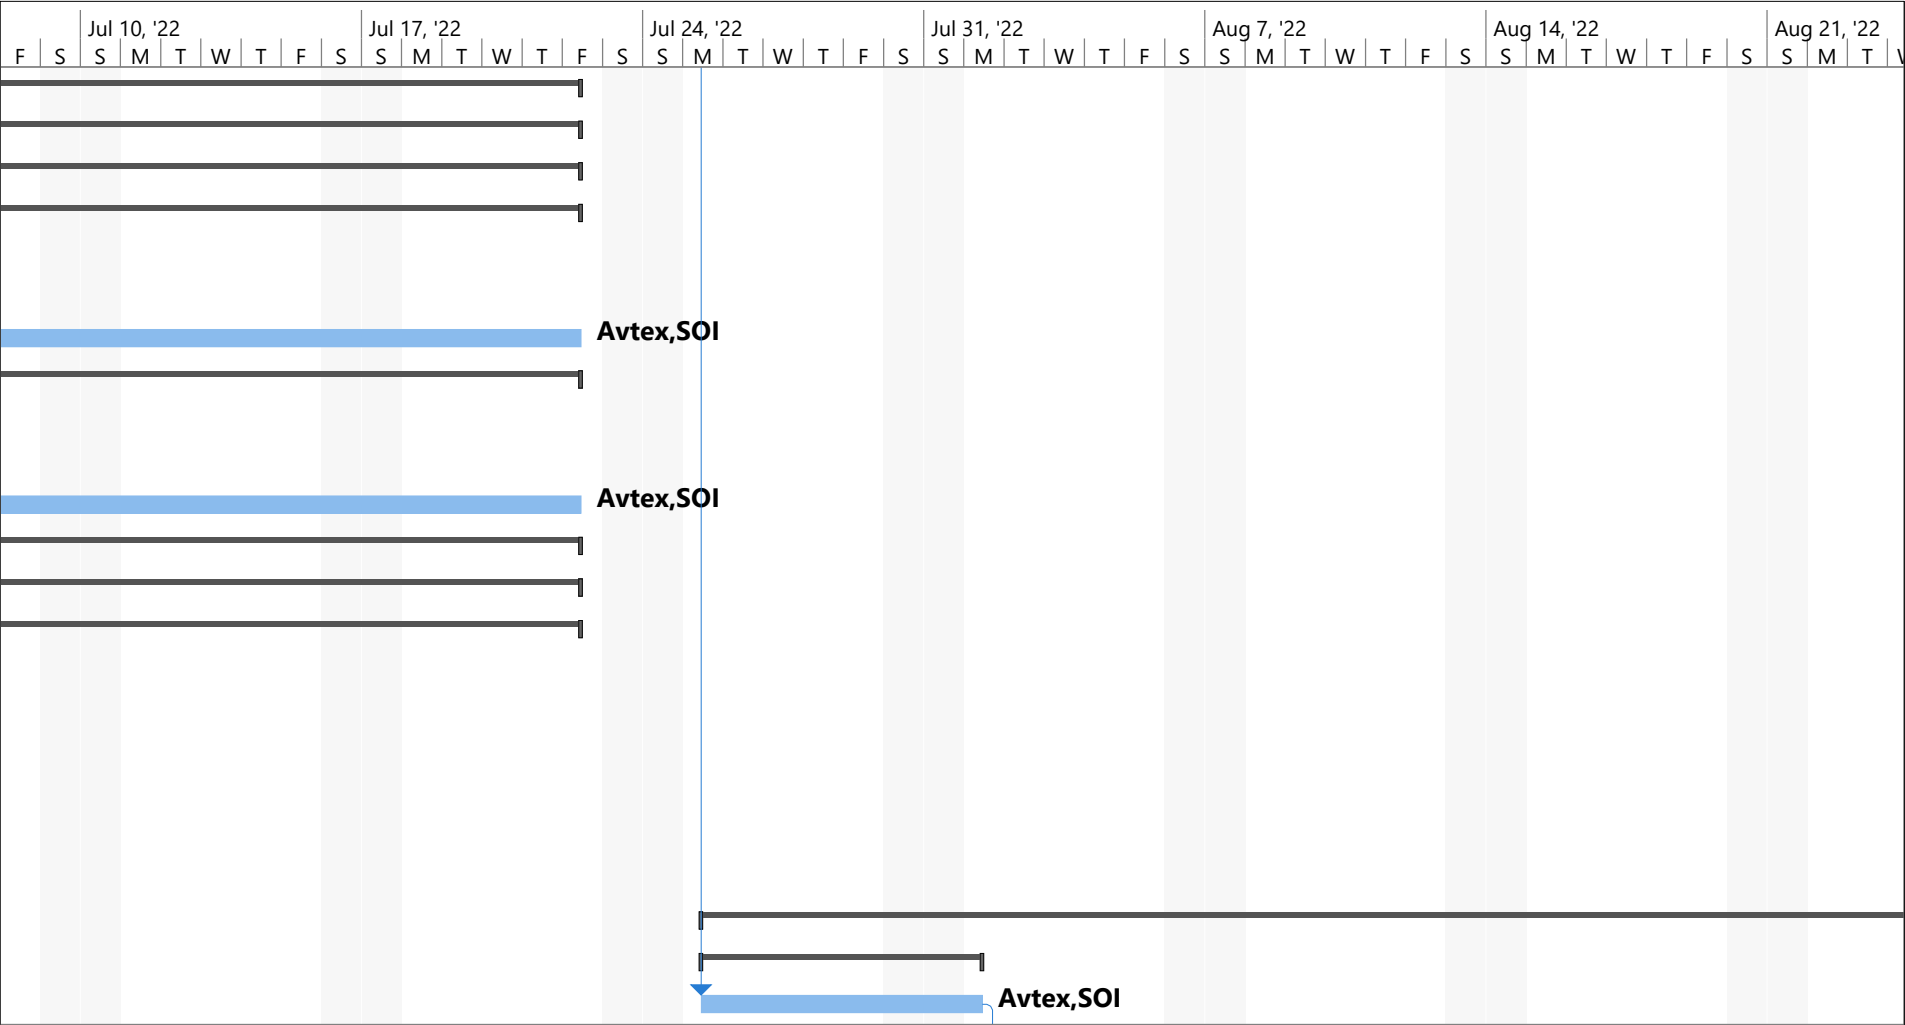


Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

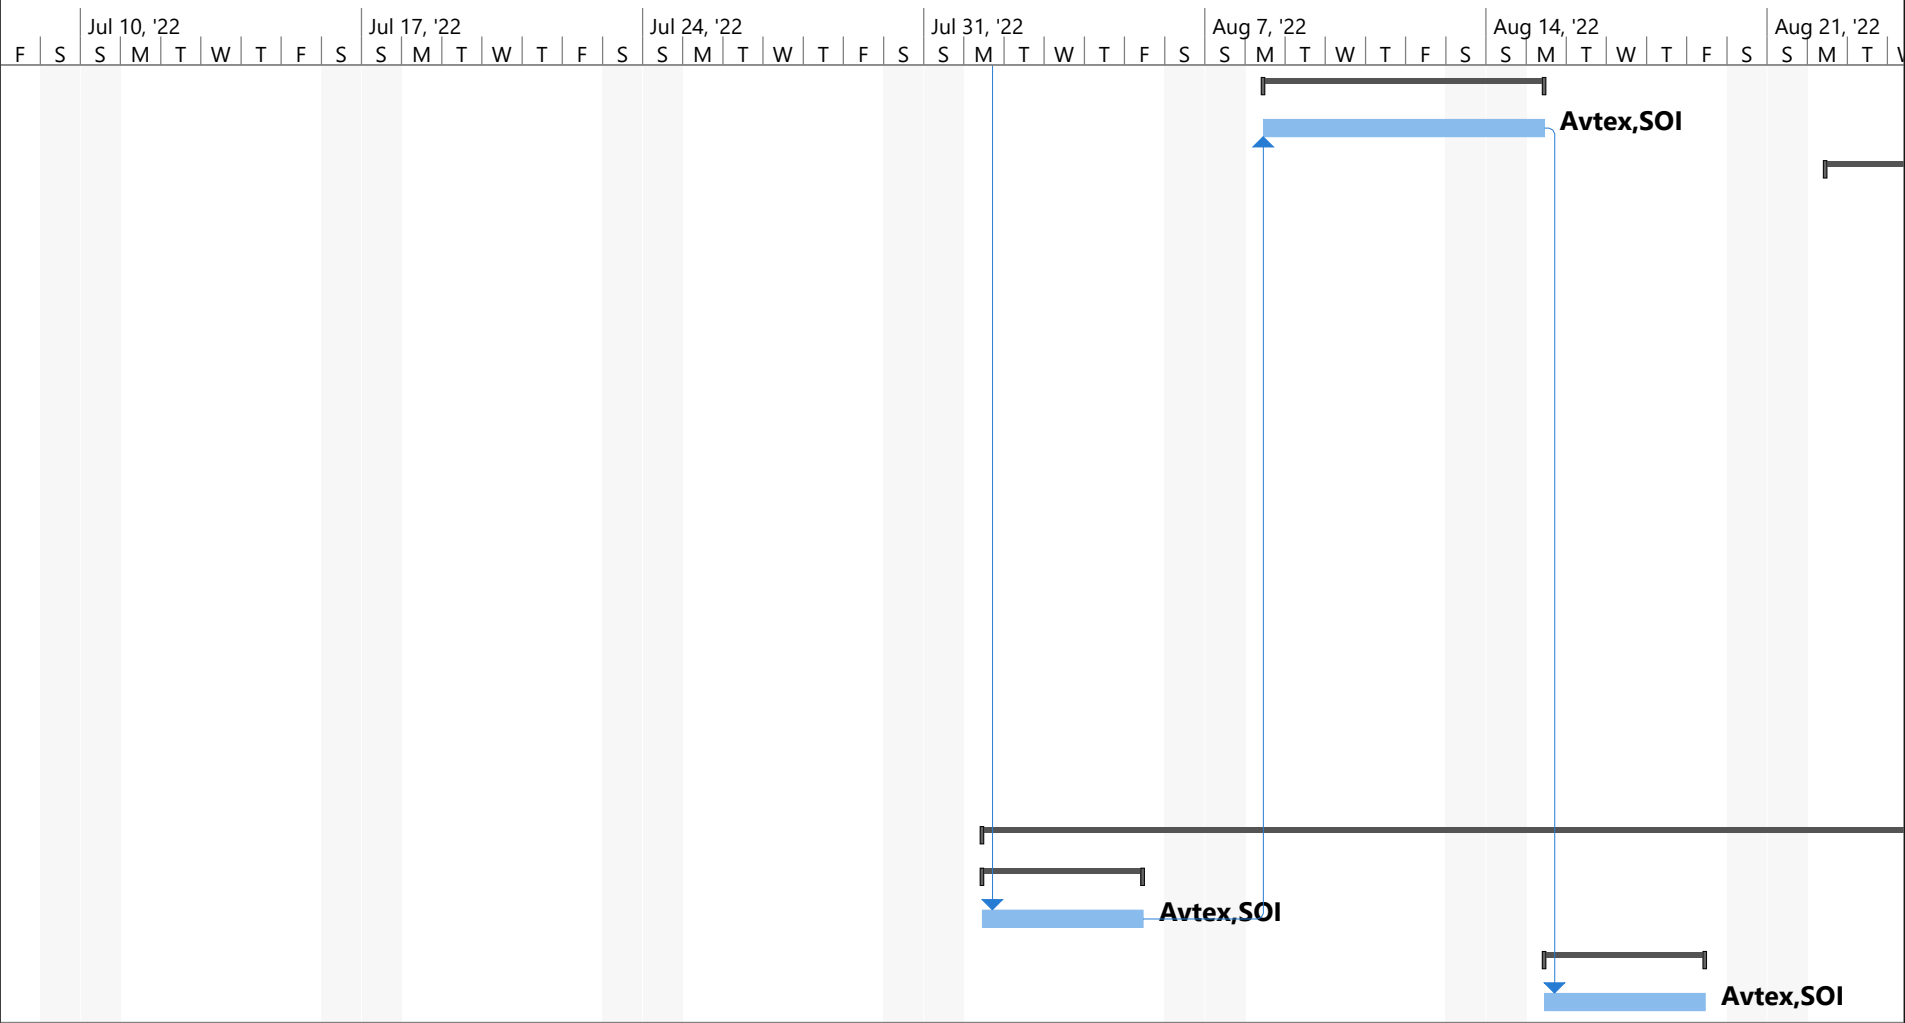





















Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21






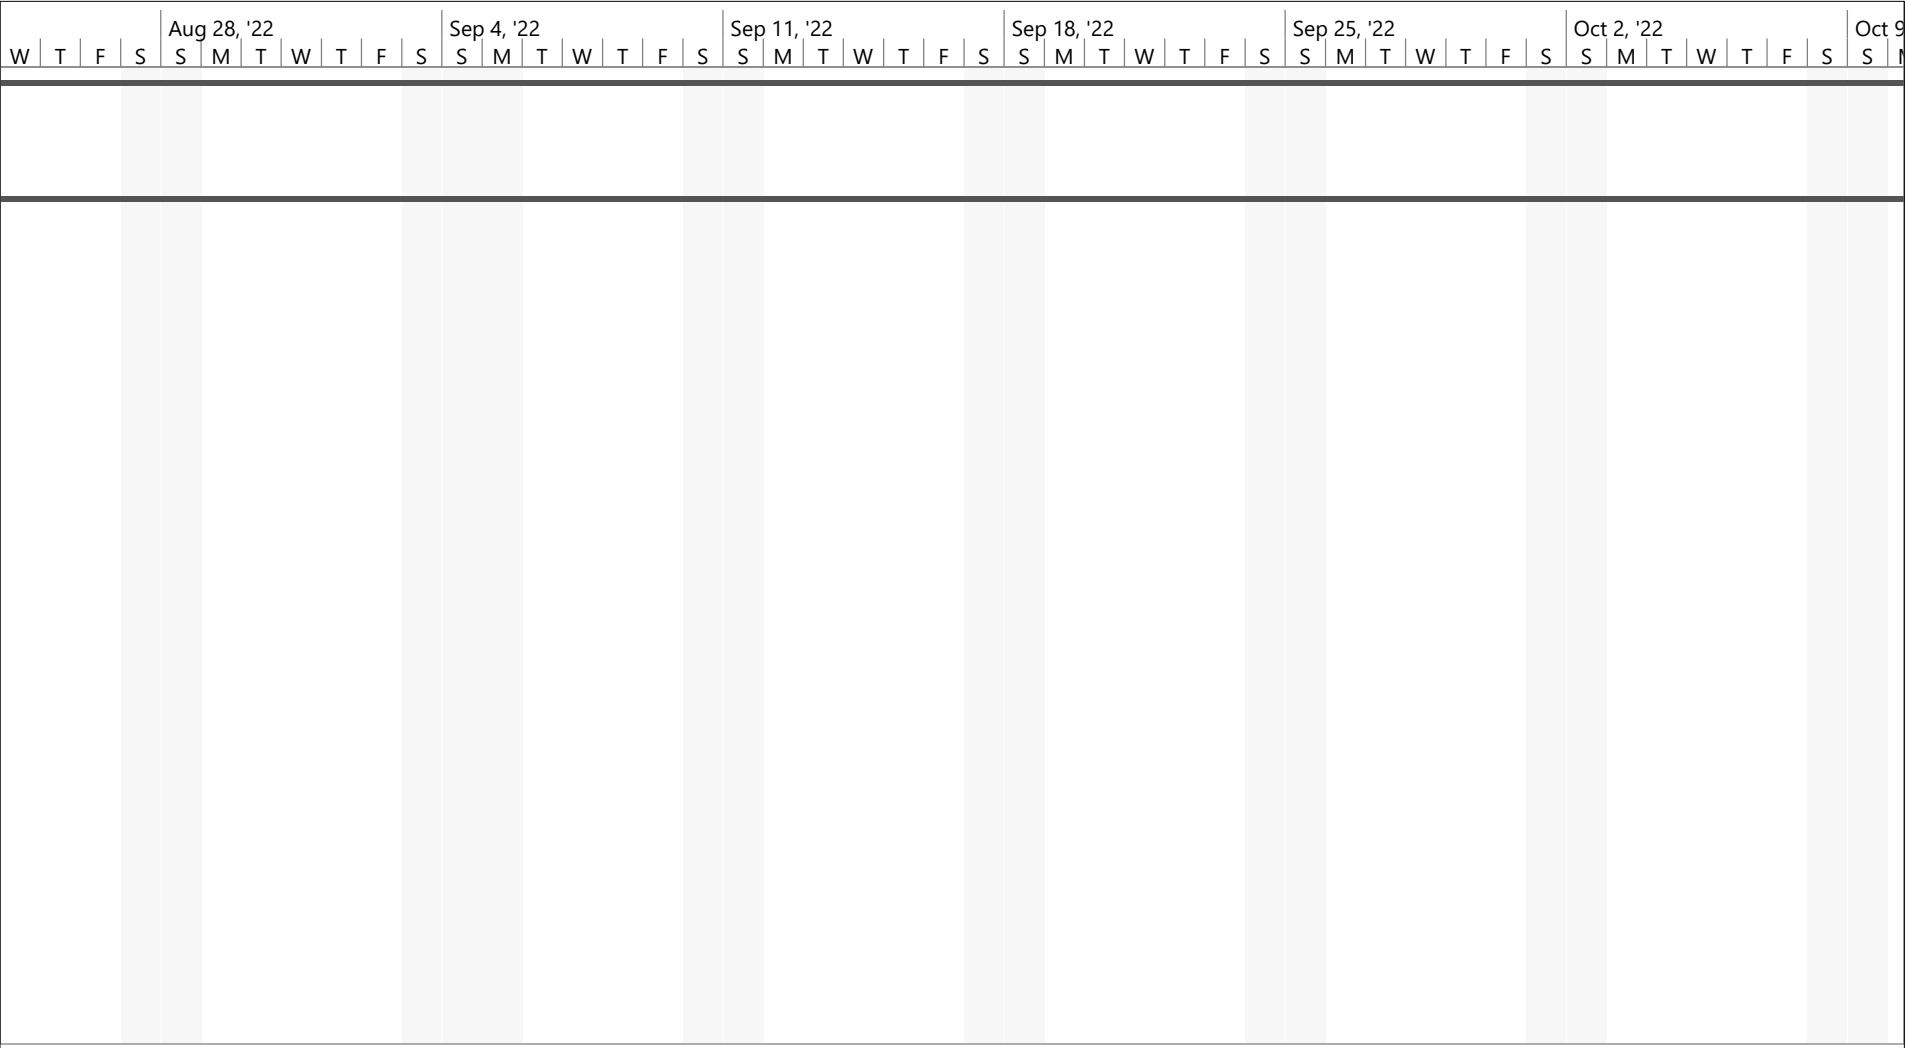



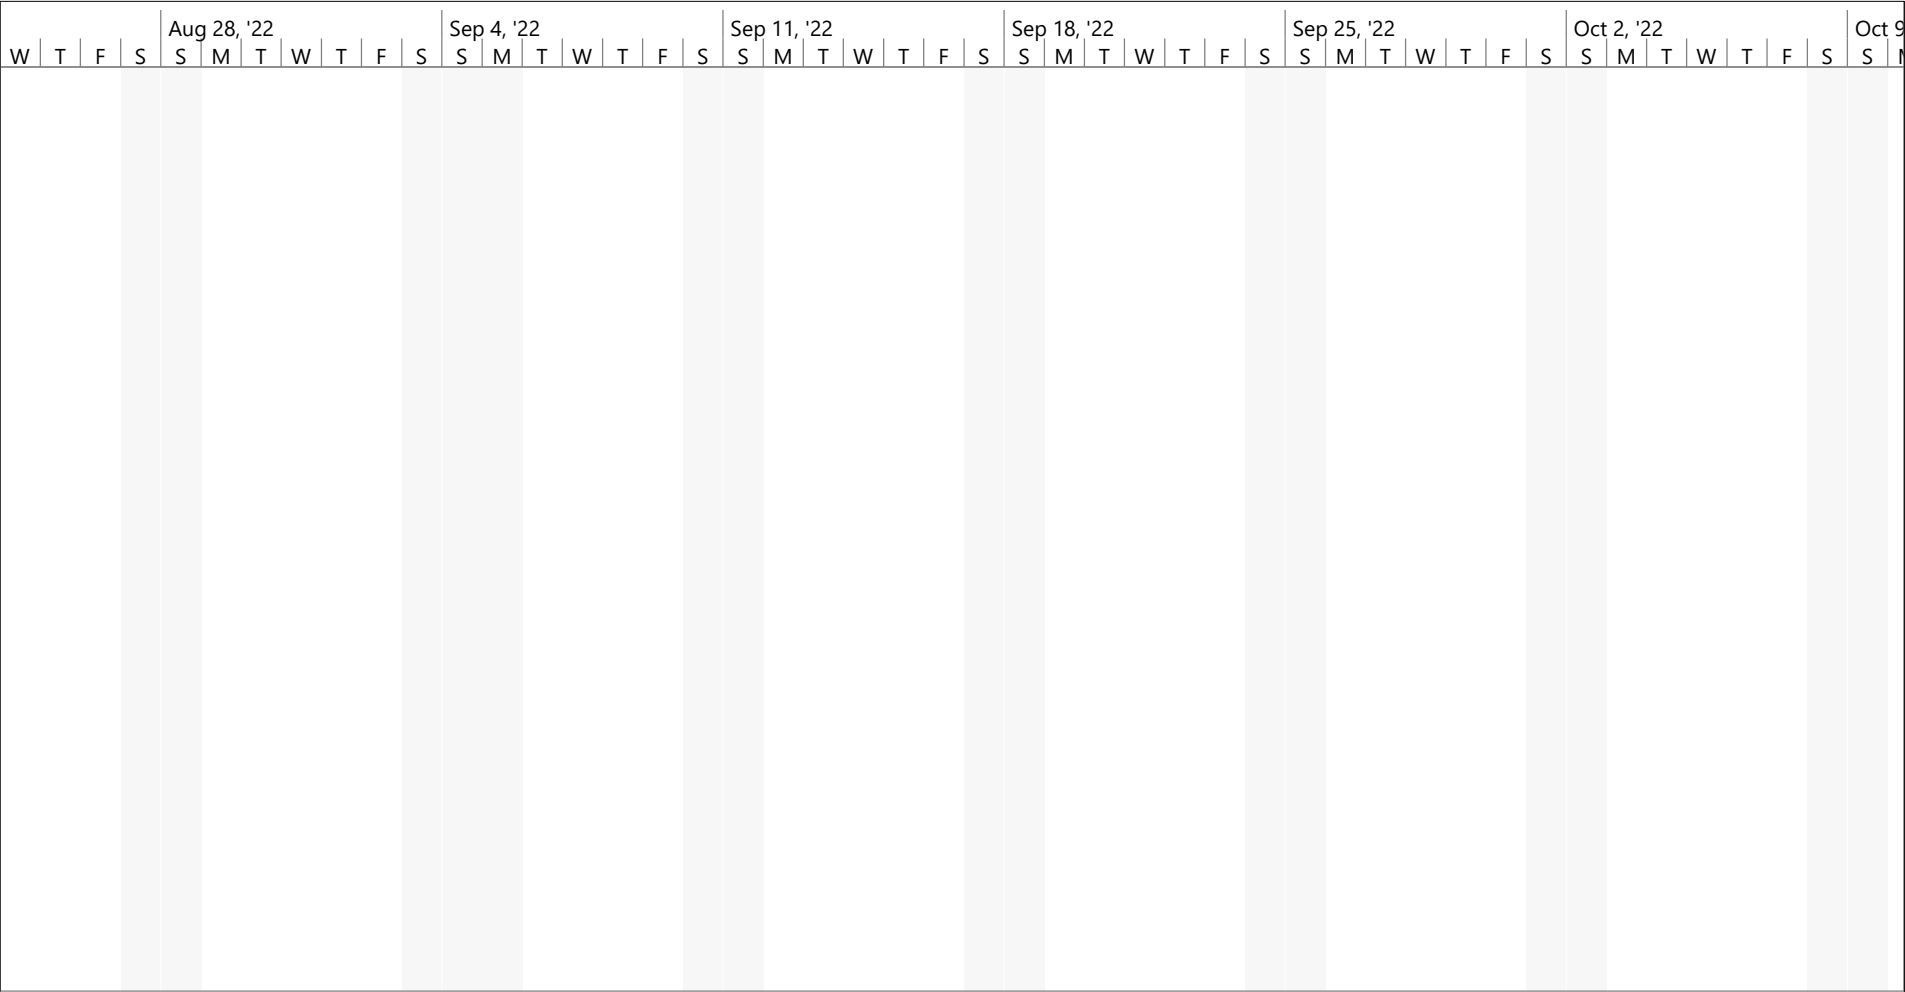









Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

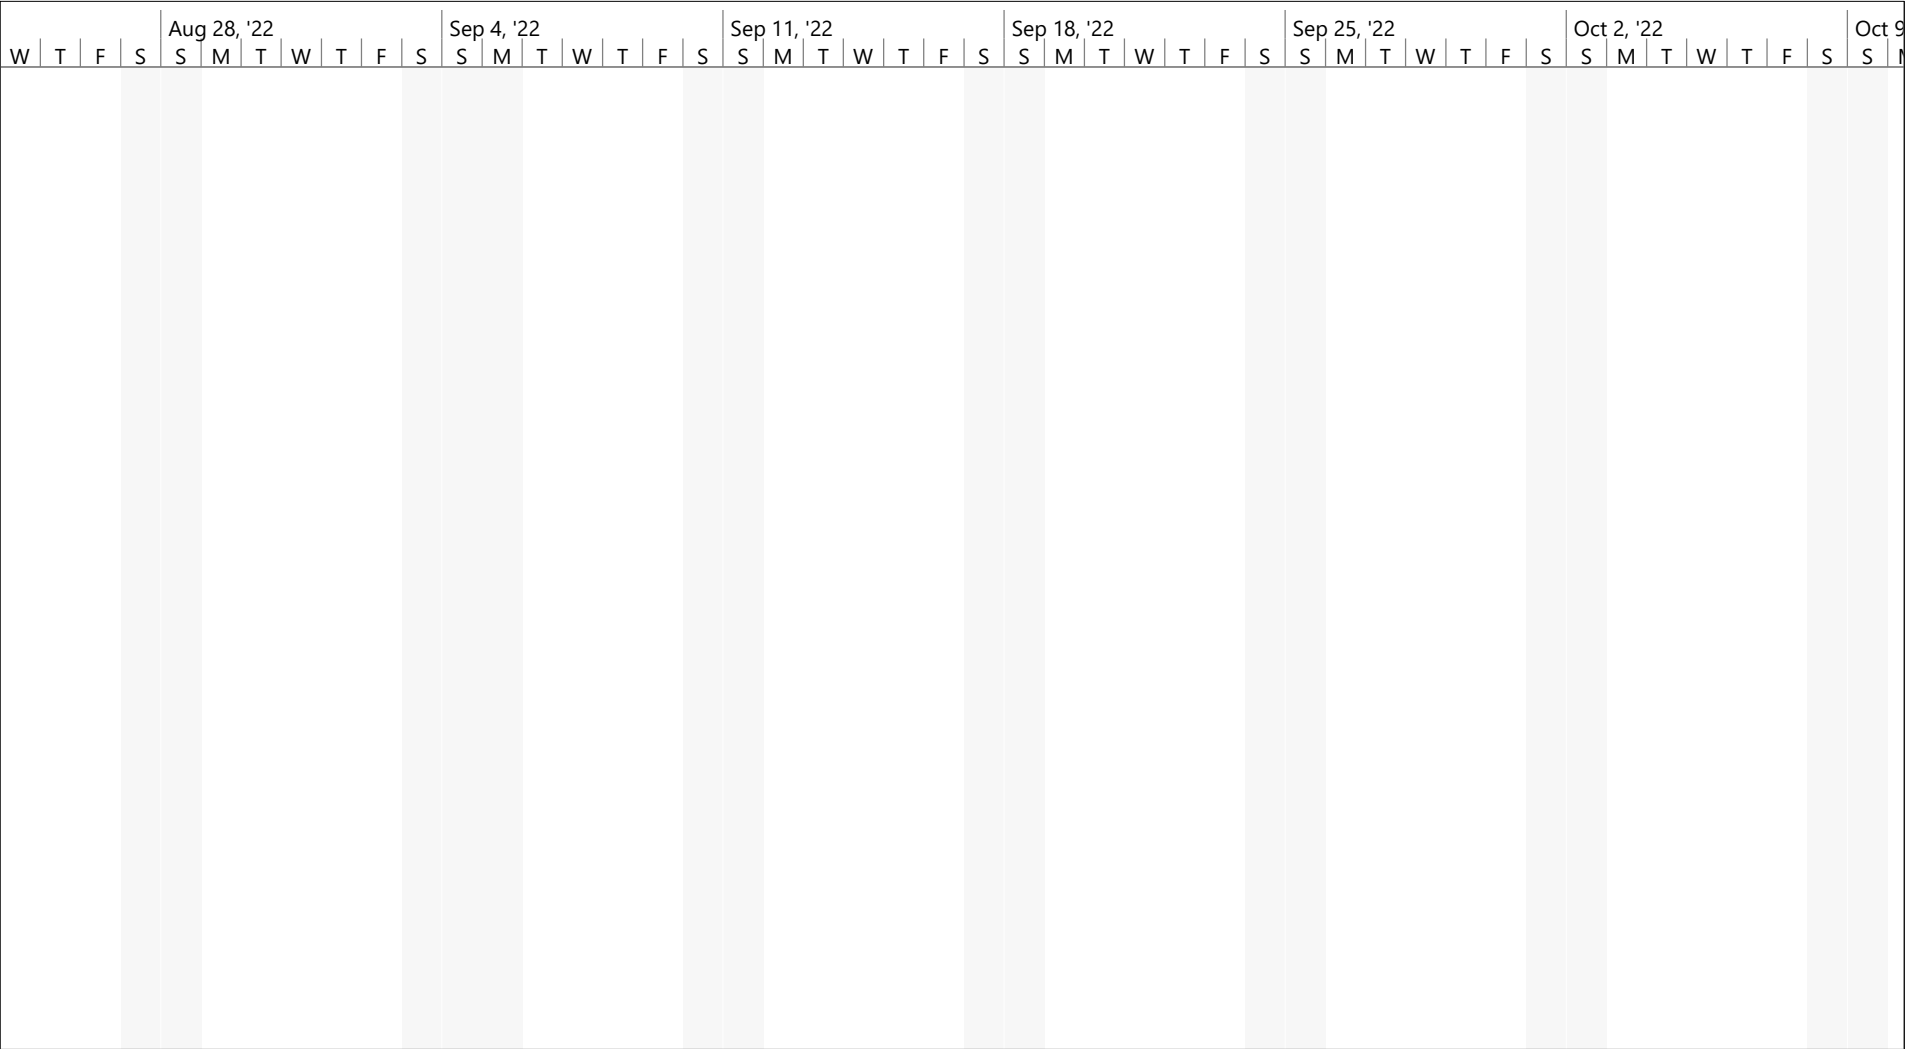


Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

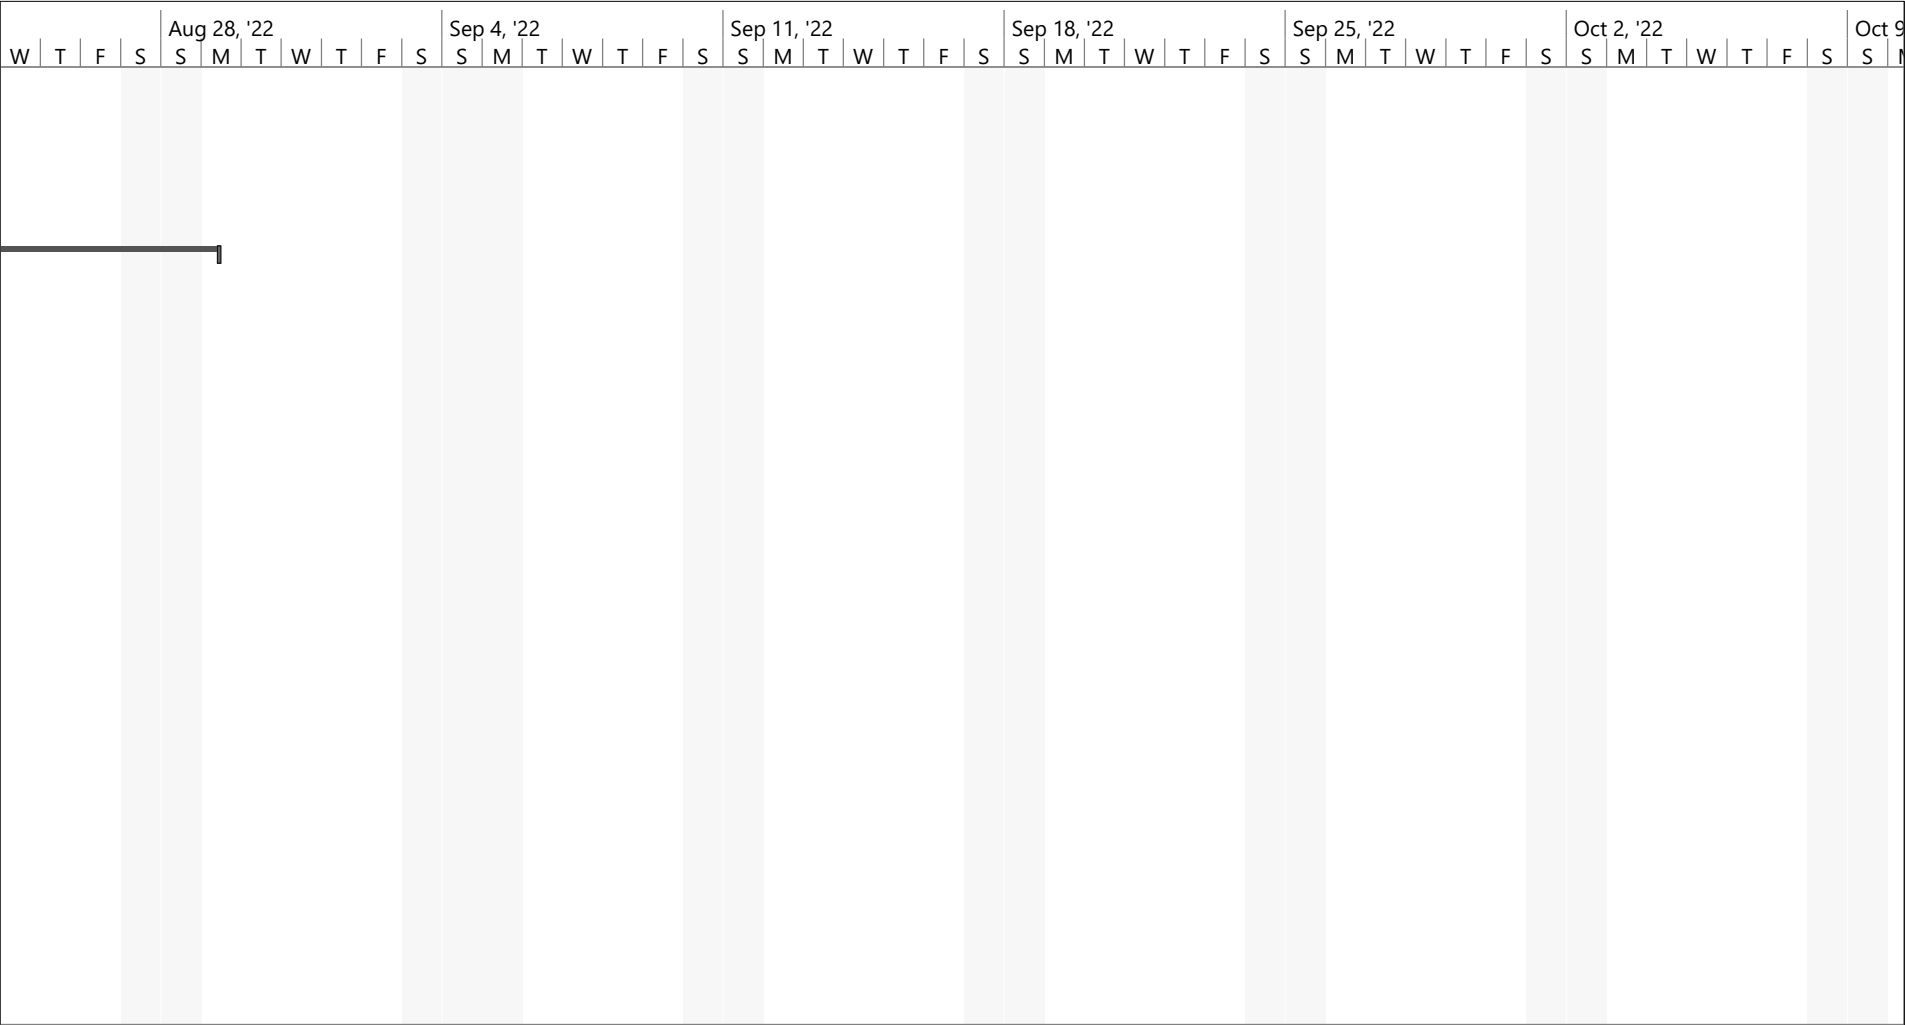








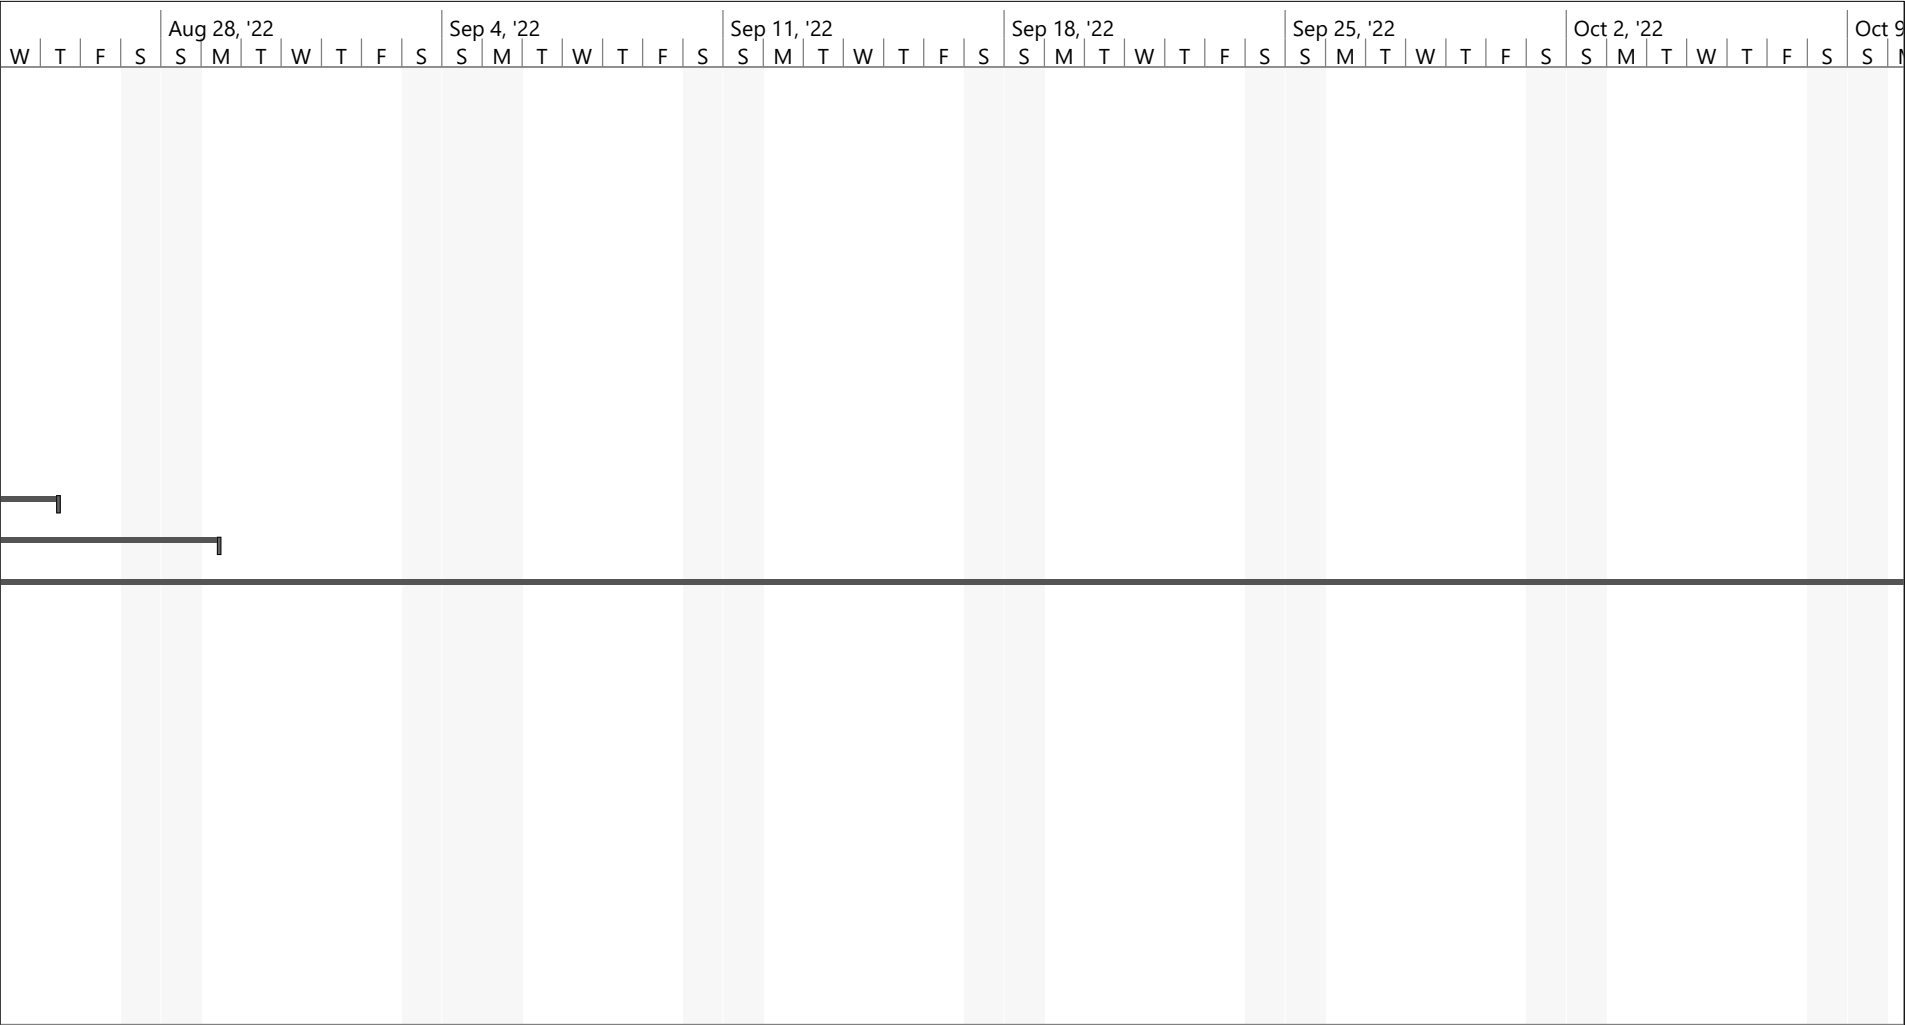












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

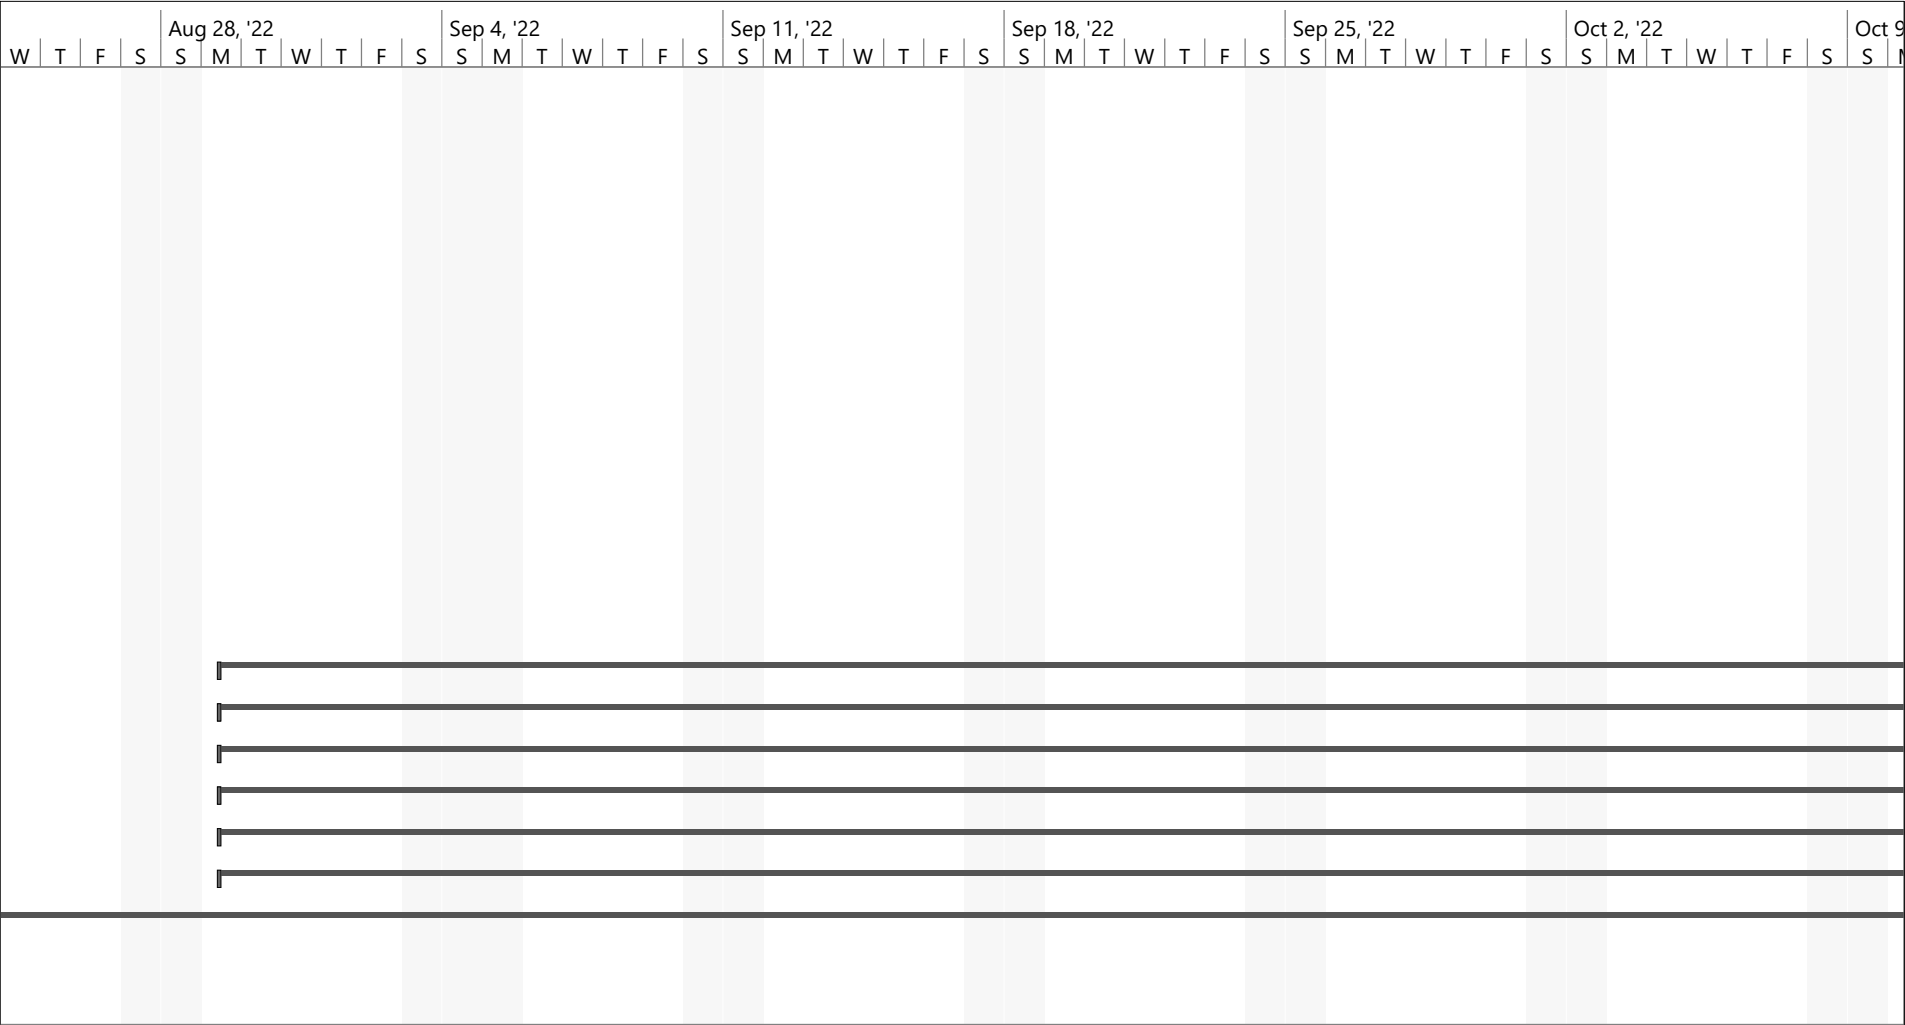


Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

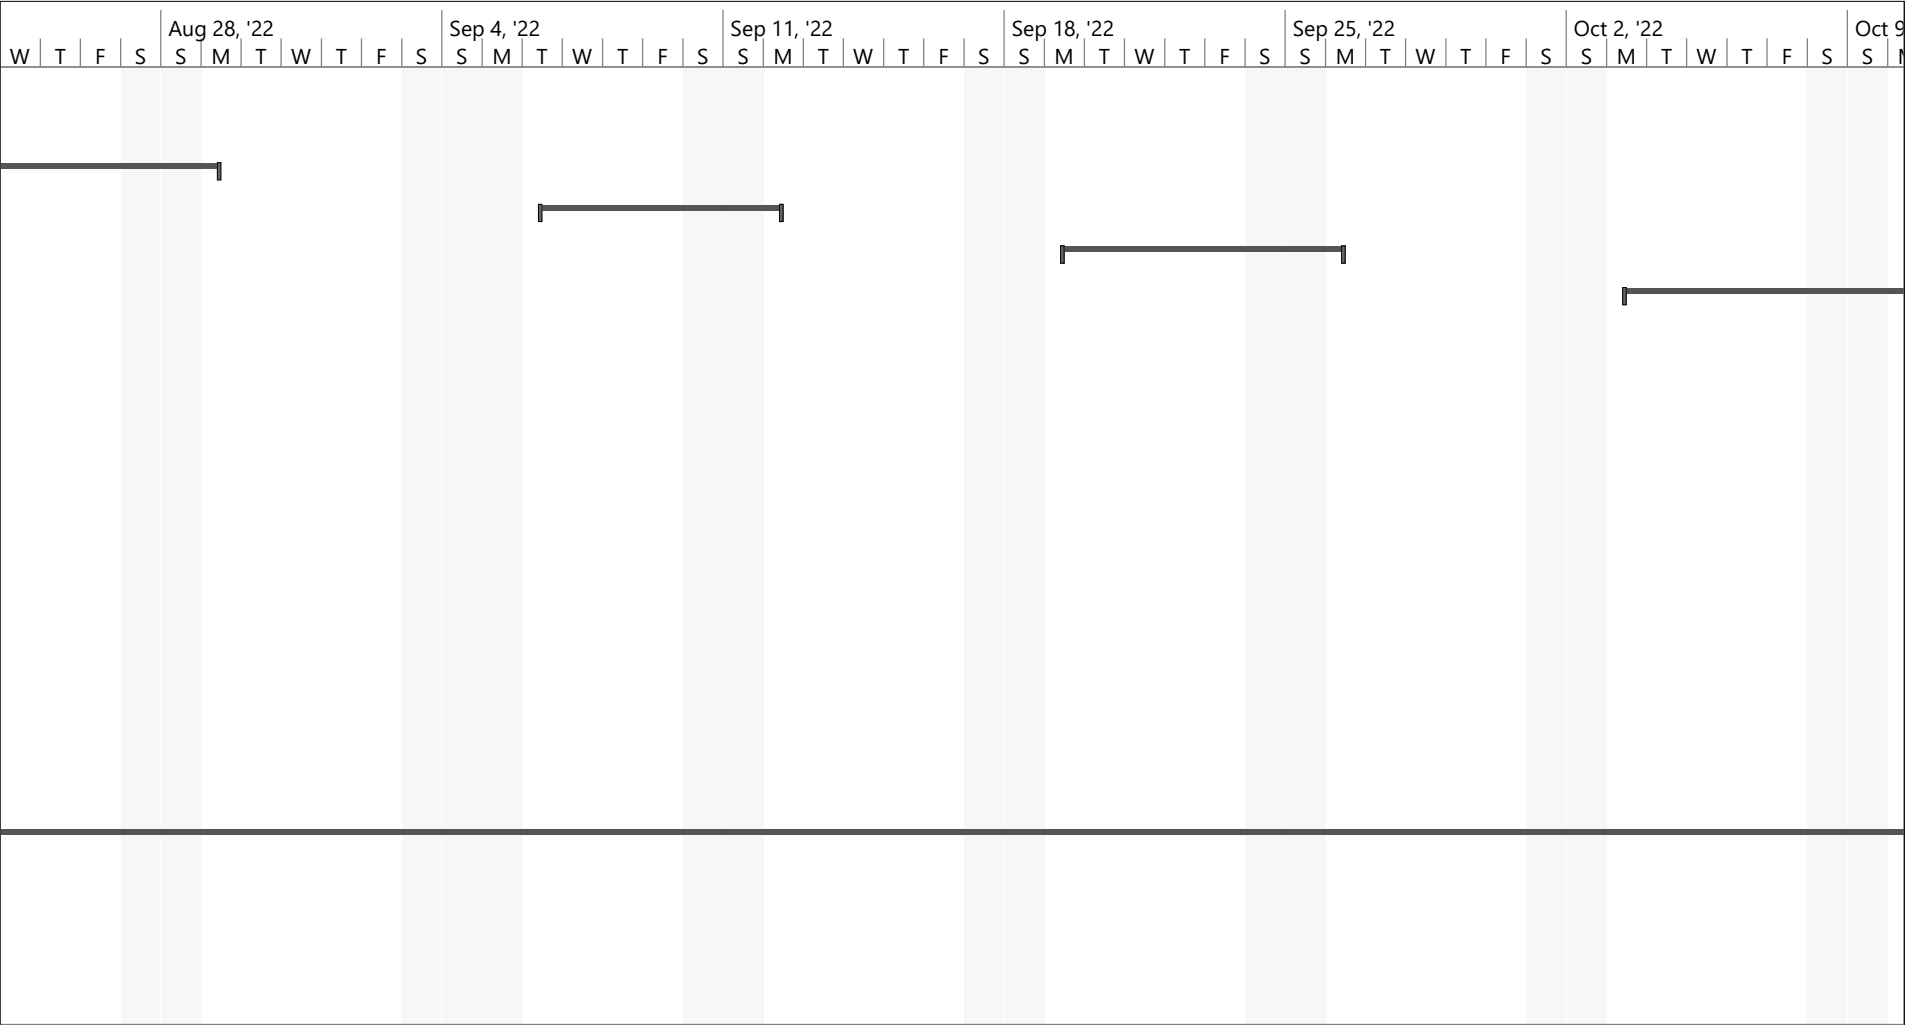








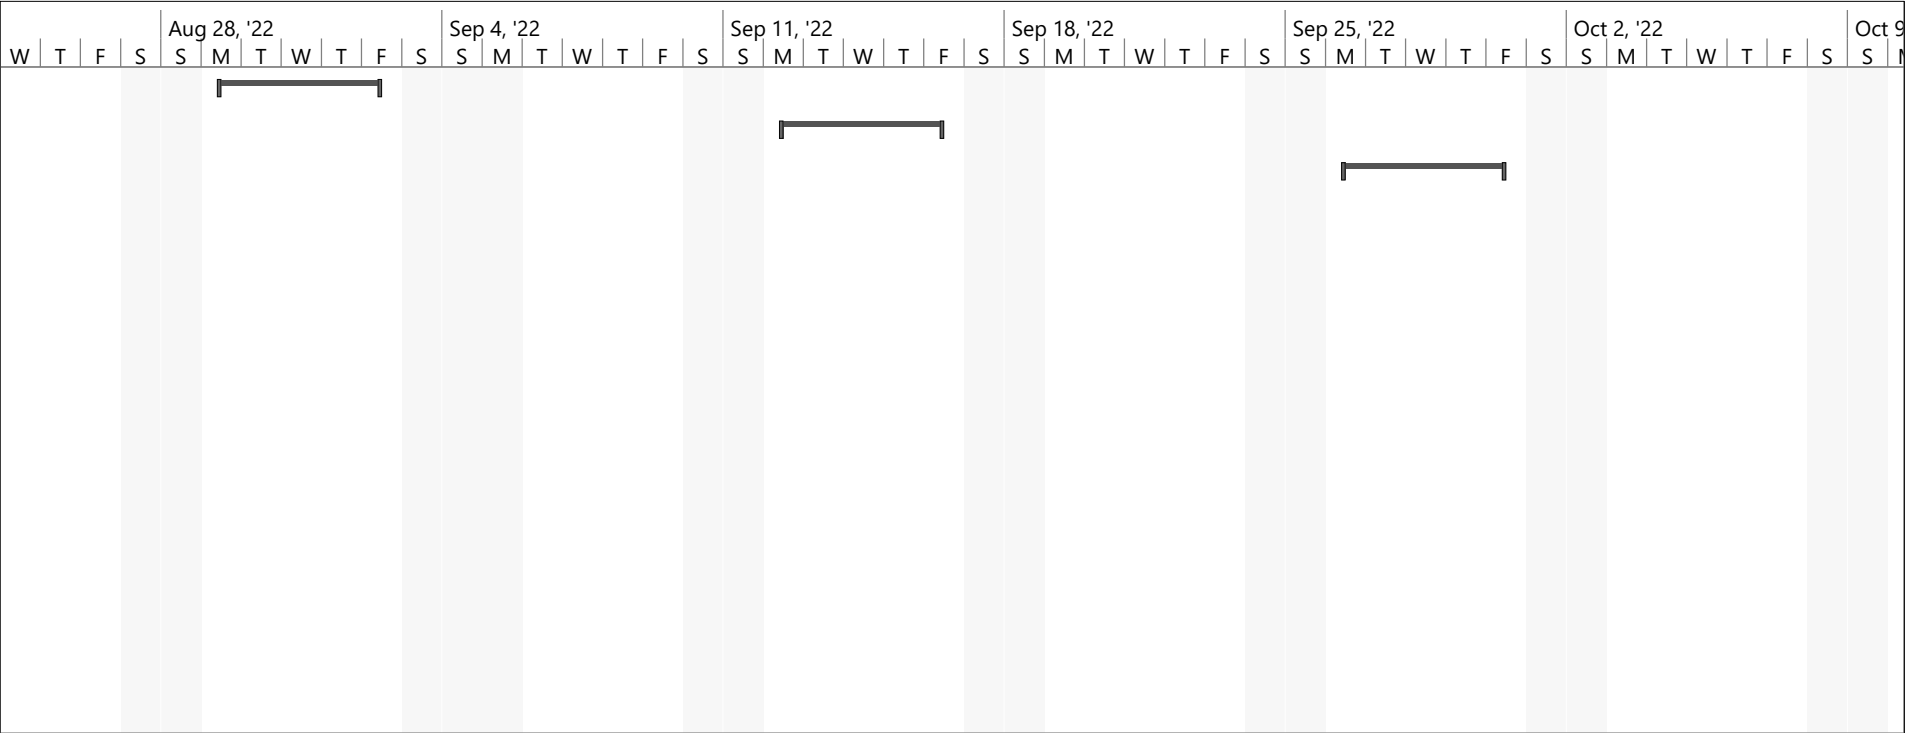












Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			







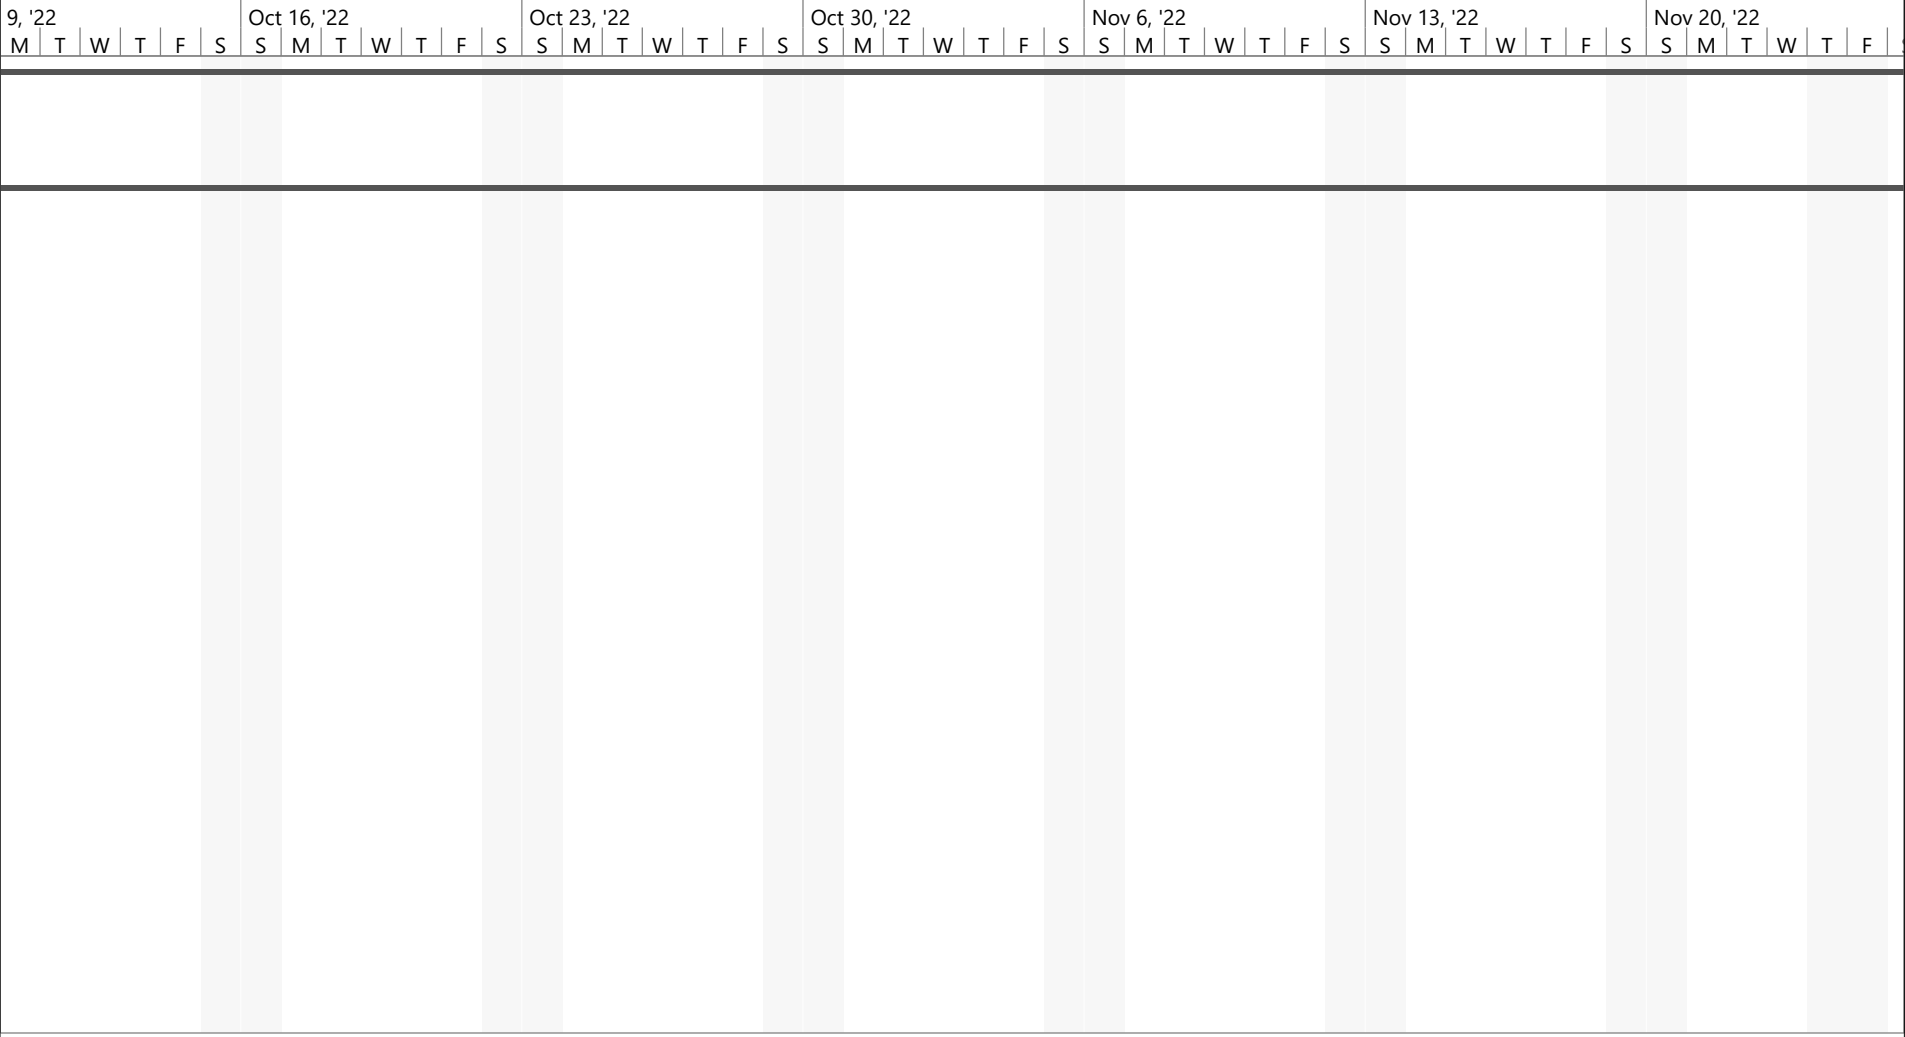














Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21








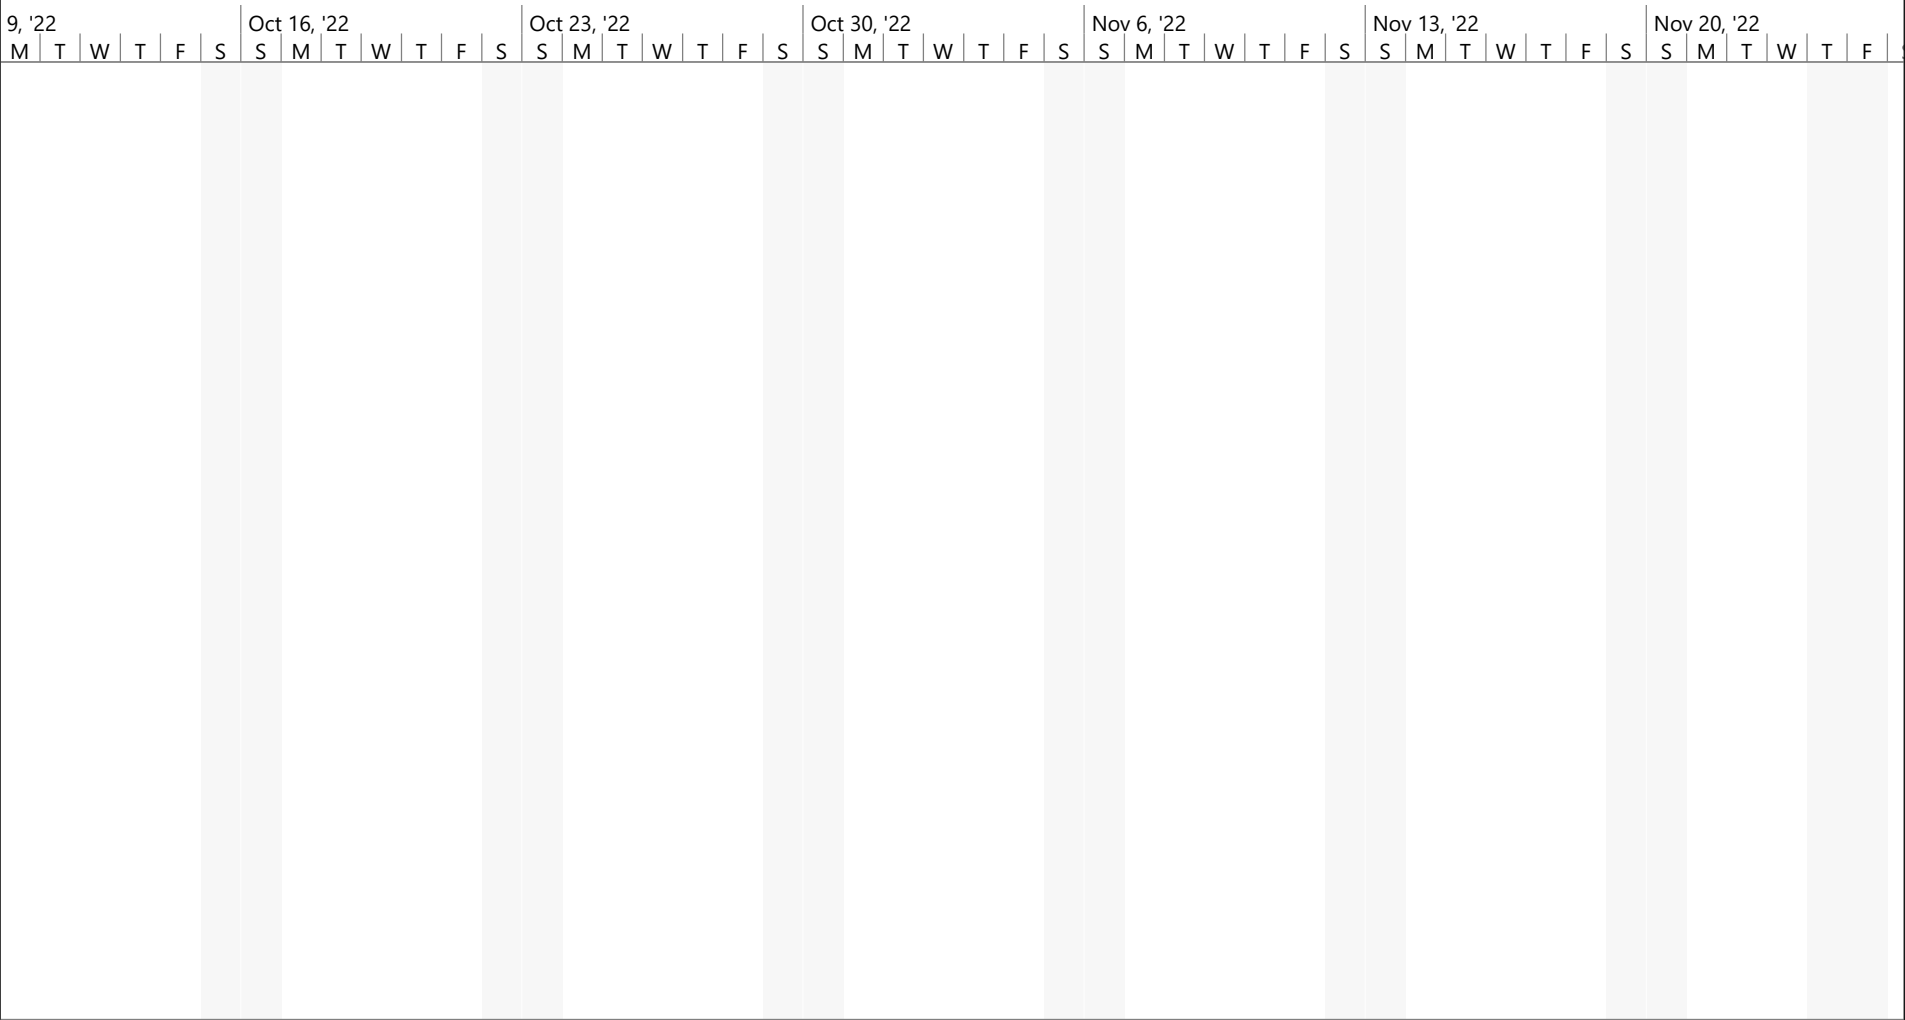











Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			







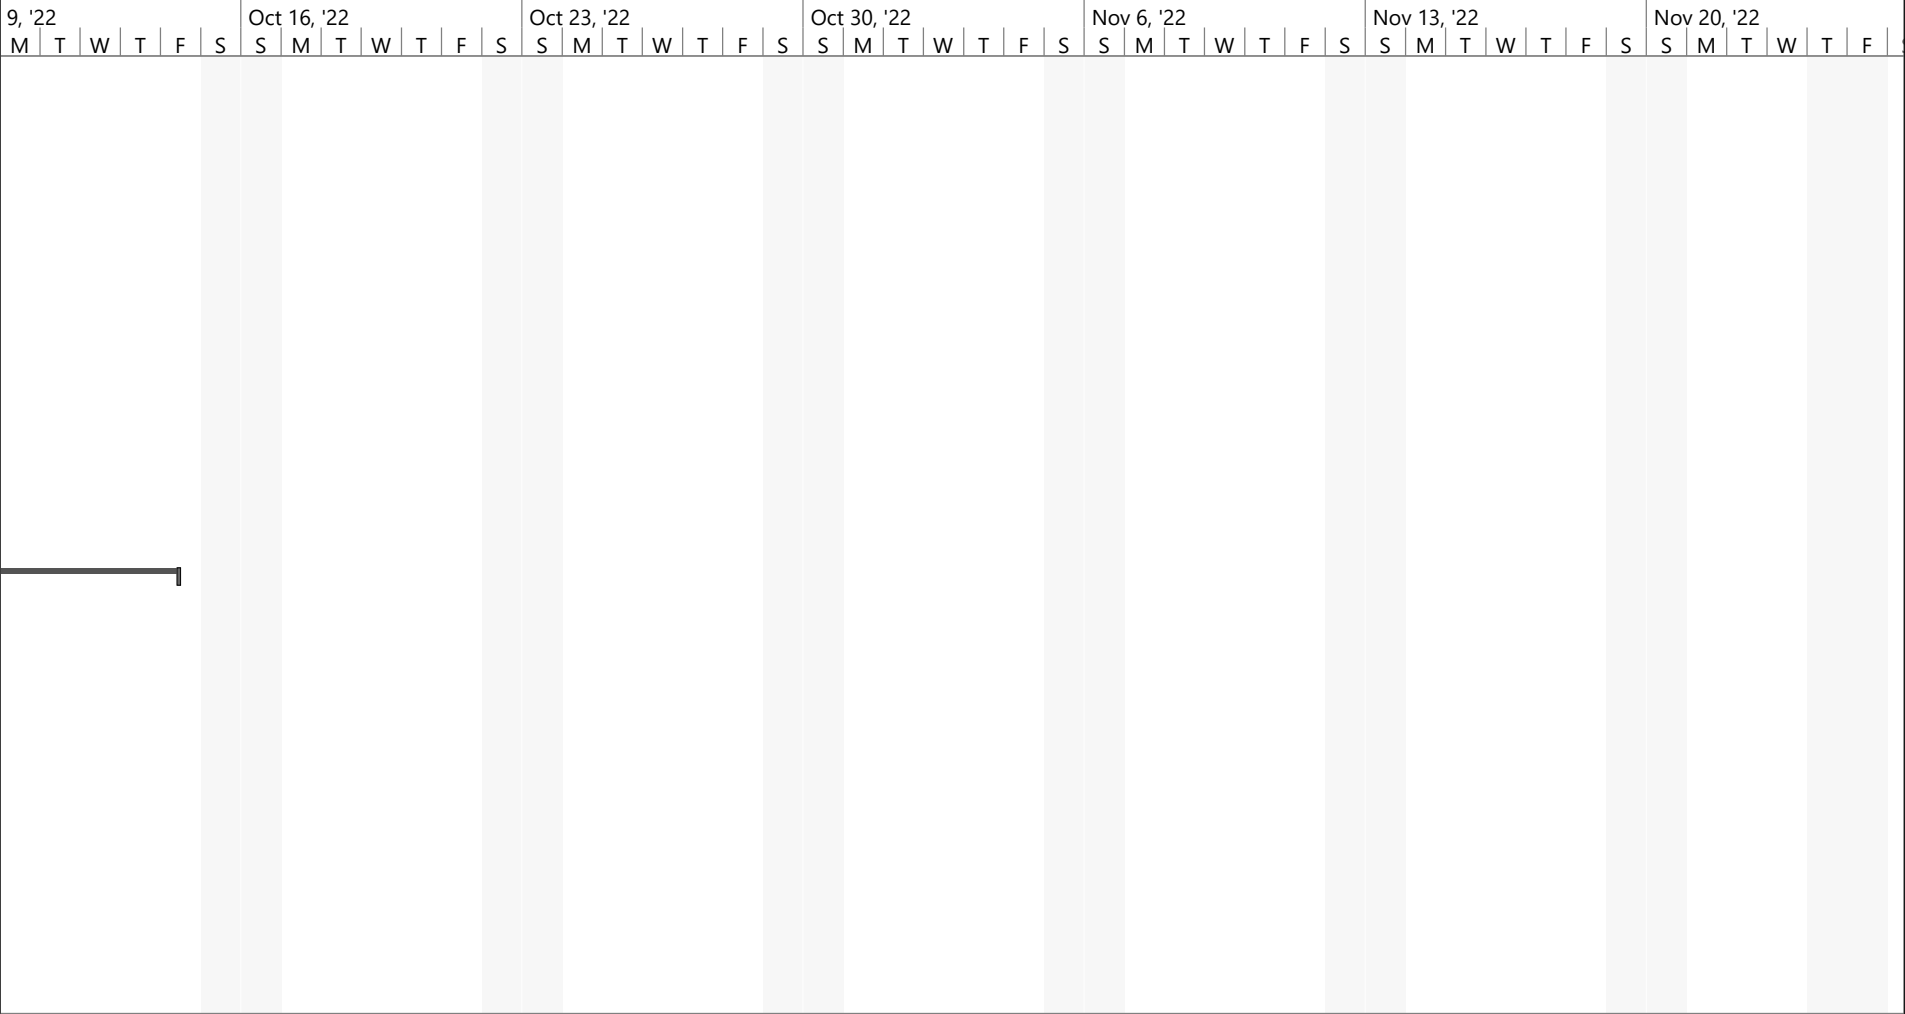














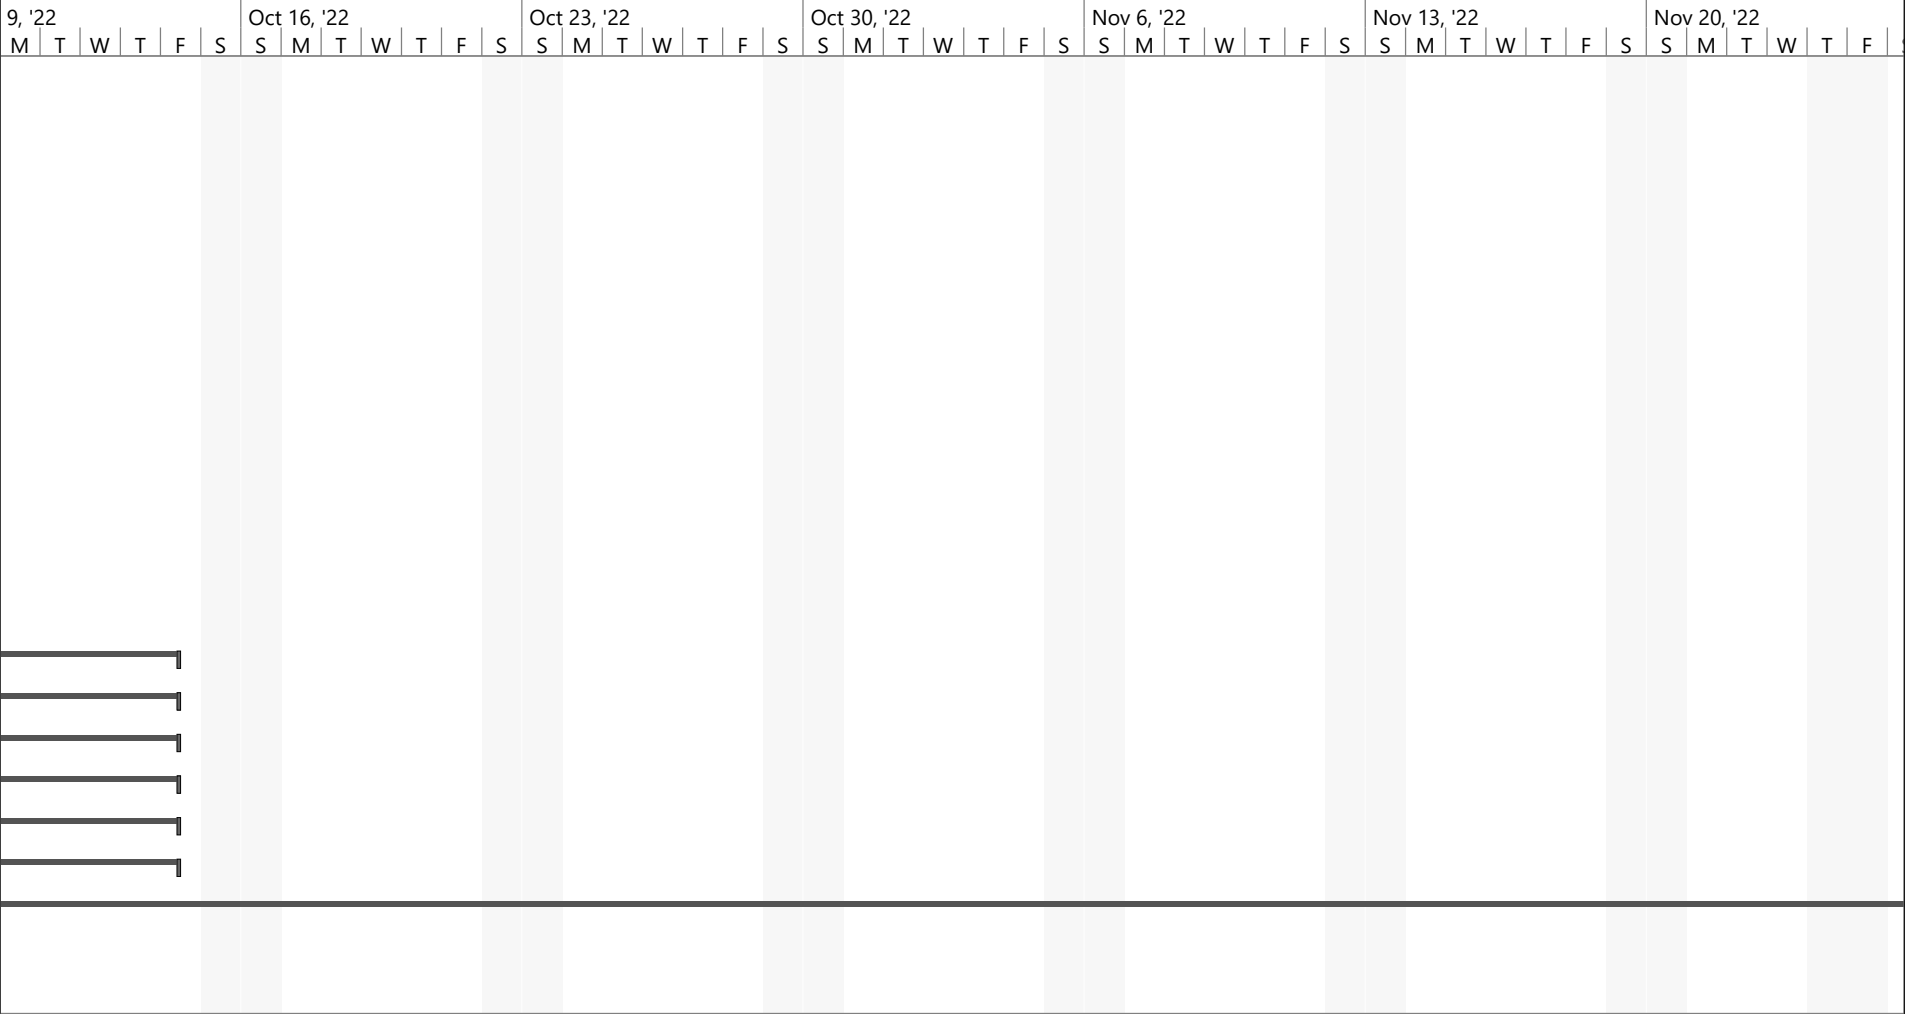
Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















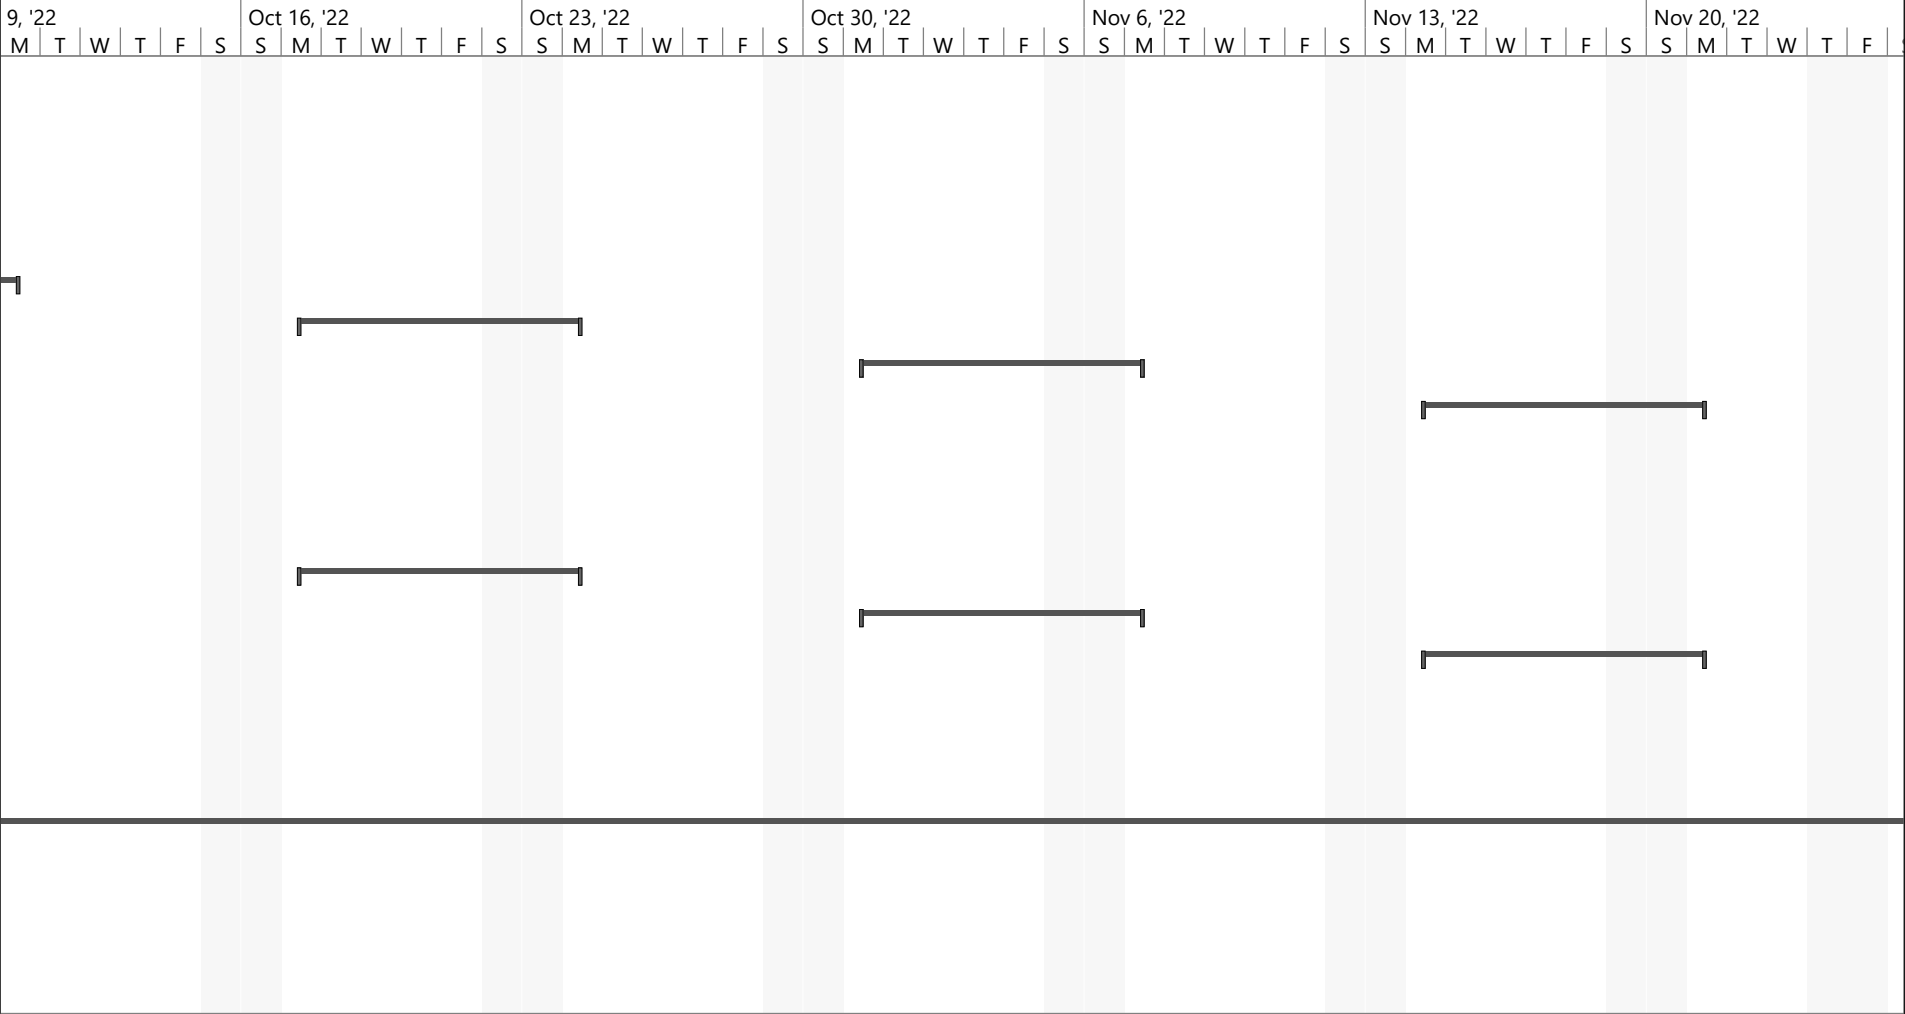
Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21








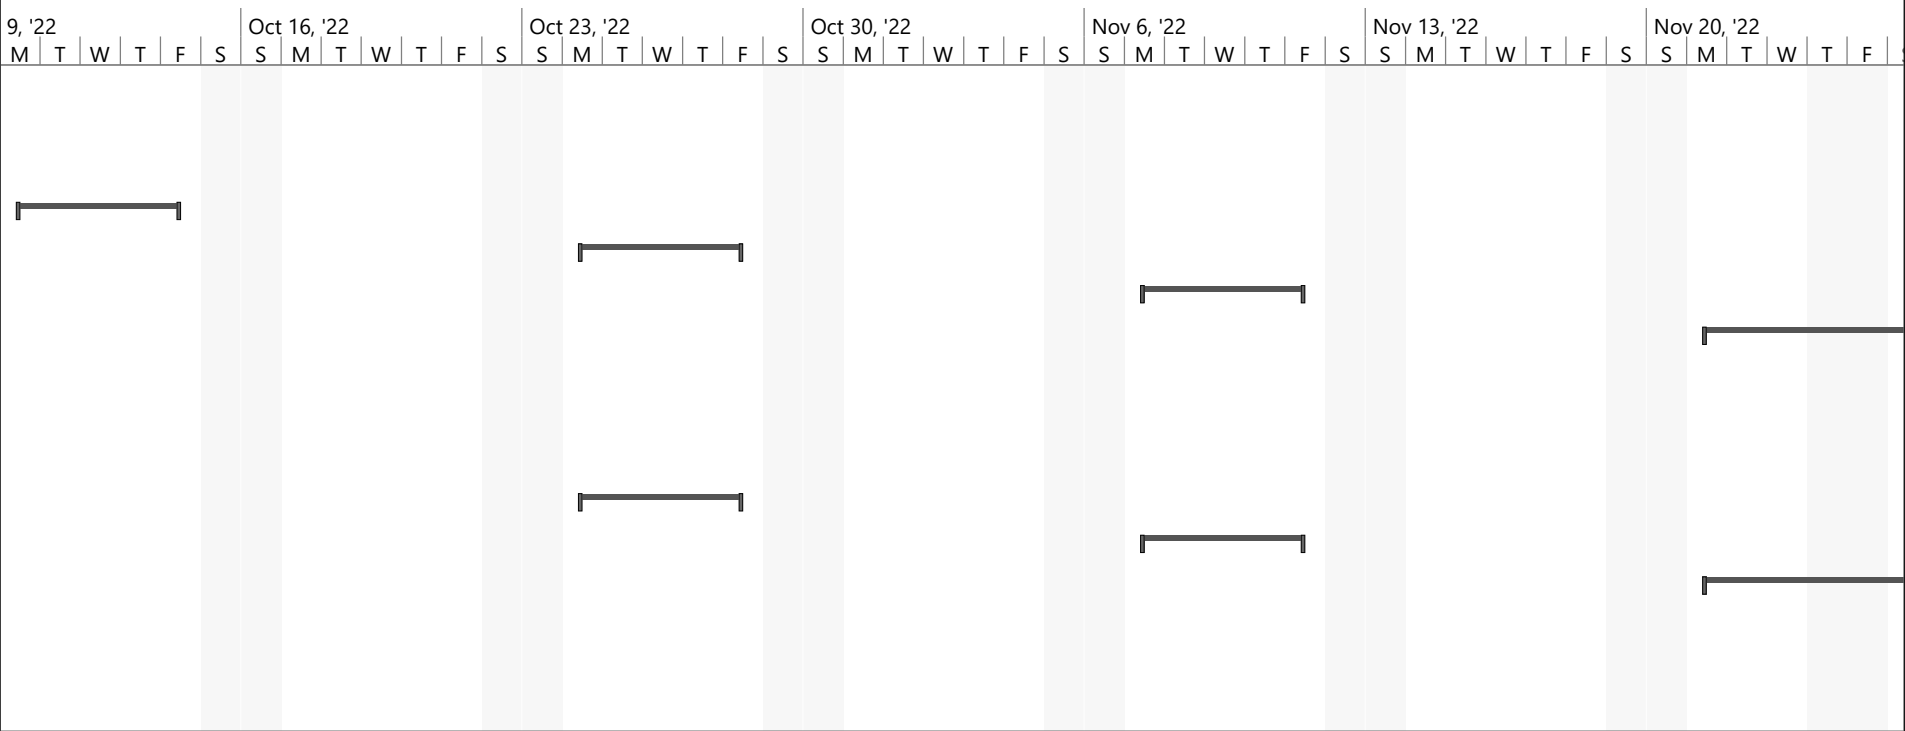











Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			















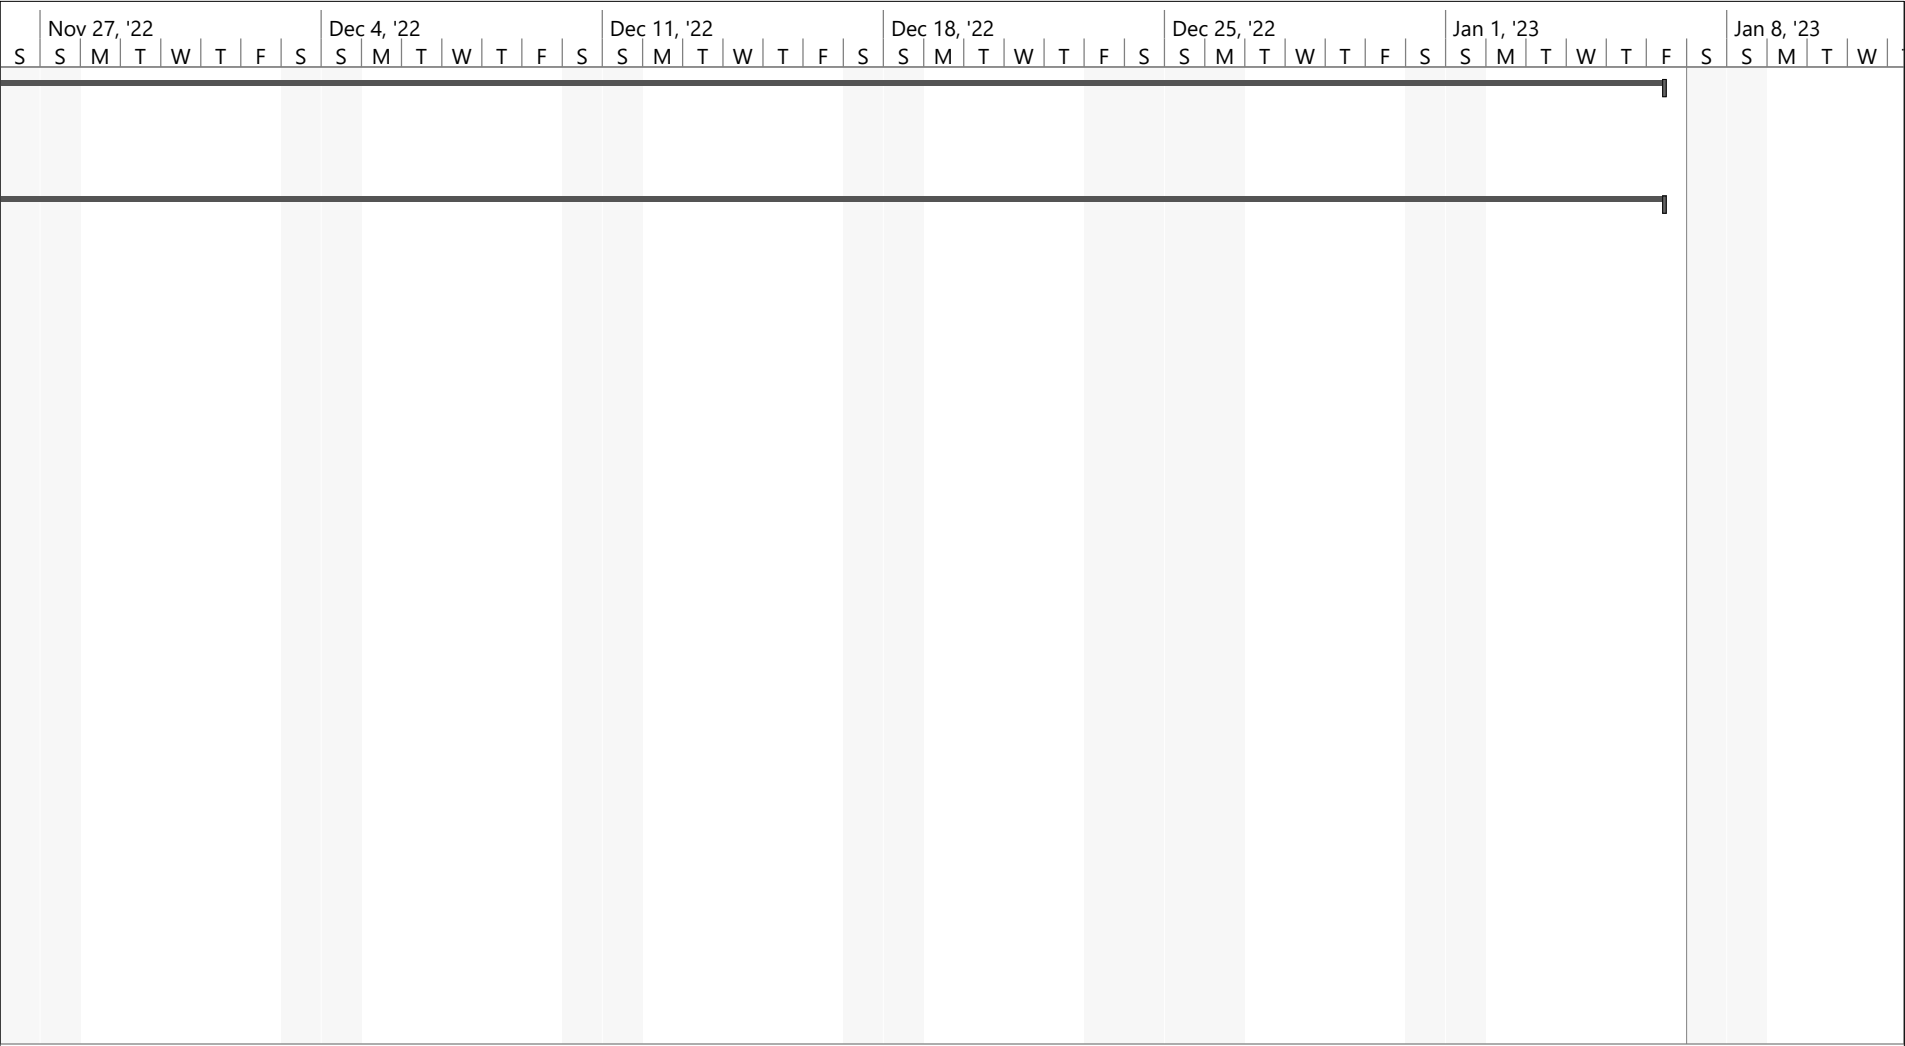







Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

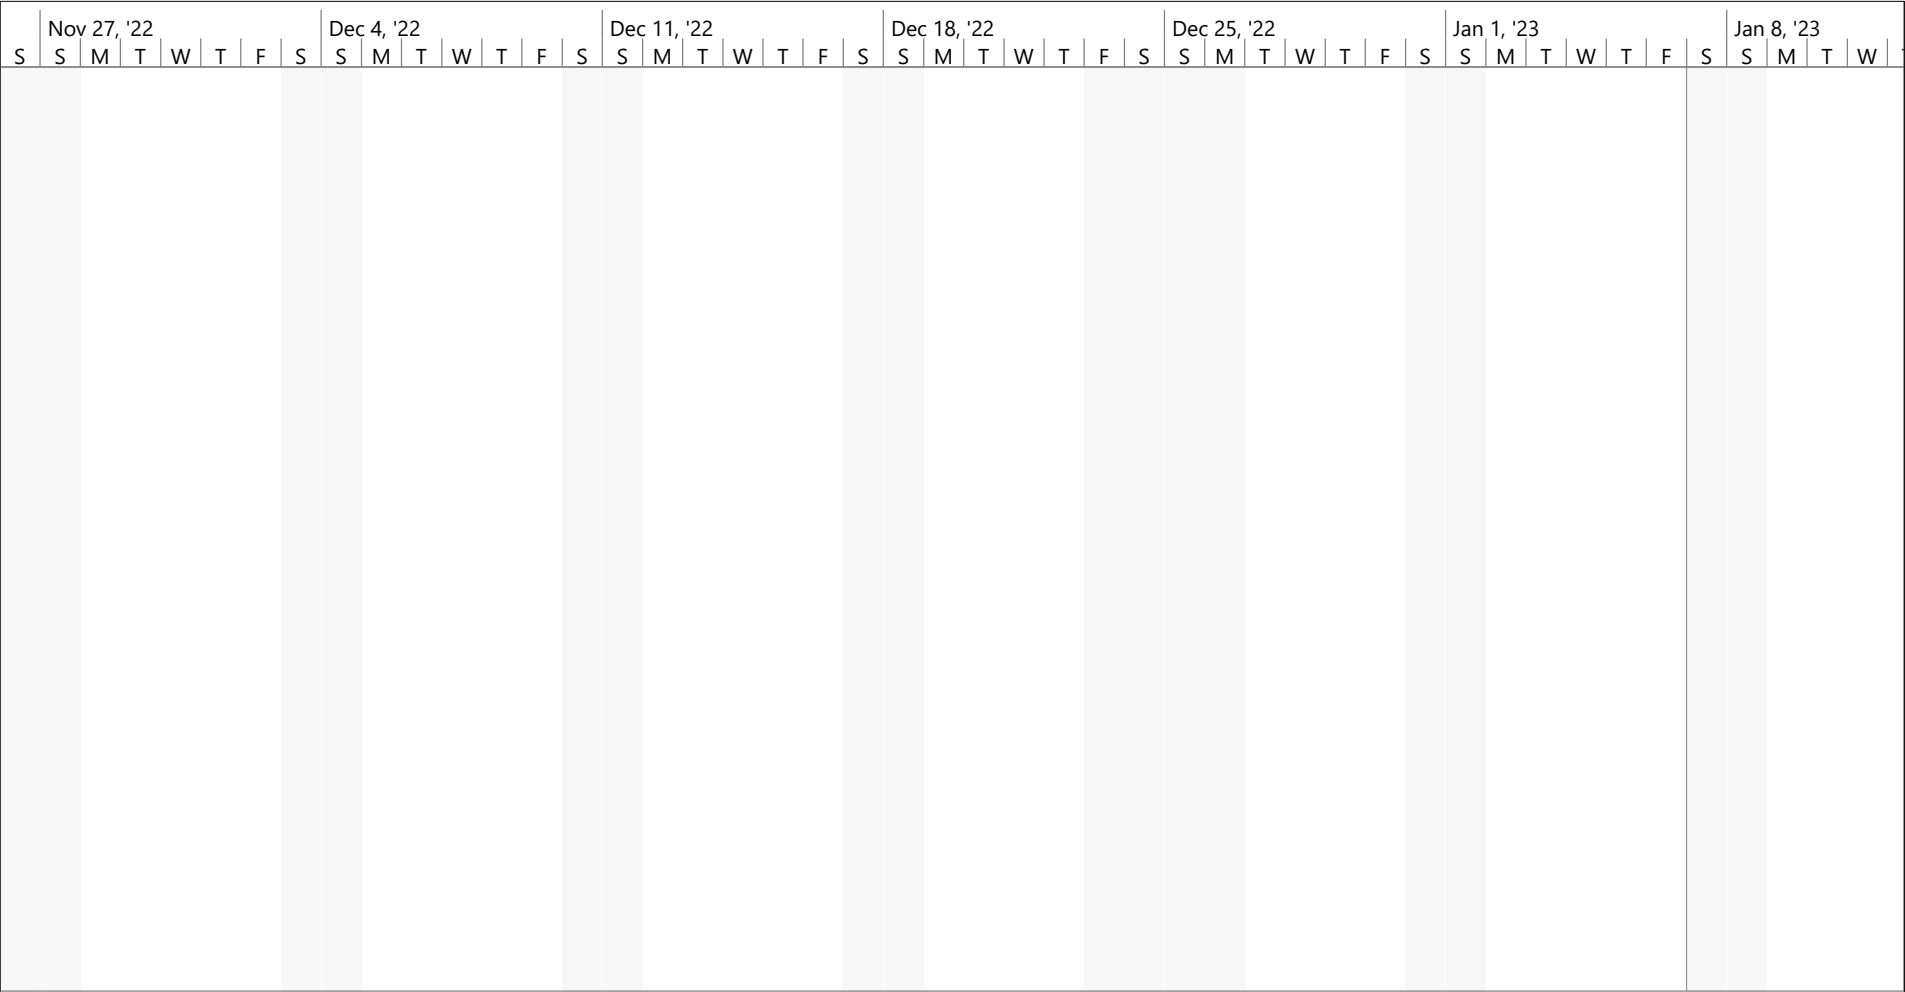


Project: Sample PureCloud Imp

Date: Fri 9/17/21




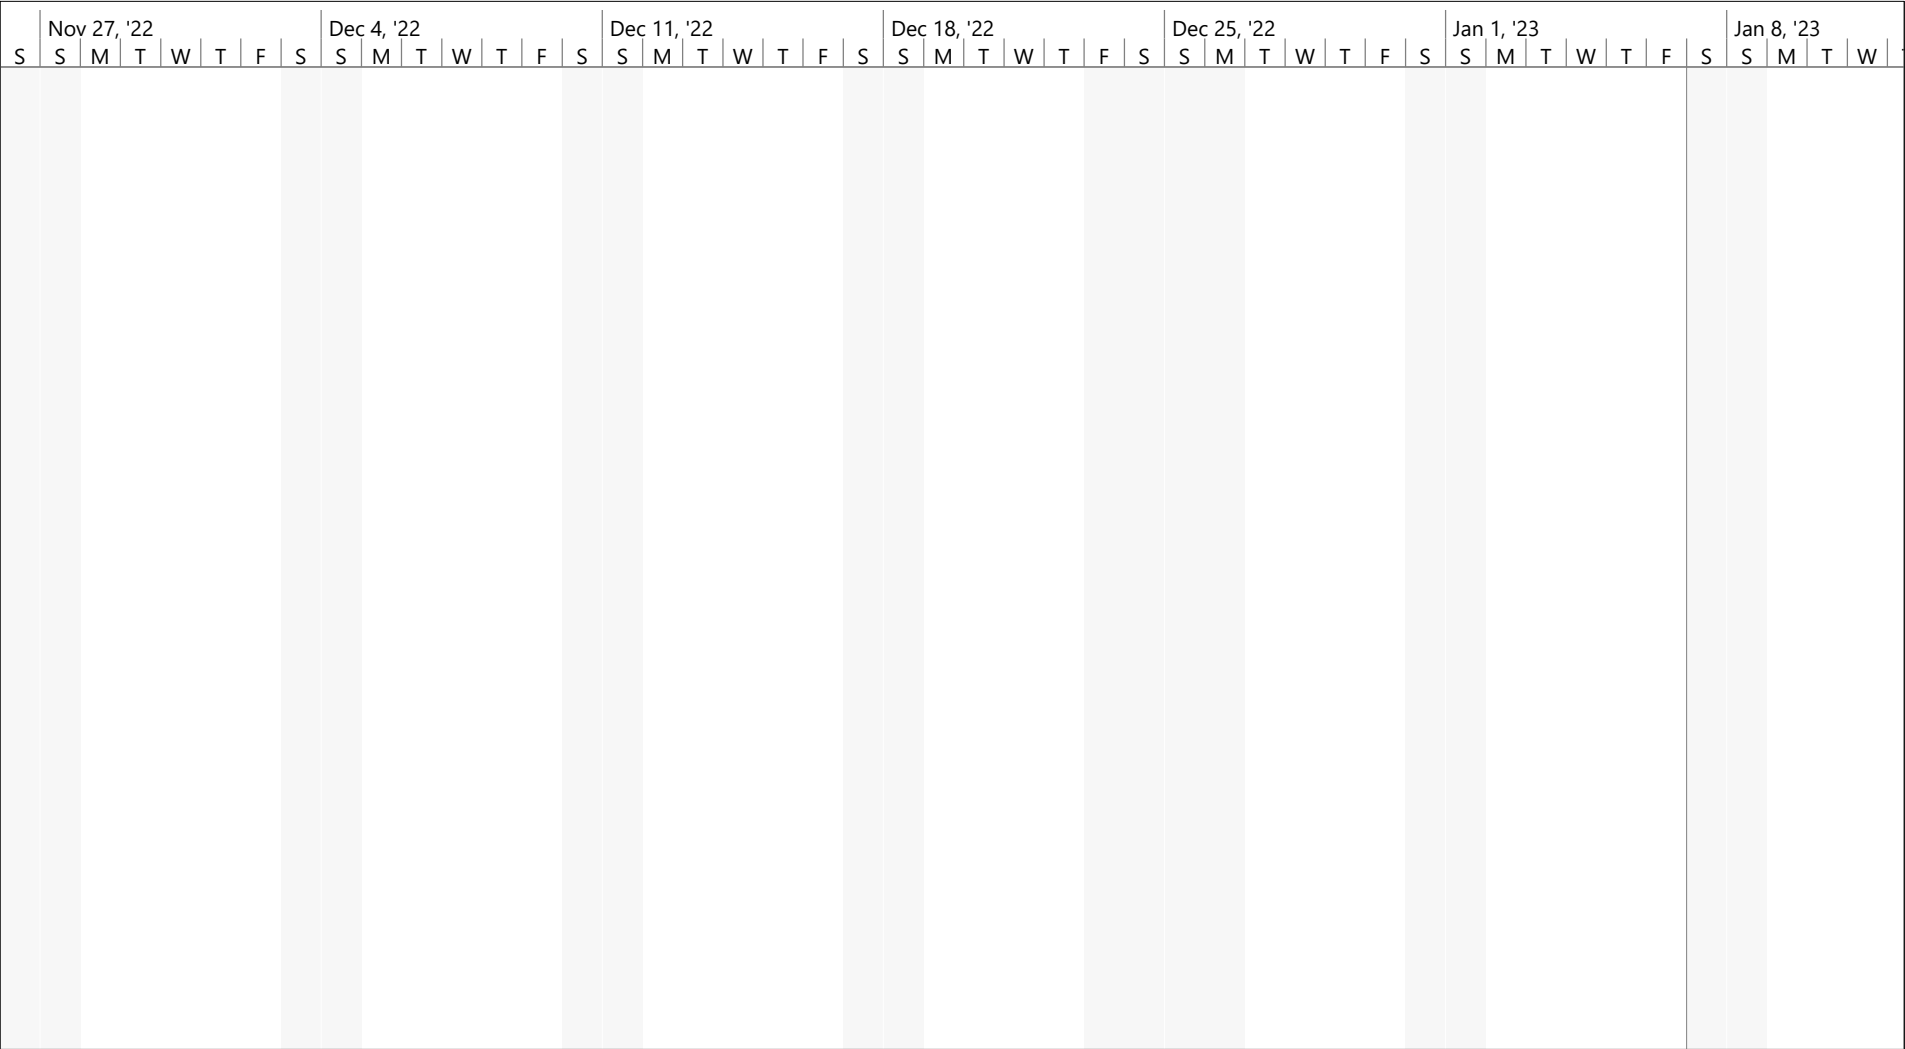



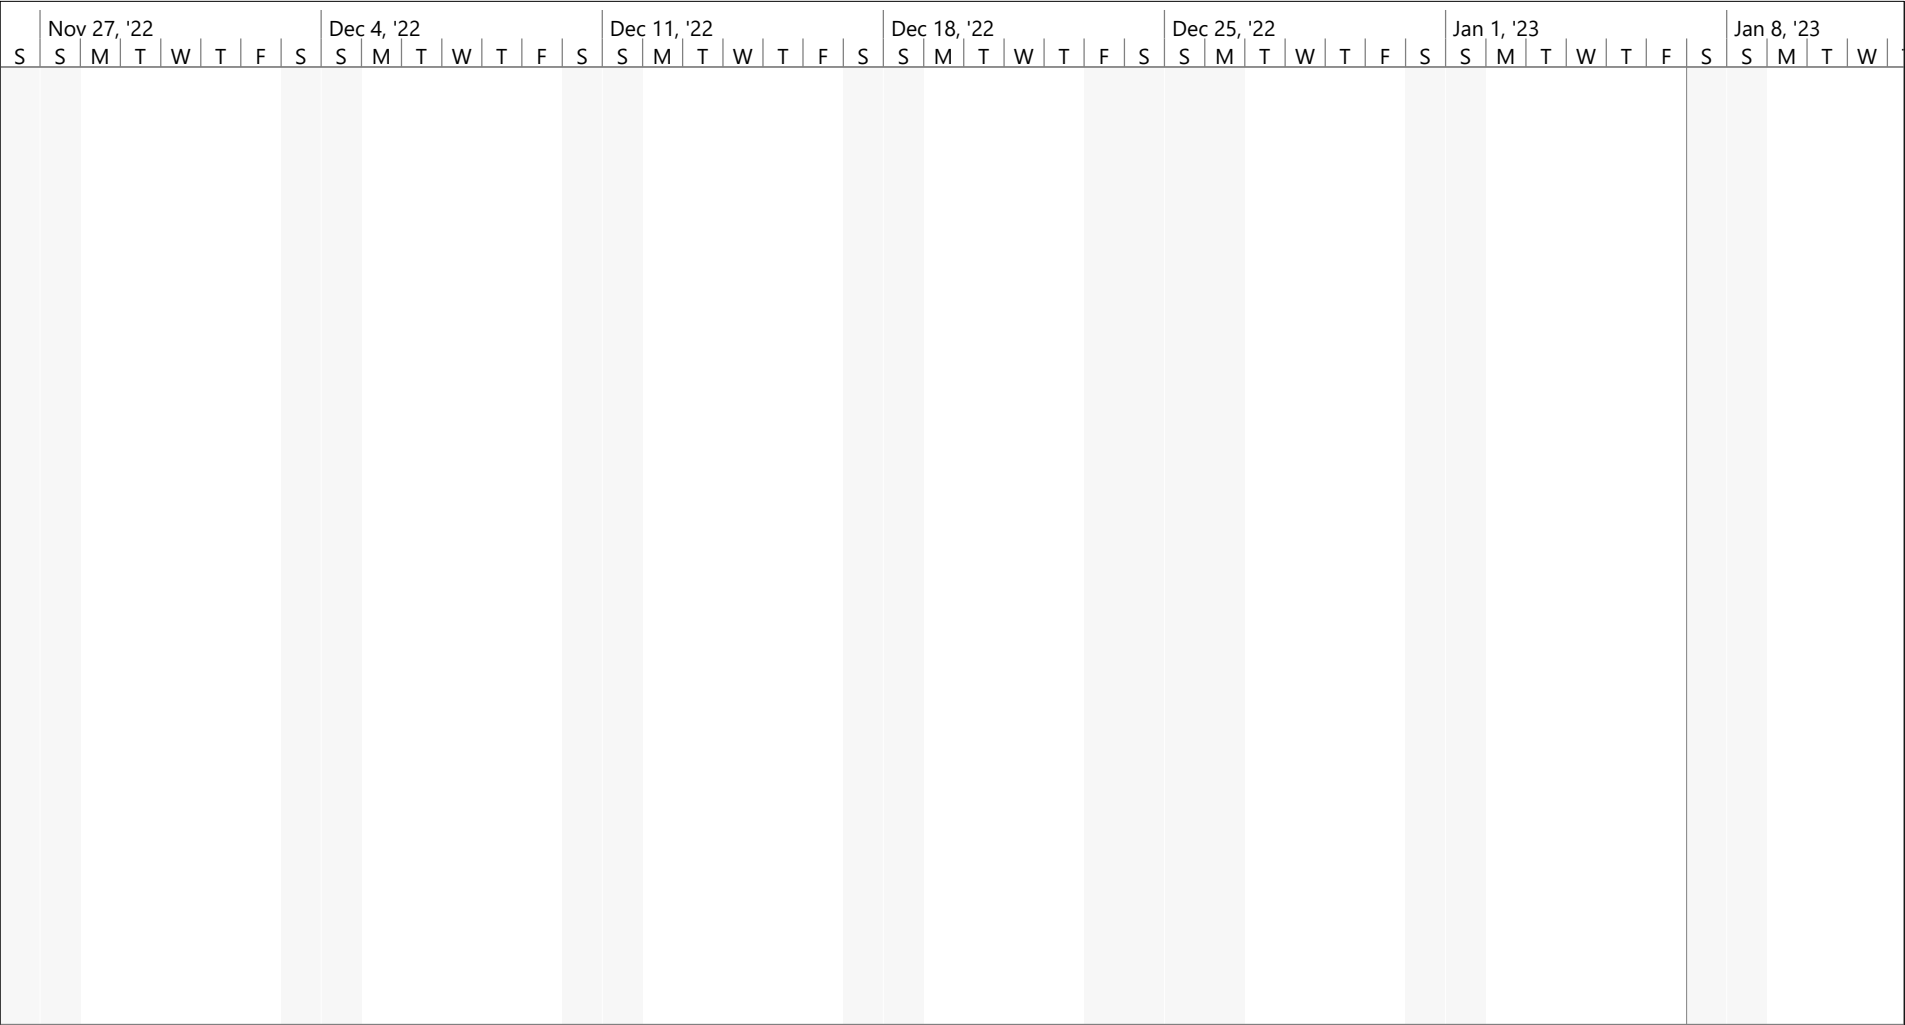











Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp Date: Fri 9/17/21	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			








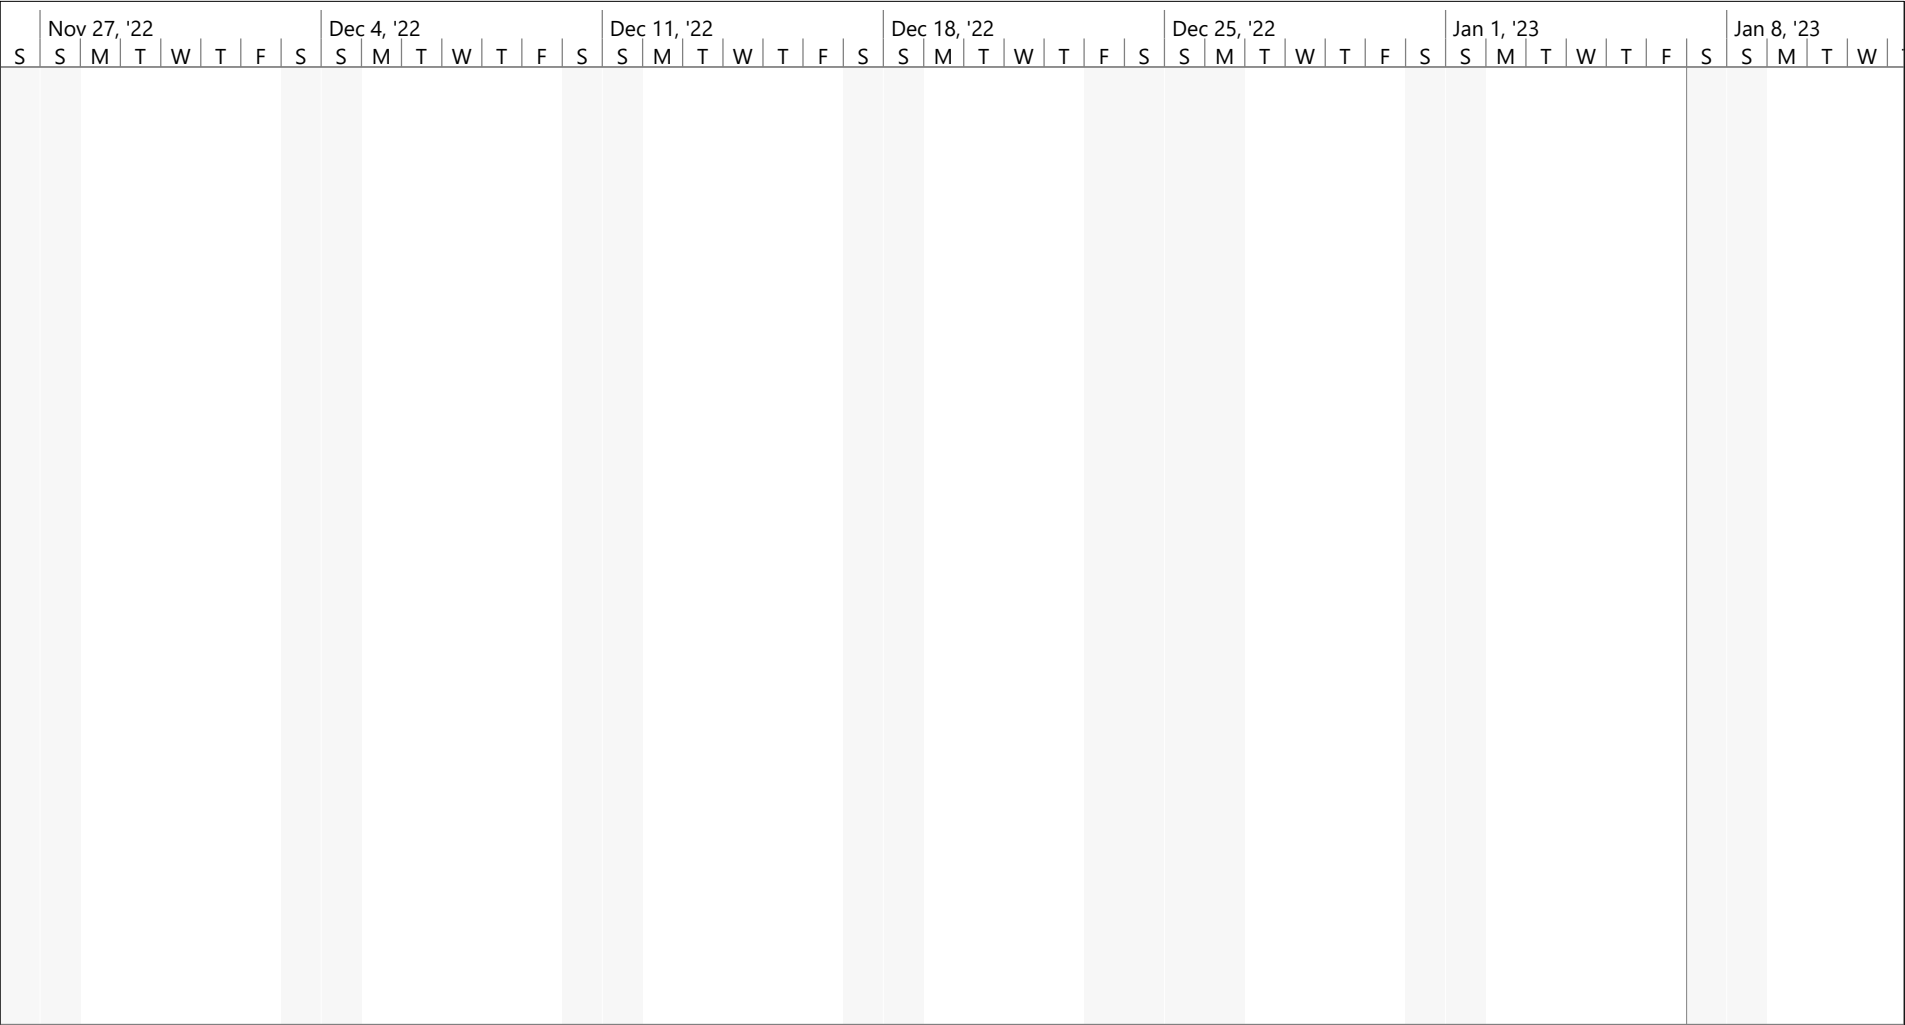














Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

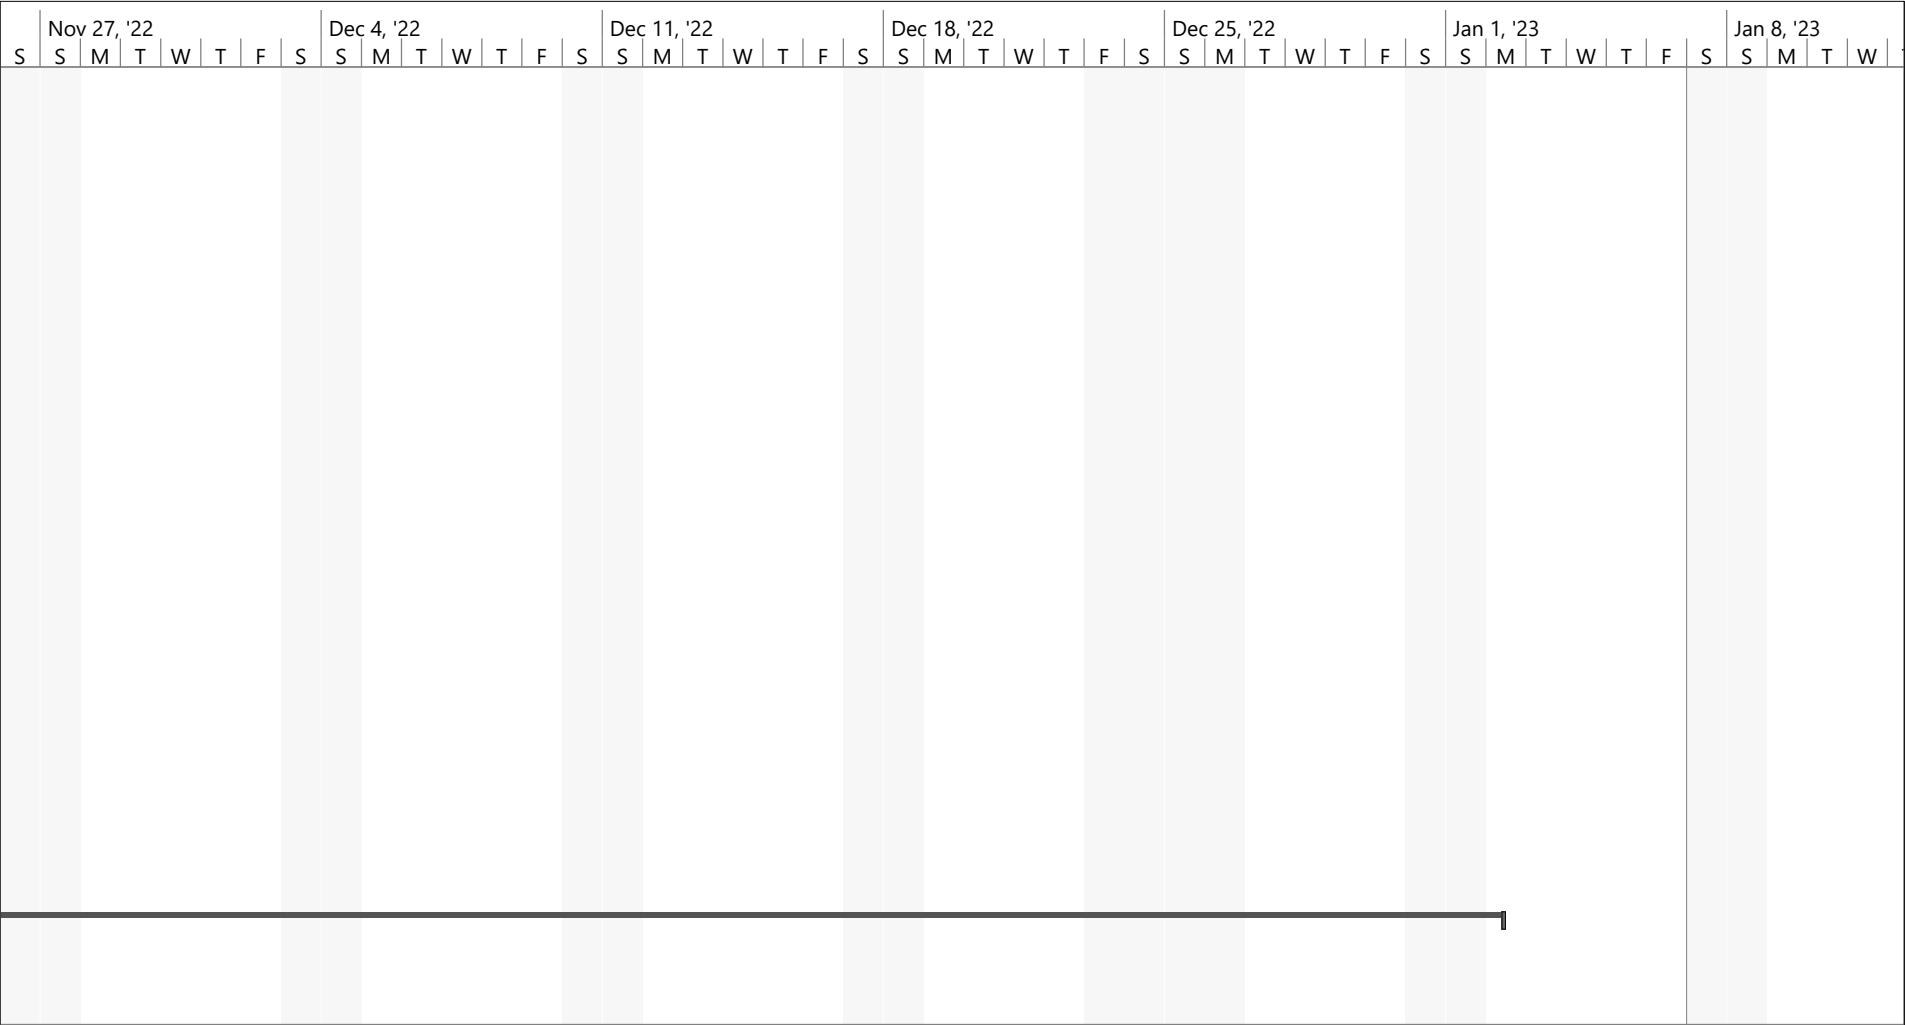








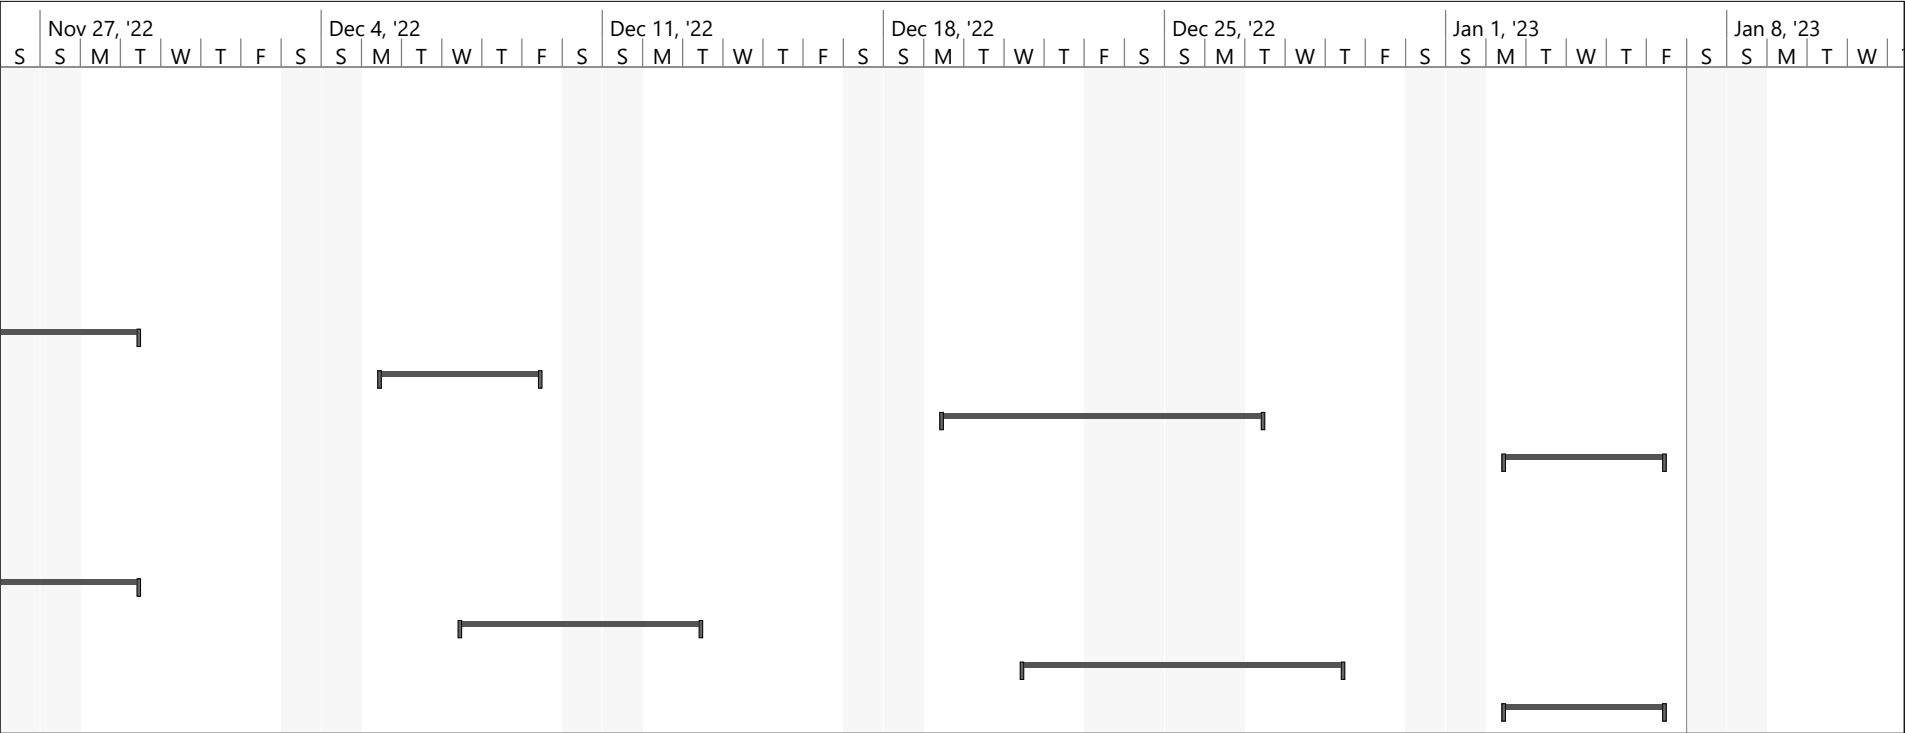










Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Sample PureCloud Imp
Date: Fri 9/17/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only	
