Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 22 – Project Area
- Paragraph 5.B(2) of Exhibit 22 – Project Locations
- Paragraph 5.B(3) of Exhibit 22 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 22 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 22 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 22 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 22 – Access to Service
- Paragraph 5.B(5)e of Exhibit 22 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 22 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 22 – Map of Project Area IBO-917

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-917

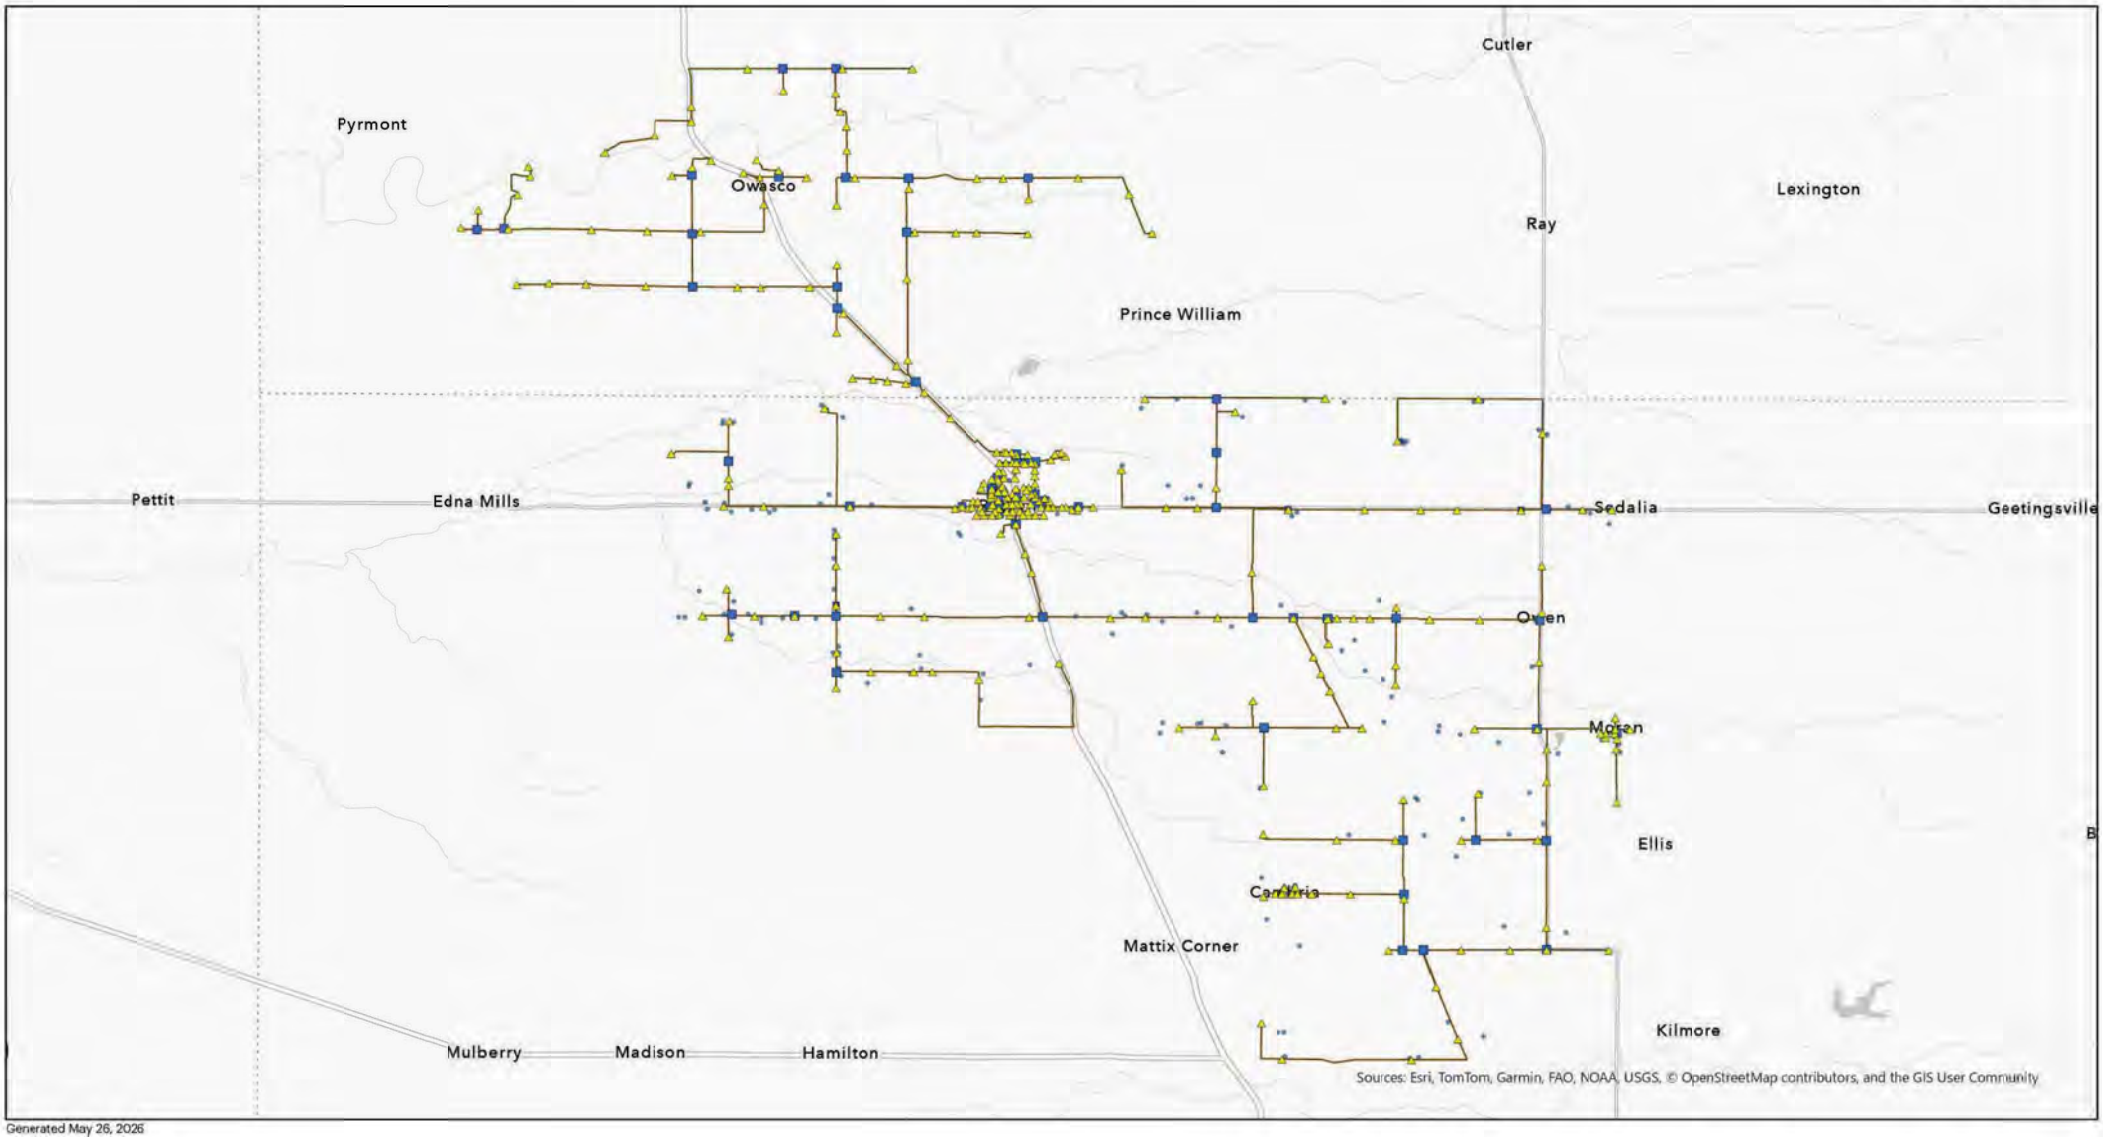

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 22 – List of Locations in Project Area IBO-917

Brightspeed IBO-917 Location List

138 locations

ID	Location ID	Is CAI	Technology	Upload	Download
1537318b5b3b23cbdb88a0aad4d743b5	1072151584	No	Fiber	2000	2000
5bceb2fe40a8bf0d021ce924301d4cb1	1072152155	No	Fiber	2000	2000
a9d02394349a3d5b45c8c899d203da7a	1072171315	No	Fiber	2000	2000
1fd46f60ba90488c7d4db376a3144359	1072174210	No	Fiber	2000	2000
134328739c4e82a0468cc615f502839f	1072151337	No	Fiber	2000	2000
e6350c76d6445270a309ebf53e264d4e	1072151361	No	Fiber	2000	2000
09726b8aba1a1463d4da0cf762712c97	1072152551	No	Fiber	2000	2000
ad452b7b723465a4e4683e94faead0a9	1072165634	No	Fiber	2000	2000
7dc613c6b0da332cd5c365e3234bfb94	1072151587	No	Fiber	2000	2000
ee81f6cb13f4a15c37fb0385df97bef3	1072151359	No	Fiber	2000	2000
9324eac83c13fc785f26c5b92592b485	1413403733	No	Fiber	2000	2000
b7df458931d5226fb5e2773aaf6f09bb	1072151582	No	Fiber	2000	2000
c0f316190bf04d0210dd26d863ec03cf	1072152135	No	Fiber	2000	2000
3a25b5ab5a96d1e5059cb311bf2f3fd5	1072169492	No	Fiber	2000	2000
9efa3ed3d24e72eb89bba92ac88837ee	1072152613	No	Fiber	2000	2000
53f8d6a10d08ff302ea8081b3a52c9d0	1072152616	No	Fiber	2000	2000
325aa84555edf53187e7823ca51e89ca	1413403814	No	Fiber	2000	2000
d270cb865c5b24f8ee5033ba66f0be1a	1072151873	No	Fiber	2000	2000
d3e1df5e36d036677ffa488a25f39894	1072151562	No	Fiber	2000	2000
5a7579ee5edd78c8ae240fd1a1e0e577	1072151585	No	Fiber	2000	2000
c603b9898582b0f47b4ac6511ab68586	1072151336	No	Fiber	2000	2000
8d6c9245c6202522de04bf4f74242915	1072151553	No	Fiber	2000	2000
1e7fca57d30d50ae742afae10f59566a	1072152623	No	Fiber	2000	2000
227b4fd5cca6838b25d61f70256c5e05	1072151591	No	Fiber	2000	2000
64b3c0613a36fcc443cdde04ba618ff0	1072151588	No	Fiber	2000	2000
83d815eeed9c1b29bb78bb585d05f084	1413403821	No	Fiber	2000	2000
640a595e7c96cd711166e9969d569524	1072151561	No	Fiber	2000	2000
848c3372286049658cd747e47e7f5f12	1072151568	No	Fiber	2000	2000
0a22eceae61f62eed2d7b9479cc8d4fb	1072171190	No	Fiber	2000	2000
8ed3ac50a25c470596a3661f839abf2b	1072171312	No	Fiber	2000	2000
97d96ec46fa1b97bb3479db737a2e61a	1072152704	No	Fiber	2000	2000
bd10c2319fb9653755f1e8478da09ba5	1072152291	No	Fiber	2000	2000
d2a64f59a5935508c9d5467bb4885c23	1072171537	No	Fiber	2000	2000
7f1515bc5556bad6f6f8e5accc5b09e7	1072151355	No	Fiber	2000	2000
1b9d6cdb1de198f1002f57357f5302a6	1072152706	No	Fiber	2000	2000
225a2bb46a71279900693ea51de109b8	1072151360	No	Fiber	2000	2000
358a286b65b0e7b86427682e8abe92d1	1072152423	No	Fiber	2000	2000
c53aa469c0f20286948be22b8c4b2d92	1072171545	No	Fiber	2000	2000
e456bb34c82334964479ddcaa040f183	1072152278	No	Fiber	2000	2000
0deeed8f71e965a76ca7c7c222f6aa50	1072152117	No	Fiber	2000	2000
d7841b654fdf3f83451ad4978d34532f	1072171320	No	Fiber	2000	2000
0fcf06270c8c124bb6886d5e0cdc0f9b	1072152549	No	Fiber	2000	2000
31158e2538d850142091d86f8fef720a	1413403815	No	Fiber	2000	2000
8a190ed51a99de224a4b590f3b956332	1072152612	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
6f0137be50bdc8048e3bc8e961a3f21d	1072151577	No	Fiber	2000	2000
fc0cd2a172cd37d0d5460dabf344055e	1072152422	No	Fiber	2000	2000
ab43f3474a958b6f2a9ee26854b81f0b	1413403707	No	Fiber	2000	2000
86d66168b8e5a0fb401879b214abeda7	1072152739	No	Fiber	2000	2000
3ac4b84caf556761249114fe0c25e9fe	1072151453	No	Fiber	2000	2000
be61b9ff972944ce2e35f356a781cc6f	1072152425	No	Fiber	2000	2000
d1223538af7d86c2c0a0c3cbdd746ab4	1072152271	No	Fiber	2000	2000
41046724b2e4a174496a56ca3c525b8f	1072152546	No	Fiber	2000	2000
38f40c9378604f27a3cf28fda497112e	1072171304	No	Fiber	2000	2000
2e0165fc40432883ec67afe76eb036b7	1072152132	No	Fiber	2000	2000
a9ca7c3d3a9c2cf1c8112da9a184ac56	1072152149	No	Fiber	2000	2000
c1465615d6fe15f7481203de7513de61	1072171406	No	Fiber	2000	2000
c7211dd4c3ff1109c67d8e26458d52ca	1072151341	No	Fiber	2000	2000
614dc057a8a54dc3e55d1a1935753ff3	1072152606	No	Fiber	2000	2000
be4a305e2ae9220db0d9449db0807ac1	1072152151	No	Fiber	2000	2000
c4150984e57489c935527728b3607ae4	1072153117	No	Fiber	2000	2000
e11746fc15c0a8c6904f73a383396259	1072152153	No	Fiber	2000	2000
dba8e4d6adedc5c6370355eef15b0a73	1072158085	No	Fiber	2000	2000
ec164d00c36678ebd483722a5c4ca3bb	1072151861	No	Fiber	2000	2000
f45cd3dee71abf5b7f3a036e616a41a3	1072171309	No	Fiber	2000	2000
d9c81676c6ec001c68ea6cf7c69ad8ae	1072168368	No	Fiber	2000	2000
d01b6a25c0d660e6b1382d7ae88d0b23	1072173791	No	Fiber	2000	2000
fd71d039ec230cb30df9b433a11cb2e7	1072171215	No	Fiber	2000	2000
c9b25d0573e474816474e7e1804ad723	1072152421	No	Fiber	2000	2000
61521b2a0896cb882ff81ee8658695f5	1072158086	No	Fiber	2000	2000
65b6c8097d708129811009329564bf06	1072152424	No	Fiber	2000	2000
439d0318dff880df2dce26834875f407	1072152286	No	Fiber	2000	2000
d06d537c1094019b34c45b2902dc4ec6	1072152718	No	Fiber	2000	2000
8cf271fb82f2dd2d38966ceb419e792f	1072165534	No	Fiber	2000	2000
dd7a7076a710e5400f12d8a2f32d1489	1072151569	No	Fiber	2000	2000
e7ef7d96776736303879c4c140de4966	1072151335	No	Fiber	2000	2000
35d6aecbdcdd797bdcbca767820e5055	1072171214	No	Fiber	2000	2000
eb1929de1fbeb943921603fdf922ffd4	1072152618	No	Fiber	2000	2000
3bb16ac689f8d09df4b3c5761732f5b8	1072171187	No	Fiber	2000	2000
59768f479e585110ba9a1473be01ea1e	1072158083	No	Fiber	2000	2000
62a1ec615f10e3e37e8c58b5a221952d	1072151346	No	Fiber	2000	2000
e7228805dbfa93a71380b28243ed52da	1072166691	No	Fiber	2000	2000
1ff938a3688a698a166f5bc8623a4fc4	1072152629	No	Fiber	2000	2000
ac2eb2a0fb6a04badaeee4a8fa192f1e	1072169490	No	Fiber	2000	2000
efed1b01dbdf939ac781cba8b1b936ff	1072151578	No	Fiber	2000	2000
52c96d43e1dcf69ca801b50865a9e722	1072152129	No	Fiber	2000	2000
e56d4882c27540322d1f695c091b8614	1072151354	No	Fiber	2000	2000
cfb53ae4c9de1514ed70e270309c5eaa	1072152443	No	Fiber	2000	2000
76b50e429d96ef490539eb947192ea29	1072152633	No	Fiber	2000	2000
8aaf445418d537684fbd9d94861a10b3	1072152734	No	Fiber	2000	2000
6fc9ed533e28b1dc072f3c6c8230bb19	1072151580	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
e2249eb99c5ea59813da9df5ab8ca817	1072171541	No	Fiber	2000	2000
9fa586f9b79dfebfa0fd67125158806e	1413403817	No	Fiber	2000	2000
249961a47c702f6e89bcf54f12d23cbb	1072160084	No	Fiber	2000	2000
c87b856fa9db93c71e9dd67b4dd500dd	1072151563	No	Fiber	2000	2000
2bd6cf5eb0651a04939d93840a0c5eb3	1072152621	No	Fiber	2000	2000
dc6c707d8ad671530a48e72b9e2145ca	1072172160	No	Fiber	2000	2000
897cfe6574e106e6c658ac832761f8d6	1072152146	No	Fiber	2000	2000
565e885b324851ffe61ea6804ee24b92	1072169131	No	Fiber	2000	2000
99226634982643f22057a972d2ed6f6f	1072165550	No	Fiber	2000	2000
3fa67b26ecaaa5c10a98250b2c655b03	1072151567	No	Fiber	2000	2000
73c5762da42faa87f75f21a5b14c76e8	1072171216	No	Fiber	2000	2000
74f11e8002e69f8aac708e3f16103c3b	1072152148	No	Fiber	2000	2000
7d9163bd72764d8a6bbf718984448e66	1072168883	No	Fiber	2000	2000
64643d5ff13488b1e5771e4b1ad9bc0f	1072151745	No	Fiber	2000	2000
6f6208f6e3421438c9cb005843373b4a	1072151583	No	Fiber	2000	2000
95c4aba922bb7b7b4e7b8678c567dec5	1072151551	No	Fiber	2000	2000
d71b8862a0559197150f9dad77d2c638	1072152624	No	Fiber	2000	2000
248bbdb2e1524ec04342959000bf84d2	1072152163	No	Fiber	2000	2000
3d8bcb5cc0bc4dbfdf8873a47393729a	1072151545	No	Fiber	2000	2000
f88bf1a086e5af71d24e62d7c9c7eb93	1072152731	No	Fiber	2000	2000
48ac757d055dbb4cc7c7de38d8bf32b4	1072171361	No	Fiber	2000	2000
f051db755c58f6c66ad539052acc7a11	1072160033	No	Fiber	2000	2000
aac13015bed04fe550f630f7b0bb80af	1072152611	No	Fiber	2000	2000
0a61d98414a4e4ae263ce5e165a415ba	1072171218	No	Fiber	2000	2000
04387a1e0589a3de18c6a481969184ff	1413403816	No	Fiber	2000	2000
633815dec299fa5e84095703973115ac	1072171310	No	Fiber	2000	2000
cf41dda194c5c8dc17d035270b8c91d3	1072168901	No	Fiber	2000	2000
4dea2f47354d336324ad8cf80270b0b6	1072160083	No	Fiber	2000	2000
ab20ded6d5ba4ef5c53a3f03f1d8d297	1072165513	No	Fiber	2000	2000
6a7e6cbd77b0b8c36422b71c160d69f7	1072165633	No	Fiber	2000	2000
272bc961387f3654b7d8051babf63036	1072166695	No	Fiber	2000	2000
3ba2150250d3504b072a19e1b7c9e9a3	1072152632	No	Fiber	2000	2000
17a18a82e3b56b3f36d161e47d1a3990	1072152607	No	Fiber	2000	2000
24d3d589c07c1958fa987f5b8662571a	1072152282	No	Fiber	2000	2000
50b7b6deb36e2100cd4428ad856be1df	1072152713	No	Fiber	2000	2000
637af27a224239443ff3db2f084964a3	1072151559	No	Fiber	2000	2000
26ac4a897bb1f3aacf2c1910c64e9c4e	1072166689	No	Fiber	2000	2000
7d669df523c70565df1e14042ea8caa0	1072152274	No	Fiber	2000	2000
7c30fec3735f8aac8a91eeb4fe297e7e	1072151576	No	Fiber	2000	2000
90ccaf0114bd609a35f9e3b429977288	1072151571	No	Fiber	2000	2000
e73f0a19df1a8a2388f08f21f75d6c56	1072152626	No	Fiber	2000	2000
53d0becc791155397e341bcb8bdd4b69	1072171219	No	Fiber	2000	2000
71b9712eeba77bb7c9607d9ee55f263e	1072169491	No	Fiber	2000	2000
b19b8ceb5076ad8a0b19efd77e6dfdf9	1072152279	No	Fiber	2000	2000
3a32f5e4f3b55f5078e54365bd19bca5	1072152119	No	Fiber	2000	2000
0ef90be0f307152a3e7bfafaf2896e72	1072169489	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
925f9e619539d15cfd16fead2232fb41	1413403734	No	Fiber	2000	2000
ac497a4c80e8e008b07f08bc755706e8	1072152159	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 22 – Budget for Project Area IBO-917

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$4,500.00	$0.00	$4,500.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$585.00	$0.00	$585.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$34,596.00	$0.00	$34,596.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$10,260.00	$0.00	$10,260.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$1,876.00	$0.00	$1,876.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$90,432.00	$0.00	$90,432.00
Permitting Costs	Permitting Costs	Professional Services	$9,483.00	$0.00	$9,483.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$11,195.00	$0.00	$11,195.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$10,003.00	$0.00	$10,003.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$39,420.00	$0.00	$39,420.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$11,681.00	$0.00	$11,681.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$42,624.00	$0.00	$42,624.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$897.00	$0.00	$897.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$526.00	$0.00	$526.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$1,188.00	$0.00	$1,188.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$4,240.00	$0.00	$4,240.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$1,641.00	$0.00	$1,641.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$2,250.00	$0.00	$2,250.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$132.00	$0.00	$132.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$1,069.00	$0.00	$1,069.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 22 – Disbursement Schedule for Project Area IBO-917

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 22 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-917

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 22 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 23 –Subaward Conditions and Statement of Work for Project Area IBO-851

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 23 - Specific Award Conditions for Project Area IBO-851.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$205,987.00]
Total Project Cost = (subaward funds + match)	$205,987.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-851 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 23**. The Project Area is depicted in the map in **Appendix A of this Exhibit 23**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 23**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $205,987.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $205,987.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 23** in the area depicted in **Appendix A of this Exhibit 23**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 23**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 23 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 23;
- Appendix A to this Exhibit 23 – Map of Project Area IBO-851;
- Appendix C to this Exhibit 23 – Budget for Project Area IBO-851;
- Appendix E to this Exhibit 23 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-851;
- Appendix F to this Exhibit 23 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 23 – Project Area
- Paragraph 5.B(2) of Exhibit 23 – Project Locations
- Paragraph 5.B(3) of Exhibit 23 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 23 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 23 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 23 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 23 – Access to Service
- Paragraph 5.B(5)e of Exhibit 23 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 23 – Wholesale Rate

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 23 – Map of Project Area IBO-851

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C


brightspeed

IBO-851

addr_point
central_office
dtap
oh_route
splice_closure
terminal
ug_route

N

0 0.210.42 0.84 Miles

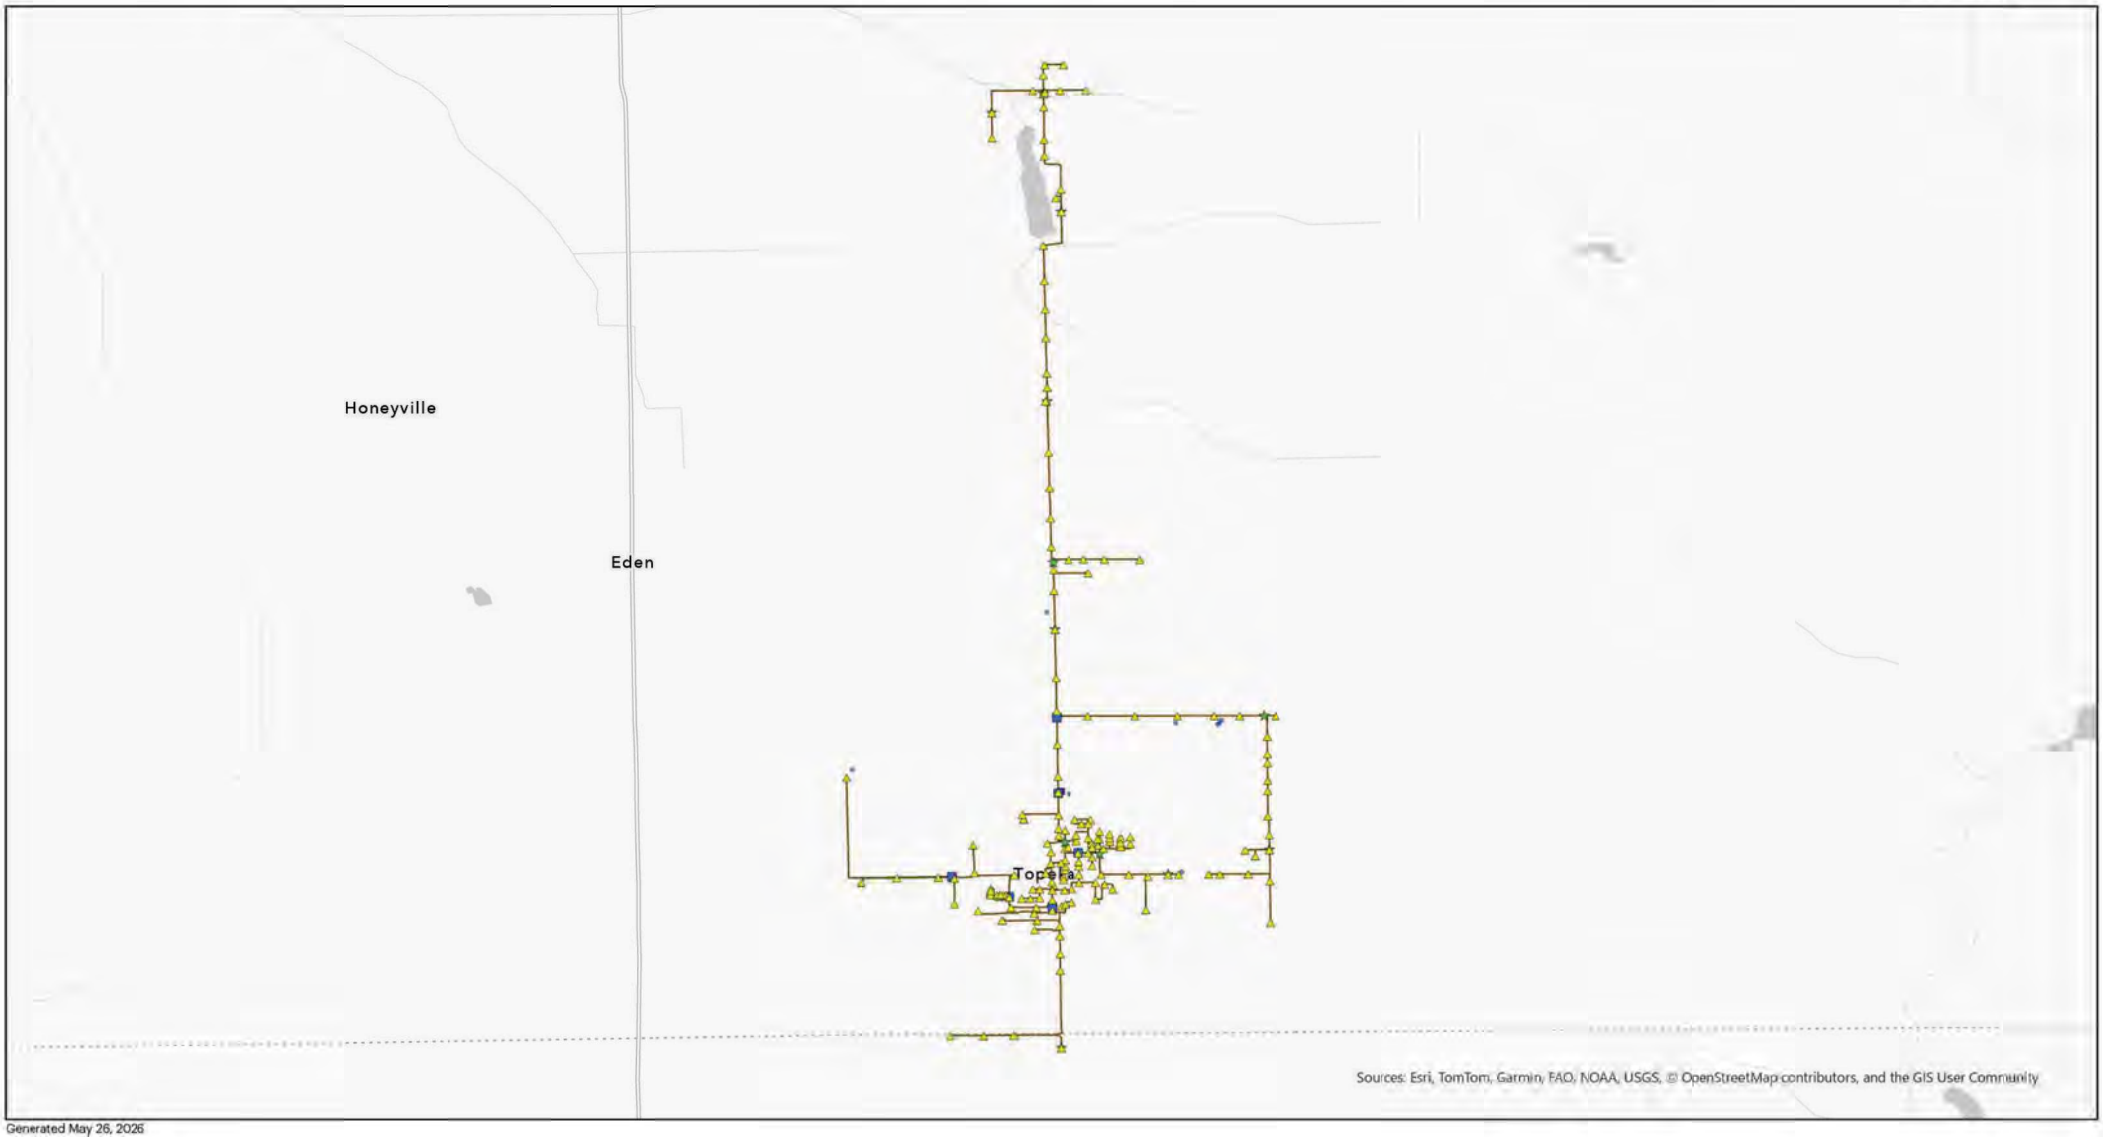

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 23 – List of Locations in Project Area IBO-851

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-851 Location List

9 locations

ID	Location ID	Is CAI	Technology	Upload	Download
50751b27a127f5273cf6bf8a0b5a8c81	1286970948	No	Fiber	2000	2000
640be997175b9f42fded798c8bc196e1	1286969517	No	Fiber	2000	2000
7721f39a221c5d7af31ce1fe39c92772	1286970977	No	Fiber	2000	2000
3caf8ae12f0d1088dab855303d4d147a	1286969921	No	Fiber	2000	2000
d7adb74fb4ae53dbc2f7fd01dc2a6b1d	1286971812	No	Fiber	2000	2000
907255202fdc99d5af09fb8123da51e6	1286971777	No	Fiber	2000	2000
52393ad10b268398e9159a8a6315c7a9	1286970703	No	Fiber	2000	2000
24d38c53b8f60b56fd4e0f8bac9036c2	1286971767	No	Fiber	2000	2000
12119eeacce6dcd9c38ee8e12e37179a	1286971823	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 23 – Budget for Project Area IBO-851

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Pole Attachments	Pole Make Ready Costs	Professional Services	$13,580.00	$0.00	$13,580.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$53,520.00	$0.00	$53,520.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$46,962.00	$0.00	$46,962.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$810.00	$0.00	$810.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$1,069.00	$0.00	$1,069.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$789.00	$0.00	$789.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$5,756.00	$0.00	$5,756.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$3,000.00	$0.00	$3,000.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$180.00	$0.00	$180.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$1,782.00	$0.00	$1,782.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$15,858.00	$0.00	$15,858.00
Permitting Costs	Permitting Costs	Professional Services	$12,874.00	$0.00	$12,874.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$2,664.00	$0.00	$2,664.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$1,537.00	$0.00	$1,537.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$15,198.00	$0.00	$15,198.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$13,965.00	$0.00	$13,965.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$2,814.00	$0.00	$2,814.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$5,652.00	$0.00	$5,652.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$1,977.00	$0.00	$1,977.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$6,000.00	$0.00	$6,000.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 23 – Disbursement Schedule for Project Area IBO-851

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 23 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-851

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 23 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 24 –Subaward Conditions and Statement of Work for Project Area IBO-169

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$474,950.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$474,950.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$474,950.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 24 - Specific Award Conditions for Project Area IBO-169.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[32.19%]; [$225,502.00]
Total Project Cost = (subaward funds + match)	$700,452.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$474,950.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-169 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 24**. The Project Area is depicted in the map in **Appendix A of this Exhibit 24**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 24**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $225,502.00, which is 32.19% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 32.19% for a total match of $225,502.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 24** in the area depicted in **Appendix A of this Exhibit 24**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 24**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 24 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 24;
- Appendix A to this Exhibit 24 – Map of Project Area IBO-169;
- Appendix C to this Exhibit 24 – Budget for Project Area IBO-169;
- Appendix E to this Exhibit 24 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-169;
- Appendix F to this Exhibit 24 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 24 – Project Area
- Paragraph 5.B(2) of Exhibit 24 – Project Locations
- Paragraph 5.B(3) of Exhibit 24 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 24 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 24 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 24 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 24 – Access to Service
- Paragraph 5.B(5)e of Exhibit 24 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 24 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 24 – Map of Project Area IBO-169

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-169

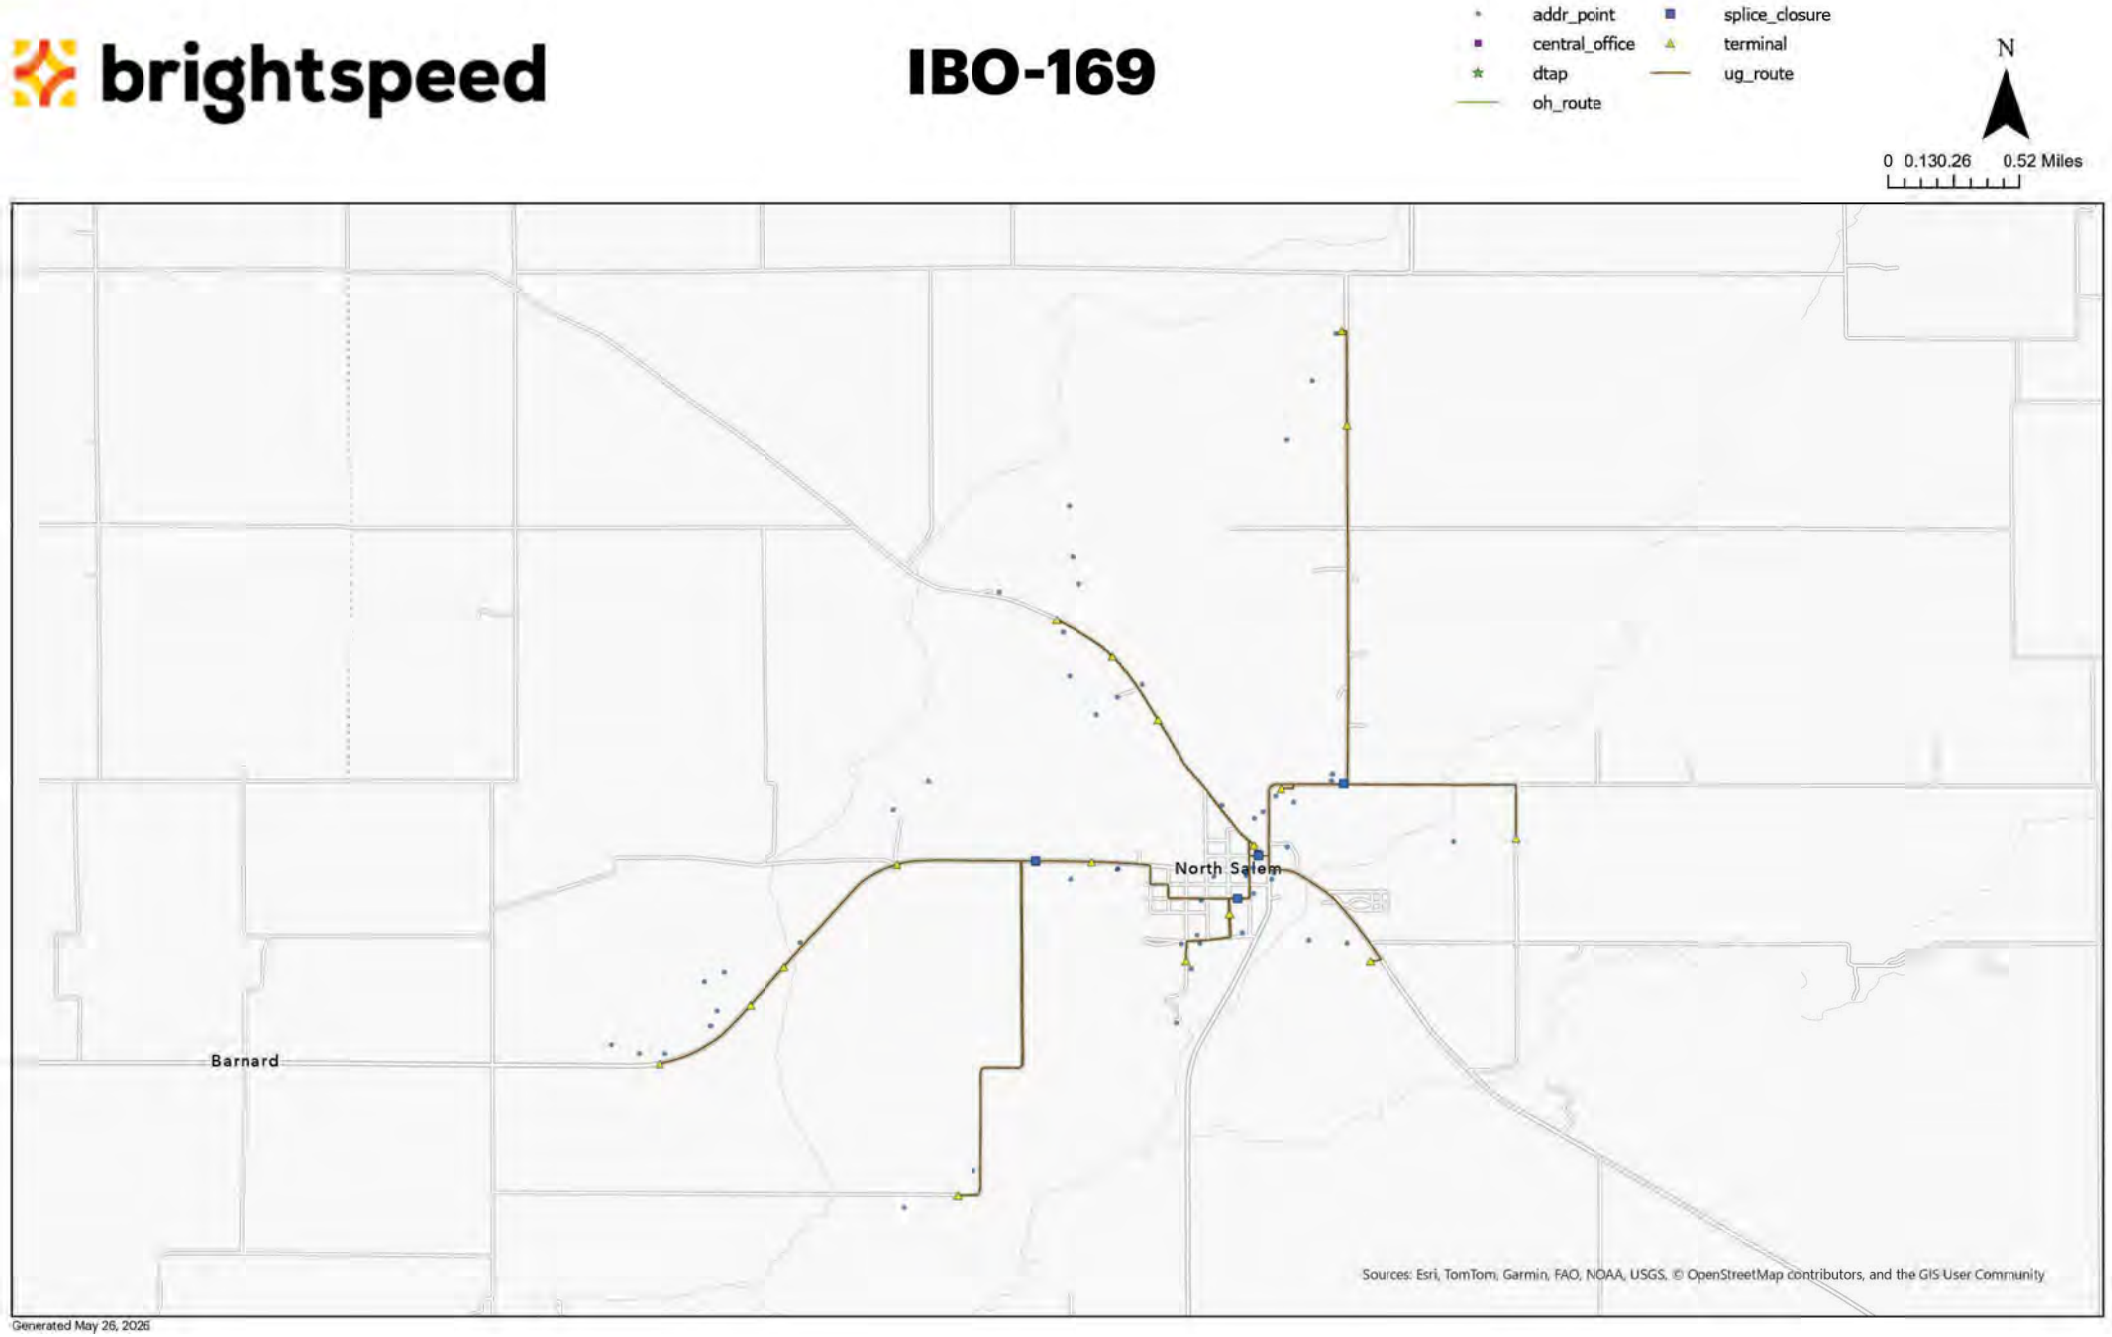

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 24 – List of Locations in Project Area IBO-169

Brightspeed IBO-169 Location List

51 locations

ID	Location ID	Is CAI	Technology	Upload	Download
b1e69ad027ef65a3b49351aaa0125742	1086694079	No	Fiber	2000	2000
f48fbefd7718ec6ccd6a6d3d18ae18bc	1086694142	No	Fiber	2000	2000
18b1c780e063f8b34c283fc54e87d1ef	1086693845	No	Fiber	2000	2000
8def833655a46dda7120ebca6debd9d4	1086694042	No	Fiber	2000	2000
668e41c70a4593f1fd9596662ac67712	1086694131	No	Fiber	2000	2000
602215634fead4f6858f8f3ded3b70e3	1086693778	No	Fiber	2000	2000
83343200fa1d481f305ed1582bfad4cd	1086694268	No	Fiber	2000	2000
58d307fea90efd01454281d8b8d04b02	1086694307	No	Fiber	2000	2000
660b8a3133c22c9b82854d890908312d	1086694269	No	Fiber	2000	2000
81d643033da61198cc4c64f6858ba0fb	1086693596	No	Fiber	2000	2000
50a9ed2aba1212d3042b027c00c1ff6d	1086693772	No	Fiber	2000	2000
08750705a1cb8eb2beb5b52824552b6a	1086694326	No	Fiber	2000	2000
03172c0812b546cef5a3137f5d87b8e9	1086693729	No	Fiber	2000	2000
23d6f292b8dd3a29d32d88fbfe8a7925	1086694026	No	Fiber	2000	2000
b46c848bc01da35f27acdfddedab5599		Yes	Fiber	2000	2000
dbdd4d7d1128780a5e7830e09db78083	1086694005	No	Fiber	2000	2000
6eb6b828c9904b06b32396dc07cec5a9	1086694381	No	Fiber	2000	2000
0179df8452a31d06bf966f9b73923942	1086694779	No	Fiber	2000	2000
63046762ade7ca8375916a65a6d603e5	1086694372	No	Fiber	2000	2000
5079726b6ddd7fe75647557ee6944b57	1086693988	No	Fiber	2000	2000
b14c8c7e170b452c1876e023dc5dd015	1086694052	No	Fiber	2000	2000
ae8c1ba23832b8234e4c08b56631a238	1086693984	No	Fiber	2000	2000
5ccd2c22b754e4b841491f2250942210	1086693894	No	Fiber	2000	2000
bd4cd847b6bfe0d77d1bc309b5afaf64	1086693727	No	Fiber	2000	2000
f5b51d9c3574e6c7cab083f16d1f2faa	1086693745	No	Fiber	2000	2000
7d0af2827cdb02bdc2c5248b8fc4acc7	1086693582	No	Fiber	2000	2000
3acdf11b92e5fe2a07c12ee64260be04	1086693717	No	Fiber	2000	2000
0227f756c1e484fcaf302bc76315db18	1086694760	No	Fiber	2000	2000
da868c6c15b34aa8dd972d6bea72d09f	1086694617	No	Fiber	2000	2000
6b89375bc544acc0d241df1f3fb9aea3	1086693955	No	Fiber	2000	2000
9a1b6587adfb591050d6090279201568	1086694146	No	Fiber	2000	2000
f0f27b7bd11f99ad43fbcd71a5bbb504	1086694128	No	Fiber	2000	2000
43841ba1da42d67c2b10af1d14036db7	1086694375	No	Fiber	2000	2000
ab16e58a4a27f631a1c08e81370b02d0	1086693893	No	Fiber	2000	2000
6022f8dc6a72a9ee95f6288bd25c2da8	1086693752	No	Fiber	2000	2000
ac7327f71796fca1e9459576a1a18939	1086693580	No	Fiber	2000	2000
6981a0458e36bb185c19817da2318f62	1086693777	No	Fiber	2000	2000
949c94540add5f846f26d864e6e08971	1086693746	No	Fiber	2000	2000
797b699cc1b47a64cfd7e48d3fb9794b	1086693576	No	Fiber	2000	2000
4d795ecb4e6bb9b08e67f696573901df	1086693847	No	Fiber	2000	2000
2c3eea8530669b11188440f742fd902a	1086693581	No	Fiber	2000	2000
aca6966dfa6c62a41a3fe68c41a003e9	1086694303	No	Fiber	2000	2000
e17a396f2e3d9e25f088e5994dc87e98	1086693573	No	Fiber	2000	2000
9d4681d1dc5dccf152b102aa040ef416	1086693758	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

ID	Location ID	Is CAI	Technology	Upload	Download
b9ec370cb4d328c9408b367d397111d8	1086694613	No	Fiber	2000	2000
0cb0cf1b65ed3972bd0bf89a7e08cc92	1086693572	No	Fiber	2000	2000
999dbd773650242275722908c04db663	1086694607	No	Fiber	2000	2000
fe3f81d323dc67c85c34ce7c6d98e83d	1086694605	No	Fiber	2000	2000
3188d1d715ff592ad1baa10ea44108ba	1086694595	No	Fiber	2000	2000
5158e0faf16b3fecd41321f485d89d00	1086693728	No	Fiber	2000	2000
922ad1fd5b42afde8603d11ad97b6f63	1086693747	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 24 – Budget for Project Area IBO-169

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$5,345.00	$3,881.00	$1,464.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$14,800.00	$0.00	$14,800.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$1,148.00	$831.00	$317.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$44,946.00	$32,627.00	$12,319.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$8,911.00	$6,469.00	$2,442.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$31,400.00	$0.00	$31,400.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$6,429.00	$4,667.00	$1,762.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$50,304.00	$36,517.00	$13,787.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$2,630.00	$1,910.00	$720.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$5,346.00	$3,882.00	$1,464.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$52,487.00	$38,110.00	$14,377.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$19,048.00	$13,830.00	$5,218.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$22,500.00	$16,337.00	$6,163.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$2,700.00	$1,960.00	$740.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$46,170.00	$33,516.00	$12,654.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$10,500.00	$7,622.00	$2,878.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$576.00	$418.00	$158.00
Permitting Costs	Permitting Costs	Professional Services	$42,610.00	$30,931.00	$11,679.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$177,136.00	$128,586.00	$48,550.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$155,466.00	$112,856.00	$42,610.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 24 – Disbursement Schedule for Project Area IBO-169

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 24 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-169

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 24 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 25 –Subaward Conditions and Statement of Work for Project Area IBO-938

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$316,929.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$316,929.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$316,929.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 25 - Specific Award Conditions for Project Area IBO-938.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[25.00%]; [$105,643.00]
Total Project Cost = (subaward funds + match)	$422,572.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$316,929.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-938 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 25**. The Project Area is depicted in the map in **Appendix A of this Exhibit 25**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 25**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $105,643.00, which is 25.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 25.00% for a total match of $105,643.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 25** in the area depicted in **Appendix A of this Exhibit 25**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 25**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 25 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 25;
- Appendix A to this Exhibit 25 – Map of Project Area IBO-938;
- Appendix C to this Exhibit 25 – Budget for Project Area IBO-938;
- Appendix E to this Exhibit 25 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-938;
- Appendix F to this Exhibit 25 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 25 – Project Area
- Paragraph 5.B(2) of Exhibit 25 – Project Locations
- Paragraph 5.B(3) of Exhibit 25 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 25 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 25 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 25 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 25 – Access to Service
- Paragraph 5.B(5)e of Exhibit 25 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 25 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 25 – Map of Project Area IBO-938

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-938

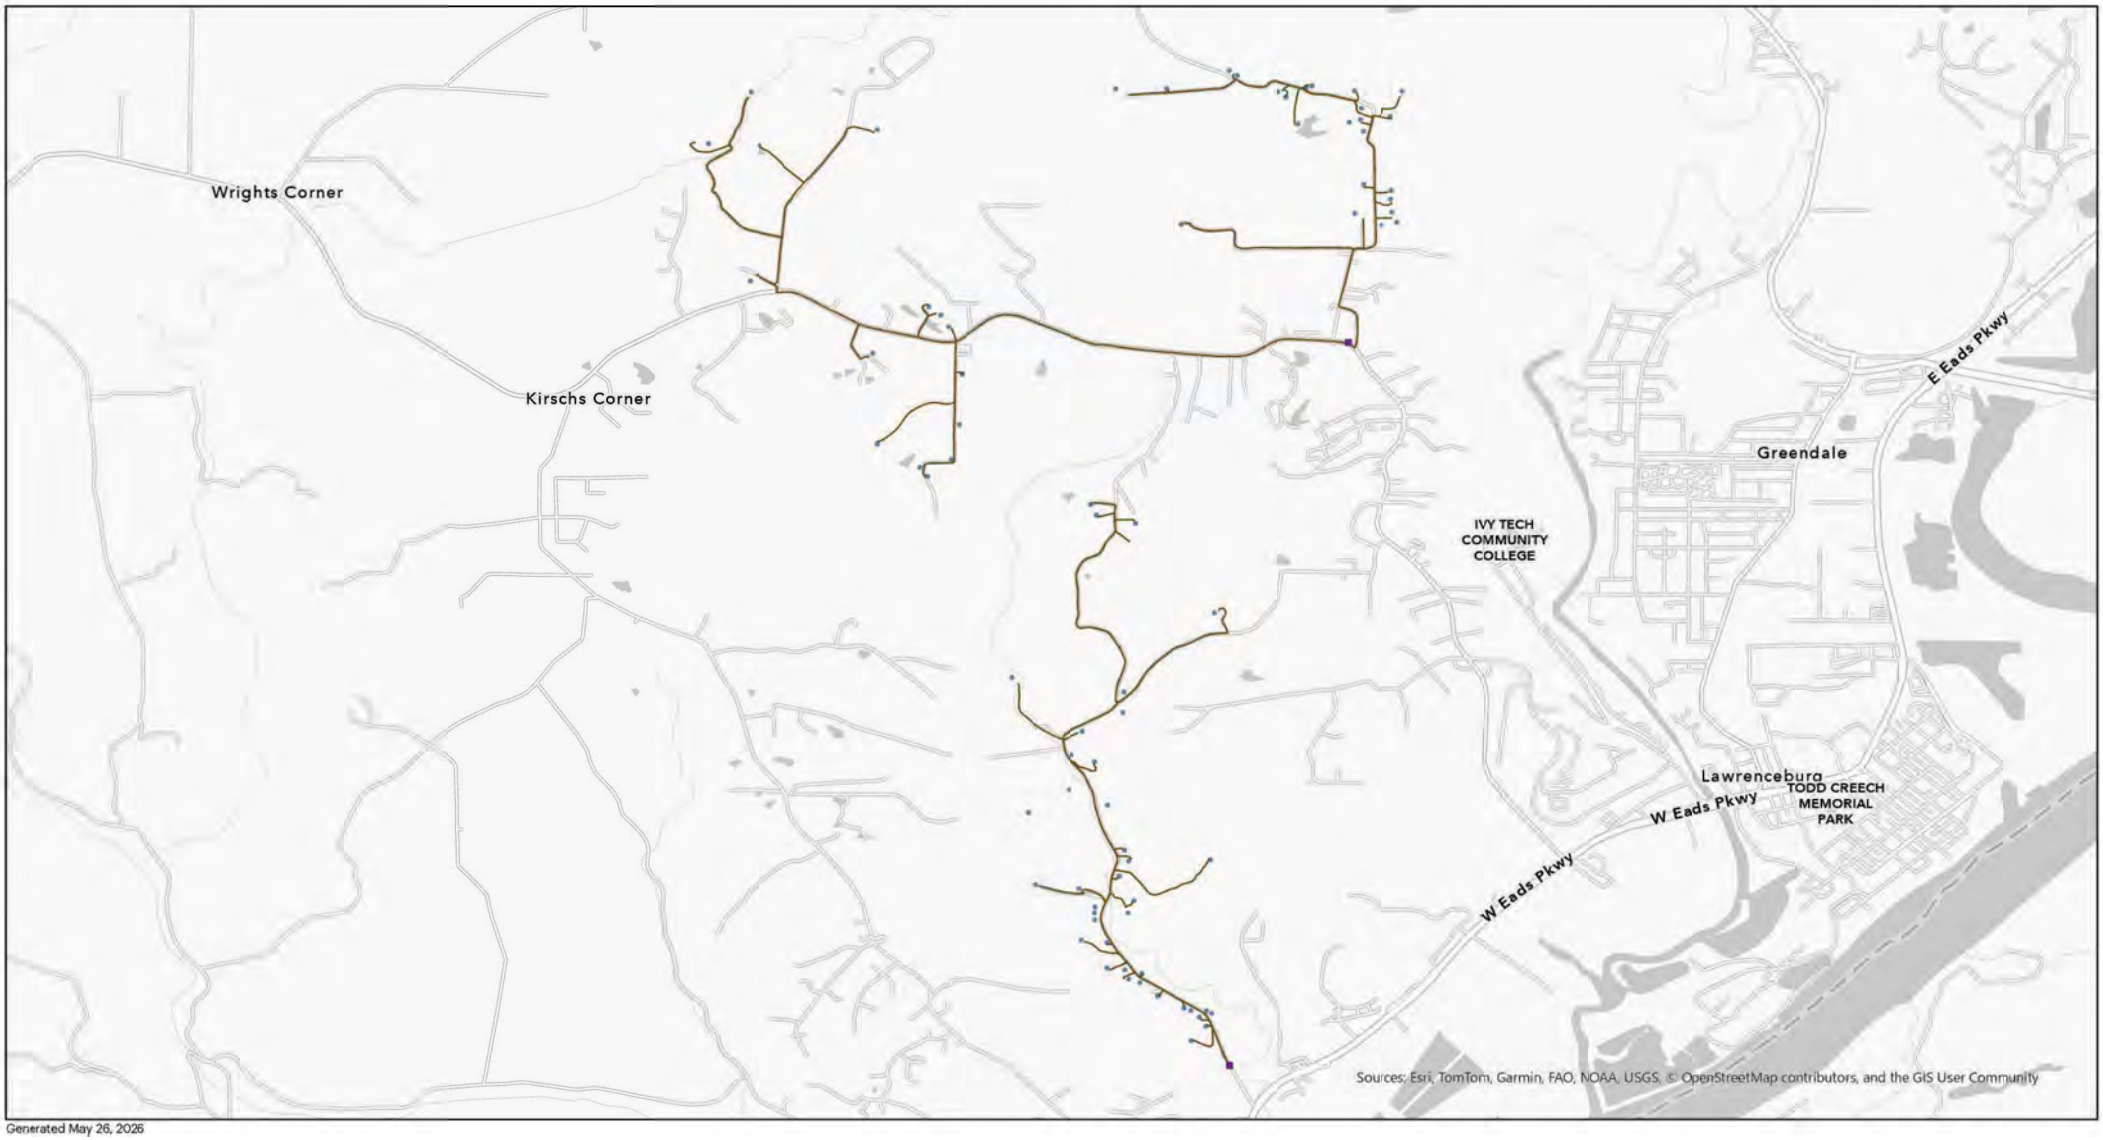

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 25 – List of Locations in Project Area IBO-938

Brightspeed IBO-938 Location List

78 locations

ID	Location ID	Is CAI	Technology	Upload	Download
d6b5b9a6732a4b7e264ebc1a967e1d9a	1015008481	No	Fiber	2000	2000
1207d621fb40618df4f5b0f1b400d867	1015025174	No	Fiber	2000	2000
90ecd89d935b1b0484caa3ae97be8692	1015026871	No	Fiber	2000	2000
0c1fbb983a2d4c4faa708c4c80632501	1015023949	No	Fiber	2000	2000
cadc11a7072080e9b755efbed890674e	1015009617	No	Fiber	2000	2000
e75ea74f53e0de91782f0051eb1829c2	1015023954	No	Fiber	2000	2000
0516a74781e8fc58a0585a7e12739e96	1015025185	No	Fiber	2000	2000
286d443ab1fe542303c70a40d34851ad	1015024142	No	Fiber	2000	2000
a0f7e08848fbfa7ac6660e2776e361c6	1015025184	No	Fiber	2000	2000
49d3eebc98e42eec8265bee5cbd9cdb4	1015024143	No	Fiber	2000	2000
381c467ef0a347999dce89447686c293	1015026860	No	Fiber	2000	2000
5642765c9ebb6a05d481db6f6709831c	1015029667	No	Fiber	2000	2000
e896eef9e48f937da84ffe6b45db2bec	1015023950	No	Fiber	2000	2000
a5344898b9b3d4976f60c1cac076f7aa	1015029471	No	Fiber	2000	2000
3653fb7dac551f76adc06fd5fdb63d86	1015024640	No	Fiber	2000	2000
8c45d0d0a6a454362032cd52768bdf9a	1015029682	No	Fiber	2000	2000
07d5754cf465ace0bb781c01804984fb	1015024110	No	Fiber	2000	2000
e30c82e7098a1ccb512cd1ed4fd891b1	1015020083	No	Fiber	2000	2000
41c135a36b8f9673b6aa07908507e7b9	1015009605	No	Fiber	2000	2000
9aaf99d8f5a77109eb515d92085e9fe4	1015024146	No	Fiber	2000	2000
93cbe579601ea65c78e93dd8a366c06c	1015009615	No	Fiber	2000	2000
ec1fc1b6b9005474c564406d4eed2ace	1015009608	No	Fiber	2000	2000
084456784fa0970eec8402f1cbc5bc85	1015024149	No	Fiber	2000	2000
cacd3964d2651e88b9298852332494cd	1015025172	No	Fiber	2000	2000
a7c541b7e47a49a74b32f9cbfc298fb9	1015009613	No	Fiber	2000	2000
f4ffbb453808b4867db2bf4535f5e6c3	1015023953	No	Fiber	2000	2000
8a96c7f898794e7c20d9723ecf87b061	1015026866	No	Fiber	2000	2000
221131930e607908e6b2bf74e29b43c6	1015023716	No	Fiber	2000	2000
b5fd03e9f4d1c079f734b816dbc122b5	1015023958	No	Fiber	2000	2000
e1eac860b7361768e67830e732dde482	1015026872	No	Fiber	2000	2000
49a98ff3912c6e5c58fcb94cf2c64b19	1015022111	No	Fiber	2000	2000
bc02b76cf20c7b1b460de1f3caa05b5f	1015029709	No	Fiber	2000	2000
75d015cf86e3e709be1c3f71f5a803f3	1015023729	No	Fiber	2000	2000
289379215552fc189ee18fb493efe23b	1015009620	No	Fiber	2000	2000
85f957738dc5f534b311781b9e99be34	1015020047	No	Fiber	2000	2000
2644c7b8861b40bb209f1ef1872f8a74	1015025176	No	Fiber	2000	2000
2200126d34ef6af14a6b5931ff9ae22f	1015008480	No	Fiber	2000	2000
96a851774cc8196b506cc97cca647fe2	1015024139	No	Fiber	2000	2000
4ba361230ce33a6b957fbd85527f7688	1015029680	No	Fiber	2000	2000
d31f301f05b79cb27446202c86c977ea	1015009611	No	Fiber	2000	2000
32c49054d303f899ba4582d819bd24d8	1015009612	No	Fiber	2000	2000
373ce5a47ac8b312668ba74d7a32d97d	1015009618	No	Fiber	2000	2000
adfaf4366c8e4955fb6b44be00cfc7cc	1015023957	No	Fiber	2000	2000
9578eb22bb226696f53edc8f175d5698	1015024151	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
2d750c419a5028cde1e842fd1631de55	1015024140	No	Fiber	2000	2000
4e115ae80ff58ffa7dbc780893993327	1015009606	No	Fiber	2000	2000
0f745a202cfcad1524ee3adfbe17e029	1015026069	No	Fiber	2000	2000
f8a6418f4df9ea2ddb7f5002cebec16b	1015023723	No	Fiber	2000	2000
c049b1d88c251de3f171568365ddb4d8	1015026865	No	Fiber	2000	2000
cb6e40887056f7728adcf63825e89617	1015024138	No	Fiber	2000	2000
4827cb541816cf6f1121cf9e08080dd7	1015009607	No	Fiber	2000	2000
ef6279963b258b21d2cba0af8fbd9ddd	1015023959	No	Fiber	2000	2000
24e18c68ffdb3c6b6729a9310ef740ff	1015022086	No	Fiber	2000	2000
0be1aefc4439aad65c840d25686148ef	1015024659	No	Fiber	2000	2000
13c99da45a93b5c4471402f30c0263c3	1015008482	No	Fiber	2000	2000
1f05fba21f31dab78bcd1e17da2809dd	1015023947	No	Fiber	2000	2000
39376d72b886a7442065a2c3fe809862	1015009609	No	Fiber	2000	2000
0330859ab356feda2b3f0ec231d4fe61	1015024653	No	Fiber	2000	2000
0715bd39ce4d72841a93cb7d0d85a711	1015009616	No	Fiber	2000	2000
0ba57d6b2198265dc6bd94369cdfe3d7	1015023680	No	Fiber	2000	2000
b7d27da16f8110cb57ef22788422d621	1015029666	No	Fiber	2000	2000
9aabc83f644772655fd4a3c5c11c99e2	1015020032	No	Fiber	2000	2000
b2b7bc9bfc641a8b8925f28355443876	1015020078	No	Fiber	2000	2000
fcaf464c0223073f5e290dc513fb4b4a	1015009604	No	Fiber	2000	2000
15bbf9ff120f0cdd60f4e34e19378332	1015029683	No	Fiber	2000	2000
5d15b0f43aac360da558d9af7ec2fb6b	1015024662	No	Fiber	2000	2000
c059e7c09ee10b9430d33e7f56d3cd66	1015024646	No	Fiber	2000	2000
f956118abbf0b3e99c18006a7e4e7597	1015022100	No	Fiber	2000	2000
c9c68a7be506a8cfb2022aa4bc85bb8e	1015020056	No	Fiber	2000	2000
4a620de33d49d4a83f5cbe68497a6a78	1015009603	No	Fiber	2000	2000
5b15c993d2400bd1bbea1e46a54ac10c	1015024634	No	Fiber	2000	2000
698c51e8dade48de5aee2cefb6e2bfc4	1015029674	No	Fiber	2000	2000
0aa934984930135f2c68e6689b30e654	1015024147	No	Fiber	2000	2000
02ea5d03ea531442454ad1206e3e8728	1015024148	No	Fiber	2000	2000
8286fd21946dc4911df5637cc8182e03	1015009614	No	Fiber	2000	2000
be46fc35724dd0e2fbcf8b2209a59626	1015023951	No	Fiber	2000	2000
c3b35ab7567db223e5cd0936111476de	1015024145	No	Fiber	2000	2000
cfbc3460a3ed3fd28ea57a3f6867a97d	1015024631	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 25 – Budget for Project Area IBO-938

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$12,000.00	$10,885.00	$1,115.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$1,440.00	$1,306.00	$134.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$5,250.00	$4,759.00	$491.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$312.00	$283.00	$29.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$24,017.00	$21,772.00	$2,245.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$94,652.00	$85,803.00	$8,849.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$2,138.00	$1,939.00	$199.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$83,070.00	$75,304.00	$7,766.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$4,690.00	$4,252.00	$438.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$3,838.00	$3,480.00	$358.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$24,700.00	$22,391.00	$2,309.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$23,384.00	$0.00	$23,384.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$1,048.00	$952.00	$96.00
Permitting Costs	Permitting Costs	Professional Services	$22,769.00	$20,640.00	$2,129.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$49,612.00	$0.00	$49,612.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$26,880.00	$24,367.00	$2,513.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$1,578.00	$1,431.00	$147.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$2,970.00	$2,694.00	$276.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$28,046.00	$25,439.00	$2,607.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$10,178.00	$9,232.00	$946.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 25 – Disbursement Schedule for Project Area IBO-938

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 25 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-938

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 25 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 26 –Subaward Conditions and Statement of Work for Project Area IBO-1037

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 26 - Specific Award Conditions for Project Area IBO-1037.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$80,474.00]
Total Project Cost = (subaward funds + match)	$80,474.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-1037 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 26**. The Project Area is depicted in the map in **Appendix A of this Exhibit 26**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 26**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $80,474.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $80,474.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 26** in the area depicted in **Appendix A of this Exhibit 26**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 26**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 26 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 26;
- Appendix A to this Exhibit 26 – Map of Project Area IBO-1037;
- Appendix C to this Exhibit 26 – Budget for Project Area IBO-1037;
- Appendix E to this Exhibit 26 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1037;
- Appendix F to this Exhibit 26 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 26 – Project Area
- Paragraph 5.B(2) of Exhibit 26 – Project Locations
- Paragraph 5.B(3) of Exhibit 26 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 26 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 26 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 26 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 26 – Access to Service
- Paragraph 5.B(5)e of Exhibit 26 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 26 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 26 – Map of Project Area IBO-1037

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-1037

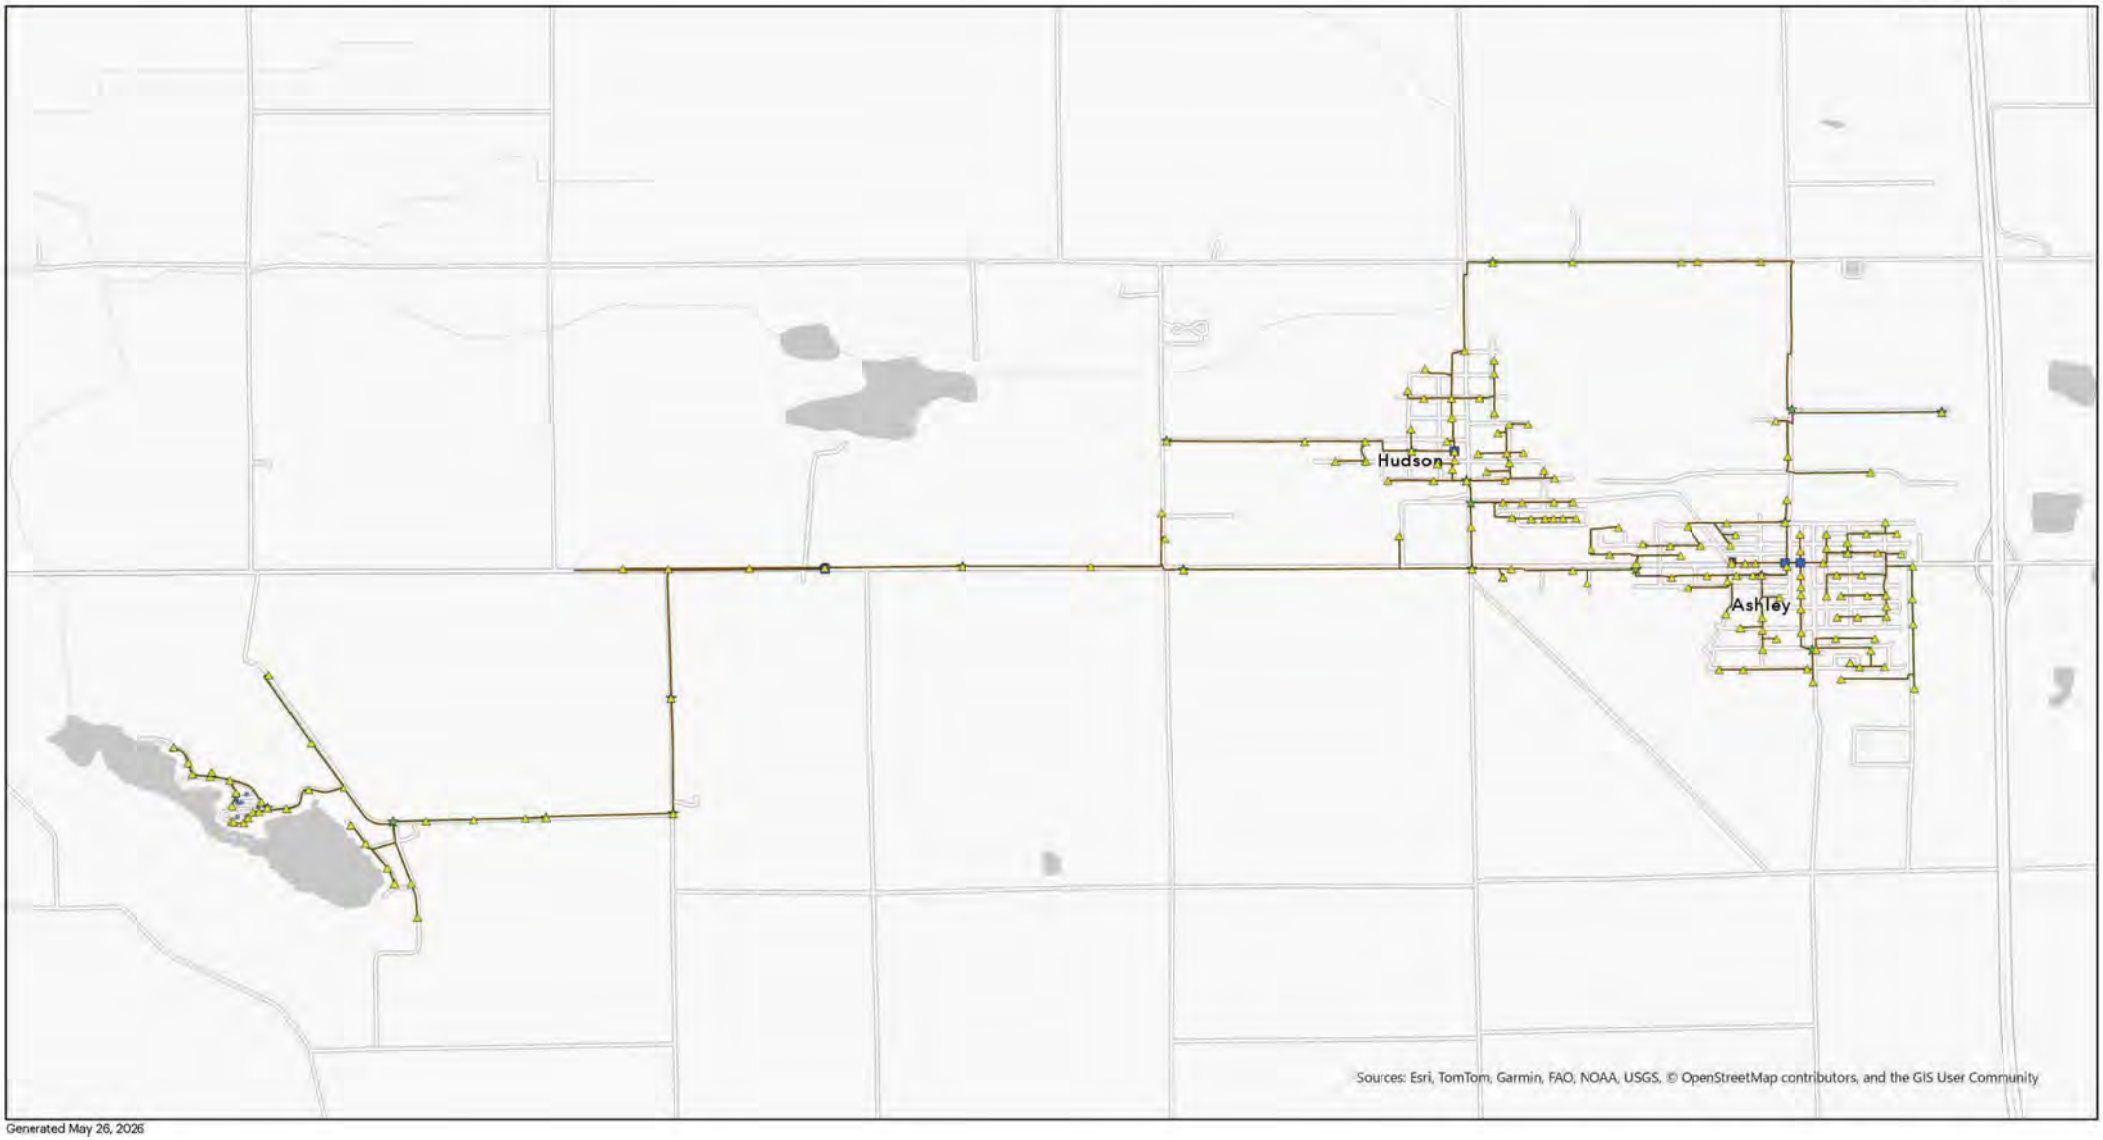

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 26 – List of Locations in Project Area IBO-1037

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-1037 Location List

8 locations

ID	Location ID	Is CAI	Technology	Upload	Download
5945f8a39ef2c2d361d1dbe86dc6e65c	1051642181	No	Fiber	2000	2000
458273f05e01a8682d4fe7c6b8a5ccfc	1413406026	No	Fiber	2000	2000
068fba6bcd3c48d4c4ddd6f3c93b9d20	1051642135	No	Fiber	2000	2000
018a4dce09977f7d8b0fbe2f97891381	1051642145	No	Fiber	2000	2000
62ca92db1baf4b6836fc84cd00af0cf6	1051642150	No	Fiber	2000	2000
49ffe45d1e499f69d22d92c56f5c2fcf	1051642119	No	Fiber	2000	2000
b546bf418f82ad316cd608d62707b572	1051642128	No	Fiber	2000	2000
c6e5ee1254870593b3e94094eea688ab	1413406034	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 26 – Budget for Project Area IBO-1037

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$594.00	$0.00	$594.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$5,863.00	$0.00	$5,863.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$2,032.00	$0.00	$2,032.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$0.00	$0.00	$0.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$938.00	$0.00	$938.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$1,500.00	$0.00	$1,500.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$60.00	$0.00	$60.00
Permitting Costs	Permitting Costs	Professional Services	$4,760.00	$0.00	$4,760.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$5,619.00	$0.00	$5,619.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$5,021.00	$0.00	$5,021.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$19,788.00	$0.00	$19,788.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$17,370.00	$0.00	$17,370.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$0.00	$0.00	$0.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$3,000.00	$0.00	$3,000.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$5,130.00	$0.00	$5,130.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$2,128.00	$0.00	$2,128.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$5,024.00	$0.00	$5,024.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$315.00	$0.00	$315.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$1,069.00	$0.00	$1,069.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$263.00	$0.00	$263.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 26 – Disbursement Schedule for Project Area IBO-1037

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 26 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1037

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 26 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 27 –Subaward Conditions and Statement of Work for Project Area IBO-992

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$675,092.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$675,092.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$675,092.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 27 - Specific Award Conditions for Project Area IBO-992.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[57.60%]; [$917,045.00]
Total Project Cost = (subaward funds + match)	$1,592,137.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$675,092.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-992 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 27**. The Project Area is depicted in the map in **Appendix A of this Exhibit 27**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 27**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $917,045.00, which is 57.60% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 57.60% for a total match of $917,045.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 27** in the area depicted in **Appendix A of this Exhibit 27**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 27**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 27 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 27;
- Appendix A to this Exhibit 27 – Map of Project Area IBO-992;
- Appendix C to this Exhibit 27 – Budget for Project Area IBO-992;
- Appendix E to this Exhibit 27 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-992;
- Appendix F to this Exhibit 27 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 27 – Project Area
- Paragraph 5.B(2) of Exhibit 27 – Project Locations
- Paragraph 5.B(3) of Exhibit 27 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 27 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 27 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 27 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 27 – Access to Service
- Paragraph 5.B(5)e of Exhibit 27 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 27 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 27 – Map of Project Area IBO-992

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-992

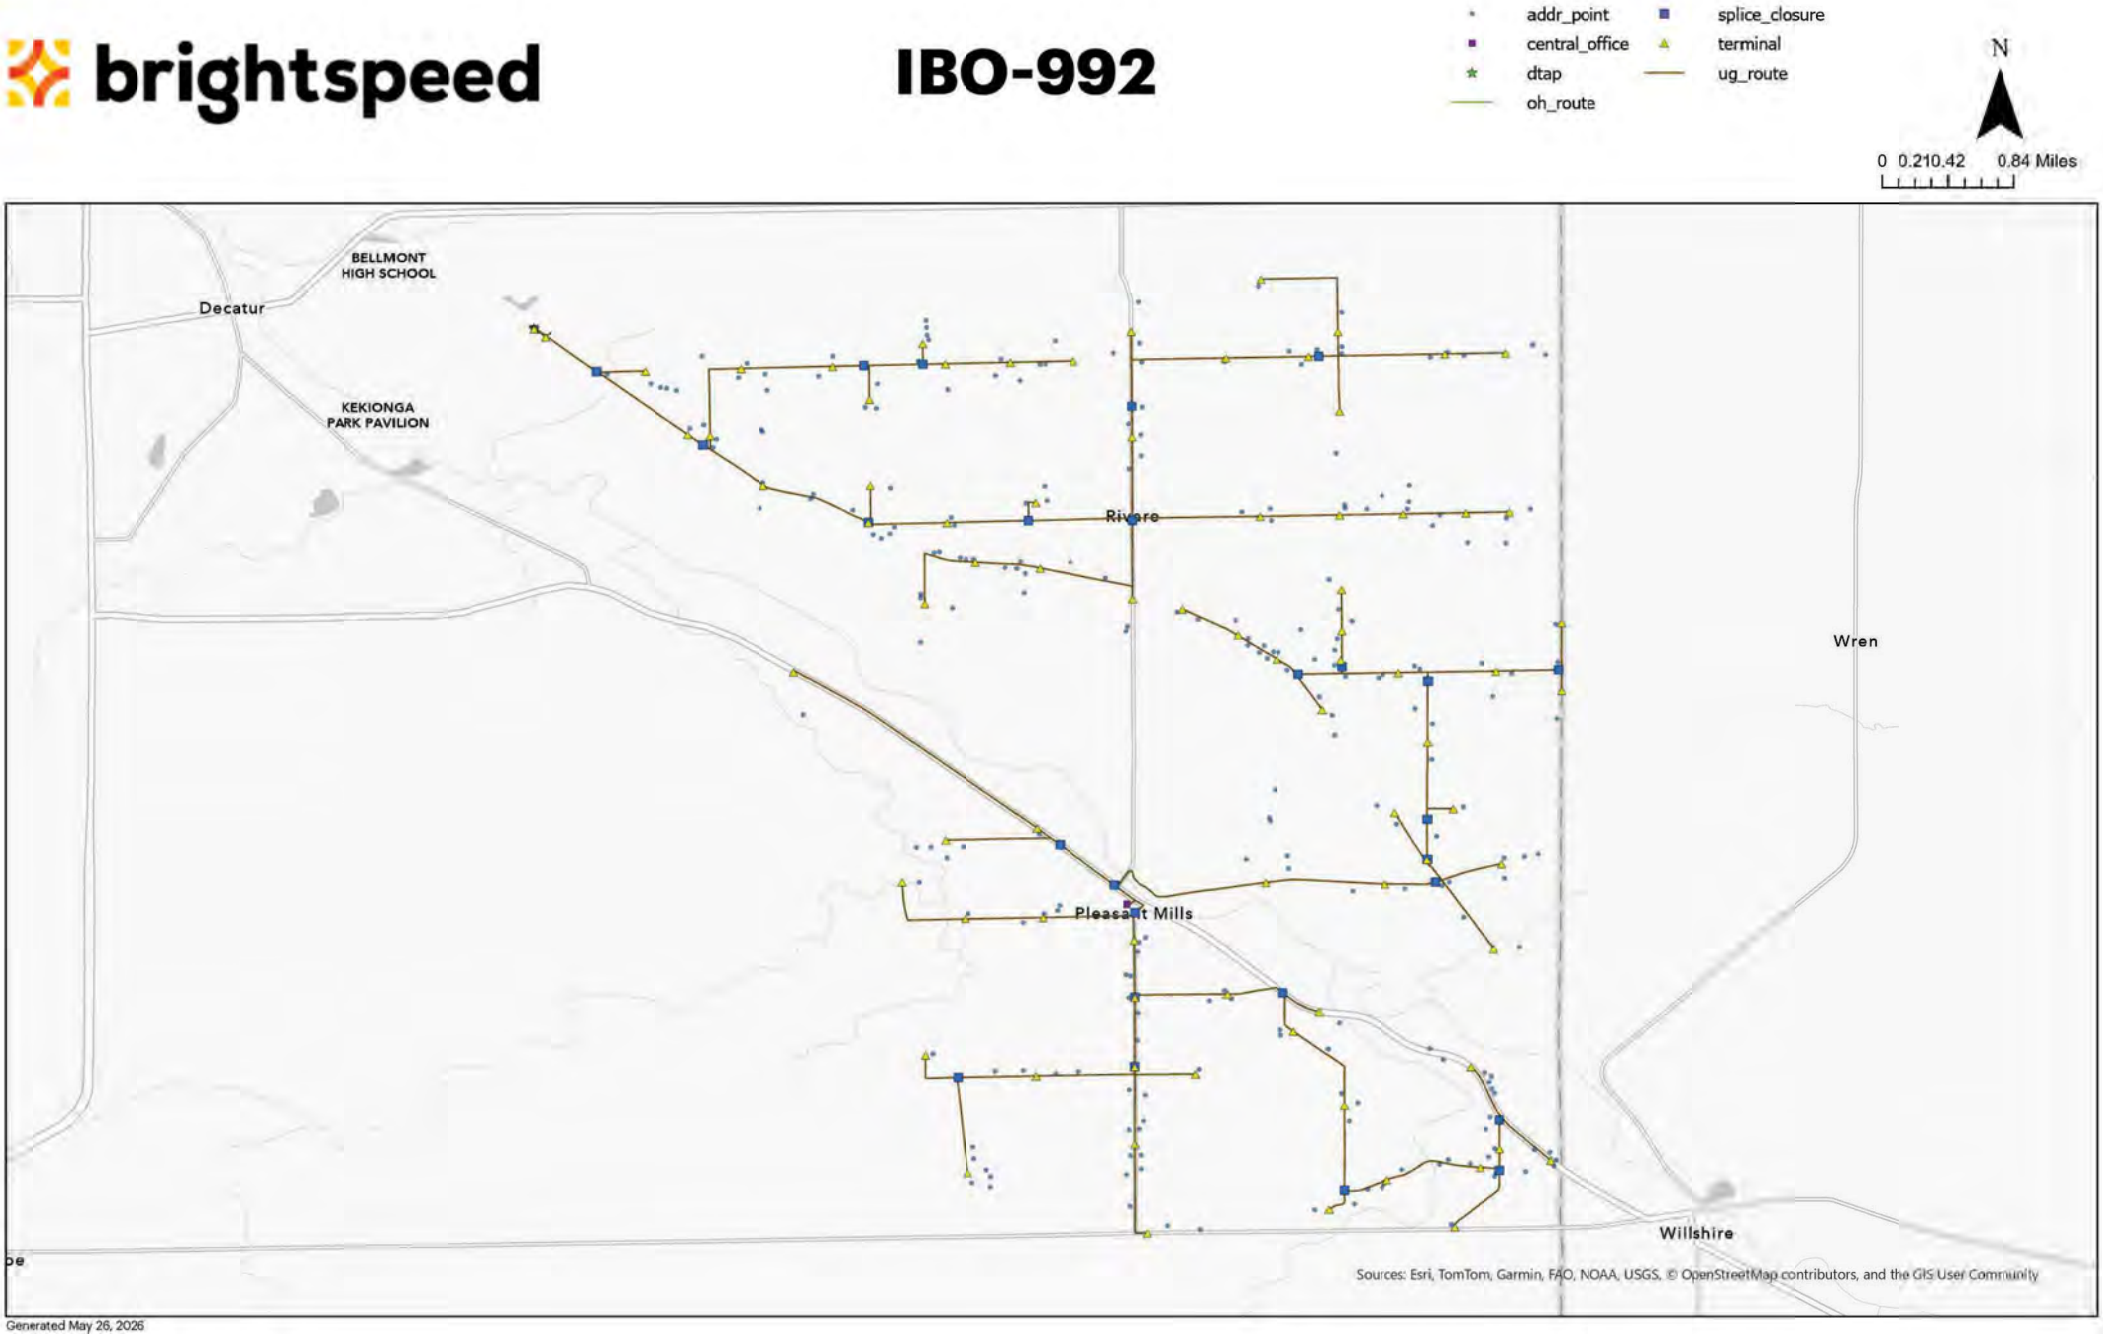

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 27 – List of Locations in Project Area IBO-992

Brightspeed IBO-992 Location List

243 locations

ID	Location ID	Is CAI	Technology	Upload	Download
f26eda22f1314f05e8c603ceb9687068	1144646051	No	Fiber	2000	2000
3157cf37d168be899a441a9d3d5c7e77	1144642271	No	Fiber	2000	2000
5edabd727139d956df83c549c2083429	1144649204	No	Fiber	2000	2000
4c763d66747c18c01f655e8cc6c63f6d	1144643483	No	Fiber	2000	2000
1afccfae16a9ed5977101d72cbce99cb	1144651639	No	Fiber	2000	2000
3f9d68778724ddbea21a7ba611e169b4	1144651638	No	Fiber	2000	2000
f11c3c96222f87563f3570aaea856227	1144646297	No	Fiber	2000	2000
618d032b7577e4bb3aca9c262835c052	1144648521	No	Fiber	2000	2000
909afd6855ffd70cf43072ecc7025932	1144647826	No	Fiber	2000	2000
fa024acf16597672b29922604aec1fd4	1144646099	No	Fiber	2000	2000
b40811c7e1acdb6bbf7395437eb23c74	1144643480	No	Fiber	2000	2000
0cc7df5c5e51c503f2779bcdf7f240db	1144646548	No	Fiber	2000	2000
76863b84547c6c6a6a344c44bfe2db04	1144646143	No	Fiber	2000	2000
2eec355f2825ab76cf495650bf45f18f	1144649220	No	Fiber	2000	2000
f87f6c66dd871253ff733c48a0850267	1144641421	No	Fiber	2000	2000
394611003b8f64cd1b96ae546ae5a1a4	1144646116	No	Fiber	2000	2000
3c6163365717c5ca8cb0bff816ccb8d1	1144647026	No	Fiber	2000	2000
673dd0f19195b6fd82e828a33ff3fa44	1144646105	No	Fiber	2000	2000
4fe841104d50d9289f1e45b4c3261343	1144643463	No	Fiber	2000	2000
0dfd106b58374d03a1be341e63a2f845	1144648511	No	Fiber	2000	2000
590cdd28a7ebf69b5946312dd35b0596	1144649201	No	Fiber	2000	2000
814531f94511ebc2581067abbedd69e8	1144642240	No	Fiber	2000	2000
a1808071a741b6b62079b15b8ef228e1	1144649215	No	Fiber	2000	2000
1071208567edf04cbb410aaa95bb5ca0	1144646303	No	Fiber	2000	2000
cd0f6edf52c9aa0cc8801b890b6a9a6c	1144648520	No	Fiber	2000	2000
476f2dc513ffdf5b2b4adf34bc178032	1144645701	No	Fiber	2000	2000
0d761f40563d15e0d04206d39fc7d533	1144647013	No	Fiber	2000	2000
833739955b9b6c21c036d5bf66be71a1	1144649212	No	Fiber	2000	2000
70857061234c359e1e5b13622f1c64bd	1144643464	No	Fiber	2000	2000
b56313c09f3a8c7945d6d599736545c2	1144647835	No	Fiber	2000	2000
61ffe4ca98808639a6b8b1408b3d6b71	1144648535	No	Fiber	2000	2000
a5994f4a7c2300e7a1700216b3c01527	1144647045	No	Fiber	2000	2000
5624a27afd9716850932807023d98279	1144646126	No	Fiber	2000	2000
78dbd50f079762d1b8cf802f69c902a0	1144646115	No	Fiber	2000	2000
d3e1e2a293c4e052936a94c997ada942	1144648557	No	Fiber	2000	2000
706a70818dccabb0cca737bcd6843913	1144646091	No	Fiber	2000	2000
bb19c3bca885abaf6c9b3958582a2c1f	1144648515	No	Fiber	2000	2000
1cd20f158605e8160d3705ebb5519346	1144649214	No	Fiber	2000	2000
ada19e41441950cb2d21a7f3fe9215c9	1144647839	No	Fiber	2000	2000
4db071cdb6b1975dabc285e6fc8b2f7b	1144643477	No	Fiber	2000	2000
ce5f03efceef26c88793e8fe291ca5a3	1144648534	No	Fiber	2000	2000
e8080368844c0ec55df93715569979b9	1144648546	No	Fiber	2000	2000
cfc983881d749cbbf2b82fb0820ee6c6	1144642241	No	Fiber	2000	2000
d0239c55c0012bb423c99d2c7215dd95	1144649224	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a3dd948628d24d28d71929105ca04d67	1144651667	No	Fiber	2000	2000
c76ad0e09f3ff67ba10701ef5cc71ce3	1144648540	No	Fiber	2000	2000
a43a8a7238552cbae8fb16916a7a2159	1144648548	No	Fiber	2000	2000
55abb6083257c706cbc3cb519876a67e	1144642648	No	Fiber	2000	2000
5e5953422827027dfb12ca06f936a029	1144647000	No	Fiber	2000	2000
3a4a5fbb434d4617c817ab98f96987c2	1144646125	No	Fiber	2000	2000
a157bab95d1ec9aa4179b99db9c32902	1144651668	No	Fiber	2000	2000
82033db2ad74f4768c5611cba124c4ba	1144649217	No	Fiber	2000	2000
8ffc78536daa8345b0fcd107c2a65326	1144646094	No	Fiber	2000	2000
98aeb6cb8b629812b224da49027f687f	1144642257	No	Fiber	2000	2000
16998661d7469a2d70b3dfea1baeb2b0	1144642036	No	Fiber	2000	2000
25302822af2957b0b041fed13a35fc1b	1144646090	No	Fiber	2000	2000
7f2653b95ef65e253f5c9cc93d43e45b	1144646129	No	Fiber	2000	2000
0eb53646f02357a8bcd25a01d5481a9f	1144648516	No	Fiber	2000	2000
400b3ddbc0c960cddb0f09ffc16f8fb3	1144651646	No	Fiber	2000	2000
4e58b33928e2f9f0f87a290a374169d1	1144648513	No	Fiber	2000	2000
48726708422344b9f9d65d320ee62248	1144648522	No	Fiber	2000	2000
a05073c8d2cdb92b1a577dd7e1205ee9	1144651633	No	Fiber	2000	2000
e75dbcf3d8af75e949b7ff273148058b	1144648544	No	Fiber	2000	2000
4017397e219fe8a661adf8f056f9b6c9	1384961970	No	Fiber	2000	2000
9be7319b2dc1c96f3a8fece9b4003526	1144642259	No	Fiber	2000	2000
7f704a7546dd8b92b5306bd676f0faaa	1144648545	No	Fiber	2000	2000
8c0e4ba1c37f3d4a239e4f507e0f0559	1144647040	No	Fiber	2000	2000
e0fb29c89a4a103260d275f995480d17	1144648554	No	Fiber	2000	2000
9265bc2b0f1800e91ea7852128e0c92e	1144646139	No	Fiber	2000	2000
aeae8e67e558f6631fd3421910007e02	1144648551	No	Fiber	2000	2000
850158835ca4faace12e37c3fbe0dc11	1144648550	No	Fiber	2000	2000
3a4f83222ece8e8313f9f9936190c460	1144643476	No	Fiber	2000	2000
cb4d64d162a42872e3d683483773ccfd	1144648552	No	Fiber	2000	2000
74fe9c5ca4431c775309258d2a25182d	1144643482	No	Fiber	2000	2000
e488b0f8ac108185fb4e1a04c9595324	1144646119	No	Fiber	2000	2000
7ee3914dab8c7e93ff92ae00cf7c9933	1144646044	No	Fiber	2000	2000
546c466eb2ed0d65d1e7247d33c7d826	1144642266	No	Fiber	2000	2000
0dcfe583833d48bf5ded0a9a6a32a8f8	1144649221	No	Fiber	2000	2000
a2b6db25240f5b46611c970f20109463	1144646037	No	Fiber	2000	2000
3712bb3c583dc22253b0e682ad1eddd5	1144647003	No	Fiber	2000	2000
53a25522fdd7f6cae9438d908dea416e	1144643471	No	Fiber	2000	2000
3d5b2600be1f77381cedaa759fa1048a	1144641385	No	Fiber	2000	2000
63204e32cf6daba22b78694cf07f2809	1144643467	No	Fiber	2000	2000
dd1e9ff07aa5ffdc506bc8e47203f1b1	1144649205	No	Fiber	2000	2000
9f55ef05cf1d265fa28cba8c635fda47	1144647004	No	Fiber	2000	2000
717fa1a168ee2f2cb88f9db2e5f01254	1144651655	No	Fiber	2000	2000
55764bbdcef8d2f844091199ee59677a	1144646098	No	Fiber	2000	2000
5ed4128eeb4c72f77dfee3406382e36d	1144651886	No	Fiber	2000	2000
ec3d3b190b4cafae966aab0aed77f355	1144651630	No	Fiber	2000	2000
7fcf66841a2acbb76df57b646f13839c	1144649218	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
27c6357df9eacd18100d0d0d9a47fb55	1144647009	No	Fiber	2000	2000
f35f2ff8220ad290ce420b0ae2bd8c4f	1144642245	No	Fiber	2000	2000
e0bf82046d74566aba8813f9b4b0b8be	1144641431	No	Fiber	2000	2000
0a40a091c54d9fa65d5591c3b4092174	1144646140	No	Fiber	2000	2000
1691c5651ad336bce3fbb685ce1d2411	1144646294	No	Fiber	2000	2000
6eda84c36b60eee1e609cf4a0d270b47	1144651665	No	Fiber	2000	2000
d891923bd881895b421ea8d25a00e1c3	1144646104	No	Fiber	2000	2000
13796c5dc3c9986d6df6841635f68711	1144647837	No	Fiber	2000	2000
aea580615012aa81bfb9ade8dc086721	1144649209	No	Fiber	2000	2000
10d4cc97699dac566899075bc617e761	1144643460	No	Fiber	2000	2000
0f7189c208a4c2d507daba474577440a	1144646118	No	Fiber	2000	2000
1761cb3b6d0eb37adf2e101d34e6cb25	1144651640	No	Fiber	2000	2000
90ec9b068db8c73acf07575fc5a35d57	1144643465	No	Fiber	2000	2000
f581ad18d52b07e57009160dcbf7c6ce	1144646113	No	Fiber	2000	2000
e75f833d7198488bb91eead40d3bf400	1144646561	No	Fiber	2000	2000
de530247aa66869559bb34149be8fdc8	1144643475	No	Fiber	2000	2000
2a331c8e5df1039fab7a9fe5c24b26a9	1144646101	No	Fiber	2000	2000
166f8ea1b3f128874d8202b3ebeac431	1144643466	No	Fiber	2000	2000
562e524606f5fffea206255c7f5b149b	1144646048	No	Fiber	2000	2000
1f383dec4e2245dbb20daa7aa95c5771	1144646304	No	Fiber	2000	2000
0778c77ebd6b58438d4d47ef03584bc9	1144645977	No	Fiber	2000	2000
37c3f693edbe6861e6cfe28c467c83b3	1144647006	No	Fiber	2000	2000
72fb64ebae5325ef59d38ba7b8ff5e58	1144648538	No	Fiber	2000	2000
154e2a860c4aabf21b0f7784447821bf	1144642041	No	Fiber	2000	2000
8d8404ec6714e6a102baa771c1169b46	1144648510	No	Fiber	2000	2000
3529cd64edb3346b2587686f3459417e	1144651647	No	Fiber	2000	2000
ed69de0753cbc330685965417052184b	1144649211	No	Fiber	2000	2000
d0b5b0cccd41e0294aed59539ce6da83	1144646133	No	Fiber	2000	2000
f8e08d82352311c25b6fc9fbe40b58ca	1144648553	No	Fiber	2000	2000
a2d64abdb5e17fe6f127975409ce7771	1144642654	No	Fiber	2000	2000
7c51b0a492c9588919c8f67dc36d6d03	1144648527	No	Fiber	2000	2000
1b11c7bca31fd832f44a836fd25f180b	1144648543	No	Fiber	2000	2000
35862bbdd10cd56238869b263f8c7254	1144642658	No	Fiber	2000	2000
32b33549a4e48db6e7f66baf1012ce68	1144646049	No	Fiber	2000	2000
5d81663881081051c0e2872e013be05f	1144648533	No	Fiber	2000	2000
0ed84e2a17a41b7de0955e196e59cce0	1144649207	No	Fiber	2000	2000
fd98b834f8f0aa9b1a66f4f92c57aa97	1144646567	No	Fiber	2000	2000
98a7ba30fb01f484d7fe464fb74e8954	1144646141	No	Fiber	2000	2000
27accfd2bf82e3afa869b9121ff1540e	1144647827	No	Fiber	2000	2000
e44955144dc39f5ae6661d7594e361a0	1144647042	No	Fiber	2000	2000
400d5f10e13956858eddb1b67d2a8eed	1144642067	No	Fiber	2000	2000
77a71e715d978f26c5cfe7bf17149cc8	1144647051	No	Fiber	2000	2000
33d921cc4caad8d5924dc7c6641e2f36	1144646092	No	Fiber	2000	2000
9011fc591b525afb797a7d40f883e3fd	1144646039	No	Fiber	2000	2000
3b4c18b89e9d774af1dbfcd30aa8a236	1144643479	No	Fiber	2000	2000
57109e7b0704e72cd3c1d3ac8466a96b	1144649200	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
8e8695d11038b1e88fa7874c81f797b0	1144648530	No	Fiber	2000	2000
209f2ee488e496b6ae4ff131a2eb99f8	1144646132	No	Fiber	2000	2000
cbef674c3a2e3dc08a36db2cfb7beda2	1144642258	No	Fiber	2000	2000
4d5caddcec89a10458c1b45d45e8b2a3	1144648556	No	Fiber	2000	2000
99837373a37f539dfda45263e78fa257	1144648525	No	Fiber	2000	2000
06a98ab4fb5e447a92317a607ee90a60	1144646117	No	Fiber	2000	2000
932ed2e1b0786a331d1d252796b681f2	1144646144	No	Fiber	2000	2000
003c9713433fd4a46f2f90706792f5de	1144642256	No	Fiber	2000	2000
60f26277806907c3782391384f191a21	1144643470	No	Fiber	2000	2000
69830a3f91f405228ca4622b548a5dd5	1144642260	No	Fiber	2000	2000
43d72938b3d2fb944487e18dfc6fed20	1144649225	No	Fiber	2000	2000
5ee54bf6e27e6ae88ff4a363777003a0	1144651669	No	Fiber	2000	2000
820ac8dfcc961fa00695e724f94516c3	1144651649	No	Fiber	2000	2000
345051dea8488e709c53a76175419bd5	1144642040	No	Fiber	2000	2000
fbad1f18c8d29b8766a23b962179c4a9	1144648531	No	Fiber	2000	2000
4c8d2c366d717eb5a1cb90f304fe96c7	1144647039	No	Fiber	2000	2000
52bb7bc6dc143ae860922fd9836c5c10	1144645952	No	Fiber	2000	2000
5de9d2f7ea5d88fb6ec1aa2a1ebed6d2	1144642272	No	Fiber	2000	2000
2b2e70f3ab5738c8ac5d996dfaceb764	1144649222	No	Fiber	2000	2000
d51a16497fe8e7c07359bad4da4cb364	1144643468	No	Fiber	2000	2000
aef55d42e4355156ccb7f68baf6efdb8	1144648512	No	Fiber	2000	2000
0cfe01f132666807dc5a03bad8358bc6	1144646052	No	Fiber	2000	2000
5e5625fa3f25ccc670a864bd4502ce96	1144646047	No	Fiber	2000	2000
aafc593784e3a8788bf38babfbdade5f	1144648509	No	Fiber	2000	2000
e2c3f0bd05888507933d457b97898b36	1144648536	No	Fiber	2000	2000
6af75a67307530ab026ace1276f4a564	1144649216	No	Fiber	2000	2000
31db82c8742c60a1eefcf44d0d7aff6c	1144646301	No	Fiber	2000	2000
ddaf2cf3a85bc087eb08fe0ac3ae0fbd	1144646127	No	Fiber	2000	2000
9c8aee49959d918dea6dbf79d436885c	1144646108	No	Fiber	2000	2000
bd36c01479600de57f3c060bc2282486	1144646042	No	Fiber	2000	2000
e0eaa7f6cf6475c1ab64cacea857c6fc	1144646088	No	Fiber	2000	2000
3baee8e0f0dce08a42b3d76ba121b771	1144646046	No	Fiber	2000	2000
8fc55362f1adbc1a7efd62f26a8c12c8	1144643478	No	Fiber	2000	2000
ca4af78e1d2e6b8145b78be9932ea27c	1144646043	No	Fiber	2000	2000
bfa9efcf31705cac385bd3bbbd71030a	1144651662	No	Fiber	2000	2000
f4f1b89e808ba18f1c702d0bab8f6a83	1144648508	No	Fiber	2000	2000
e86e438a9d7b53c3564859a8da7e21e3	1144648518	No	Fiber	2000	2000
e897f04eac8bece398b877b6a24f1ee2	1144648532	No	Fiber	2000	2000
a4b138f7b474436a317e8a1ddb2e5752	1144647014	No	Fiber	2000	2000
4b7a905c248ccbea7166379adbff6b45	1144647831	No	Fiber	2000	2000
7c559e33e083d8b09604ba951573d33c	1144647056	No	Fiber	2000	2000
8fd699180ab314a6b3deb8fc58075c1a	1144649202	No	Fiber	2000	2000
187f4ae878570c8c169ff4944e38dbdb	1144647015	No	Fiber	2000	2000
3c255bc747df942764f6e46cf3ca1567	1144646045	No	Fiber	2000	2000
eb2ebea8c629834cdc219967c938b8be	1144648514	No	Fiber	2000	2000
eb4d837fe32c411cfe7aad0d23ed550f	1144651644	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
8a1ba421015e37f239e83398ae728581	1144646038	No	Fiber	2000	2000
d4f654af84fa05f4eb38d3fbd0b6fc11	1144646041	No	Fiber	2000	2000
6acd51174e6028ba575b538e6bb00ce8	1144648549	No	Fiber	2000	2000
a94ac170ac204c920c62e09430e45943	1144648539	No	Fiber	2000	2000
da4196525d7d6d6bff42ae35fb8ed93a	1144648524	No	Fiber	2000	2000
6436b11e05aac703ce7f2d3dab0d9f88	1144647043	No	Fiber	2000	2000
ea3fe81c987d60cfe8fd0eee3dd6792d	1144648529	No	Fiber	2000	2000
2842f5eea8fb869d38391bf58e1de225	1144651664	No	Fiber	2000	2000
cd3b47cf06ea7ad28e9cb3bc83637ded	1144646296	No	Fiber	2000	2000
746e542e52b9637398264703cc0b7699	1144648537	No	Fiber	2000	2000
124a1c312e1709d7f24db82415b93e8c	1144643469	No	Fiber	2000	2000
aa70484e46eceefc65bc1297388aafda	1144646295	No	Fiber	2000	2000
1f6b1c3c0d6dc626f3821c42fd3ed55c	1144646050	No	Fiber	2000	2000
fc19593a96f25c82ecd5000ee6e39fcf	1144648519	No	Fiber	2000	2000
a139e101197ab437d719652300a389f2	1413394520	No	Fiber	2000	2000
b82da28a485b76761746cba25dda2e20	1144643461	No	Fiber	2000	2000
b30cb7b95f34b89584c311dd8145aaa3	1144643474	No	Fiber	2000	2000
a5f0cabe523618f8e132346c3e04775a	1144647012	No	Fiber	2000	2000
6845bb46f5e53289a45cc767e595e8e3	1144642653	No	Fiber	2000	2000
c96eed80c35b7ef96931de851974894f	1144648523	No	Fiber	2000	2000
ffdcc8573baf313f748ae8f8db6bfc55	1144641630	No	Fiber	2000	2000
32240070429d71c26b14684108e3a8ea	1144651660	No	Fiber	2000	2000
bbeee64a217280af0d5819efd2cdbbff	1144648528	No	Fiber	2000	2000
e9fbe9cde12398cd5e948b3d510b6da0	1144648542	No	Fiber	2000	2000
69712366d34258d6443cd03204b7bea1	1144648526	No	Fiber	2000	2000
80578c5eeb69a4801ab5e2c1801ef3d2	1144649223	No	Fiber	2000	2000
9c5725063490bdf082b893bc50a4d797	1144651642	No	Fiber	2000	2000
9297fc060b3ab9704e7d54e8ab6ab049	1144647052	No	Fiber	2000	2000
888590f7308d9a63c3deace2df9de5b1	1144646138	No	Fiber	2000	2000
ad64d0df1677258fbe848664304c82c3	1144649226	No	Fiber	2000	2000
85317b609fcf64ccb9d11dc1a749ed60	1144642038	No	Fiber	2000	2000
a697f8546405089dca44adfd6d984540	1144646107	No	Fiber	2000	2000
e1d0df172016fee62c9297d3a1f0dbc9	1144648541	No	Fiber	2000	2000
a776a8496be456494addcd8c7c8deffa	1144649208	No	Fiber	2000	2000
1bba769e6b000661745cb60a3b8a9e96	1144646036	No	Fiber	2000	2000
18059635cf19c5bc90e08770add3ddf0	1144648547	No	Fiber	2000	2000
10cea60b3d9fb957fdf04c7e963cfa69	1144642243	No	Fiber	2000	2000
66895aa6e113578901098bc106314826	1384956506	No	Fiber	2000	2000
7a88f9306160eafc4d6bb59d184cb6dc	1144647058	No	Fiber	2000	2000
926dd7d27f50e24ea87c9d3d919ef7fd	1144645944	No	Fiber	2000	2000
dc50c509cc4c347ec12e0f071fdfcb21	1144646112	No	Fiber	2000	2000
ed4005e4002317002d12ae0fc90b07ca	1384956507	No	Fiber	2000	2000
5a540517462100fa58dc3d55022f3bd4	1144646553	No	Fiber	2000	2000
70838b52d703b04bc6d05d2bd69e6f57	1144646137	No	Fiber	2000	2000
b88dfd0e85946ab24e0aa2aee01a6d87	1384962860	No	Fiber	2000	2000
256237ffcf523f6c86dfab2298718fa0	1144646095	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
bf78977bb952addb52b27d3ad6513075	1144647027	No	Fiber	2000	2000
d3185e00fb36f44125a1f0df382d803f	1144641480	No	Fiber	2000	2000
22580c82ddf8500ddaabf21d8c2cdca6	1144648517	No	Fiber	2000	2000
5ac4909e199a3769571ec07fcd022e57	1144646100	No	Fiber	2000	2000
b26fee507689f95dd0a6f3d78858b091	1144643473	No	Fiber	2000	2000
23f08e29cd94c046337fb342b31dfe9b	1144646040	No	Fiber	2000	2000
eac00c8b3d9553832459329692efba68	1144648555	No	Fiber	2000	2000
46e1f3ff7665b91fdad1dde580e928ef	1144646559	No	Fiber	2000	2000
64347fe74fd348a4e356335dd3ecc215	1144642267	No	Fiber	2000	2000
3e7026c0bd08006f92275712f5f2ca03	1144643462	No	Fiber	2000	2000
45947cc125150297c9213f9015cf65b4	1144646299	No	Fiber	2000	2000
3701cb3cbc1eb8707c2246087eed3378	1144651657	No	Fiber	2000	2000
bd2fa5a271334f75c89033564eb8d480	1144646142	No	Fiber	2000	2000
07b1686346e7f544bf6e8ffa7a66e3c4	1144649213	No	Fiber	2000	2000
7f4a0e9bd38b3cdbd07db32b0aa588b3	1144649210	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 27 – Budget for Project Area IBO-992

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT Installation labor	Installation of OLT in the central office	Construction Services	$1,212.00	$599.00	$613.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$5,670.00	$2,804.00	$2,866.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$10,690.00	$5,286.00	$5,404.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$11,286.00	$5,581.00	$5,705.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$109,572.00	$54,183.00	$55,389.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$39,764.00	$19,663.00	$20,101.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$72,520.00	$0.00	$72,520.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$369,788.00	$182,770.00	$187,018.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$324,540.00	$160,406.00	$164,134.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$96,330.00	$47,612.00	$48,718.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$21,000.00	$10,379.00	$10,621.00
Permitting Costs	Permitting Costs	Professional Services	$88,953.00	$43,966.00	$44,987.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$105,015.00	$51,904.00	$53,111.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Pole Attachments	Pole Make Ready Costs	Professional Services	$93,830.00	$46,376.00	$47,454.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$5,523.00	$2,731.00	$2,792.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$18,291.00	$9,040.00	$9,251.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$153,860.00	$0.00	$153,860.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$14,715.00	$7,274.00	$7,441.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$4,578.00	$2,266.00	$2,312.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$45,000.00	$22,252.00	$22,748.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 27 – Disbursement Schedule for Project Area IBO-992

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 27 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-992

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 27 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 28 –Subaward Conditions and Statement of Work for Project Area IBO-1022

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$36,087.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$36,087.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$36,087.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 28 - Specific Award Conditions for Project Area IBO-1022.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[69.45%]; [$82,036.00]
Total Project Cost = (subaward funds + match)	$118,123.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$36,087.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-1022 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 28**. The Project Area is depicted in the map in **Appendix A of this Exhibit 28**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 28**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $82,036.00, which is 69.45% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 69.45% for a total match of $82,036.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 28** in the area depicted in **Appendix A of this Exhibit 28**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 28**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 28 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 28;
- Appendix A to this Exhibit 28 – Map of Project Area IBO-1022;
- Appendix C to this Exhibit 28 – Budget for Project Area IBO-1022;
- Appendix E to this Exhibit 28 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1022;
- Appendix F to this Exhibit 28 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 28 – Project Area
- Paragraph 5.B(2) of Exhibit 28 – Project Locations
- Paragraph 5.B(3) of Exhibit 28 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 28 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 28 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 28 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 28 – Access to Service
- Paragraph 5.B(5)e of Exhibit 28 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 28 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 28 – Map of Project Area IBO-1022

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-1022

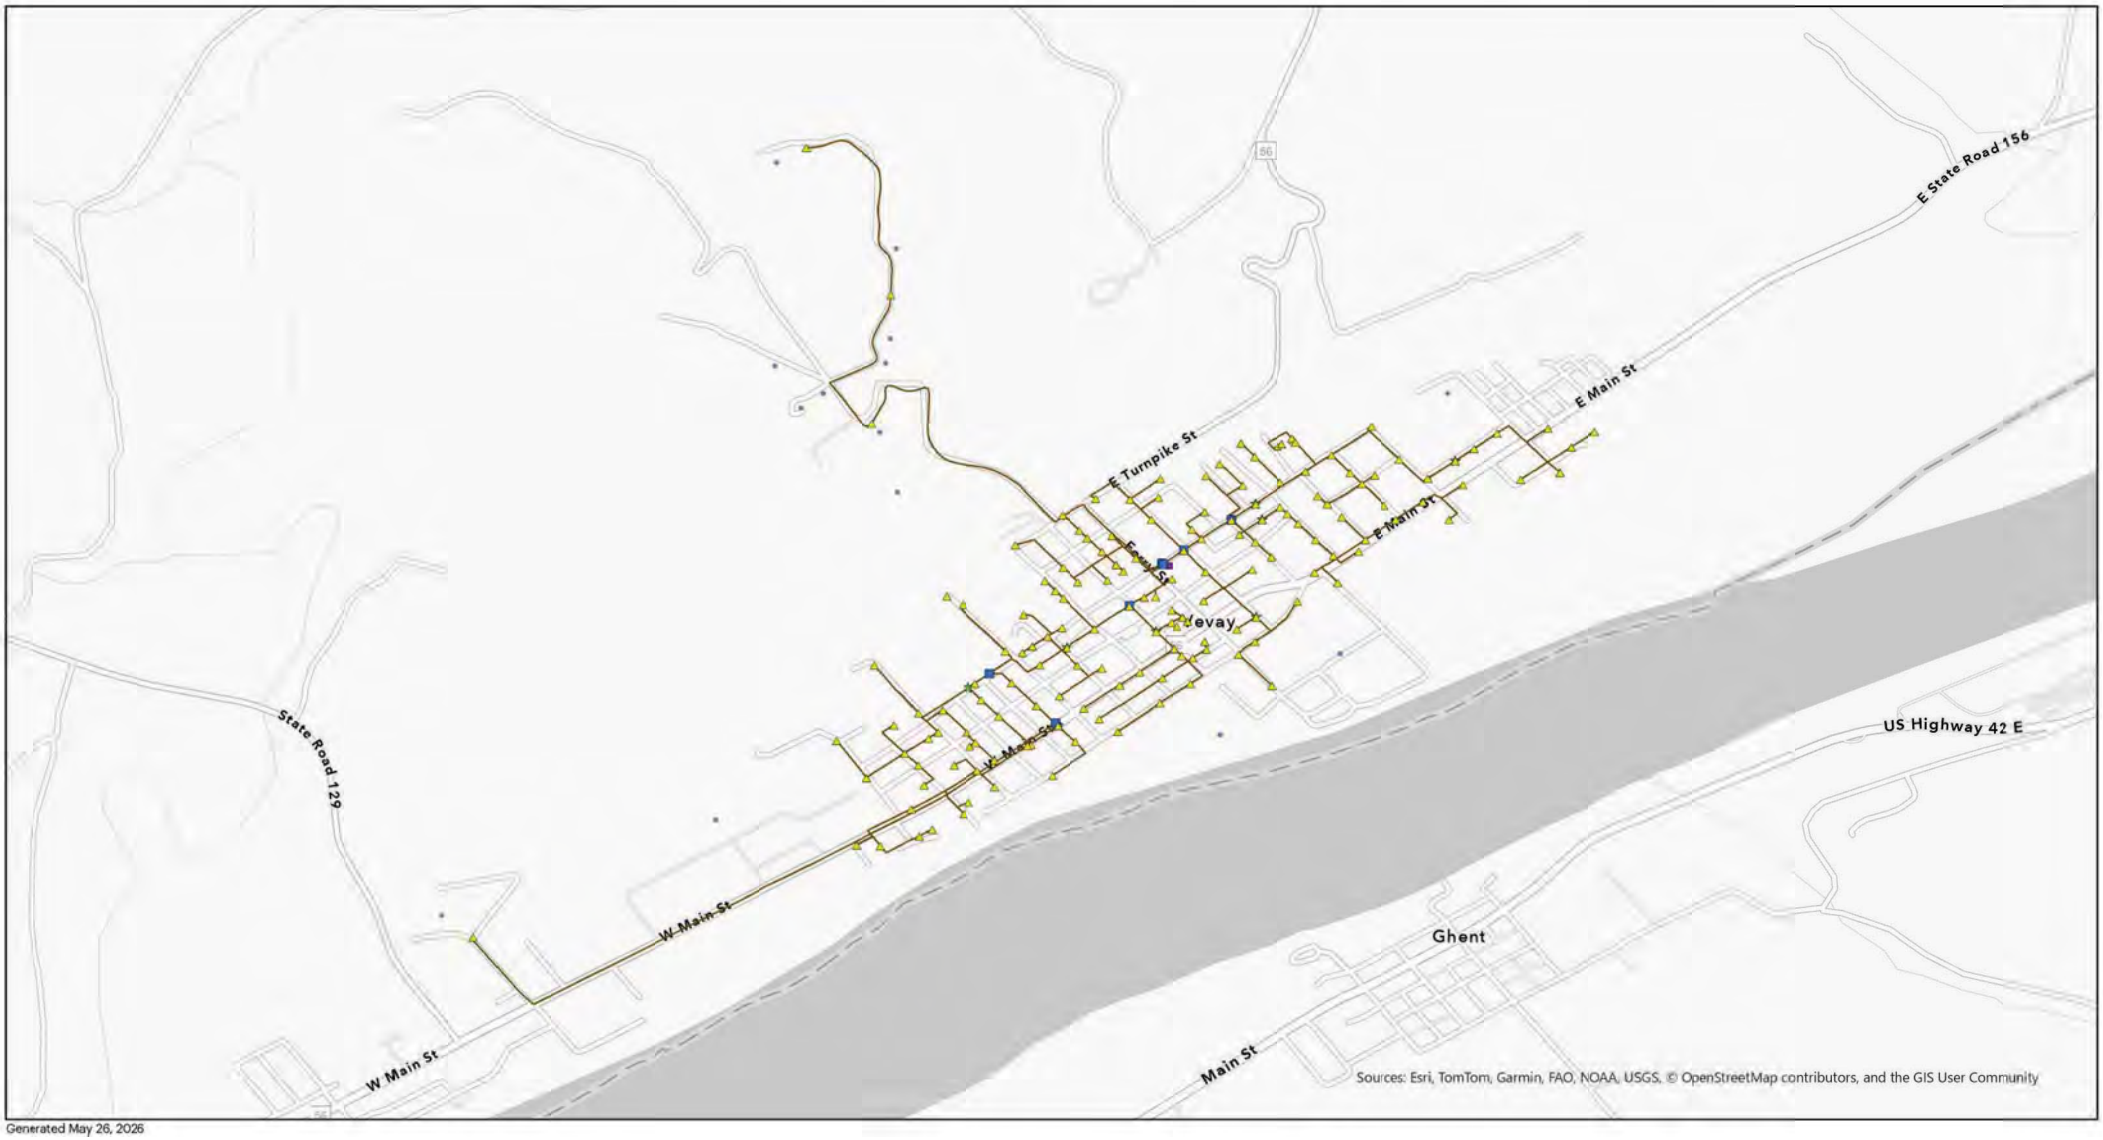

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 28 – List of Locations in Project Area IBO-1022

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed Location List

14 locations

ID	Location ID	Is CAI	Technology	Upload	Download
8b3673c15acb02d1274ed465ef8f5aec	1009936505	No	Fiber	2000	2000
9dcba4f1f2117c1beda019f3a5371176	1009936551	No	Fiber	2000	2000
213243c6a88647f0b87ae45ac0be5436	1009937270	No	Fiber	2000	2000
d26e7f865b4e7dc344f89e6691a39e85	1009937265	No	Fiber	2000	2000
1845a6d57d56562f74d305754c887701	1009937664	No	Fiber	2000	2000
66fa1dfcc77ce40ade97b523309913d1	1009937271	No	Fiber	2000	2000
37a1ca93ccfe18636556ff6941ea173b	1009937700	No	Fiber	2000	2000
ac9304cb135b0bf1f87244dce0014eb0	1009937266	No	Fiber	2000	2000
f4a8085099d18c2558a52bccb138abb1	1009937268	No	Fiber	2000	2000
127b31dadfc7b3856def834abc06f98c	1009937261	No	Fiber	2000	2000
c91e08045c3f5fbc42da552222222622	1009937707	No	Fiber	2000	2000
2d9730ce68882ea379cf7eb5ac9bed2e	1009937023	No	Fiber	2000	2000
a3bf1937127f479342e2729e065e12e2	1009937016	No	Fiber	2000	2000
77b8ac606bfd1b29b0370ddad1997efa	1009934565	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 28 – Budget for Project Area IBO-1022

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$3,000.00	$1,030.00	$1,970.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$450.00	$154.00	$296.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$1,069.00	$367.00	$702.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$526.00	$181.00	$345.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$891.00	$306.00	$585.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$4,144.00	$0.00	$4,144.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$440.00	$150.00	$290.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$1,500.00	$515.00	$985.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$1,250.00	$428.00	$822.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$96.00	$33.00	$63.00
Permitting Costs	Permitting Costs	Professional Services	$6,851.00	$2,350.00	$4,501.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$7,410.00	$2,542.00	$4,868.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$1,407.00	$483.00	$924.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$8,792.00	$0.00	$8,792.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$8,439.00	$2,896.00	$5,543.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$3,062.00	$1,051.00	$2,011.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$8,088.00	$2,775.00	$5,313.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$7,226.00	$2,479.00	$4,747.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$28,480.00	$9,770.00	$18,710.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$25,002.00	$8,577.00	$16,425.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 28 – Disbursement Schedule for Project Area IBO-1022

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 28 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1022

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 28 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 29 –Subaward Conditions and Statement of Work for Project Area IBO-886

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 29 - Specific Award Conditions for Project Area IBO-886.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$46,292.00]
Total Project Cost = (subaward funds + match)	$46,292.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-886 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 29**. The Project Area is depicted in the map in **Appendix A of this Exhibit 29**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 29**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $46,292.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $46,292.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 29** in the area depicted in **Appendix A of this Exhibit 29**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 29**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 29 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 29;
- Appendix A to this Exhibit 29 – Map of Project Area IBO-886;
- Appendix C to this Exhibit 29 – Budget for Project Area IBO-886;
- Appendix E to this Exhibit 29 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-886;
- Appendix F to this Exhibit 29 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 29 – Project Area
- Paragraph 5.B(2) of Exhibit 29 – Project Locations
- Paragraph 5.B(3) of Exhibit 29 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 29 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 29 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 29 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 29 – Access to Service
- Paragraph 5.B(5)e of Exhibit 29 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 29 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 29 – Map of Project Area IBO-886

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-886

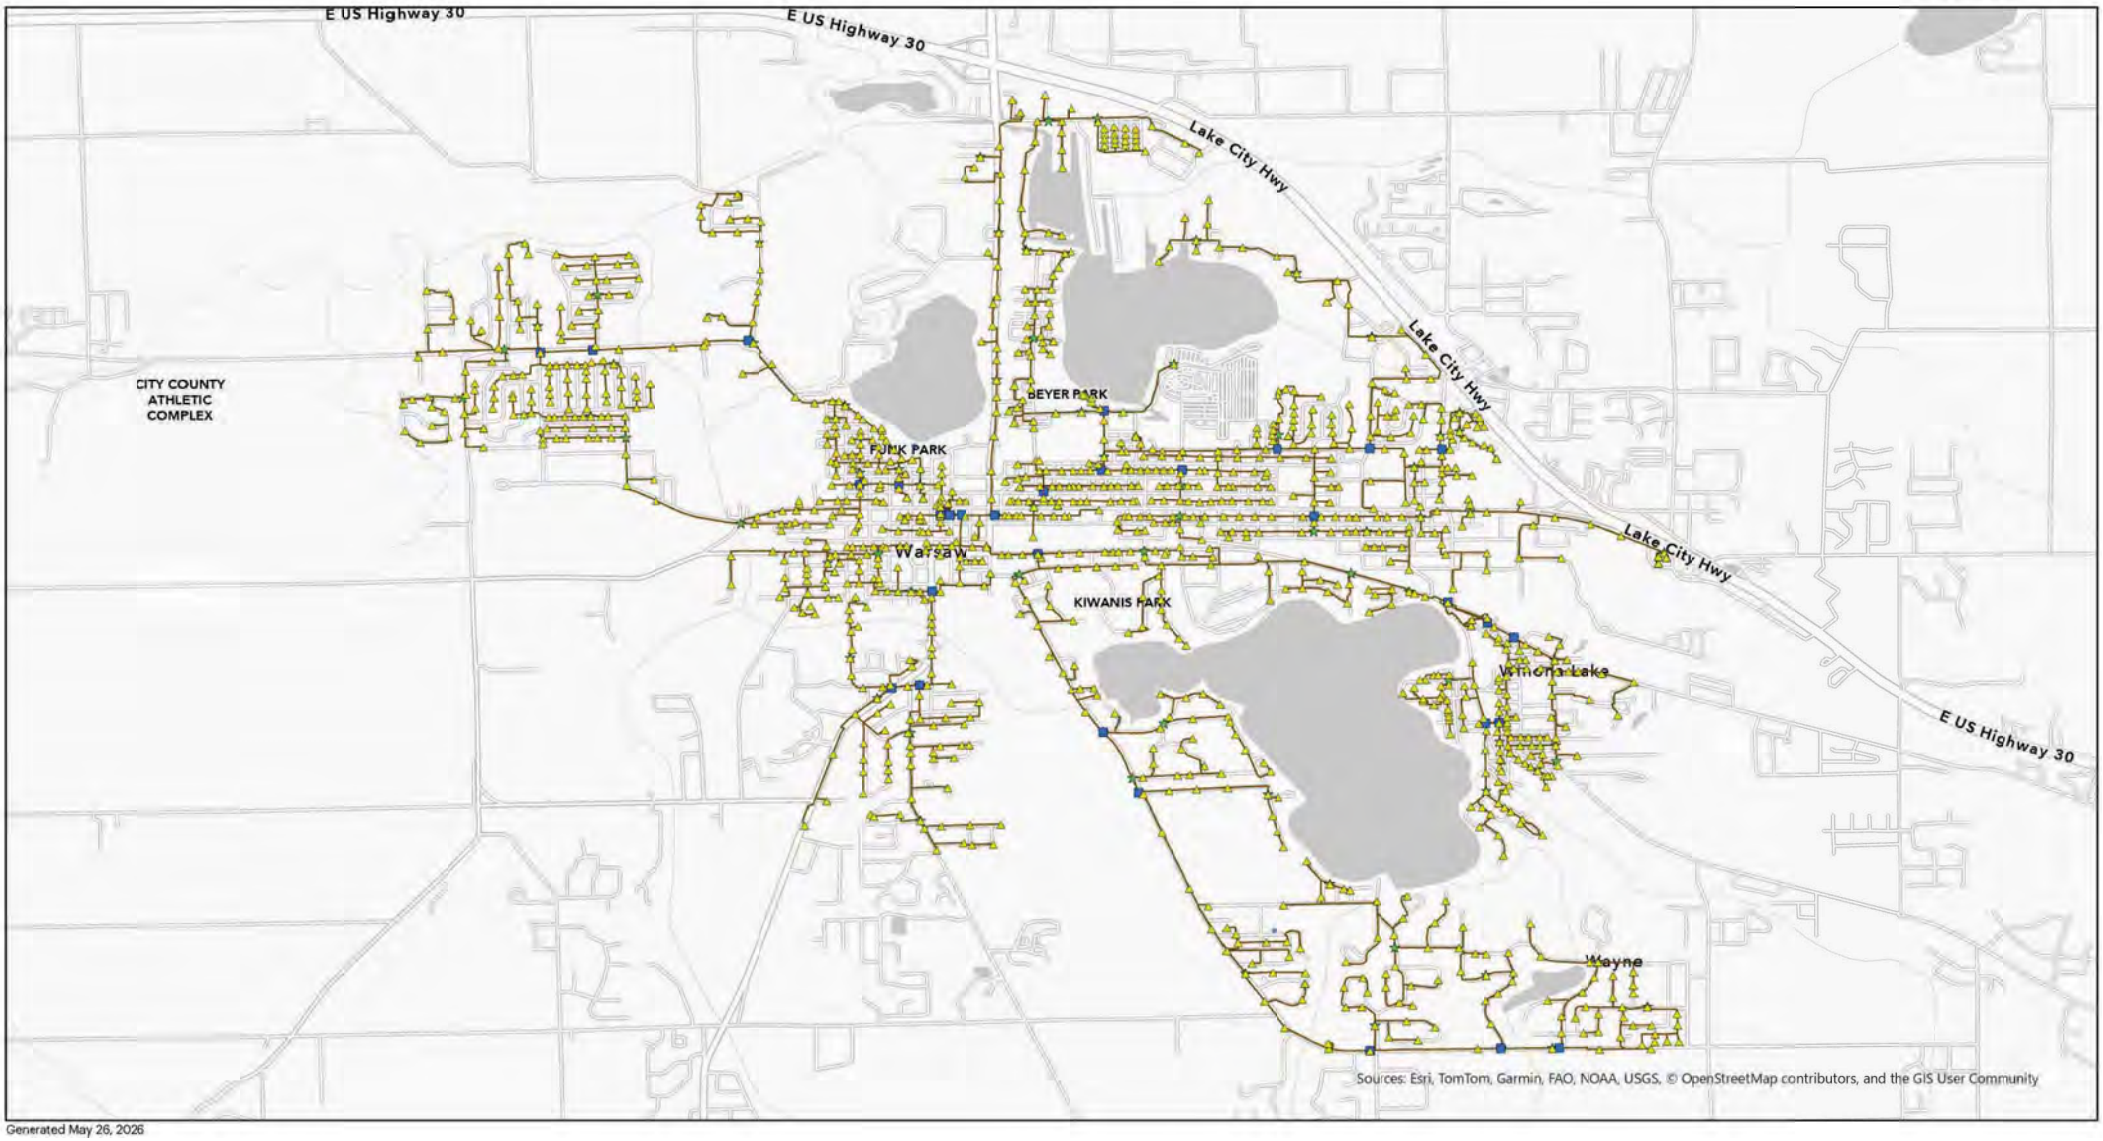

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 29 – List of Locations in Project Area IBO-886

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-886 Location List

2 locations

ID	Location ID	Is CAI	Technology	Upload	Download
283a03506e493c71020d940d70ddd163	1292832649	No	Fiber	2000	2000
a4fce105b1c2e7a5e514f404f478806e	1292829240	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 29 – Budget for Project Area IBO-886

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$1,256.00	$0.00	$1,256.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$537.00	$0.00	$537.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$750.00	$0.00	$750.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$36.00	$0.00	$36.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$455.00	$0.00	$455.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$3,053.00	$0.00	$3,053.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$3,135.00	$0.00	$3,135.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$469.00	$0.00	$469.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$263.00	$0.00	$263.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$297.00	$0.00	$297.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$3,566.00	$0.00	$3,566.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$1,294.00	$0.00	$1,294.00
Permitting Costs	Permitting Costs	Professional Services	$2,894.00	$0.00	$2,894.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$3,417.00	$0.00	$3,417.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$12,032.00	$0.00	$12,032.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$10,566.00	$0.00	$10,566.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$592.00	$0.00	$592.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$1,500.00	$0.00	$1,500.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$180.00	$0.00	$180.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 29 – Disbursement Schedule for Project Area IBO-886

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 29 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-886

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 29 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 30 –Subaward Conditions and Statement of Work for Project Area IBO-1001

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$1,459.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$1,459.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$1,459.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 30 - Specific Award Conditions for Project Area IBO-1001.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[98.74%]; [$114,716.00]
Total Project Cost = (subaward funds + match)	$116,175.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$1,459.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-1001 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 30**. The Project Area is depicted in the map in **Appendix A of this Exhibit 30**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 30**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $114,716.00, which is 98.74% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 98.74% for a total match of $114,716.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 30** in the area depicted in **Appendix A of this Exhibit 30**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 30**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 30 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 30;
- Appendix A to this Exhibit 30 – Map of Project Area IBO-1001;
- Appendix C to this Exhibit 30 – Budget for Project Area IBO-1001;
- Appendix E to this Exhibit 30 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1001;
- Appendix F to this Exhibit 30 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 30 – Project Area
- Paragraph 5.B(2) of Exhibit 30 – Project Locations
- Paragraph 5.B(3) of Exhibit 30 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 30 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 30 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 30 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 30 – Access to Service
- Paragraph 5.B(5)e of Exhibit 30 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 30 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 30 – Map of Project Area IBO-1001

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-1001

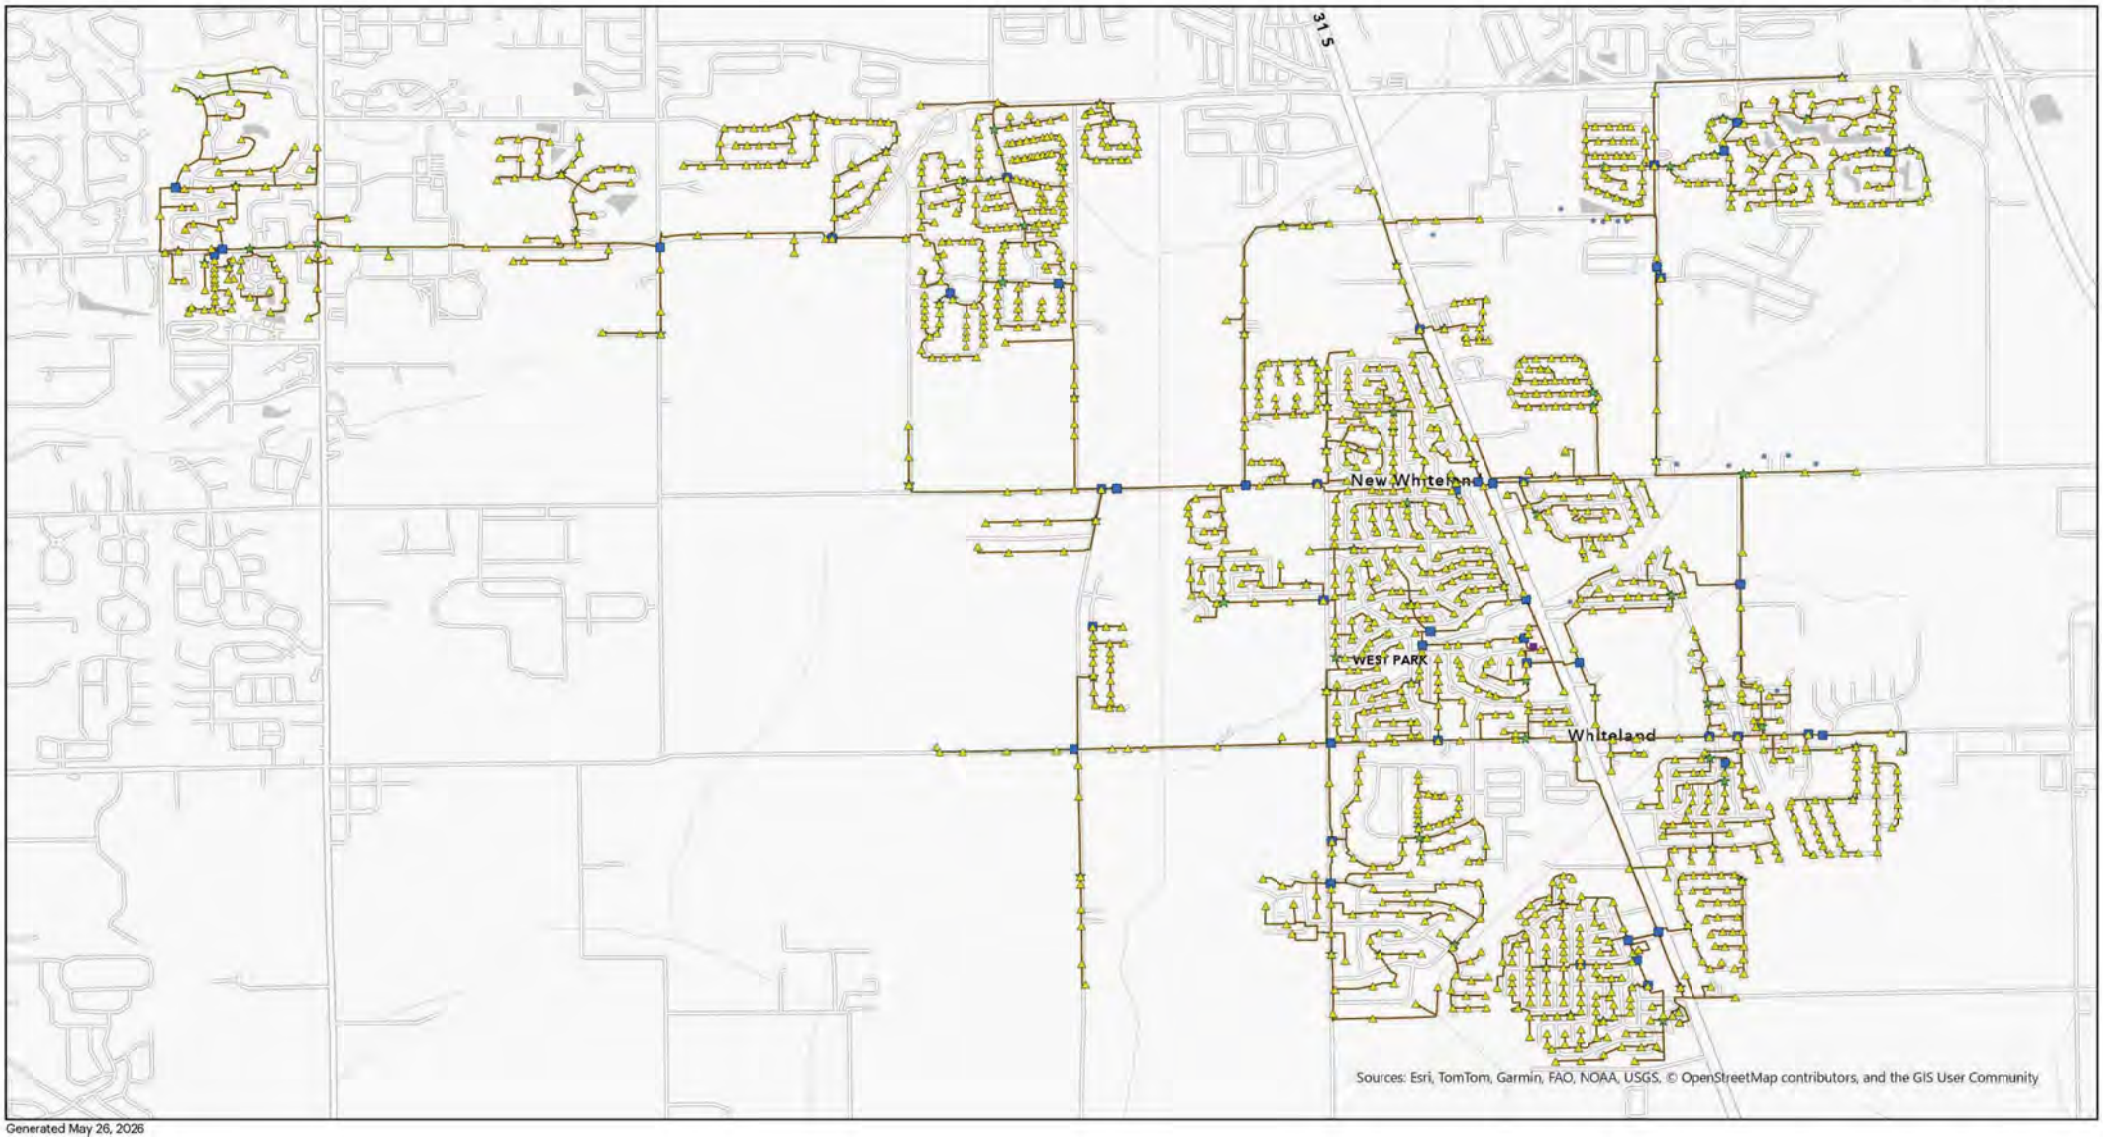

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 30 – List of Locations in Project Area IBO-1001

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-1001 Location List

13 locations

ID	Location ID	Is CAI	Technology	Upload	Download
0832d9501a26cc3c7853cd532fabf319	1043887481	No	Fiber	2000	2000
e649f6149756b5cc9a2f8cc53d4e529d	1043872181	No	Fiber	2000	2000
6f51f85a0c4d1604332a0b04e9758257	1043924966	No	Fiber	2000	2000
dfe3e77d149e8b0d6a82460a39c79d17	1043873549	No	Fiber	2000	2000
d8b17607a43261b8508c021268b08ae2	1043926555	No	Fiber	2000	2000
d912c23b2a51cb80231a269b07121d03	1043872190	No	Fiber	2000	2000
e69028d43c1472cab3ed316b6c70e52f	1043925658	No	Fiber	2000	2000
52fa049db328b9de7ae0dfa2ccdfb880	1043872197	No	Fiber	2000	2000
592fd2288b2c8b7063d2e71d85e81683	1043872170	No	Fiber	2000	2000
ec172c1f5add15fe8bce5dbade7b314e	1043872236	No	Fiber	2000	2000
73c4797e1bf62efba35750ff78a8d184	1043873562	No	Fiber	2000	2000
7cff41666902486a0e449bd6ea837d4b	1043873553	No	Fiber	2000	2000
c29d943012fa4120f2834880d79d9276	1043873558	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 30 – Budget for Project Area IBO-1001

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Pole Attachments	Pole Make Ready Costs	Professional Services	$7,093.00	$100.00	$6,993.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$27,952.00	$395.00	$27,557.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$891.00	$13.00	$878.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$1,069.00	$15.00	$1,054.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$526.00	$7.00	$519.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$96.00	$1.00	$95.00
Permitting Costs	Permitting Costs	Professional Services	$6,724.00	$95.00	$6,629.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$7,938.00	$112.00	$7,826.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$8,792.00	$0.00	$8,792.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$1,134.00	$17.00	$1,117.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$4,144.00	$0.00	$4,144.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$3,006.00	$42.00	$2,964.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$24,534.00	$347.00	$24,187.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$7,315.00	$103.00	$7,212.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$450.00	$6.00	$444.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$3,000.00	$42.00	$2,958.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$8,283.00	$117.00	$8,166.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$321.00	$6.00	$315.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$1,500.00	$21.00	$1,479.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$1,407.00	$20.00	$1,387.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 30 – Disbursement Schedule for Project Area IBO-1001

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 30 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1001

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 30 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 31 –Subaward Conditions and Statement of Work for Project Area IBO-910

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$828,316.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$828,316.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$828,316.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 31 - Specific Award Conditions for Project Area IBO-910.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[65.34%]; [$1,561,605.00]
Total Project Cost = (subaward funds + match)	$2,389,921.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$828,316.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-910 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 31**. The Project Area is depicted in the map in **Appendix A of this Exhibit 31**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 31**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $1,561,605.00, which is 65.34% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 65.34% for a total match of $1,561,605.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 31** in the area depicted in **Appendix A of this Exhibit 31**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 31**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 31 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 31;
- Appendix A to this Exhibit 31 – Map of Project Area IBO-910;
- Appendix C to this Exhibit 31 – Budget for Project Area IBO-910;
- Appendix E to this Exhibit 31 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-910;
- Appendix F to this Exhibit 31 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 31 – Project Area
- Paragraph 5.B(2) of Exhibit 31 – Project Locations
- Paragraph 5.B(3) of Exhibit 31 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 31 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 31 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 31 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 31 – Access to Service
- Paragraph 5.B(5)e of Exhibit 31 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 31 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 31 – Map of Project Area IBO-910

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-910

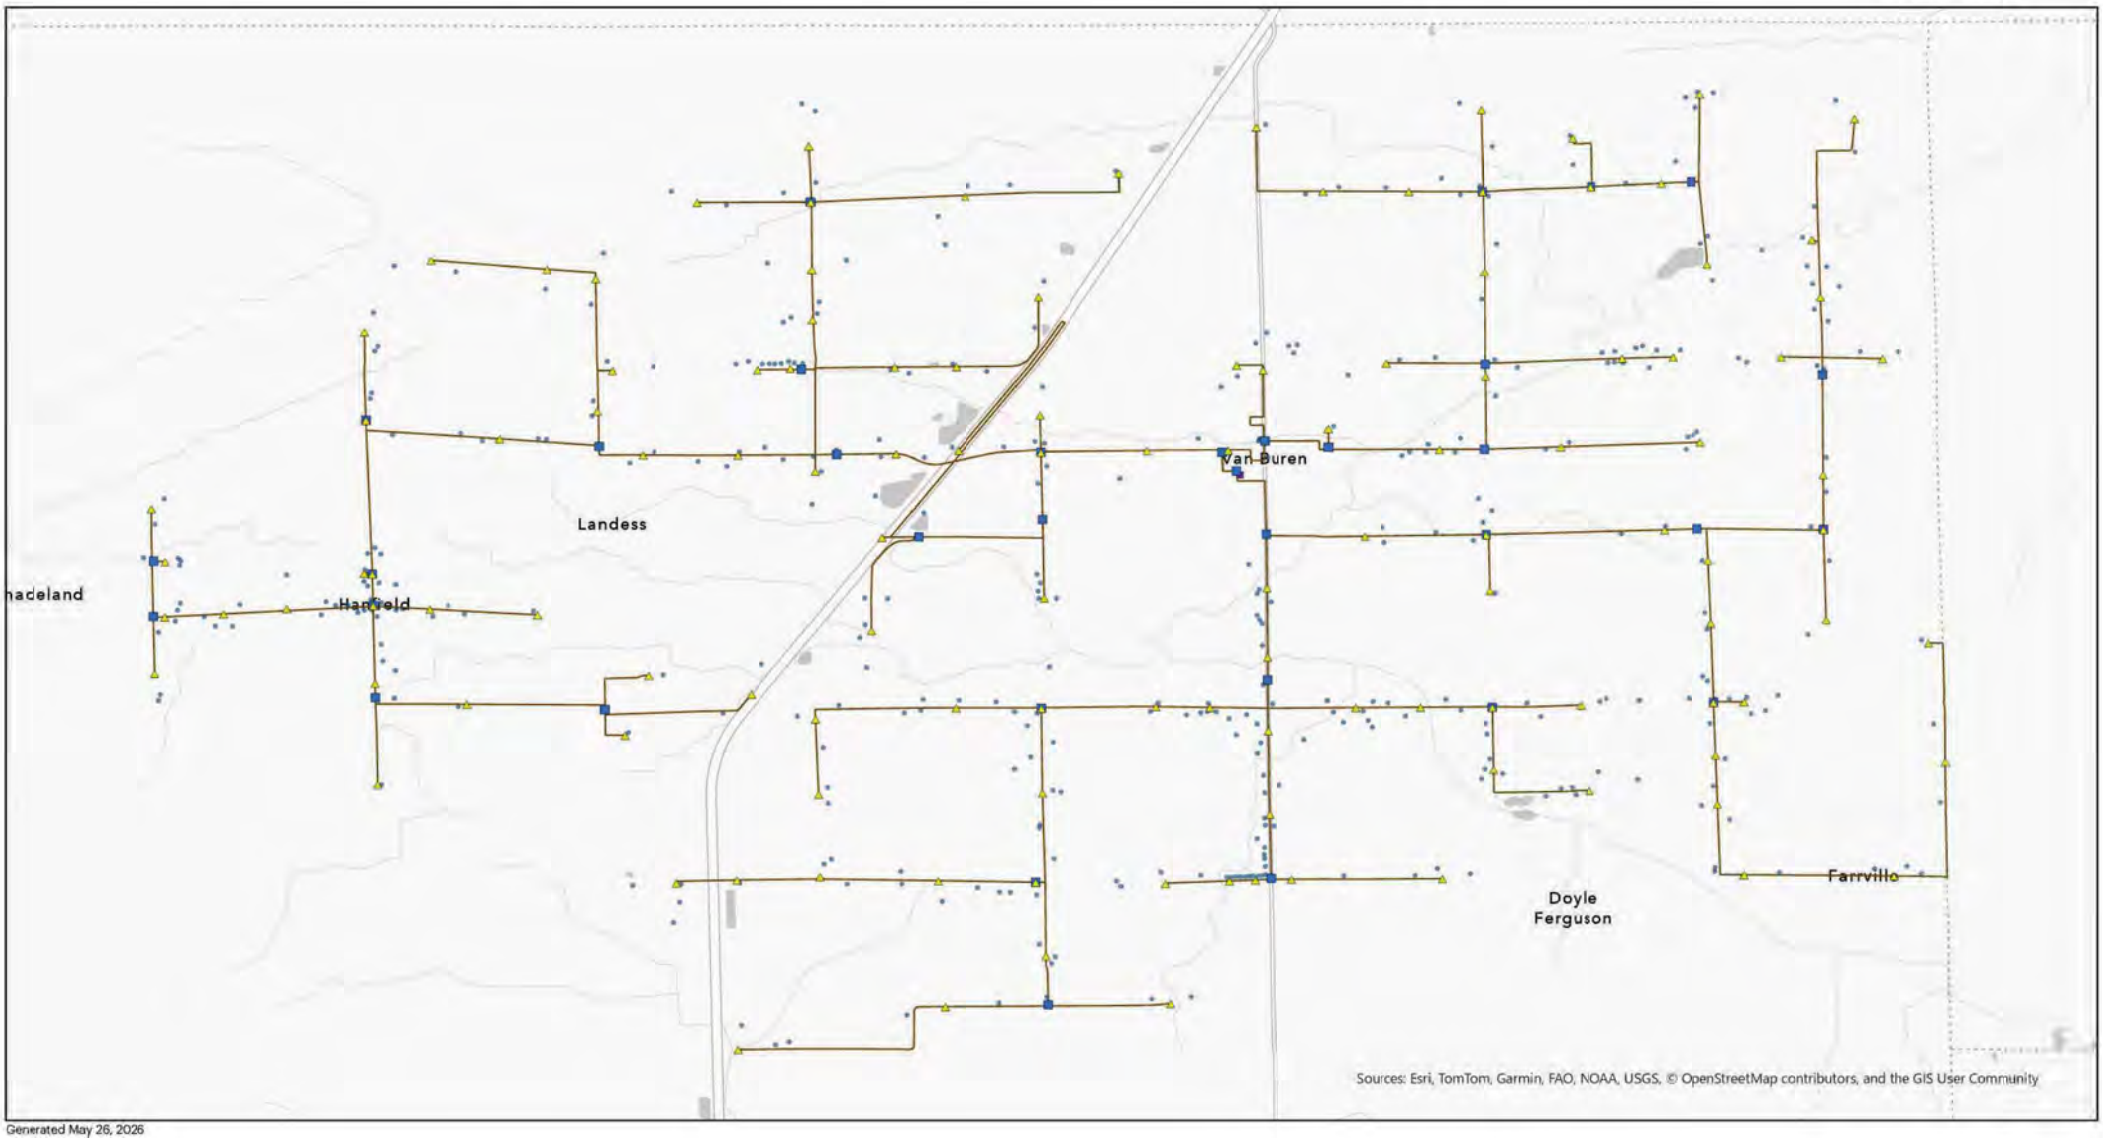

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 31 – List of Locations in Project Area IBO-910

Brightspeed IBO-910 Location List

387 locations

ID	Location ID	Is CAI	Technology	Upload	Download
4b8695423afff7633289e5f7cb13f324	1045125883	No	Fiber	2000	2000
cdef6e86b5921994892c46d110b2d08f	1045125139	No	Fiber	2000	2000
d1fde370f5a1f80aabd35368f08bef9a	1045112765	No	Fiber	2000	2000
a3054dbd65ff0f789a991a4f7b2d6270	1045113356	No	Fiber	2000	2000
35ae66344610f0c37083d4a4a29583d0	1045112759	No	Fiber	2000	2000
f05e6910fa6d3fe232914dea8c9a4974	1045113066	No	Fiber	2000	2000
15dcc1d0a9f476e30b1de661de1cc70b	1045113082	No	Fiber	2000	2000
e427fb0a5362aff61b860e8cecdd884f	1045113774	No	Fiber	2000	2000
064df91d6dc624246735e94143222a0a	1045113650	No	Fiber	2000	2000
f17db369b48b78c85b647fc00bfdc172	1045134321	No	Fiber	2000	2000
0187841dc3467d21d3e7fbf1ca871ddb	1045125900	No	Fiber	2000	2000
9e0944c6bceffb3a5e5cf36572d2a2a6	1045125444	No	Fiber	2000	2000
35d3152ac4c6af46b43cdfab3d8314c0	1045130669	No	Fiber	2000	2000
88ec21a37edb9332af9fb2bcb4ed6677	1045113206	No	Fiber	2000	2000
d00d92d33ec8fe3f891bead9e9652976	1045125446	No	Fiber	2000	2000
7081c377de161e973d9185e39f3f97a1	1045112907	No	Fiber	2000	2000
61b97cf8733e4e402b1df1961e99e483	1045125136	No	Fiber	2000	2000
3fa01d8229e58383fc16f1076049bc29	1045113768	No	Fiber	2000	2000
a38efdac4aad50bd657195d035dcf647	1045125452	No	Fiber	2000	2000
b630de5aaea1833d27bb5d3b95e0bbc3	1045112829	No	Fiber	2000	2000
27aa827333c58d279c412a13ef12fca2	1045125431	No	Fiber	2000	2000
72b71b608c2fece7f1bba424c983aeba	1045112912	No	Fiber	2000	2000
f17228e495e7f5d04b6aff17bfa38d24	1045125453	No	Fiber	2000	2000
7df61a6f8fcf353cd431bc0edd334760	1045113044	No	Fiber	2000	2000
24cb071d35f4d2e3541b6010044953b6	1045113652	No	Fiber	2000	2000
a7f729f04b3c4570173c7608a8117ee1	1045113769	No	Fiber	2000	2000
109c23ed688cb98e323215ab017d66aa	1045112898	No	Fiber	2000	2000
3938fad78ba411f3cad51e11818624c8	1045113821	No	Fiber	2000	2000
6767694fc4688dd0944f43b8ce469c91	1045112756	No	Fiber	2000	2000
7953b2147327d1bf8a88dc1335fa7b86	1045112897	No	Fiber	2000	2000
9a3ecc19257c110add7b16c137bd90e4	1045125884	No	Fiber	2000	2000
ba9ebdad60985bfd848cfb1c61041bc8	1045125922	No	Fiber	2000	2000
c236b04be3349ceb1169340b738bb1ce	1045125898	No	Fiber	2000	2000
ab119031d0e70d5c412995562c16ba07	1413410714	No	Fiber	2000	2000
cb94a3e24a137a00de2bbf1f0504ce0c	1045113682	No	Fiber	2000	2000
d55f63581127e12cfea26426112834a8	1045125477	No	Fiber	2000	2000
90ee005598dc5e1473d6caa304e51caf	1045112891	No	Fiber	2000	2000
bb57207e3ab2011b1c1ba9aff064963e	1045126842	No	Fiber	2000	2000
5fef8b90936455d93d4eebc5909f09b1	1045125897	No	Fiber	2000	2000
7c7242c557d1c5fbdbea29c3e5149378	1045130678	No	Fiber	2000	2000
6de62ea3f95ef9c8ac0502f90849b7a4	1045113759	No	Fiber	2000	2000
f5b8d766206d52bd0f9548d37c091e24	1045112749	No	Fiber	2000	2000
335b7ae0809215b06dfdb0538f1cad3b	1045113361	No	Fiber	2000	2000
3ea5127ce61a854656108245fa309b6a	1045125906	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
9ec35f248f2f18d6ca56a373e700a713	1045125448	No	Fiber	2000	2000
f132c5e6102137f7fbfe19e763800f96	1045113340	No	Fiber	2000	2000
b40c6e5d48dfce238937b75e8601f644	1045113789	No	Fiber	2000	2000
d01509c34acdfdec772304cb7d0d3b4f	1045113760	No	Fiber	2000	2000
671c5925753bdc80af86b7e0508ba27b	1045113761	No	Fiber	2000	2000
6d7b48c1eb14c575acba606f1e948dbb	1045125460	No	Fiber	2000	2000
b5b63c9117a1c3aabf2971a5496d0524	1045126836	No	Fiber	2000	2000
ae413e528b759349f5cd66fd50d2c6ce	1045113324	No	Fiber	2000	2000
101da0fef55206837d4f9b66428ed7ca	1045126854	No	Fiber	2000	2000
e280037a33be3d278397beca89eba625	1385356793	No	Fiber	2000	2000
47016c17edd1fd919b2bc390ea674f9d	1045125768	No	Fiber	2000	2000
7967395514ade5676b1f4ab2cd245323	1045125912	No	Fiber	2000	2000
e586f226415516e06dd522d27d7ab828	1045113762	No	Fiber	2000	2000
e4c1aefaa926a8aac75af8e8712c67cf	1045125467	No	Fiber	2000	2000
dcffd122b01253dda4007e65ba6b1a59	1045125773	No	Fiber	2000	2000
1676186d5377191d4274dcc70953cd08	1045113696	No	Fiber	2000	2000
b5792e78a30ccadcececca112d1f4a42	1045129063	No	Fiber	2000	2000
7cb41bac102199476bdbda745e70fac5	1045125903	No	Fiber	2000	2000
809d9ecb8739e5105a408798463cb4b5	1045125891	No	Fiber	2000	2000
4e2b8288308195e52dc8d1004c6f2bb0	1045113540	No	Fiber	2000	2000
7fede4ae3f34992b79f1b21367754331	1045125455	No	Fiber	2000	2000
a67b3ebbc74c6d0bb51a4cc97e95a934	1045125437	No	Fiber	2000	2000
d8c687303519da059ee1f0f07d56a3b3	1045113805	No	Fiber	2000	2000
a10eaee8fccea387556b8a0e153e6fc3	1045113537	No	Fiber	2000	2000
9780bfb769ece03b73519f6c99579da8	1045112766	No	Fiber	2000	2000
e9bb15a71d55a930ef1f9732f257f504	1045125907	No	Fiber	2000	2000
42fc5b37976abe4cc6115a32e533ab46	1045134111	No	Fiber	2000	2000
f1747497b780987d0a37981b6d180351	1045130688	No	Fiber	2000	2000
0c39b4d35f79542e11763a188ad6ae35	1045129099	No	Fiber	2000	2000
14ff7bab81d7f1dc279b7f80a5b2de09	1045125458	No	Fiber	2000	2000
88fe003e003049f307e410e4f6d80666	1045113772	No	Fiber	2000	2000
7bfc29cf2fbe83cd8ab2cc7cd3a6d172	1045113358	No	Fiber	2000	2000
d880cdfb650e1cea9a37c2121249ca35	1045112914	No	Fiber	2000	2000
f8d267947b8c0bd40731ced72b5c18be	1045125893	No	Fiber	2000	2000
1f9e9f943cb9d6cc30096068cfe57d8a	1045125501	No	Fiber	2000	2000
4b97a942d005ea04a93df97acf3e6b5a	1045125445	No	Fiber	2000	2000
4a99db16650afa5f77322e27c9a5c744	1045113203	No	Fiber	2000	2000
f7dc57416b72f2e0d67c0e704221be6b	1045113334	No	Fiber	2000	2000
8c63bc4867e54619c6b1af3f28ec86fe	1045113668	No	Fiber	2000	2000
fee1741def41051fd0b2ababe8d07d19	1045134029	No	Fiber	2000	2000
334afdfb12a6114eb25da4a6319f2e05	1045113815	No	Fiber	2000	2000
e63cfb98f721283f3656e688c1472135	1045125899	No	Fiber	2000	2000
b8dd2f2ca3eceac88cd2ba9fde47f6dc	1045113064	No	Fiber	2000	2000
64229ec35b714afb955c6c87c567cdda	1045112737	No	Fiber	2000	2000
e48dd12706749c6c3ca4e1f5d534a3cc	1045134032	No	Fiber	2000	2000
b0672024451beca4cfaa16b4b30f3f1a	1045125441	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
c8c62c37bcc53245f547aa45a6da7280	1045113068	No	Fiber	2000	2000
0e3759c907e1ec1a2b2771c7fc88907e	1045113697	No	Fiber	2000	2000
8edac415c37e9bdc0c1e205700f22112	1045112910	No	Fiber	2000	2000
82b13028fcd439167ba5216c71849325	1045113045	No	Fiber	2000	2000
ae0e8aea46775a4bed8351d4dfa8ffef	1045113771	No	Fiber	2000	2000
bf224265be3254f2cc253b7622104810	1045113781	No	Fiber	2000	2000
15cf728d15fed269d09006d0f66ae621	1045129092	No	Fiber	2000	2000
733a2eb0e1c7dd4740006b1f29ad1b7c	1045125787	No	Fiber	2000	2000
fc1941547966e777c7d6022ecfe472b3	1045125159	No	Fiber	2000	2000
7afbe00c84a9ed08410d78c2809fb2ec	1045125465	No	Fiber	2000	2000
00ade1d64c7b429c9297885ab9aadc71	1045125875	No	Fiber	2000	2000
88c159d12dc1a528dadc388fb35bb746	1045112750	No	Fiber	2000	2000
56ff079334d73d4ed526b3a20354155e	1045125904	No	Fiber	2000	2000
5ddd3c6eefa0eb4940e63fbb8528f63e	1045113817	No	Fiber	2000	2000
d9fc73487dacf6854a268bfcf46f7686	1045113527	No	Fiber	2000	2000
3c15b5a09121cf5394b904418b21a8ad	1045125819	No	Fiber	2000	2000
cd4039de001018d4ff3d5889dbe2536a	1045125886	No	Fiber	2000	2000
838da515b36d83837a3b1c87a1e87eec	1045125926	No	Fiber	2000	2000
3004e5da2a4b5080242fee68bc8db5ab	1045112988	No	Fiber	2000	2000
08cce78d8dedda2b4d55f3c1df3f7119	1045112731	No	Fiber	2000	2000
a0d98558cd6dfc97ad21e2a2c50c6a27	1045113692	No	Fiber	2000	2000
5e06bbcb47c7cf9f60687ae3400840bb	1045130673	No	Fiber	2000	2000
26b58fb989bcd3943ff5989e4fe175fe	1045112923	No	Fiber	2000	2000
41a4ce3da3efb06b68671ba11b1d001d	1045125882	No	Fiber	2000	2000
b4e9de0804f10af78d42276dd126530b	1045113765	No	Fiber	2000	2000
df90db79220dd8f78c1fbe16370b69b7	1045113359	No	Fiber	2000	2000
4b75b69bb34dc5f1a4c0a9720ddf569e	1045125464	No	Fiber	2000	2000
05799683113051l9e05b26e6bc675110	1045112748	No	Fiber	2000	2000
147be154789acb2989c99862bd0ab3c7	1045113060	No	Fiber	2000	2000
d9a570d81f2d96a4af086bd76e760376	1045125450	No	Fiber	2000	2000
994c229007946be320c92bd05e7ef098	1045113083	No	Fiber	2000	2000
cd91be5f3324a79bf7c324c0e6c78269	1385356696	No	Fiber	2000	2000
ad34f6a171a3735647239084e9be6408	1385356549	No	Fiber	2000	2000
557aafb10d4864857666558bf47222f0	1045130677	No	Fiber	2000	2000
5e28d1f6ea062a51161553c85bc83e74	1045125881	No	Fiber	2000	2000
f31ea320d802061436e0550491b8afa9	1045113811	No	Fiber	2000	2000
dcd2f79fd83eabc1d6e7460a1b4856f6	1045130680	No	Fiber	2000	2000
f0bc5ee5ed4522cdde991c663dd9392a	1045125160	No	Fiber	2000	2000
b8eb36f61880843700798bbbd5f435fc	1045113663	No	Fiber	2000	2000
c5988b50a8961f28b89e1edda98c0d96	1045113662	No	Fiber	2000	2000
2378dc3dde59d3d6153fbdda4044f79b	1045113543	No	Fiber	2000	2000
47bdad5766189a66a7db6af0c927d52d	1045113767	No	Fiber	2000	2000
2f22446ab29dd00872b828b3488cf816	1045125430	No	Fiber	2000	2000
90d01d0694195846bf25fa5e8bf9ac51	1045113084	No	Fiber	2000	2000
f5866e5725b01293dd6e3f30d0de6df6	1045113787	No	Fiber	2000	2000
eb3ad68eec85491ed60de2591bb0c9b7	1045112895	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
c0a6e92027e9358458318ae83e1bdecf	1045112767	No	Fiber	2000	2000
067837c2075341b2378aeb9539ccfd48	1045113763	No	Fiber	2000	2000
3f0ed75090c2c65b36f6ecd2a1471791	1045130668	No	Fiber	2000	2000
ee15c125bccc4c1e6bf43df62be7505a	1045113783	No	Fiber	2000	2000
33b96795da975a331a0aa7bc247fdd25	1385359967	No	Fiber	2000	2000
1cc7a2a9273d640bfd79817536d4ba92	1045112769	No	Fiber	2000	2000
133b2022de0ebb2575f4e09a391f78ee	1045134326	No	Fiber	2000	2000
139ca046a1316b1d1cd07840a1041018	1045134323	No	Fiber	2000	2000
d30779c1aebe52d39b096dfd559547bf	1045125916	No	Fiber	2000	2000
21f056544dc08d33bea2797403857aed	1045112836	No	Fiber	2000	2000
4ac284e93b35dfbd5491e4e8eb33c5e0	1045125920	No	Fiber	2000	2000
63410b625def541601e830245e039880	1045112878	No	Fiber	2000	2000
4f08c5ba21a46be74408246d659a2d5d	1045113816	No	Fiber	2000	2000
ca1c4dcaab197a131af82072a4643981	1045112733	No	Fiber	2000	2000
163c806df9d618df8c7cce1489001362	1045113219	No	Fiber	2000	2000
d84986679b1872a761f695378512e9b7	1045112777	No	Fiber	2000	2000
5c12c0c50a8d873fd2c7d6311f1ae5ed	1045125770	No	Fiber	2000	2000
d3fbc03fdf70b6c2d61694550ae774c5	1045125461	No	Fiber	2000	2000
3ba8f883d7fbfe4e2bcef9d71c6539b5	1045129094	No	Fiber	2000	2000
463af1270771e001a4a27516b00e8f17	1045113085	No	Fiber	2000	2000
ca0636c1fc2ae076c2adfb2e2998e0a8	1045113254	No	Fiber	2000	2000
7cc54b73fb90cf3f89fdd9a09c93377a	1045113684	No	Fiber	2000	2000
0080be597c70a532c4a29d9239c06796	1045113204	No	Fiber	2000	2000
f7c0079c9ed5be0eb33df4e1416e9861	1045125888	No	Fiber	2000	2000
75d2d4567b465f405524f5da6bde3f40	1045113672	No	Fiber	2000	2000
c902b849e3f493c39e0d3d0930f36f70	1045113819	No	Fiber	2000	2000
77650b8f84618b1d60accfb729141f9a	1045125781	No	Fiber	2000	2000
7e74da9834d48e24f2b460a5c63986ae	1045125438	No	Fiber	2000	2000
24f3f74ea95fabf0c9748564d3be6676	1045134030	No	Fiber	2000	2000
d95b707e2a4a3fa904f5014f4e6a52d1	1045113544	No	Fiber	2000	2000
d62fe00eec151179d4ddeed38c917754	1385360755	No	Fiber	2000	2000
07f5816159a64fc6de1e07f24d9455cd	1045125778	No	Fiber	2000	2000
44baf7a25446e35c06c3de20cfe06f64	1045125475	No	Fiber	2000	2000
e1fbba601bcedaed476bd78f429285ee	1045125463	No	Fiber	2000	2000
27a99672541744713b8603b283342305	1045112755	No	Fiber	2000	2000
b285c4ba9c123d25ad8191cd00445f79	1045112760	No	Fiber	2000	2000
ec535d1615d966f59f738bdadbe9f958	1045113059	No	Fiber	2000	2000
f75f33b19d4c94518cbe22bf91045ede	1045125873	No	Fiber	2000	2000
f974426280ad751df760275369490634	1045126808	No	Fiber	2000	2000
001db6564fd3903a94e4d3cc6385633b	1045125469	No	Fiber	2000	2000
bcac5f0ff8c36fdae2cb557de0fc5c28	1045125909	No	Fiber	2000	2000
fbde5b0325e7ec9bf6881244298e0dbd	1045125763	No	Fiber	2000	2000
d4161750a664539022558a5665e93bdb	1045113542	No	Fiber	2000	2000
2ffd292c47f2d28ec2a8ba3aca7a08a1	1045125433	No	Fiber	2000	2000
3bbaab7e28f6e6e449e5fe01c209d36b	1045125161	No	Fiber	2000	2000
e86e639653b9896ac2f2345a05b170d1	1045113778	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a5134d420d244910cac674a1b524d901	1045125771	No	Fiber	2000	2000
84a7cd35ec56959ae41fdce10ce43b7c	1045113067	No	Fiber	2000	2000
69f70808a365b5846974c89be018eee1	1045125442	No	Fiber	2000	2000
1f1d5a8494d2f78dd0682ca266218711	1045113087	No	Fiber	2000	2000
7c06dde6456b48d986384c65f76b5e7c		Yes	Fiber	2000	2000
fe3956956454b01100bdb5012ea65f50	1045113786	No	Fiber	2000	2000
fdb8e69e3187013601fa4203350250ec	1045112758	No	Fiber	2000	2000
03ee091d7a480d43afe7898043902798	1045112892	No	Fiber	2000	2000
baf0a2d7ef9293418cf67d685c1bc6e4	1045113528	No	Fiber	2000	2000
e63834a72d027a25c7104de4b430d89a	1045125880	No	Fiber	2000	2000
b8b6a4669f69543bd960013f8ae6bf89	1045125468	No	Fiber	2000	2000
7359b60124126df48b79545210e4061f	1045130666	No	Fiber	2000	2000
6fb3cfba711eecd6a5c8a4fb1bf62fb7	1045125466	No	Fiber	2000	2000
c91a0c264a32a4b2556e9f2a062de392	1045113680	No	Fiber	2000	2000
4b9e4dc5ca6fb42ffdb4d478c35515ed	1045113813	No	Fiber	2000	2000
eb8034315c7406330f0eee39f78a63f6	1045112917	No	Fiber	2000	2000
5bc2dce4dc276ea2eacd253ac88c81e1	1045112739	No	Fiber	2000	2000
df029001079b27453d79a97f69b5b424	1045112911	No	Fiber	2000	2000
c226faa2d098af833af9d05ea021bb3a	1045113062	No	Fiber	2000	2000
3a8b8402c1ae20643e9039c36a0aca02	1045113367	No	Fiber	2000	2000
f90fdbe4942d94b4cbd713f15849befc	1045125434	No	Fiber	2000	2000
25281fcbb91e3d39911d810159662e10	1045125158	No	Fiber	2000	2000
e4f5a470fa320419358c309b9540b27e	1045113076	No	Fiber	2000	2000
f5e26bd135a05273d1832f3ff558468f	1045112879	No	Fiber	2000	2000
402a3472acb02a94e77157498516b58e	1045113688	No	Fiber	2000	2000
b8d9cea330c174e5cea252124da8867e	1045134028	No	Fiber	2000	2000
093b396a7bff18bdb3b0330965609d85	1045125860	No	Fiber	2000	2000
2a94d9e10cc4e1e1e8036aa4c3df0519	1045126807	No	Fiber	2000	2000
f8c45e699fcae9e8616498d05bca1935	1045113809	No	Fiber	2000	2000
f8c6ee32e9ff4e59fecd8a05190ece2c	1045112776	No	Fiber	2000	2000
0f798619b0c3bd4b4eec9264d924e66c	1045113041	No	Fiber	2000	2000
0cbd6ec257e06ec169088673f3ea9067	1045125772	No	Fiber	2000	2000
c75d728f6a4006ef0182d7fd2f5a5f9a	1045125910	No	Fiber	2000	2000
d4333442b17e93ca3ab0bf9da043b359	1045126860	No	Fiber	2000	2000
4ab5888b8796c70d6b841d7f02e39193	1045125911	No	Fiber	2000	2000
76186ba418091463dbdb5cc3b7143645	1045112918	No	Fiber	2000	2000
d7d50cccce974b4752f36dee4e6ec22a	1045129091	No	Fiber	2000	2000
d61171a435daf68ebb533d9b61f5be37	1045112909	No	Fiber	2000	2000
f0d6f094e32d4d79678fc2791dd27dcf	1045125476	No	Fiber	2000	2000
843f996c89a2060d9917199b1b333b04	1045112747	No	Fiber	2000	2000
5c9559cd2c40c7a722b1233df17b926d	1045125901	No	Fiber	2000	2000
5c2fac50f60460608b4929037899d437	1045113526	No	Fiber	2000	2000
dfdf05ee297180da688a68a8b4da84ef	1045125454	No	Fiber	2000	2000
60ac7f4c773918ddea2c0ad53343e879	1045113764	No	Fiber	2000	2000
508db77aceee0d1c986f6747586cd0a2	1045112752	No	Fiber	2000	2000
11a2b18820b350157ff98418472757c3	1045112915	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
f391808b521ba7aba0a4c79301410fb2	1045125459	No	Fiber	2000	2000
e78d007bdb91d8b6566390d291d21e17	1045125887	No	Fiber	2000	2000
02cb40f4b56537552e43aab2134c7c85	1045112835	No	Fiber	2000	2000
e58eec0f1a49a5cd52fba1de23542c4c	1045113665	No	Fiber	2000	2000
4eda2dbb1be1fa9f33710ec8351ee8cc	1045130929	No	Fiber	2000	2000
6bee31313c14d5f821e22bc37b852ca4	1045130664	No	Fiber	2000	2000
a8937c83492957d95c51b85163120c5e	1045112734	No	Fiber	2000	2000
ae68dae1534ec753d95b6b153b240e77	1045113782	No	Fiber	2000	2000
3387fcccb4de17781e664240e3421d6a	1045125774	No	Fiber	2000	2000
41179920789a4d2abb6ae2308a49ff8c	1045125915	No	Fiber	2000	2000
7fe06ef7cb838546ef68c8ec968ca720	1045112772	No	Fiber	2000	2000
9b65f78a411e3ace4a08967b531302bf	1045112763	No	Fiber	2000	2000
b948c1e03278f659bf599ff88ff59f55	1045130928	No	Fiber	2000	2000
05fa784e098187699e066047dc90ec8a	1045113074	No	Fiber	2000	2000
f499756d191a5d6c88ebc3072fe8db5c	1045134031	No	Fiber	2000	2000
f6e80389792de8034fc3370b84dce45f	1045125471	No	Fiber	2000	2000
5f7acf1466040102e49a1aac4dc994ee	1045125156	No	Fiber	2000	2000
dc5c9a79f0f78291fd2719d22af2827a	1045125877	No	Fiber	2000	2000
5435750b707145ad1a4763f2f8bcb2ff	1045112880	No	Fiber	2000	2000
1fef8f31c3684bf558de121e2d8b7385	1045113536	No	Fiber	2000	2000
e1d939a3d3f0b3f7cd5afb89777daae6	1045112736	No	Fiber	2000	2000
7de18f1371089dd33647ec56aa0f6270	1045113524	No	Fiber	2000	2000
5f9dfece04de1b424fa6a4a786aba504	1045125443	No	Fiber	2000	2000
1581ded2595ea078efcb883f0c20297c	1045125918	No	Fiber	2000	2000
ec81014cad3d3b2e08d26778b1b38788	1045125791	No	Fiber	2000	2000
bce18d1cd548dd629b7b08ea98691f5e	1045113042	No	Fiber	2000	2000
8c85745e198606f7d126edf9411023f2	1045112742	No	Fiber	2000	2000
45d26c7f50e51a51428ef80cc2d5cbb4	1045113349	No	Fiber	2000	2000
48f1e970ceaaaed3c3c2b07992148528	1045112890	No	Fiber	2000	2000
54019bb61c547c9acbaca34cd693b200	1045125905	No	Fiber	2000	2000
390ebada20e4fbb5014739f3c322cb40	1045113812	No	Fiber	2000	2000
701136cd240c4f4f9537d2113950c080	1045125890	No	Fiber	2000	2000
bd4f3cc0725c457e0ba563dab1f8a196	1045125923	No	Fiber	2000	2000
dcdd7f4f004040dcefd9fffe7811e34d	1045125470	No	Fiber	2000	2000
a0f2fad4ec2388371ce5a62186f34b4b	1045113081	No	Fiber	2000	2000
533fff62d628d137879d8aeb09474759	1045125892	No	Fiber	2000	2000
56e5e9981e122f60b6b14d924a5155a2	1045125876	No	Fiber	2000	2000
69d9d9b84b1f84bef25f8c8ba2a9cd72	1045125913	No	Fiber	2000	2000
0336806ba51a53a9af93dacd4447e259	1045113664	No	Fiber	2000	2000
2558cf96f000e102f16de88187daea9d	1045112922	No	Fiber	2000	2000
8fe4d05befbf09fd93943ace6b5585ed	1045113810	No	Fiber	2000	2000
e36dc036370628adcff1dc7c8e7a672f	1045125879	No	Fiber	2000	2000
e948bf8d622b930d3e67baea5ad63372	1045113263	No	Fiber	2000	2000
1ea25cec874e257fac680f9c2772064d	1045134037	No	Fiber	2000	2000
92b5810fedc31db6d7bd4671178afebf	1045112779	No	Fiber	2000	2000
fb51da6d62bbd7acbdfe549c5029ca20	1045112959	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
c537a0a5ffac676b56b9205a32e99657	1045113661	No	Fiber	2000	2000
739ae31ce088569d3f0ecd30334e222b	1045113530	No	Fiber	2000	2000
de6eb5d5b9843c37a74d74ed3335e109	1045112913	No	Fiber	2000	2000
cd44985b04f8a17827c6de2ae5a001e8	1045125782	No	Fiber	2000	2000
b8c4f3682e2ada7331f9708aa115ccee	1045113541	No	Fiber	2000	2000
fca6b62688f3aa3a3a69902beb8f730b	1045130670	No	Fiber	2000	2000
1e011c94b4b0f42c550e6057c23d0ed5	1045112764	No	Fiber	2000	2000
4305cf00e25378d136399d90c59fb1f4	1045125921	No	Fiber	2000	2000
e1202662abb6c350baa7e07731c8c702	1045112773	No	Fiber	2000	2000
3fe5d7c710330df3a777b7bb5a843355	1045125779	No	Fiber	2000	2000
d40bac63563fd03e0b53e77710ced763	1045125775	No	Fiber	2000	2000
fa89a506a2b1aeee90d12d2858780f7d	1045125138	No	Fiber	2000	2000
f861b4948a9421985bc9108287f5f944	1045129064	No	Fiber	2000	2000
64cb96e129cc25305ac69e54dc8705ae	1045113063	No	Fiber	2000	2000
04dba7740a1e0ff552e06a98c6d88112	1045112745	No	Fiber	2000	2000
566c71c92ba17c4fcc63aaf4b765d2ce	1045130681	No	Fiber	2000	2000
f0be1e76ad9837d14698752f1ce07e14	1045112908	No	Fiber	2000	2000
35986627b9a62fc65c99bf90cc951841	1045112916	No	Fiber	2000	2000
55eb493f7d3c7b7c9f40be23b3f11f00	1045125818	No	Fiber	2000	2000
425b0a2546ca1888571633dab5aecdb2	1045125889	No	Fiber	2000	2000
a01b4b33278640ac91a598c63fb489d8	1045113547	No	Fiber	2000	2000
52bc6a3b3da714ffdd360b4d4862b4ed	1045113770	No	Fiber	2000	2000
2e711c46db79149058cf740f6863400c	1045125157	No	Fiber	2000	2000
21d70a7356d57e2a7d9bd4b2bd747823	1045112757	No	Fiber	2000	2000
f87ff8f2d2ceab493d5e7e68db3ae546	1045113333	No	Fiber	2000	2000
4791892c51740d605ac95b3e48209948	1045112768	No	Fiber	2000	2000
6f486f5e773db8738172b04c400297c7	1045113070	No	Fiber	2000	2000
a082ba33584abb127eadb7d851fef4bd	1045113220	No	Fiber	2000	2000
3e1e399c0d282a882b57dbfa85404d7f	1045113357	No	Fiber	2000	2000
1f756cbc601fc76172bba943dca3d325	1045113758	No	Fiber	2000	2000
19933a1dde8a0c2cf35d1600ea1baa47	1045130663	No	Fiber	2000	2000
fa3b3c8c66777067907504863a35ca20	1045125789	No	Fiber	2000	2000
73acd86afe437778bb8af23641c10cfd	1045112893	No	Fiber	2000	2000
91c742ed139a097fecd294215ef07d9d	1045113341	No	Fiber	2000	2000
66303afcc9a19b632d1f73cab0a082d3	1045125902	No	Fiber	2000	2000
eb762fcb769d8f9124436eb2fa7cb859	1045130675	No	Fiber	2000	2000
a18bc4387c79370f86eebe97a5a2acc7	1045125451	No	Fiber	2000	2000
5ab51d494b6d7751e9cb2643fc5a661c	1045125440	No	Fiber	2000	2000
0d4074d3d0b8d2aa72db95ec238f6ffc	1045113548	No	Fiber	2000	2000
386013619b8feacdea78b4ccef39fa32	1045130665	No	Fiber	2000	2000
c70d192e97e61d2f85c95f651e702cc3	1045113694	No	Fiber	2000	2000
d4bacbc9b4b5f4252c64654f483a7ed0	1045130667	No	Fiber	2000	2000
f811a5b59e59c5deb9b79db7d8b15675	1045112741	No	Fiber	2000	2000
f32d76f40e8f1b72f0f1ce87d55d3539	1045130679	No	Fiber	2000	2000
7cdeb09da1f8b5becaf00812b83891da	1045125780	No	Fiber	2000	2000
21856ed3a76525239395ea9c1cd0c9c1	1045126835	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
b94782ca22db79c483ad18b0783b659d	1045113818	No	Fiber	2000	2000
4adf7d106aa182e47fac5a726cbda1f1	1045112751	No	Fiber	2000	2000
cd53ebed2d3ff2a400ac65eab36f6708	1045113651	No	Fiber	2000	2000
23c850ace3e13e651b8b1be08e5194a0	1045125908	No	Fiber	2000	2000
0f41654a43d46cae2e26a748b4572c0f	1045113061	No	Fiber	2000	2000
e424a86a3a31498d44f958f8d948845f	1045112775	No	Fiber	2000	2000
cd0e9b3090a39e0a6ae4d7b1a0933957	1385356572	No	Fiber	2000	2000
90946f2757b143036211b9183df0b5a9	1385356548	No	Fiber	2000	2000
4a1cf71074904b25967837d79cada8f4	1045130671	No	Fiber	2000	2000
b06601ef7d63c0fc73bdf5db9c82a23a	1045113365	No	Fiber	2000	2000
35822d949ebf5b6620c23fcfc650ef7d	1045113667	No	Fiber	2000	2000
d3b6e83c5f62db51cdf882321e5cec06	1045134331	No	Fiber	2000	2000
87ac1e958653522ad2ad3518dceb01da	1045113539	No	Fiber	2000	2000
c3ce61024dc762f4cff50bd6d35fe178	1045113531	No	Fiber	2000	2000
2ecc0a178bb39222e390226e39eecb20	1045125439	No	Fiber	2000	2000
1b04be68d843ae8ffb557c7d934d47a5	1045125919	No	Fiber	2000	2000
b7dffcc8289bd233f63d52d4b1d97bc5	1045112778	No	Fiber	2000	2000
c78ec3bdfc37497d6e6567705793879c	1045113698	No	Fiber	2000	2000
0ca95dbbbc5b1d328161fed15e195601	1045125914	No	Fiber	2000	2000
5f755e890ab6931538ee4566e1642b3b	1045134108	No	Fiber	2000	2000
95267459e59ce32c91bec3f284d20272	1045113077	No	Fiber	2000	2000
805b16a5ef1100b9a2067eda7529e564	1045112906	No	Fiber	2000	2000
1052996e838b0bbfc031de19d03a03ef	1045113773	No	Fiber	2000	2000
ecb4c89656dd6e6c431a52e114006506	1045125301	No	Fiber	2000	2000
e20c2a46a9e0ecbfd8b3789d770bcedc	1045113069	No	Fiber	2000	2000
e9d7bbdbab0c59a327a2612697435fed	1045112903	No	Fiber	2000	2000
3f6794f925b0a3ed5e30ae88a14c1330	1045112905	No	Fiber	2000	2000
ddae604d658bb21b52793f1da548275e	1045129065	No	Fiber	2000	2000
56c255d4f9d8e16ad90c8a27515bb12a	1045125435	No	Fiber	2000	2000
5207b4ddf571b4ce08d06e4640591620	1045113689	No	Fiber	2000	2000
3f39cbe16bc1b304eabb5f77b8f3c41b	1045126868	No	Fiber	2000	2000
855374d58f33477f5c1e783f7c393e8c	1045113065	No	Fiber	2000	2000
a173237b5d6abaf49e86dc5bc3dbd4dd	1385356570	No	Fiber	2000	2000
b8396bc19d0caf2a876f44cfa75f26ef	1045113086	No	Fiber	2000	2000
48024b3304ffa391ac6ac86ebfd80022	1385360337	No	Fiber	2000	2000
aadb4d669c64713cf16d659aaa144cf1	1045112881	No	Fiber	2000	2000
0679928b5b0ea1ae0fb3ce92a73fc610	1045125917	No	Fiber	2000	2000
3a65fba9142c26e846ffd0f9efe1ea90	1045113080	No	Fiber	2000	2000
50f73fe8b1d006bcee0862f74130bd07	1045113079	No	Fiber	2000	2000
2f530250f740eb043e58f9cdab00ef06	1045126834	No	Fiber	2000	2000
08ec541c2e2ae9ef944767334168940a	1045134328	No	Fiber	2000	2000
681f3258f7e29abc4d691134a927e274	1045125885	No	Fiber	2000	2000
8e34e9dfe33d56c2f412eb019b94235c	1045112735	No	Fiber	2000	2000
445da72515cb01038c531014f7e6272d	1045112753	No	Fiber	2000	2000
d725e4f6e0d3931e2e2fbe97b086bae2	1045112919	No	Fiber	2000	2000
13f1b50af676f875d58a65d033854104	1045113525	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
01d41bbd89937e620f49f79836803ebd	1413410544	No	Fiber	2000	2000
ed35b30faee9efb03a783b7c97569b09	1045125878	No	Fiber	2000	2000
df9b293bdb755dac77f157af5b516573	1045125786	No	Fiber	2000	2000
0911c1fc83c793fc1cd54204f69b34d2	1045113109	No	Fiber	2000	2000
aff0d56a5cdbf593832e84080915db2d	1045125436	No	Fiber	2000	2000
30dd1e7ecfda1a0b46c7579e9270a088	1045113043	No	Fiber	2000	2000
b20104412531981abfe236f19f1bac73	1045113538	No	Fiber	2000	2000
aff97bb20646b07ccacd9c39316679c3	1045113075	No	Fiber	2000	2000
c75cd0b93ed4ced222bbda76792baa52	1045125792	No	Fiber	2000	2000
1d8dc76770942851ac34eb987dd0cba2	1045112902	No	Fiber	2000	2000
cc463ed1fac8144f9f13ca465ad01b88	1045113532	No	Fiber	2000	2000
c0a4c60645d73c555c640a4e2864e5f0	1045112904	No	Fiber	2000	2000
3af70ad003cce37f7a4c9e1ccedcb273	1045113546	No	Fiber	2000	2000
5454c5e06b31135ee246c2fe70b33fb2	1045113040	No	Fiber	2000	2000
415e7edd0078af0525c768958fd39945	1045113814	No	Fiber	2000	2000
538f5f322e6dfa7d46ca2a5bd1730e1b	1045125456	No	Fiber	2000	2000
54920613cd7b6fea11fa9b027fba6d77	1045126867	No	Fiber	2000	2000
d2488ae7172515ba53c4f1282bfcd609	1045125769	No	Fiber	2000	2000
8f8d16dc5c08629b8996cd3cae33f49c	1045125137	No	Fiber	2000	2000
94567f232f257d0f628b75750ddbcfcf	1045125462	No	Fiber	2000	2000
1dbd4d2eca97213da379a0790fe441c8	1045112732	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 31 – Budget for Project Area IBO-910

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$31,500.00	$12,867.00	$18,633.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$1,800.00	$735.00	$1,065.00
Permitting Costs	Permitting Costs	Professional Services	$132,067.00	$53,944.00	$78,123.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$162,680.00	$66,427.00	$96,253.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$27,202.00	$11,111.00	$16,091.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$246,176.00	$0.00	$246,176.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$67,500.00	$27,562.00	$39,938.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$155,914.00	$63,685.00	$92,229.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$139,309.00	$56,902.00	$82,407.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$549,020.00	$224,253.00	$324,767.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$21,429.00	$8,753.00	$12,676.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$59,036.00	$24,106.00	$34,930.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$6,914.00	$2,823.00	$4,091.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$481,842.00	$196,814.00	$285,028.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$143,070.00	$58,438.00	$84,632.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$115,736.00	$0.00	$115,736.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$16,929.00	$6,913.00	$10,016.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$8,415.00	$3,436.00	$4,979.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$14,966.00	$6,111.00	$8,855.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$8,416.00	$3,436.00	$4,980.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 31 – Disbursement Schedule for Project Area IBO-910

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 31 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-910

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 31 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 32 –Subaward Conditions and Statement of Work for Project Area IBO-872

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$1,124,660.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$1,124,660.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$1,124,660.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 32 - Specific Award Conditions for Project Area IBO-872.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[65.84%]; [$2,167,287.00]
Total Project Cost = (subaward funds + match)	$3,291,947.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$1,124,660.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-872 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 32**. The Project Area is depicted in the map in **Appendix A of this Exhibit 32**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 32**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $2,167,287.00, which is 65.84% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 65.84% for a total match of $2,167,287.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 32** in the area depicted in **Appendix A of this Exhibit 32**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 32**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 32 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 32;
- Appendix A to this Exhibit 32 – Map of Project Area IBO-872;
- Appendix C to this Exhibit 32 – Budget for Project Area IBO-872;
- Appendix E to this Exhibit 32 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-872;
- Appendix F to this Exhibit 32 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 32 – Project Area
- Paragraph 5.B(2) of Exhibit 32 – Project Locations
- Paragraph 5.B(3) of Exhibit 32 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 32 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 32 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 32 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 32 – Access to Service
- Paragraph 5.B(5)e of Exhibit 32 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 32 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 32 – Map of Project Area IBO-872

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-872

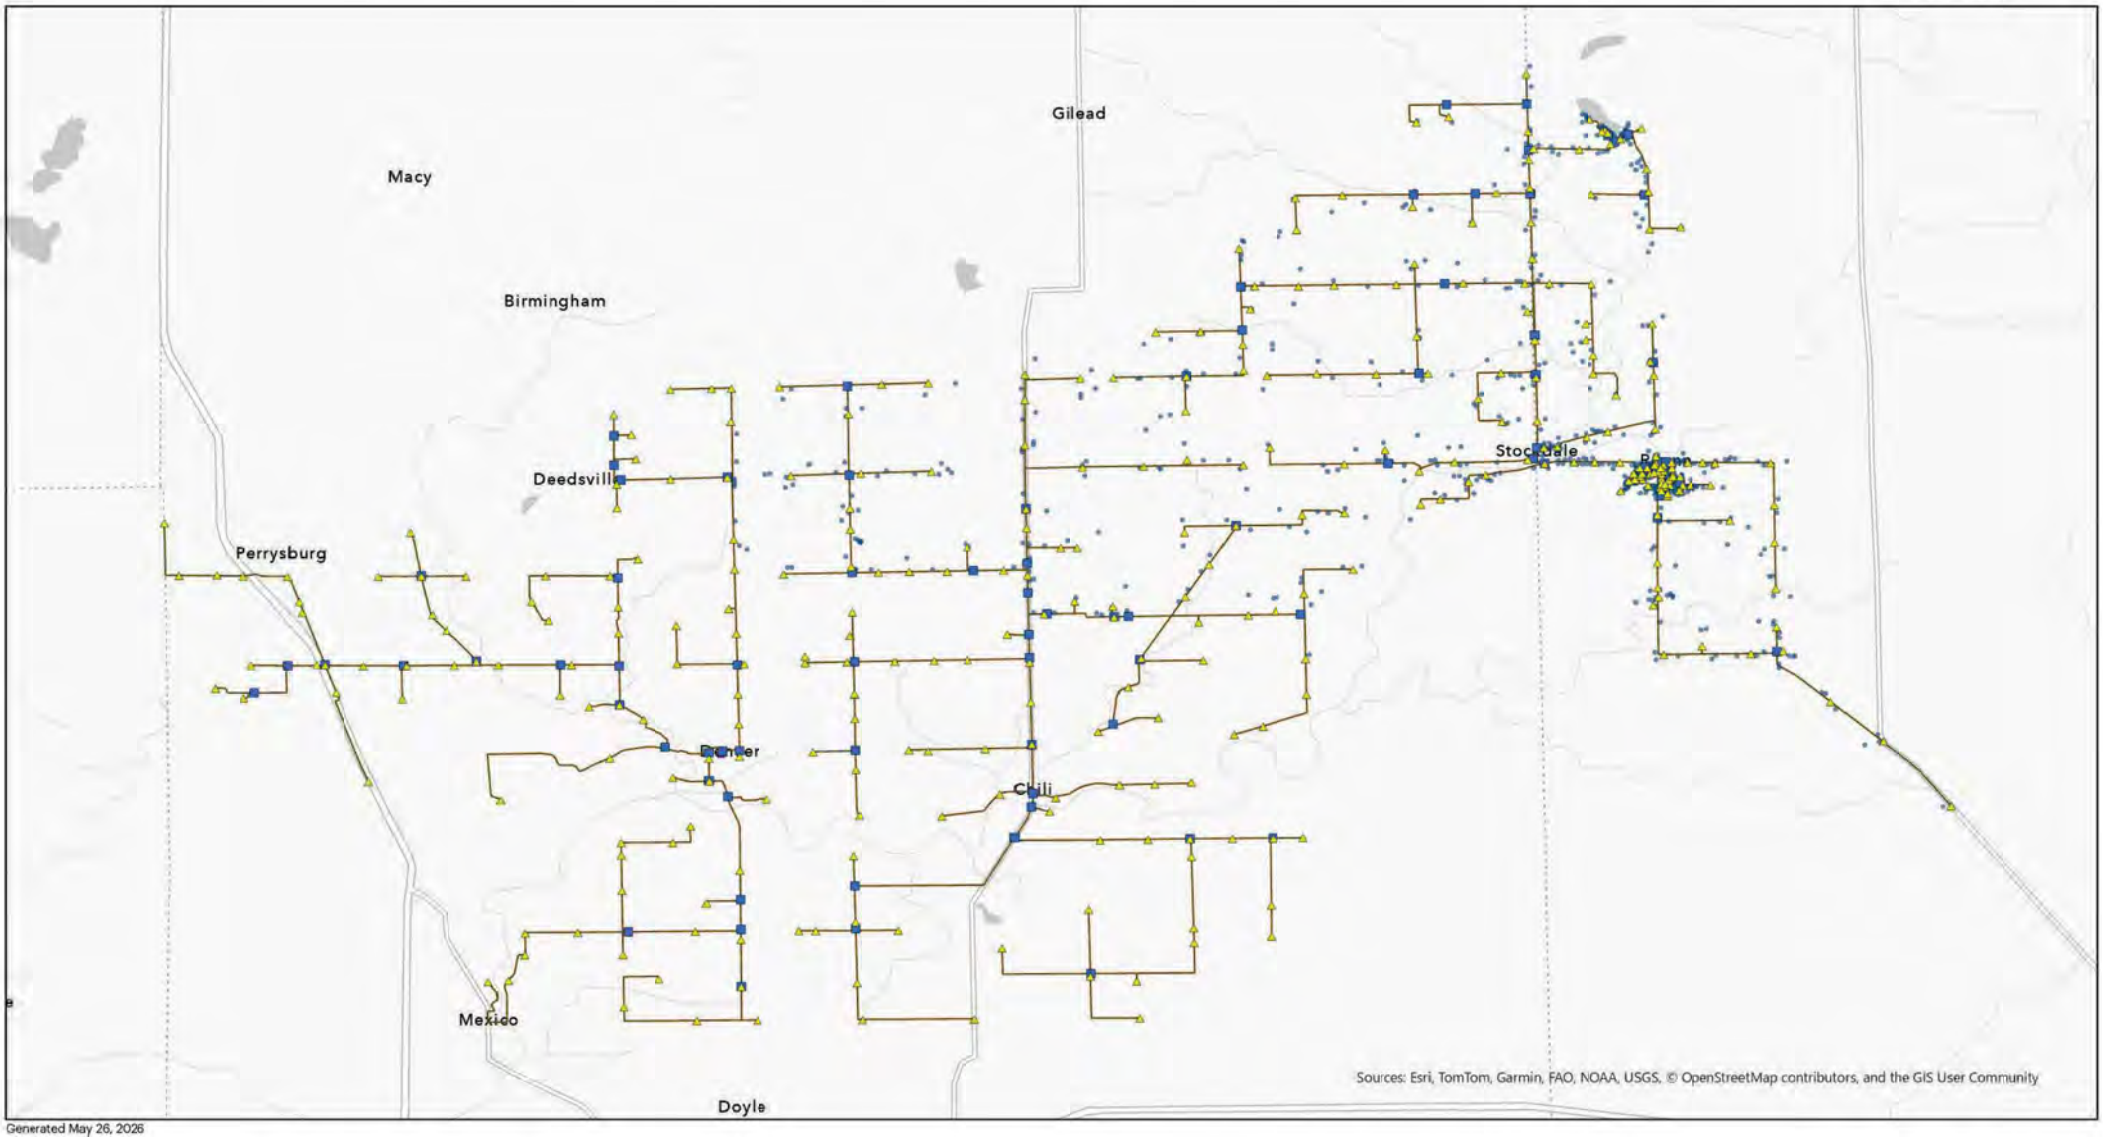

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 32 – List of Locations in Project Area IBO-872

Brightspeed IBO-872 Location List

715 locations

ID	Location ID	Is CAI	Technology	Upload	Download
95f5a839734ae29d1edf963e9e28f5bf	1137118585	No	Fiber	2000	2000
22aaa2c6634e074513f809717fb38cf5	1137118579	No	Fiber	2000	2000
aaa7ee4a8f5611a96f2e889dc52460a3	1137118987	No	Fiber	2000	2000
bab1ae61d8b29b00fc9792adf6708482	1137118596	No	Fiber	2000	2000
64030788b8842251b9a0c83cadc6b80b	1137119241	No	Fiber	2000	2000
3b87b8e495f5f74173eebb86d1bc9044	1137119412	No	Fiber	2000	2000
bd27ed1fc91a1adf067da0a82055d184	1137119320	No	Fiber	2000	2000
34d2900d1050100f74d7664c92ef9be4	1286942744	No	Fiber	2000	2000
5c6d2f872af064c26b02c141944d9197	1137118489	No	Fiber	2000	2000
5e198997e6bcbd9d6a191610f470c500	1286942730	No	Fiber	2000	2000
1f20e994f1787fcd62a4800deec4f46b	1286924938	No	Fiber	2000	2000
185c4ff4c9a6d61a2662ed30167b09c4	1137118995	No	Fiber	2000	2000
20351f8f3d425d2efcab18f10db836bc	1137118992	No	Fiber	2000	2000
3c7cfa88dbbfa69d872d08198d9183b0	1286925597	No	Fiber	2000	2000
7d37e4c982fff1c8a1654e888340c530	1137118603	No	Fiber	2000	2000
41e1987601babb66a6b9b93d1f70736d	1286942706	No	Fiber	2000	2000
c8e691ca553118d556d1712688230052	1137119364	No	Fiber	2000	2000
7d3254bd0fe3079900dc7006217f2d0e	1137118586	No	Fiber	2000	2000
447e57981b88db5fec2b778548f75548	1286942664	No	Fiber	2000	2000
d98783488a1845dcb06622eb5af2e856	1286942752	No	Fiber	2000	2000
37cfe946d37fff8fcecd426c169842b5	1137118508	No	Fiber	2000	2000
6777cf111943635a4ac2a9744a0891ee	1286926258	No	Fiber	2000	2000
36ad19542bea0907ca38780dcb5d9656	1137119061	No	Fiber	2000	2000
510842e1970745621e8a6789cdcd04c8	1137119385	No	Fiber	2000	2000
d980346c1dbe7ddb6d23ef7e263c9eaf	1137118517	No	Fiber	2000	2000
6de1014b8e2ff1b7a2766af8d148b513	1137119314	No	Fiber	2000	2000
e2e0f23232f7d72e01400765be4e5900	1286925093	No	Fiber	2000	2000
9024e628e5de825d0682262c4eb6b3d4	1286942649	No	Fiber	2000	2000
e4a265d8ef0455d124e00d4bf9063328	1286925116	No	Fiber	2000	2000
d964d9c11dd51b9d07fbb54a36470839	1137118855	No	Fiber	2000	2000
c8e670b13d2394743b88962540cdc896	1137127927	No	Fiber	2000	2000
1aca15c4987fb699e331f778827f6dc1	1137119243	No	Fiber	2000	2000
efbd75f1342be2d90af26977a9e7fb6c	1286926275	No	Fiber	2000	2000
f90070c6c586f596362f0a432cd57c76	1137119184	No	Fiber	2000	2000
7c14acb34f7f956445fe0c119a157aaa	1137119226	No	Fiber	2000	2000
2750996387ff599d6e84f2cf194af168	1137119326	No	Fiber	2000	2000
e3c8f678c60cc5178566257de6f3b218	1137119217	No	Fiber	2000	2000
9df9507ddd2fe486f689169a57ce728f	1137124995	No	Fiber	2000	2000
76e724a5b6943e6aeec8c2f5cbdd4976	1286942749	No	Fiber	2000	2000
e7aed867ed5eb30e91d89b57034b2015	1137124985	No	Fiber	2000	2000
867c80a2ebd38d63886c1279464a99f8	1137124988	No	Fiber	2000	2000
ac80bc15c734ca45cdf972f0935c78dc	1137118655	No	Fiber	2000	2000
2885122926f8739080ea69fb5b0a8ed5	1137118576	No	Fiber	2000	2000
d4b28595d205f9b3f9dcd50714732163	1137119329	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
60a8f7ecb7dc44f2e4fff7680aa4ed33	1137119223	No	Fiber	2000	2000
99af608c3a8d090578afc6c6e19a6352	1286924776	No	Fiber	2000	2000
c2a383914b0ab0ff2150ae1e9835652b	1137124595	No	Fiber	2000	2000
759b4f80ec4371ce4e016a9dab5a0b1f	1286924020	No	Fiber	2000	2000
db1618aad011f8027166edd9a845b817	1286925100	No	Fiber	2000	2000
ea30bdd819edd384723a36e52047fa23	1137118761	No	Fiber	2000	2000
071c7485b725ca9cf8d3cf14af0af5fd	1286924038	No	Fiber	2000	2000
ada6b3ac8d27d68b9c8dcf685622e6d1	1286925085	No	Fiber	2000	2000
a2ac5e2338a2f2fcffd56b3b04ea1aae	1286924027	No	Fiber	2000	2000
0be9761a1f2f5d2ea8e2990b9aad0488	1286926466	No	Fiber	2000	2000
65c780cbafc2b9cc88c51caac5b80902	1137118494	No	Fiber	2000	2000
a9b9b9370ef9712063a711f09dd66736	1137119300	No	Fiber	2000	2000
35a091cac21d9fd24ac873dae5f1c97b	1286942553	No	Fiber	2000	2000
156213851101662548e1a00ccd5392db	1137119007	No	Fiber	2000	2000
411b1a0fa129d8bf0075e2a9314e0ea1	1137119063	No	Fiber	2000	2000
f869353d2e0be5c450c4be50192011a3	1286942555	No	Fiber	2000	2000
520e54277d0931e9f6acf8a98287fd79	1137118977	No	Fiber	2000	2000
1f2709ac2b1ddab46c33fdadd33799e9	1286942729	No	Fiber	2000	2000
d62fe6ad8fec225c202899479aaf9cb0	1137119378	No	Fiber	2000	2000
fe05524f580df036b0b3cc6b6e9d8a6c	1286924927	No	Fiber	2000	2000
7a26e5fef4f2553594273e4c736c9200	1137118481	No	Fiber	2000	2000
d28e09027405863416d171371e3d6aa6	1137119339	No	Fiber	2000	2000
58408b77afbc13376c41032562df4b74	1137118983	No	Fiber	2000	2000
da272e19bbf4830fd49609842a04e58b	1137119210	No	Fiber	2000	2000
b37d372ffd5d07a12254c3da9c667bf0	1137119239	No	Fiber	2000	2000
791bf40ae8b56fe1b57ef0424a951739	1286925596	No	Fiber	2000	2000
94e54a38d31e119425426b01b827ed2e	1137119333	No	Fiber	2000	2000
8d45322d46329e5d4dfca301fe768e47	1286926464	No	Fiber	2000	2000
1bd3be440f70fac993dae2408a49920b	1286926257	No	Fiber	2000	2000
e995b0937064423c9e6f51bb1952d8a3	1137119000	No	Fiber	2000	2000
eaf5e17c6488523e6a692b931e7af027	1137118591	No	Fiber	2000	2000
1b8d68edeb7f8fccb3b8a4c299618c8f	1137118779	No	Fiber	2000	2000
f4b6ef169d4e1ffac52520fa57ad59bd	1137119224	No	Fiber	2000	2000
06a41f87552971ca85a4e3506cc11c94	1286924343	No	Fiber	2000	2000
0166eff5b39937006a97d6c7bc186016	1137119229	No	Fiber	2000	2000
7a0efa8dbc28a5a7696e6c2042b94932	1137119409	No	Fiber	2000	2000
d2dbc1b1ccc7893924d3cf0afa9c0414	1137119401	No	Fiber	2000	2000
ab7611151736436a274a1ec0d333aa0c	1286942549	No	Fiber	2000	2000
ed7448bcee4c71e636df133d09e05a60	1137118853	No	Fiber	2000	2000
d6a5616783311fc1bfcc631aee98b3ab	1137118672	No	Fiber	2000	2000
0edc284cd3a8a1594194691b1d2efb07	1137119381	No	Fiber	2000	2000
5a2795ac63f1e2a8da4b306df8f7b9ef	1286925604	No	Fiber	2000	2000
e96a4c124eccf4288346a92b5abb78a6	1137118510	No	Fiber	2000	2000
0939052c928502e1fd1b23090077753a	1137118575	No	Fiber	2000	2000
6706dee8f622ca8d8184b932d8e86182	1384718818	No	Fiber	2000	2000
95cc5ecc5819fb0626a0a9476214bd04	1286942745	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
af2049eb76aa5b2c66439875cf0bcf36	1137125671	No	Fiber	2000	2000
a8f53d508fa71eeed1b338427198d144	1286942655	No	Fiber	2000	2000
ff77753b3193b2fec42089c602ef1a60	1286942709	No	Fiber	2000	2000
3efb8bc7917123338e60edce932c7e5e	1137118998	No	Fiber	2000	2000
e3419f79c86f13cc9a7f98420ab08e02	1137118986	No	Fiber	2000	2000
998ca10784166a2adb7f5a9e37b807e7	1137118480	No	Fiber	2000	2000
76eea61d7b7e31e01d15eede95e74d59	1286925102	No	Fiber	2000	2000
eb491811405499cbe7b479565f1845a3	1137118798	No	Fiber	2000	2000
9098d96b43fda9aeb6bf78dd95d5e538	1137119334	No	Fiber	2000	2000
4087017fd292fe9bfcdd67fb9096d546	1137127928	No	Fiber	2000	2000
06270f758ec1a4eb6fd2c2f9c040a97a	1137119309	No	Fiber	2000	2000
c002165875755cee68a043692ca84a9f	1137119220	No	Fiber	2000	2000
51143a91bcecdf833326e4fbfce9b19e	1286925098	No	Fiber	2000	2000
bc8444315664afd5f791dcc1e82ba519	1137119230	No	Fiber	2000	2000
ccbc63fdcdd672ac2873f9864a48b0e1	1137118808	No	Fiber	2000	2000
098d4bdde4cbfb25708454edddbf1303	1137118572	No	Fiber	2000	2000
ca75f73349a8cc62ecf68bc0109e7bd5	1137118604	No	Fiber	2000	2000
8e9008e92c26604fb14bbe343d144b2f	1286926456	No	Fiber	2000	2000
28e0cc84bb8e6e59b88f21875dae8fc2	1286942648	No	Fiber	2000	2000
45bdf393f813b6740105ccabeb1b9b91	1137119338	No	Fiber	2000	2000
4873200d2c08c1490299a36186d09e59	1286924059	No	Fiber	2000	2000
d97f0853dc913e1ea391485e687777e1	1137119197	No	Fiber	2000	2000
6b13e84889bf362721c3221aedcd838f	1137118788	No	Fiber	2000	2000
fbead805f5b10080c7ebf20561418228	1137118614	No	Fiber	2000	2000
fb6d1d50843db5476ec434db881887ab	1385111291	No	Fiber	2000	2000
14b981bcb419e24aaf6498095cdb9e8a	1286926250	No	Fiber	2000	2000
d291df1ff485695d138e93d2129b38bb	1137118990	No	Fiber	2000	2000
bde0b3eee79f67b997a66b01adb391cb	1137119193	No	Fiber	2000	2000
cbb5600e6bbe29060e022b989f66d8f0	1137118514	No	Fiber	2000	2000
40997e787072c95f0209d16b5ca8324c	1137119213	No	Fiber	2000	2000
1b44caeaf81ee4e989e38c9513023920	1137118781	No	Fiber	2000	2000
9106d8a71f9f635ff8d0071cabe79f70	1286925598	No	Fiber	2000	2000
caeb150e4d27d3cc9e099bb794218e52	1137118807	No	Fiber	2000	2000
dd6fee7335bffaa1300a52fb0f1d6620	1137119299	No	Fiber	2000	2000
0dcaa235b5f565957a6fb11ec6e4302b	1286942638	No	Fiber	2000	2000
411cf76d8034c9e728ad445bb3436a61	1137118573	No	Fiber	2000	2000
cbe95d11cf00223a32bc39cc6952273d	1286924932	No	Fiber	2000	2000
e9b813d0a437d74e1c14ca3282638e17	1137118982	No	Fiber	2000	2000
ae04845e1d8615d5c72cf9d2cded01a8	1286924054	No	Fiber	2000	2000
5640c52903ecbc5c737fa4aa84589309	1384721724	No	Fiber	2000	2000
b88d8aa5e649dcb4ea133f8d6f510009	1137125675	No	Fiber	2000	2000
44c75f6eeff46501f562456d222a00da	1137118854	No	Fiber	2000	2000
860187a2889ea0bea66202d27ff7a764	1286924345	No	Fiber	2000	2000
0206acebfd221b7e46706516efe481ac	1286924789	No	Fiber	2000	2000
4a4665bda154465a0d11a1beda6cd340	1137118980	No	Fiber	2000	2000
c540b916294906e3aadb05a37fb3cd11	1286942756	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
2c987afc1077b4d1b23944e36465932a	1137118587	No	Fiber	2000	2000
f5763282321a1b03556d81ef4b684129	1137119319	No	Fiber	2000	2000
9d5863f6205d5fc32a4a40d49443890b	1137119417	No	Fiber	2000	2000
e2ca2ba566cb20b723d8b1910267f110	1137118594	No	Fiber	2000	2000
e3821a8eb270a830af2e3babec1acf03	1137119403	No	Fiber	2000	2000
c36e5c8b0463f484d2f0d6453e4d44e5	1137118870	No	Fiber	2000	2000
edb51c462f989b8e7c9bf81128ea3011	1137118981	No	Fiber	2000	2000
c0052a64c6ab36b9ac5e98a821c210d2	1286926820	No	Fiber	2000	2000
4f471bad81fdf28bc6eb5610b1316a08	1137118571	No	Fiber	2000	2000
3a2d6aac802673507af0a766f42426ac	1137118775	No	Fiber	2000	2000
94e16ab51b839552bfc4e5972801ab77	1286942712	No	Fiber	2000	2000
b93c2e4e66a1af1edc0c9361cfe56073	1286942656	No	Fiber	2000	2000
c3f0481175fc20ae1d569c6bb568b822	1286926018	No	Fiber	2000	2000
1705f9c521540eeea8e2e5390de431a3	1137118776	No	Fiber	2000	2000
040ed9b5a498765e4e929dcf10f1a570	1286942632	No	Fiber	2000	2000
75d945278cd1908860a43f511cebf4c5	1286926458	No	Fiber	2000	2000
31611b38c2f2ed34fc18dba4b47a53f7	1137119269	No	Fiber	2000	2000
d435b0ec8db1c79ddfed37c8adcc03af	1137119366	No	Fiber	2000	2000
2928365e1fa3b686fd395a7a7c6300a7	1385111739	No	Fiber	2000	2000
973c77fb55cf1d273f824038fa779569	1286942644	No	Fiber	2000	2000
3bde938ae7445b9289b78a07c88ddb1b	1137124997	No	Fiber	2000	2000
a194b14c584087664ad80115f0eb78d6	1137118509	No	Fiber	2000	2000
45e30e2b517286d7cdec4ccaa248f879	1286925106	No	Fiber	2000	2000
aea5ca7d785bb3174144273b7616df5b	1137118607	No	Fiber	2000	2000
75ae0324b96fc64e8a21751cd690e8db	1137118820	No	Fiber	2000	2000
24ff2c2dd0444bf6f9e386eddb72bdaf	1137118860	No	Fiber	2000	2000
30472308adbb0552da599c45bce9931c	1137119207	No	Fiber	2000	2000
3a7de76c1d5d2836501d7cddeadef10f	1137118611	No	Fiber	2000	2000
ab31f399e026c4d90ea023dfa3d5097c	1286924021	No	Fiber	2000	2000
ab822c5eac8b8ab55f9d1e764ece3f75	1137127935	No	Fiber	2000	2000
5505e85610d4aaf1225ecf93a50824cd	1286942711	No	Fiber	2000	2000
b1b02424def66cd51b74ea7354a1f7f3	1286942726	No	Fiber	2000	2000
17ccba226b14ebfde22eaf6561eddb32	1137118780	No	Fiber	2000	2000
4e10aaf5cd5a495db766a932235cbfac	1137119218	No	Fiber	2000	2000
048b1b5dac40b25fca7f04d1754dd831	1385111381	No	Fiber	2000	2000
6ff9796c6cff2f1109c1eaafc5346606	1137119306	No	Fiber	2000	2000
93521adec2813c24c9a4cea2c7c3a3e9	1286942704	No	Fiber	2000	2000
b7a11405446434de246909d0fe5add86	1286942753	No	Fiber	2000	2000
b87816092d2c5b636ab2b068b66722b3	1137119242	No	Fiber	2000	2000
04da5014bac01df6d7b7ec744939e0df	1286926454	No	Fiber	2000	2000
f0e8e7444601290b617be9f29586d73a	1137118790	No	Fiber	2000	2000
60fd1076c926c55647beac6659e5aa4a	1137119330	No	Fiber	2000	2000
5b896d67c0387df362bca656b7c1d041	1137125704	No	Fiber	2000	2000
e8d1da19216f7769adf94d23425b2105	1137124994	No	Fiber	2000	2000
ad21d57d764d2e66818931d5dfcae272	1137118858	No	Fiber	2000	2000
606e0186bf85110d9e36e36e9ed1e1f5	1137119359	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
e2ac7a4b475b3cbc356744703d0cd718	1286926459	No	Fiber	2000	2000
179703e0379cb7f5b9b11f05b0d4d211	1286942557	No	Fiber	2000	2000
0df6c9a1a1a34c24bfad02c01ca279ec	1137119321	No	Fiber	2000	2000
daf150ea4eaf572187bfd1f6e2932428	1137119377	No	Fiber	2000	2000
5072cc8b9fea6a412d66051e0d3f011c	1137119327	No	Fiber	2000	2000
6500accd74efc09d33c6a1688a307d93	1137118653	No	Fiber	2000	2000
08f79ef4c6e3dc7499adc0c317a92aa8	1286924930	No	Fiber	2000	2000
d71d797dd1cd401ab7aadf6475670f1d	1137119183	No	Fiber	2000	2000
90bf82c22cfcab34754efce2a117b69d	1137118791	No	Fiber	2000	2000
bade99444b49ba0d81bdc3528afbd70f	1137118792	No	Fiber	2000	2000
c63956842bac127e69fb6531d98713a8	1137118994	No	Fiber	2000	2000
28ffa332c60996b122868ba7a7617821	1137119194	No	Fiber	2000	2000
76ca9b1da1a4f385b3de9e16d8630491	1137118817	No	Fiber	2000	2000
030defdc51bea912787f84e2e967bbe5	1286926032	No	Fiber	2000	2000
11a8302fb7e9b7c6c546dfc3512d747d	1137119368	No	Fiber	2000	2000
55e0bf36825dfc83181b2c67c06448d3	1137119002	No	Fiber	2000	2000
80eea03213ba1824f57c4e5a5b687371	1286942746	No	Fiber	2000	2000
d17a7ad54ab2f5a70ba29d0f3a97bde5	1137119349	No	Fiber	2000	2000
8bc075e67f1163c9169b10e53a5af863	1286925087	No	Fiber	2000	2000
8ddccd14c19bdd588bf843c7a468bfcf	1286942747	No	Fiber	2000	2000
30d4d71561c64c302f7b7297c5a7db92	1137128002	No	Fiber	2000	2000
8eb1ba1bae1390a7b5f8e66c48d32b02	1286942556	No	Fiber	2000	2000
18453d81cda67ffe815421e5c7402060	1137124993	No	Fiber	2000	2000
95359d310c44d3035734fd48ce1d9b1b	1286924057	No	Fiber	2000	2000
72ed86e2fe4adc83ac7f3264f607cbd2	1137119058	No	Fiber	2000	2000
3fbb954df41c160f6c7dfa202192286b	1137118609	No	Fiber	2000	2000
9e79e77711142cee8a3272379dfac928	1137118773	No	Fiber	2000	2000
d3adeeb4e6643ef863a751757cf86780	1286926460	No	Fiber	2000	2000
eabf2d9a6df73dae2805f67e48b1dd63	1137127955	No	Fiber	2000	2000
1e516ca1adf7d41f32ce19b4f51b45f0	1137118785	No	Fiber	2000	2000
128a94f0a819f2e68226ea4c577d171a	1137118845	No	Fiber	2000	2000
aa6dc507b6526f2a83e3aa4c0752da54	1286942538	No	Fiber	2000	2000
8a497db57ce93593ce9d615f4e52d13a	1286942707	No	Fiber	2000	2000
4c18af7df29c70b97ad01628771d312e	1137118834	No	Fiber	2000	2000
af96783e7ea62bebc6403c9d58b99b36	1137119350	No	Fiber	2000	2000
8c6a7a0cbc078e2f637a8cdc194cbfda	1286924916	No	Fiber	2000	2000
10f9fdbfc39ae8348f4c4cc75171a033	1286925096	No	Fiber	2000	2000
37a44b0cd6e7eacb5416476b346f3572	1385112571	No	Fiber	2000	2000
7e5aa24da0b2c370cff5b473ec4c2a25	1286926254	No	Fiber	2000	2000
729175e51edd2d7612dd2fafbb587d41	1286942751	No	Fiber	2000	2000
cbabe88818d8f6d6cd3b0f76336ad37a	1137118593	No	Fiber	2000	2000
63f7e6ab4ac1f7addc5811da09a4087b	1137118848	No	Fiber	2000	2000
f925ec66ca72b606e68c9034e805b36a	1286942548	No	Fiber	2000	2000
f5fdd798390edfb1402bfc97917cbf91	1137118770	No	Fiber	2000	2000
e2f33b245355c56a18b4437afed133a8	1137118620	No	Fiber	2000	2000
451ba9ad0811b231ddf2c68c7d8d082d	1286926244	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a20d672bf2c74a2b10b2bc9791561d68	1286925109	No	Fiber	2000	2000
2b73c39edea7fe3808a74fce8a80cc33	1137118505	No	Fiber	2000	2000
5c3e7c598178c3318ce0c265277c4665	1137119225	No	Fiber	2000	2000
318481c2006ce715049a6f955cfe6217	1137110775	No	Fiber	2000	2000
27f9e0c33946501bb972e55c45f0e7df	1286924017	No	Fiber	2000	2000
ba24b220514ec94e4c77b269a391107d	1137119322	No	Fiber	2000	2000
0188448e06b1e2b9e5dd45a6d0b40f9a	1137126684	No	Fiber	2000	2000
0bbd093f8b7fd2019f8834e537dd6a6b	1137119056	No	Fiber	2000	2000
f61014072324634e579de5c674cb0e25	1137119360	No	Fiber	2000	2000
7748efb5c406e1c9258c9fe633f3f7b2	1137118830	No	Fiber	2000	2000
7c497b85945ce3be86bc59f230bf7878	1137119064	No	Fiber	2000	2000
36b8a1c52f11d14c81bc21fcf6721582	1137118608	No	Fiber	2000	2000
de3755ef7ff1d256d67c168c030a3e84	1286942552	No	Fiber	2000	2000
1e30f05196411dbee7f67bdf341edac2	1413416741	No	Fiber	2000	2000
c523952e646c771f2cda37708df40cda	1385111289	No	Fiber	2000	2000
4abd1b5cd3eb3cd036a5a8c64a437a4a	1137118859	No	Fiber	2000	2000
9f7242fec17f326595dd366c6f7605dc	1137118765	No	Fiber	2000	2000
4839c6af3c69589199aa08902dfeaa3f	1137118520	No	Fiber	2000	2000
d194acd94e67a0d041e471b626c6fdcf	1137119370	No	Fiber	2000	2000
ba0f8cba0d4bccd56e750386494d1f85	1137118507	No	Fiber	2000	2000
ab8ef50f6ab83a048846921cb9fd366f	1137118806	No	Fiber	2000	2000
46be5998de4b1a125e5291934d8eca5e	1137119051	No	Fiber	2000	2000
c500a1eb15961aea43cb8205f57dbf55	1137119200	No	Fiber	2000	2000
380c6ff1ac2e90e19a1e322112626fa5	1137118810	No	Fiber	2000	2000
64c4a9227a77ebd246c9b14e84bf8ab5	1286924035	No	Fiber	2000	2000
feb26125f7a00d422d39edbc8086cf17	1137124991	No	Fiber	2000	2000
2db243f1ec297819bac74e7f78d994f5	1137118582	No	Fiber	2000	2000
c78708f3d5870e015bc3384494d74adb	1137119308	No	Fiber	2000	2000
eccb713a5a881c27f498c4634901e3ac	1286924064	No	Fiber	2000	2000
febb7c43556bd07ce2ef5ff3320ca79d	1384721713	No	Fiber	2000	2000
201695f17c811dacced2eee11cb68dfa	1384721722	No	Fiber	2000	2000
2a744a1add2660758c251b3e7153234e	1137118782	No	Fiber	2000	2000
8f2c828836f6619fd9c38b40fe1723fd	1137118501	No	Fiber	2000	2000
ac460018414c5aba8719d103c2cb64cc	1137110779	No	Fiber	2000	2000
d91f8765471c8cb51e29ce2f15eabbeb	1137124996	No	Fiber	2000	2000
89234cc882e82d6d664bf7d87aececa9	1286942625	No	Fiber	2000	2000
087e2a32d1b96a00b8e63fb2199bc953	1137119003	No	Fiber	2000	2000
4e0ab96bc4ef58995bfc2ad39d0adeb2	1137119351	No	Fiber	2000	2000
b1d3e92d9c940b29247dc3a821196139	1137119059	No	Fiber	2000	2000
7a5f3358798ca524dabab60c2c6c8703	1286942651	No	Fiber	2000	2000
a049766236d56f47eb6a026bd05141d5	1384721531	No	Fiber	2000	2000
0b6fbf49f69eb7b92211a1495f75d847	1137118568	No	Fiber	2000	2000
4f06220a9094345ed4eef9b009b2ce6d	1286926451	No	Fiber	2000	2000
1b6fc0945f19e4530343a4d001de282d	1137119411	No	Fiber	2000	2000
d3feab68c37d3a02fc13333ee245d778	1137118804	No	Fiber	2000	2000
5effee3e9700a435cea9dc2b36cd0584	1137119202	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
e05072c48eb878bcb0aac498ad675cf5	1137119302	No	Fiber	2000	2000
99371b803f1cf4775dbe7ae97bb6350d	1137119304	No	Fiber	2000	2000
c9d3d02f84067d7768ff14dac5b80d2b	1137119353	No	Fiber	2000	2000
2e4f72981f6245881cbdcb55d5cacb09	1286926457	No	Fiber	2000	2000
d4cd6657ca179ef7f9738f3f0a9c9508	1286926253	No	Fiber	2000	2000
06ddc8839c905d27182b6fdfe4e94d10	1286926818	No	Fiber	2000	2000
aa293a894a1ba223498ddd3803a0bedc	1286926033	No	Fiber	2000	2000
abfec29ebc809df894d7b8e1bd63190d	1286924036	No	Fiber	2000	2000
9c0b12ef68c9a59b36eb49aa221d190c	1137126619	No	Fiber	2000	2000
889996f41b4ccc6e1ab4b5653bfb4b07	1137119367	No	Fiber	2000	2000
578485ab6a45549057699ce6ab5ee62d	1137119298	No	Fiber	2000	2000
ceff4a4048b3c415ea934ee67e516457	1137118580	No	Fiber	2000	2000
73e14841dae0553779c7f48aa9e7525d	1384721714	No	Fiber	2000	2000
250da6ba779ab8cae0715e19640479ee	1286926246	No	Fiber	2000	2000
f351ab01def14afe6083656b17b4dff9	1137119414	No	Fiber	2000	2000
12d2443aa47bdf6a77d38c995badf894	1137118758	No	Fiber	2000	2000
d55eb564afd81ab2fc762a78ebf4da8e	1137119323	No	Fiber	2000	2000
3e28b1694b3f8eabed1f34e440991fac	1286926022	No	Fiber	2000	2000
b93a457dd8c0ffaad25aa325f2557a7f	1286942560	No	Fiber	2000	2000
627b28782b55f63a85616c9fd0ed762e	1137119313	No	Fiber	2000	2000
cf82a5c5136f0825ce3368c853391b51	1286925606	No	Fiber	2000	2000
1a36572df601d223079bb6a003b8d920	1137124596	No	Fiber	2000	2000
662872f89af3357c3b6789224229c60f	1286926251	No	Fiber	2000	2000
d66810eaef09b284abfd9413e6837a6f	1286926467	No	Fiber	2000	2000
31b7ce373715d5425d80580d665df5a7	1286942654	No	Fiber	2000	2000
3d1df8e127bc8bb37f58c1c8ec523259	1137118490	No	Fiber	2000	2000
d8374730a5185bf845e12980620ad185	1137110782	No	Fiber	2000	2000
9a4fef882a8528e0c5737c8099cec037	1137119342	No	Fiber	2000	2000
4bfd6258a296f2193b1f4da5272b7c76	1286924771	No	Fiber	2000	2000
e77ca4af00fc2992639548438078ae30	1286942650	No	Fiber	2000	2000
57a7661996b997d85ae350fbd5d5c9dc	1286942722	No	Fiber	2000	2000
d20f58a6890246e07457a8c346cbd72e	1286926249	No	Fiber	2000	2000
cfbfae856985f3c2e8b35cff880045a7	1137119231	No	Fiber	2000	2000
1e7c85ec5ea86d78f79344881bd55102	1137119060	No	Fiber	2000	2000
f9dbe634aac800c89e1d50c0777fbb27	1286925092	No	Fiber	2000	2000
e55a6b6e2d7b503fe5bc364600e00be8	1137119336	No	Fiber	2000	2000
3999d318aeb6e43b0fc4f3df53ea8339	1286925610	No	Fiber	2000	2000
7783b977b984eff3a17f8c953b886233	1137118786	No	Fiber	2000	2000
e4c514fe7644d9e8ea82dc91b303563a	1137119355	No	Fiber	2000	2000
47b0da4f46a0cf629e2259eb584c2604	1137118613	No	Fiber	2000	2000
313a152cff22df5271e891d9b2a5c980	1137127920	No	Fiber	2000	2000
10c9d6a3ae0d8840b4a162bcbf9c9675	1137127921	No	Fiber	2000	2000
26d119f800ed570921f63440db75b3ff	1137119346	No	Fiber	2000	2000
3479f1c714c2a202754c288e31872401	1137126683	No	Fiber	2000	2000
127ae48844285f936cb33d1869d8c48a	1286924037	No	Fiber	2000	2000
098817c50fc8ffa1df9ffecf3e3344bb	1286925095	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
218df6954672ed7d97a3cd9954a37935	1137118513	No	Fiber	2000	2000
22ecc92fed505f3cf471086fcd4ccb11	1137118602	No	Fiber	2000	2000
cb3bb2e118db5fef8f02cba534221420	1137119406	No	Fiber	2000	2000
af048c7fa2e61e830978701d95bf1bf2	1137118545	No	Fiber	2000	2000
a5ed644f0337aed8db87f05e949e410d	1286925154	No	Fiber	2000	2000
179e4e193414ab58ecd14ee61fc8b359	1286942661	No	Fiber	2000	2000
7c24433be01b9a48de952bdf3a1a84c1	1137118813	No	Fiber	2000	2000
e65cbf51c67ebfe6cf06a33756090e00	1137126618	No	Fiber	2000	2000
5d4107acc96e088004cadf84f3900a3a	1384718712	No	Fiber	2000	2000
30ac225161b131f4f610e5d4c33be4db	1286942734	No	Fiber	2000	2000
935c5421c6e543331cbda26909002df4	1286942666	No	Fiber	2000	2000
f5623365cb4de5f818f359326784bede	1286942714	No	Fiber	2000	2000
4d7d6670a33eb47fd362fcc7388de325	1137119405	No	Fiber	2000	2000
08097f5686d64bff4c27a909a1227f28	1137119232	No	Fiber	2000	2000
45efeef60499cb9034825ef2874e9ec5	1286942737	No	Fiber	2000	2000
3f31705684f24aaff53e26cf925b0d7d	1137119185	No	Fiber	2000	2000
ba02db26c645252bfb5b7756b747b726	1137119344	No	Fiber	2000	2000
1a5ae6d9790a2c9552f645db0f1285d1	1286942750	No	Fiber	2000	2000
dfe9b33a679874dfc47417add4cae349	1137119188	No	Fiber	2000	2000
d4cc9e63364d79d50c3680d2990c6196	1286942653	No	Fiber	2000	2000
9599f48dc69444ef0b111823b81adb38	1137119011	No	Fiber	2000	2000
390f8845a8bde9ce8aea19e7415e9747	1137119335	No	Fiber	2000	2000
9556aff5e168cc37d9e789e489aaf85b	1286942755	No	Fiber	2000	2000
2e393faed854476ab5695003dce405e8	1137118996	No	Fiber	2000	2000
948b563b628cfe59ec2f50c90ab6052c	1137118515	No	Fiber	2000	2000
7d1a869683773aba0a1261e86faaf6d8	1137119345	No	Fiber	2000	2000
cdeb6f42cc2bd0157ded09c5d6458f90	1137118599	No	Fiber	2000	2000
1cc2ddc2f7449a31e5782dbb067bc932	1137118794	No	Fiber	2000	2000
f506a21c0b90fa85280983e11a5b67b9	1137119237	No	Fiber	2000	2000
c97317874fc3d4655a1c892bcaade1a3	1137127954	No	Fiber	2000	2000
ab49a56a12d2ec37415950ceaa78fca0	1286926248	No	Fiber	2000	2000
6e460399727c4cfe3a0bbaaa218d6a5e	1137118797	No	Fiber	2000	2000
0e98c0d085c3f1b34d6a129c3352408d	1286924931	No	Fiber	2000	2000
88ecb0834ae9145f1894b4f8f74c7476	1137118856	No	Fiber	2000	2000
8cc3b4ac2d4b15538f34c5a00f71dd25	1137119211	No	Fiber	2000	2000
d2d05789ccc28b7285a4fdf73c5b19cd	1137119325	No	Fiber	2000	2000
9ed2afed980873862b39f54805552ed0	1137119361	No	Fiber	2000	2000
a0bfbf09f278c0265c3fe965fb9468b9	1286924777	No	Fiber	2000	2000
e67b9d81d8e3ff3f189f4bb484e0f275	1137118835	No	Fiber	2000	2000
16293122ca7d30c948b8b116a47a028f	1286924924	No	Fiber	2000	2000
15a3d3369155f349d3589b180d54b551	1286942647	No	Fiber	2000	2000
9726f6d88593e59ab69ed7831e9d1c6f	1137119340	No	Fiber	2000	2000
04c61057b02367660256f505c227c957	1137119055	No	Fiber	2000	2000
7fcb2f5e8f25c3112e102a4e3f4f54c3	1137119348	No	Fiber	2000	2000
ce3e016e55cf8e3e7d5066b9c9eee862	1137118595	No	Fiber	2000	2000
ffc310cdab57930357702dd508dc211b	1137119209	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
286587186a9c21c800499999e64f2348	1137119236	No	Fiber	2000	2000
42c0bc688617b9b4d4042ecce5ea3034	1286942738	No	Fiber	2000	2000
0e4c938e586b49a87c37e41afdf24c43	1137119416	No	Fiber	2000	2000
ec4933d80c5b38db96b0097a87859043	1286926259	No	Fiber	2000	2000
d24fe659ac0f872c39ab3c4ea1ba4885	1137119212	No	Fiber	2000	2000
f4a7a5c48a7265180e5e6720540af229	1137119227	No	Fiber	2000	2000
2cbde7c2ba601b83c6d42526f7849b74	1286942705	No	Fiber	2000	2000
3d76762e9321723131a0c73ef2a4970b	1137110802	No	Fiber	2000	2000
029836204778d7f3aa284834be2556ad	1137118496	No	Fiber	2000	2000
1149db8346f72013a2aa91513a155943	1286942742	No	Fiber	2000	2000
d3aba20a88bc55d22323910ea1b05359	1137126682	No	Fiber	2000	2000
f4121a4eb8774b994f8fc5467f24326f	1137118570	No	Fiber	2000	2000
77fc0fbd08cab81a7003d011db83c19e	1137119186	No	Fiber	2000	2000
753dd9009c03b1df033aa1fc4eab654a	1137126617	No	Fiber	2000	2000
e4dbacb2f3abc33d530aee5d64a1af90	1286942541	No	Fiber	2000	2000
7069e2030e47fc20f19d963df80509a8	1137119317	No	Fiber	2000	2000
cee35dd1e1fe89e2d54d91d847d1fd6f	1286926023	No	Fiber	2000	2000
1c77a62b71f5d936282097dbf1b52318	1286942716	No	Fiber	2000	2000
8791f838bf1bbcf19d4baf5475b4d185	1137118506	No	Fiber	2000	2000
17bfd02edb58163ed54d2b7f15479a42	1286942725	No	Fiber	2000	2000
39a77b255ec6504247424a9a1f85b9bf	1137118771	No	Fiber	2000	2000
fea888c5874ded4a66598714ea9ff283	1137110778	No	Fiber	2000	2000
6ab1d597fb2d1fb4b589c6377ce972de	1137128001	No	Fiber	2000	2000
f25942d7ef68ce514ad12ab4367e2c87	1137118584	No	Fiber	2000	2000
e0f5a65beb690dd6dc6b691e340b177b	1137118774	No	Fiber	2000	2000
97764ab7526df2f72e7420f7d7c62bff	1137119402	No	Fiber	2000	2000
2f76815c85ad75f38788abe7eeade807	1413416543	No	Fiber	2000	2000
c3d0ec3a6f48dfebcc6bc9cd81144609	1286924051	No	Fiber	2000	2000
cf7c84ccbff11f109ea16aeaed20ba40	1137118565	No	Fiber	2000	2000
83d6e920788812ee6462f024e2784513	1286924918	No	Fiber	2000	2000
23fb91801520961c354048be17768ab9	1137118979	No	Fiber	2000	2000
98647a97c493fdd5486c396cb60db8eb	1137119293	No	Fiber	2000	2000
a0601a56f51c6cd0b136aff6f497ec48	1286925082	No	Fiber	2000	2000
0de44970346a977efcb4f9df5cce3523	1137118772	No	Fiber	2000	2000
c326b9d818cf8a576d689adcf17a34a5	1286925121	No	Fiber	2000	2000
39fe889aba1ac82e9454d067edeea970	1286942740	No	Fiber	2000	2000
c00b9bf9703b5199fa67f09f71f0b888	1137119222	No	Fiber	2000	2000
60102d6873021207a2f8e9eaae7daf67	1286924921	No	Fiber	2000	2000
c32dd57bc74a3108a2e7539fe56b5f48	1286925103	No	Fiber	2000	2000
41fed30d8a9e04acf7aaa1bc259a6aca	1286924155	No	Fiber	2000	2000
ff1e04b51f902a8964d9383a18543c25	1286924936	No	Fiber	2000	2000
f4b2c7fd37a5a48e78e96b97a0f5bbc3	1137119365	No	Fiber	2000	2000
4e4d31a49ff72a8e2a9acf16b51757d2	1137119235	No	Fiber	2000	2000
21ea7b43d26ca8785c5160766319e18f	1286925111	No	Fiber	2000	2000
51e00fd332b6ac6e14ffcd9ca011a611	1137119376	No	Fiber	2000	2000
cda38c2a309cc6e4eac4302609a2bc28	1137118484	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
4ac648ffbf156205531b19883b7b6f7e	1413416548	No	Fiber	2000	2000
c2026fcd50f069ac04bf7066d35dc8c5	1137118978	No	Fiber	2000	2000
1c7a08bb73562cce170874c67def0334	1137110780	No	Fiber	2000	2000
aa311468802858d48780550b5da1e172	1286924342	No	Fiber	2000	2000
849569d9bcde526994d4e1eb3192c5f7	1286924012	No	Fiber	2000	2000
5871a3dc5b9d903d2ca7bcbc146f5e4e	1286924011	No	Fiber	2000	2000
6d127183988b55de81898beb5c6a4d91	1286942748	No	Fiber	2000	2000
e54c5cc9bb5683ddf424d491dbb78cd1	1137124987	No	Fiber	2000	2000
e58168fec4cf171c85187ab8b167f5ae	1137118583	No	Fiber	2000	2000
2706cd7768c438bcc179177764532a4a	1137118671	No	Fiber	2000	2000
0c14a14948bf54b083d5c47bd8f85337	1137118852	No	Fiber	2000	2000
0fc60015fb70a96ac018d7849f9ed232	1137119307	No	Fiber	2000	2000
47373b04eca1539bd13eb00066199337	1286924920	No	Fiber	2000	2000
ed4d7884d96645bf783c687aaf692f0c	1137118796	No	Fiber	2000	2000
54f827e0793378115accf0f47759bdfb	1286942645	No	Fiber	2000	2000
bbc7552dc467184d00f77f3fbb5b07d6	1286942792	No	Fiber	2000	2000
e78a9631e48c244908315f6088bcdc42	1137124989	No	Fiber	2000	2000
3d3e1927f3f3eacdb15da466b8356907	1286925108	No	Fiber	2000	2000
528f3d1814791b9e5ba6dca91c36d5dc	1137118500	No	Fiber	2000	2000
8aefadd59eb362957efa01b28ae44941	1286942672	No	Fiber	2000	2000
7b1702c28b4d1d9833956ed36eaef934	1137118618	No	Fiber	2000	2000
8209ef831c7da5f4007e76b0d3a4a8c7	1137125672	No	Fiber	2000	2000
251983d6d8308cb9de6f3fb0d98e6cf9	1137119240	No	Fiber	2000	2000
eaae95134d834a8a679af6425769be08	1137118477	No	Fiber	2000	2000
cec07a158b8ab913e4196712761329fa	1286942735	No	Fiber	2000	2000
e304ab5890f69dc05d43e8a06d147817	1137119053	No	Fiber	2000	2000
3e9a18bbfabb98f2729bc7b262970ce1	1137118829	No	Fiber	2000	2000
6e568f9bce29a8a29e4e51e5d30fb094	1286942667	No	Fiber	2000	2000
a4236b0e203d01bc60216b822421d80e	1286942544	No	Fiber	2000	2000
e351230a71480d5fa0c81ac8e862989a	1137119219	No	Fiber	2000	2000
a29ec11473c7cb7c59529842c46edcdb	1137118617	No	Fiber	2000	2000
0dd6ed29b736d2f4970b807c5fe1be28	1385111817	No	Fiber	2000	2000
1b1c5ffaba76480062bb58ee53550693	1286942723	No	Fiber	2000	2000
3a3fb6b4bc8208e496b24538cd7dcc3d	1286925567	No	Fiber	2000	2000
38d0cebf7519afe5339581cb0ac27ed3	1286942537	No	Fiber	2000	2000
e652dbb6e74c2aac30f7c57985647267	1286925123	No	Fiber	2000	2000
a55c295714dc4b679269af190c262c25	1286942665	No	Fiber	2000	2000
4b9373ebac9d5903ab65e006976e8f5d	1137119054	No	Fiber	2000	2000
29ef75196b46fc6f13b17345876bba26	1137118615	No	Fiber	2000	2000
60234c9ec5e7ac14ce50ebe39beddba6	1137119316	No	Fiber	2000	2000
2cbc099d06c400aa67a485370379f587	1137118492	No	Fiber	2000	2000
77293c6c95cf8a910d2bda22d5a05f8a	1286942657	No	Fiber	2000	2000
098949e64b39e26b4c2b266878a939a5	1137118660	No	Fiber	2000	2000
81445d9edcbde17c592bb7fcde80883d	1286924047	No	Fiber	2000	2000
5e3cdbbc24daa64ee56dae246339fa7a	1137118673	No	Fiber	2000	2000
a01e223d0335c4389bc057413f83e153	1286942733	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
31df9ffce89e8e44b8a1d60dc5a9bb0d	1137119415	No	Fiber	2000	2000
ea4d001c66d2d2d2996511999b76bbbb	1137118578	No	Fiber	2000	2000
3e164db10c7956e9ece772085c0fff42	1286942546	No	Fiber	2000	2000
3e86255d34600369e62658b2cd2a85bb	1286926450	No	Fiber	2000	2000
b4a20d306889cd8d1f72ea9433ca0f66	1137118789	No	Fiber	2000	2000
8d877552ed190c5c07c5b5e5827e28f0	1137119206	No	Fiber	2000	2000
f0d6734400c58edd4f1a527186d6c8f2	1137119383	No	Fiber	2000	2000
8cb7327c1a530f290f544b0f650173ce	1137119408	No	Fiber	2000	2000
747f8791e0e16a80a20eeead4e5bb7b0	1286925084	No	Fiber	2000	2000
0b56a4fe5538ee01432eb1a389b0bb71	1286924030	No	Fiber	2000	2000
0d894e2eb69671604a213250f9d1a358	1137109882	No	Fiber	2000	2000
1b3b8aeceb1f7db0e9a4fe616b345ba1	1286924040	No	Fiber	2000	2000
8d136efb176007b1dbb56c482eec3508	1137119373	No	Fiber	2000	2000
2fa6035e177ca46f18caf9b0c7ed1467	1137119357	No	Fiber	2000	2000
3735a5d2b0870b4c835c4e0a75adc3c7	1137118819	No	Fiber	2000	2000
236658b564644769c64e39705c16a878	1137118756	No	Fiber	2000	2000
1cec7aa13212683e0373d0e9f33a9750	1286925120	No	Fiber	2000	2000
2bacf667536c55c1f4c72a40ac397e8d	1286942643	No	Fiber	2000	2000
49ee7f77a95b93196a5c055e2e49e3de	1137126613	No	Fiber	2000	2000
7a89836946ef7b58e3155d6b6f2e9aea	1286942559	No	Fiber	2000	2000
5f00103781347d8b7313418a34d8dfec	1137118518	No	Fiber	2000	2000
4bf4a615ff5826a5eff71e94bc90ac8d	1137110781	No	Fiber	2000	2000
260f8b6bbfb3c73e54fc85524dfff3db	1286924929	No	Fiber	2000	2000
c1ddbe3781bad836c5a26aef7bfcb0aa	1137118577	No	Fiber	2000	2000
5a4b589edfdfab0e08ffc96c2af21b13	1137119265	No	Fiber	2000	2000
7d4a6423b264da0ce933824d9bb78c0a	1286926255	No	Fiber	2000	2000
ce0527166f14aa96abd942a4003d8176	1137118816	No	Fiber	2000	2000
135d8942d7036cc3c5483b10d554e484	1286942539	No	Fiber	2000	2000
f8f57c36508a76eaf3cd4ae7ffe7a1ba	1286926453	No	Fiber	2000	2000
35dd20e86e7782e0a1bcfee7c9ce8a62	1286925090	No	Fiber	2000	2000
98c979cf320663f28902af14ddb6ddbb	1286924934	No	Fiber	2000	2000
6d578363ed45bb47c48ef0ef94bc799b	1137119196	No	Fiber	2000	2000
bad06446fe5a5404ce51341404b2e15e	1286942629	No	Fiber	2000	2000
0c9563dc3cdb99e4583f82e10e10391b	1137118511	No	Fiber	2000	2000
5c945d1ca272c375b6bd378fd51359d7	1286925083	No	Fiber	2000	2000
6826d2c7e519fcf3bf370df5448c1c26	1286942743	No	Fiber	2000	2000
8d36d47a363a91c5106c1544a23ca1e2	1137119420	No	Fiber	2000	2000
bf4f622bec895c3dcff5be7cd43a85cd	1286924937	No	Fiber	2000	2000
ba094ebcf8f69214b6b225d5921b6d7a	1137118555	No	Fiber	2000	2000
552ad46bff72736a2542a9188f4549c6	1137119369	No	Fiber	2000	2000
8e72ab519d9a2eec69f62f65d80f2bfe	1137110783	No	Fiber	2000	2000
d439b7cbfb148660c4a2fee4d3783e89	1137119233	No	Fiber	2000	2000
42f94960d08d56ca887ce8a545d61eba	1137118793	No	Fiber	2000	2000
0e80b545571244149aa90e0570578b19	1137118818	No	Fiber	2000	2000
91aa467f927b94eccef5d956e335e14f	1286942534	No	Fiber	2000	2000
7d6a860d82eb178f7484368aa45964cc	1137118497	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
cacc2dbd5c54d96b9de04ab7f3299d1e	1137119001	No	Fiber	2000	2000
28329c3f351f58f722aa2c5be2aba5e3	1137119215	No	Fiber	2000	2000
03ee346cce48e3326b598d85857473cb	1137118815	No	Fiber	2000	2000
5a91aed414350425d2cc6a628a1a8521	1137119010	No	Fiber	2000	2000
6a7f89fbadcc7670985d2cdecf67bffe	1286926256	No	Fiber	2000	2000
24a50f498f343bf17c66c2eea228e97b	1137118767	No	Fiber	2000	2000
6c18306641ec50a2c03e423d42d5dc7a	1137118616	No	Fiber	2000	2000
7dd3a85620825463f3818f0b44e314c0	1286926017	No	Fiber	2000	2000
1aae28d7afac5bb9e59996e48bd8fc29	1137118499	No	Fiber	2000	2000
210a48e3bcbf91641e57103e71774350	1137118783	No	Fiber	2000	2000
3736815d5a67ea4310e47c5ad48fdda2	1286926463	No	Fiber	2000	2000
eadf87a2f6d79c81446c7baa25c1275b	1286924344	No	Fiber	2000	2000
c446057a5cd6f95384657cd78720f3de	1137119006	No	Fiber	2000	2000
04fd9dc5ca7f15fa41d6638ce86bb067	1286942663	No	Fiber	2000	2000
69e798dcdd299b8ceedfeebab79eaf6a	1286942713	No	Fiber	2000	2000
84c53bab437bbf2b578fadae3b54f92a	1137118850	No	Fiber	2000	2000
6780ba0199cdf246fdd2e55c795ce44b		Yes	Fiber	2000	2000
0f3e754079ff17087ba6ec966449bba5	1137119331	No	Fiber	2000	2000
8bd6ba4b6b8119774dadd5a28120c2f5	1137119312	No	Fiber	2000	2000
3230467a11b1720d9765d61e75ac77f4	1286924022	No	Fiber	2000	2000
90d642020c8a86099c2ad98570500022	1137118656	No	Fiber	2000	2000
c3bbd8d682258c0f27bdf7fecacdc7c0	1137125673	No	Fiber	2000	2000
09904cee07b1a78f57c782a5dfd422ab	1286942592	No	Fiber	2000	2000
8d1761a16a3d8b0ba9bb80906590c75d	1137119187	No	Fiber	2000	2000
72092c680130657881dd473488921084	1137118821	No	Fiber	2000	2000
5a82e5436c65796ad4fc280788122d13	1137119413	No	Fiber	2000	2000
b421d919f15602af12192b027ec5ccd0	1137119234	No	Fiber	2000	2000
7d22df2d08d5a40996d47c78620eddc5	1286925600	No	Fiber	2000	2000
1e740812754e15ac1a74589b1dc59c06	1286942727	No	Fiber	2000	2000
faca0ba64a14df7640abf031596812b9	1286942637	No	Fiber	2000	2000
552a91f1e81aebd571f6284577164866	1137119008	No	Fiber	2000	2000
25474b49b4ee7cf9510dba13a1b41e06	1286926465	No	Fiber	2000	2000
5f687a9c0786e3aa6c3dd32dcf9bf69d	1137118997	No	Fiber	2000	2000
f4ca4ee745dbe9169c13a505fee8f678	1286925594	No	Fiber	2000	2000
989b52342e89fc55fd5b33911863b22e	1137119419	No	Fiber	2000	2000
4eb85f5f215bf6c5ae9f742e1be88ad5	1137118491	No	Fiber	2000	2000
2d3987a26dbbbf4ee103e9dcaaec55a5	1137119190	No	Fiber	2000	2000
54f1e4a59aae01504d5bc03baa78ad3e	1137118872	No	Fiber	2000	2000
b2e9e06225ae099854f26c50e8ddd337	1137119384	No	Fiber	2000	2000
dbbcc2585eb29805ca1e00705fe24660	1137119354	No	Fiber	2000	2000
e857d14ebd0f9f945d10a9621497d6cd	1137125033	No	Fiber	2000	2000
f67923e43e35e47307310b1665b0ddfd	1286942673	No	Fiber	2000	2000
4eaa4bf37ab35a376766974e5c1fc618	1137118605	No	Fiber	2000	2000
99775fd3944f16ed03f04b5e3f4a610a	1137118766	No	Fiber	2000	2000
dd637005ab77e27a6ba4ebf33fb228f4	1286924926	No	Fiber	2000	2000
5e9dac23c18e3650cdaaefee8b0aa0a1	1286942741	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a7a49f247c48453b99fc4a59b45713a1	1137118581	No	Fiber	2000	2000
f556521d38d62abcb8f5f5eec6dd75b8	1137118612	No	Fiber	2000	2000
15f2604ad1000e8c779eef8ed3162aa3	1137119343	No	Fiber	2000	2000
999f6956dc1e4811257af3d23dcbadb3	1286924034	No	Fiber	2000	2000
20070fc13cc29f60008a465eeb82062a	1137119238	No	Fiber	2000	2000
62ec1b35f211b248748775ae0ba1bd8f	1286924046	No	Fiber	2000	2000
3daeb0251fd1e8d6d144c0c3a7a6c05a	1137118504	No	Fiber	2000	2000
bcf9fdedd6d53e14035f26980b45195a	1137118768	No	Fiber	2000	2000
02da0287f87978e6d7171721de0444b6	1137119057	No	Fiber	2000	2000
e2211968d1e0077933a55729342d7c69	1137126616	No	Fiber	2000	2000
45b0229e1374b8d7c6631ef4a570642c	1137118601	No	Fiber	2000	2000
71e3457d6610ac25307ad40f00175168	1286926252	No	Fiber	2000	2000
42e90c37dbe1485aec9eab64bff47d5c	1137119216	No	Fiber	2000	2000
ed9bdf32b1937a262e4112838b7fd0c8	1384718816	No	Fiber	2000	2000
17ad755a5c64b8911666c0b825257ea0	1137119228	No	Fiber	2000	2000
128cbb7515fe08def0a66a8f82cba71d	1286942731	No	Fiber	2000	2000
c8b4afe1dfa696fe0359079d98d1f537	1137119374	No	Fiber	2000	2000
389e1bc60c47585775229717fde09d68	1286924775	No	Fiber	2000	2000
6791acdf3ed69eaa74b98bce448284f5	1137119201	No	Fiber	2000	2000
1b8d3bd38aaaea4d5046d81d6566ffd4	1286942545	No	Fiber	2000	2000
4640ac18281e5e440f35a0edbfe1f1d4	1137118597	No	Fiber	2000	2000
ceb2b7ef42bcbbfe6cbd3f5d70e8dce1	1137119192	No	Fiber	2000	2000
e099e53631201864eb5b5dd2506fa6d0	1137118800	No	Fiber	2000	2000
c0d88f6f4ab41257e9478d0bb0a828d5	1137118784	No	Fiber	2000	2000
88ea8238427d7078d1f91b545ed04c82	1137118610	No	Fiber	2000	2000
9b1894e44f61e976ea23635b2810853f	1286942715	No	Fiber	2000	2000
2c5a7b7a334f873287e556d4c3e59136	1286925107	No	Fiber	2000	2000
c207873d6864c89def96f502d14d4ff2	1137118795	No	Fiber	2000	2000
de21022354e68f3404c9523e8f50ce68	1286924023	No	Fiber	2000	2000
7b51e778d73ccb4348e2206327e6f143	1137126615	No	Fiber	2000	2000
58c3177a55ff7e60d7d72c46627e1191	1286925566	No	Fiber	2000	2000
9106e7e4346d7b336aa4f4422d397141	1137118787	No	Fiber	2000	2000
ca82794880982c98f6334c7816027457	1286942732	No	Fiber	2000	2000
56a6be4af7b88530eebd4011b0c64224	1286926455	No	Fiber	2000	2000
7e52195837712d43e43d33c1e5359856	1137118811	No	Fiber	2000	2000
2a75fb0efa201128a4e75d1208418e3c	1137119303	No	Fiber	2000	2000
bccec823086b5557e99fe9c03f4afd75	1137119352	No	Fiber	2000	2000
e6cca8b7f71d03e010df81eb66c03839	1286942628	No	Fiber	2000	2000
6222643b23f6ac1dca16ba15c9d79f62	1137118606	No	Fiber	2000	2000
77784d3efd76b03ed414d0d133856e6a	1137118592	No	Fiber	2000	2000
9a6e6b3d625f3588b7fef01fc870813a	1137118764	No	Fiber	2000	2000
800c183fe8fca4adff6357d7670ae453	1286924156	No	Fiber	2000	2000
1a968ec89c89b91e06ef8f8d5ed2dc88	1137119315	No	Fiber	2000	2000
40fb7cca6ae0ae7727fe6a9f0e50c662	1286942708	No	Fiber	2000	2000
3fa811f75eaf500e795e134bfaf243f9	1137119310	No	Fiber	2000	2000
f7be6fe6a6cf7444237a7a7f46c87b23	1286926462	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
ab769f32a441be48ddbf5939e1f797f4	1286926025	No	Fiber	2000	2000
aa2354e00219468a3d204ef50fec3b2c	1137119062	No	Fiber	2000	2000
eedbca2eaa434488594bc109d5466bdc	1137119005	No	Fiber	2000	2000
afaf70e81e8a761ea70e171ef46964ba	1137118993	No	Fiber	2000	2000
b7bb4f0508edb11ffc19c7ffd80c78b0	1137118762	No	Fiber	2000	2000
dc723ded6f1c03ac337cca335a87497e	1137119356	No	Fiber	2000	2000
3cf991af4bb9a5476b4a13ba46e2e767	1137118488	No	Fiber	2000	2000
e49d4a0b1b0829e9c8da72b06640fde1	1137119297	No	Fiber	2000	2000
7db46eb3fd3c7793db241fe776e2453d	1137119009	No	Fiber	2000	2000
a9c2bb8310ea562d1ddb179770e72731	1286924773	No	Fiber	2000	2000
ef629e68c76dda3903668f0b2e1e0831	1137119208	No	Fiber	2000	2000
c58f97205a4d986c3cd0dfdaf50d3009	1137118590	No	Fiber	2000	2000
853af26712b5101722f713cfff5309ea	1137118495	No	Fiber	2000	2000
932071e2390f26803ebe9c2d7a176b31	1137119363	No	Fiber	2000	2000
0eaa7e88d647f34c1bb2fe0b7d69cc83	1137118588	No	Fiber	2000	2000
7ac07fad4843e83a6d39ddfaf58c07f1	1137118991	No	Fiber	2000	2000
cd22feb08eaf9cf34740d22d43206946	1286942631	No	Fiber	2000	2000
c6486f066c63b359890e7b58cc79fa81	1286926461	No	Fiber	2000	2000
2f2757389ddd4ac43ed7b959e80b5d30	1137119328	No	Fiber	2000	2000
8ca2ab62937c34a4b8ddf7ede31ccedb	1137119418	No	Fiber	2000	2000
60a1793c38fe7c582e8195122ad773c1	1286924043	No	Fiber	2000	2000
c954ff1148d1085b21c5ae73c8996d28	1137124990	No	Fiber	2000	2000
d634637be119749d01daac6f6d7992ca	1137125676	No	Fiber	2000	2000
2833f62bc0d953232b7431d921af373e	1286942757	No	Fiber	2000	2000
9b70abde22e676eb3ad1145381910986	1286942719	No	Fiber	2000	2000
c36d11e98a7b0a44e79df590e8fe9cee	1137118846	No	Fiber	2000	2000
1aa083a01bb43d43d93bdd74cd36e8e4	1286926247	No	Fiber	2000	2000
65af0a1c236925c67accb97f0f33cbb3	1137118851	No	Fiber	2000	2000
44e17fa766d00e0e2c9d687f98df1399	1137118812	No	Fiber	2000	2000
a1c598dacaedbda08d22570ab519f2ac	1137119305	No	Fiber	2000	2000
3fe555479134cdb29cd17f5d6b8bdba1	1137118759	No	Fiber	2000	2000
161d21b778d6ed7d494eed0f1b940009	1286942718	No	Fiber	2000	2000
80cfb54f4242cba068ba7fac98b3f4f4	1286926245	No	Fiber	2000	2000
b88157715c7092120a7f42deccdc152f	1137118769	No	Fiber	2000	2000
c8a1c47feb1ac6df628095e15f5ae07c	1137118871	No	Fiber	2000	2000
9a17447e44c290da7a30319d2b0c6bc0	1137118478	No	Fiber	2000	2000
771be8016b9d72082edc078fa86f5671	1137118801	No	Fiber	2000	2000
27d92ecc1ae3190b35cba3d958972da9	1137119410	No	Fiber	2000	2000
2c1675cb0080eeb644d9b49833bfff99	1137118487	No	Fiber	2000	2000
daaaeb92cdfc0bd8de3582b89c861643	1137118485	No	Fiber	2000	2000
05f7ecd24452cf04380d23e6f6cf8118	1137118805	No	Fiber	2000	2000
b17c4e68c1800a0c1cbc2261f661f270	1137118777	No	Fiber	2000	2000
0f87db6b171ab4a394fc6a835f753665	1137119324	No	Fiber	2000	2000
86a0b9c799fa6330dfab60d93933dd78	1137118832	No	Fiber	2000	2000
5d3d9811f2080b367de25d12869a3370	1286942736	No	Fiber	2000	2000
4343513c2c47bcea8e43bc2f25d9f17f	1137119052	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
f46a3b839055ca8f94cea98cbcb51f77	1286924028	No	Fiber	2000	2000
14e6bafade066cd00eb6788442c7eac8	1137118847	No	Fiber	2000	2000
0e713ee962e8d3b31b6edf51892a318b	1137118778	No	Fiber	2000	2000
92a5dfce8770fdcaa1aa4af8d7950085	1137119358	No	Fiber	2000	2000
136ae4a43f988eb3e69562f784650191	1137118984	No	Fiber	2000	2000
14f53807d35aedf24fdb236228784c0e	1286924917	No	Fiber	2000	2000
014eaf3e1a9521f89c43c3a147effe2c	1286925089	No	Fiber	2000	2000
aa8e57bed4834f45980bc8ef817b42cd	1137118589	No	Fiber	2000	2000
d963817b2e56b714f9f2ca8e67f37a1f	1137118857	No	Fiber	2000	2000
25fdba623b718cd3cf50a60e55860927	1286942721	No	Fiber	2000	2000
41d52bc65a90b8732ba2d503524bda7c	1286942641	No	Fiber	2000	2000
cafb27bb8dd99dfb3465ccb32a71ab36	1137119371	No	Fiber	2000	2000
f6c0d61992653bbbf5d11789a373f134	1137118849	No	Fiber	2000	2000
f113f3b4b89d97c0b091928787b09e84	1137118803	No	Fiber	2000	2000
2c9c2107a32752af6f62cdf9ae2d5c5d	1137118999	No	Fiber	2000	2000
35dc3049f12ac2c563c537d0e0cd7122	1137124998	No	Fiber	2000	2000
f2041f8e1bc48a1acd1a36825df075a1	1286926034	No	Fiber	2000	2000
8c2cbf391b0702d1dbfe69fcbf087b97	1286924053	No	Fiber	2000	2000
ee230f709c9a9ce6c4c775181a763654	1137119050	No	Fiber	2000	2000
586a6ac4585fe5d4476147bef7a437dc	1137119341	No	Fiber	2000	2000
f5dde0665963019e0e76d1765b30d87c	1286942535	No	Fiber	2000	2000
51d58effb4b55957b330a62415cb966f	1137124992	No	Fiber	2000	2000
c82a36fe595fa7ceb643eff9f47c6720	1137119362	No	Fiber	2000	2000
617e99f063f5a57eb8a28c92ad2b1254	1137119404	No	Fiber	2000	2000
b96f15f3592e559f704d05ffb2e7f671	1137119380	No	Fiber	2000	2000
b189f7e99f10559bcb4190f41c4597f7	1286942710	No	Fiber	2000	2000
f45607f25b16b309b3745df5ae42c049	1137119221	No	Fiber	2000	2000
b5a6a7c7ac15cb2b39ee41c87b5d697d	1137118498	No	Fiber	2000	2000
1f6009122dd8f49656281bbe2444aca9	1137119337	No	Fiber	2000	2000
4ebb2c5f0c93bedcf5a5d7b5523ead35	1286924052	No	Fiber	2000	2000
f1bacf033157ba5ae175fbd24603286a	1137119372	No	Fiber	2000	2000
4bf621448e3f075cf797daf78af8b755	1137118483	No	Fiber	2000	2000
9afe69df46d984a9a754c647505f6ec4	1286942640	No	Fiber	2000	2000
f2b529f0867f0163c98b6e950dac91a2	1137118598	No	Fiber	2000	2000
6e881986abce69da29e81562886bc051	1137118814	No	Fiber	2000	2000
d04496722a71e62a71d4761b48a71ce9	1286924928	No	Fiber	2000	2000
f275f3b6be9ddadb5804f79f9d2d5ff9	1286924016	No	Fiber	2000	2000
440940badb57b253fb1917883ddfe770	1286925113	No	Fiber	2000	2000
96577cac369d282cc2304f6488b4d6ac	1286942662	No	Fiber	2000	2000
6a84432881eea12beef422baa72e6818	1137126626	No	Fiber	2000	2000
679bc53c583ff65ad1e70fdb1172c55d	1137118512	No	Fiber	2000	2000
38c69ac7a8b8f8a57207df18978f4f33	1137119407	No	Fiber	2000	2000
22a219adcf1969ade1893c5ca1aebc65	1137119311	No	Fiber	2000	2000
cf4d12626d7562cc3b56687392e854f7	1286942720	No	Fiber	2000	2000
e42dd7ee9dd1d0191e8e8979f863d271	1137118763	No	Fiber	2000	2000
03db193855f633eb8e7726747df48872	1137119347	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
bd24576bf956de3287d0db334ed400e3	1137118519	No	Fiber	2000	2000
dd114a4198de1881cbd019c4ccc9cc0f	1137118479	No	Fiber	2000	2000
0caf1437cc1afca20a800a056f975493	1137119012	No	Fiber	2000	2000
896ef03b23e0f9137cf71cbff3bfab38	1385111290	No	Fiber	2000	2000
502e2c89cf4e5b559591aec380bde29b	1137118486	No	Fiber	2000	2000
514b604c12165e029f73c7b7b9210009	1137118988	No	Fiber	2000	2000
6e2956be9868b8ce5b782fbc6dad8140	1137119332	No	Fiber	2000	2000
da2274b2bf2a394e01cd688eb53e7914	1137118985	No	Fiber	2000	2000
946d67230306484bc3073a6b76b7801f	1137118802	No	Fiber	2000	2000
3944df2b4f75257e7c2af9587150f022	1137119013	No	Fiber	2000	2000
69ab02c7e06835157b4ae42811785b67	1286942669	No	Fiber	2000	2000
568711d1044037df957baa2af6675a3d	1137119382	No	Fiber	2000	2000
0244945b9305c88d7ecb592749538949	1137119318	No	Fiber	2000	2000
14a9a0aef7085c7b340b2bfd2a8bcfc7	1137118833	No	Fiber	2000	2000
b60dc809d0d72a267872c294822a5198	1137119004	No	Fiber	2000	2000
0181ab4f96ca5b486b68ef1e7f7f9d2d	1286924039	No	Fiber	2000	2000
a4e342f25dd1d34a54022fed8eea78b3	1137118799	No	Fiber	2000	2000
b69d6f99aae632942ec6fbad7e663fac	1137119379	No	Fiber	2000	2000
213896258c62b33a939c68d1cab16ed3	1384718688	No	Fiber	2000	2000
53204484b7ec068fee5d20ebaecc7d93	1137118809	No	Fiber	2000	2000
c85d1b5a65786ce70dd50b49e2e55df2	1137126614	No	Fiber	2000	2000
57365b43c2b3383d644e0747f744f6ca	1137118493	No	Fiber	2000	2000
a74e261a5c8182ce2de6bea88c1f8af3	1286926452	No	Fiber	2000	2000
f2c3528b82ec965d0c3c5501f1309da8	1286925097	No	Fiber	2000	2000
75fb7e36e2073a15fe74a9266ad7fcc0	1137119386	No	Fiber	2000	2000
aa74f6d6967b644d87eae104e6384e17	1286942646	No	Fiber	2000	2000
c20e901d4eda31eb50f8eae91e7040e6	1137118502	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 32 – Budget for Project Area IBO-872

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Permitting Costs	Permitting Costs	Professional Services	$169,460.00	$73,244.00	$96,216.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$200,059.00	$86,469.00	$113,590.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$178,752.00	$77,260.00	$101,492.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$469,116.00	$0.00	$469,116.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$27,663.00	$11,956.00	$15,707.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$704,468.00	$304,483.00	$399,985.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$618,264.00	$267,225.00	$351,039.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$183,540.00	$79,329.00	$104,211.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$19,242.00	$8,318.00	$10,924.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$10,783.00	$4,661.00	$6,122.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$208,740.00	$90,232.00	$118,508.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$8,301.00	$3,589.00	$4,712.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$87,000.00	$37,607.00	$49,393.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$10,800.00	$4,668.00	$6,132.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$2,304.00	$996.00	$1,308.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$34,706.00	$15,001.00	$19,705.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$75,752.00	$32,745.00	$43,007.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$220,816.00	$0.00	$220,816.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$21,681.00	$9,372.00	$12,309.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$40,500.00	$17,505.00	$22,995.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 32 – Disbursement Schedule for Project Area IBO-872

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 32 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-872

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 32 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 33 –Subaward Conditions and Statement of Work for Project Area IBO-888

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$154,106.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$154,106.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$154,106.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 33 - Specific Award Conditions for Project Area IBO-888.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[73.53%]; [$428,048.00]
Total Project Cost = (subaward funds + match)	$582,154.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$154,106.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-888 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 33**. The Project Area is depicted in the map in **Appendix A of this Exhibit 33**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 33**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $428,048.00, which is 73.53% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 73.53% for a total match of $428,048.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 33** in the area depicted in **Appendix A of this Exhibit 33**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 33**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 33 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 33;
- Appendix A to this Exhibit 33 – Map of Project Area IBO-888;
- Appendix C to this Exhibit 33 – Budget for Project Area IBO-888;
- Appendix E to this Exhibit 33 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-888;
- Appendix F to this Exhibit 33 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 33 – Project Area
- Paragraph 5.B(2) of Exhibit 33 – Project Locations
- Paragraph 5.B(3) of Exhibit 33 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 33 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 33 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 33 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 33 – Access to Service
- Paragraph 5.B(5)e of Exhibit 33 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 33 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 33 – Map of Project Area IBO-888

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-888

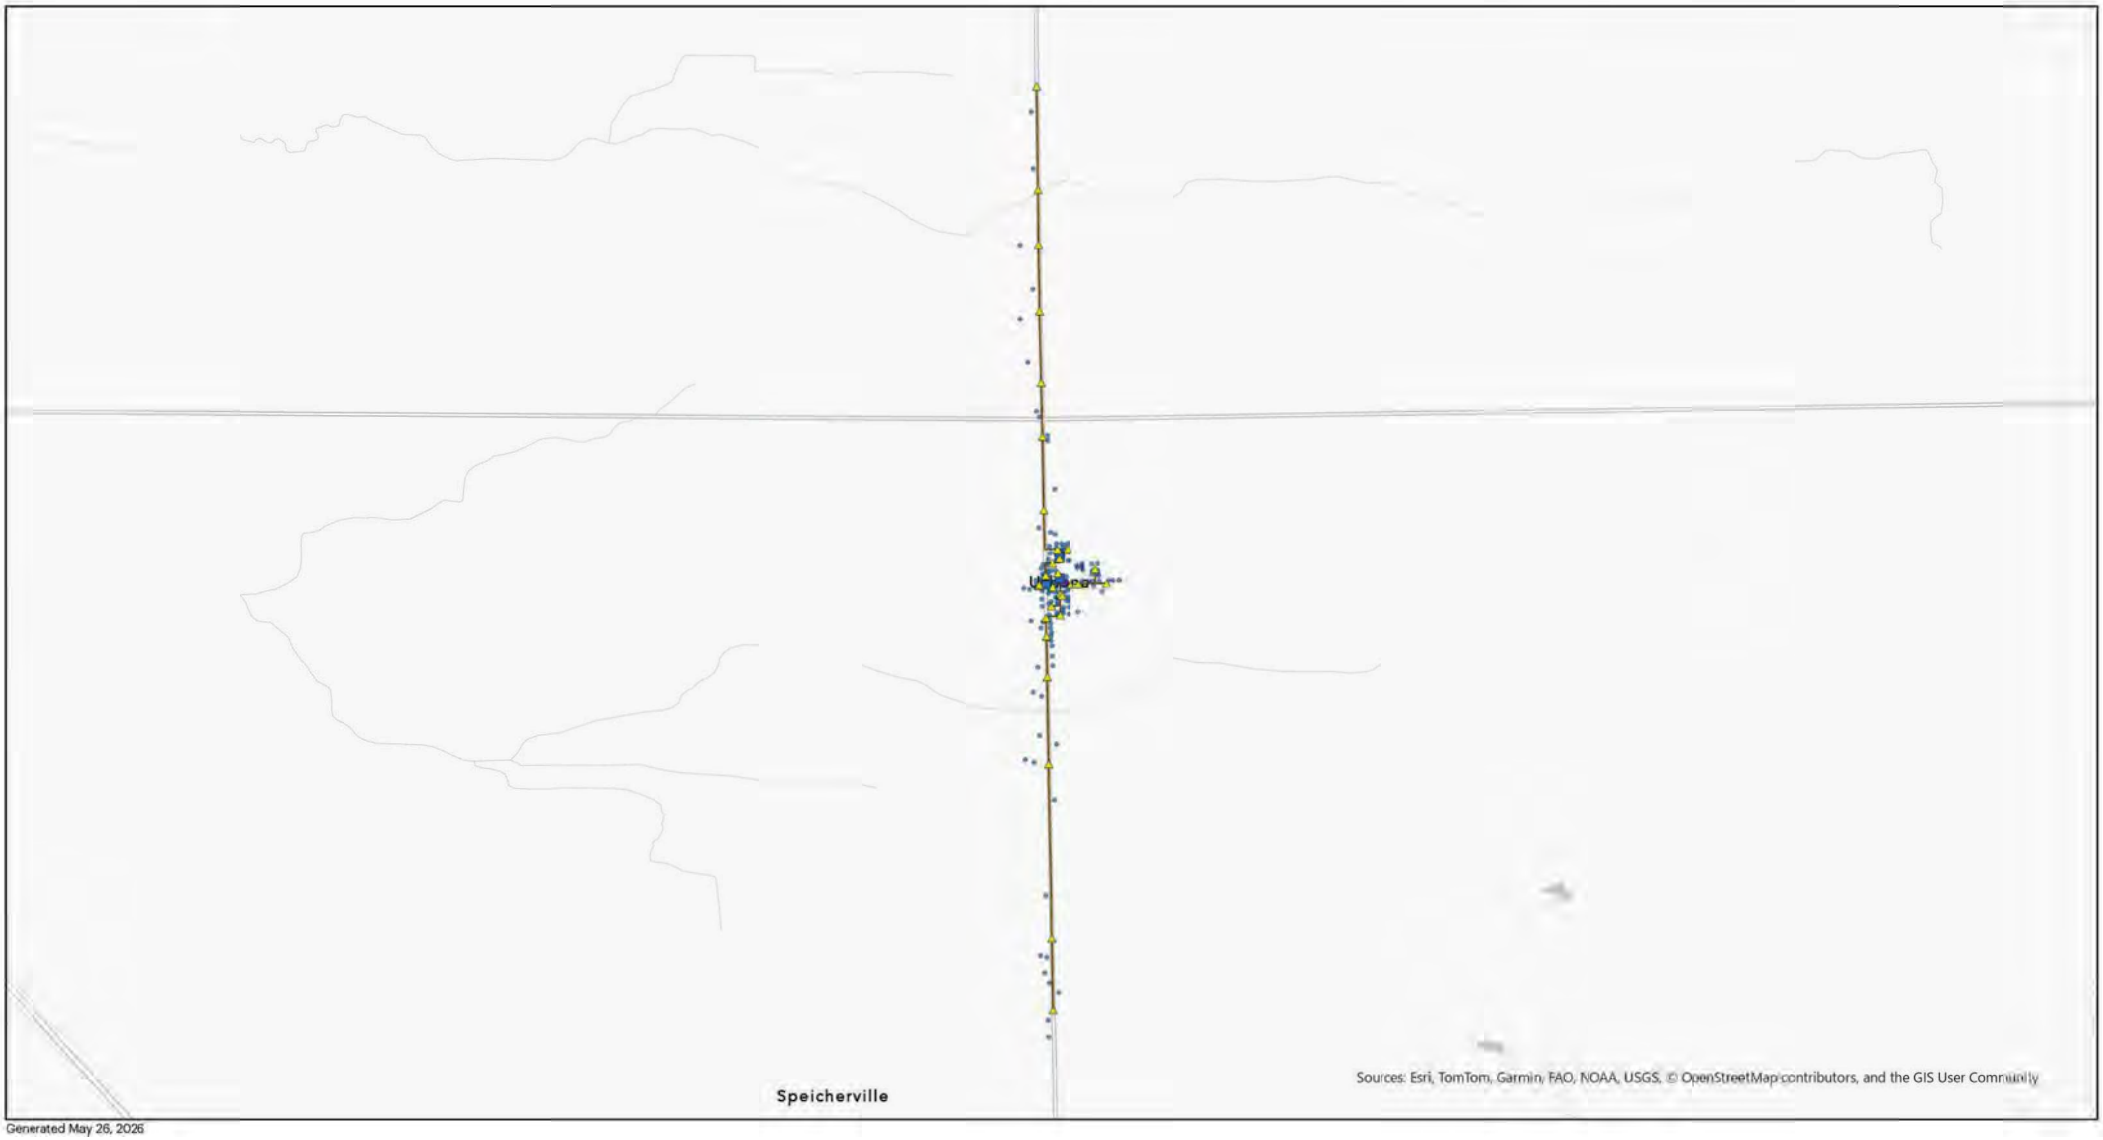

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 33 – List of Locations in Project Area IBO-888

Brightspeed IBO-888 Location List

148 locations

ID	Location ID	Is CAI	Technology	Upload	Download
c5fc7d622e9e70cb1ac9402565a66946	1137110360	No	Fiber	2000	2000
654350b5d46aa75429b0f3c85b2bd06d	1137110362	No	Fiber	2000	2000
8abe4b62f779e11705b05c6f6185a3b9	1137110369	No	Fiber	2000	2000
c61bc54bb35d1effbaae2a7587b5055f	1137109891	No	Fiber	2000	2000
71d66e5d26af16d477fc5e04cbce9382	1137110403	No	Fiber	2000	2000
8e6ca02dea6b1ff64d30fcaf9fb17f7a	1137110460	No	Fiber	2000	2000
a026ebe5ebcb81cdab5a1bd751ab533b	1137109892	No	Fiber	2000	2000
2b4599c802642278f54cdf5b2474c468	1137110428	No	Fiber	2000	2000
1fbc95f0fc2f681f68fedfa5023e7549	1137110441	No	Fiber	2000	2000
91b32b6f3c04b5cf319d4387e3af3ca5	1137110286	No	Fiber	2000	2000
79a40269898a390df3512ebdc9cccb2c	1137115856	No	Fiber	2000	2000
4362427ab90d18b59462c5785561d3b5	1137110292	No	Fiber	2000	2000
80f1b281c35ba672493db8edb18c0e76	1137110425	No	Fiber	2000	2000
1bfa2b3816f0259d693aa8ddbe3c8cd6	1137110290	No	Fiber	2000	2000
cbe01cc3a807f5e4b707e482e406fbc1	1137110459	No	Fiber	2000	2000
66fc74c7ada29223f1bc98c2cf6bc77c	1137110445	No	Fiber	2000	2000
b8b3c35908a8185eee44b32164e54d26	1137110372	No	Fiber	2000	2000
976e8d0132d6c557fca3248b11e7fc28	1137110407	No	Fiber	2000	2000
359ebdb2457e6da958e0e2ade615a3ea	1137110448	No	Fiber	2000	2000
47337a6415b1aae6d096b0a652e3062f	1137110470	No	Fiber	2000	2000
43bbf4287bed587f64d5a3ebed2310fe	1137110439	No	Fiber	2000	2000
a11cefb6356ea878a11d626871e6fd30	1137128339	No	Fiber	2000	2000
c116967b21476749d4359e69c9218aeb	1137110184	No	Fiber	2000	2000
7d7315b2c79459a7f2198ebbe2b253f8	1137110377	No	Fiber	2000	2000
0d02780300ae112ed08bbb904bc639d9	1137115349	No	Fiber	2000	2000
e5f2cb740304f027c1c952154ff54cf2	1137110447	No	Fiber	2000	2000
67b0f05e439908e1ee1ce5d76b566b5c	1137110395	No	Fiber	2000	2000
ff22a8737b325d58a1b9a9fdcfb63b5a	1137114606	No	Fiber	2000	2000
a113bf81b61868dd66c5061ae85ee3fc	1137110364	No	Fiber	2000	2000
5301537417b245c662da2382ffcc6edf	1137110293	No	Fiber	2000	2000
a2e83cee82a36aa8f9cf59d7dc995d23	1137110450	No	Fiber	2000	2000
89b3f0fa1ecc781afd97c4c5ae323867	1137110438	No	Fiber	2000	2000
9a85628a001d84c3dcae682e40e6fed7	1137110365	No	Fiber	2000	2000
0a33c2ab1b21298f4f116fdd4a5632f2	1137110291	No	Fiber	2000	2000
1b3d76d244220e7389fc09a565d6852e	1137115849	No	Fiber	2000	2000
313f8067f4076ce8c54b3120870ca69a	1137110296	No	Fiber	2000	2000
c71a5f075ca78466fc5ad00175804bc4	1137110295	No	Fiber	2000	2000
75b80232d11fa91e501c4fc38477431e	1137110402	No	Fiber	2000	2000
e09acdde0d41994fa64e70859cbd7a5e	1137115859	No	Fiber	2000	2000
100f29b8ea69fd9165cec751cb95eccc	1137110456	No	Fiber	2000	2000
27afe0d1e762c6868f1ea05148017c79	1137110368	No	Fiber	2000	2000
f8c2179824f550ad214117d22e7b0db3	1137110406	No	Fiber	2000	2000
e041c02d68ad55ef753c39a9184815d8	1137109894	No	Fiber	2000	2000
c4274f76dd6f2e077b0789894d893884	1137110300	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
b653ffc058acbeb228b4010b6a5feaf5	1137110285	No	Fiber	2000	2000
9682b69ca2a454d266525662d9f21943	1137110455	No	Fiber	2000	2000
8ad0025eeff262325ad0fc63c709a5b6	1137110298	No	Fiber	2000	2000
ffc49ad413a8df169b9e137b3e4029f2	1137110373	No	Fiber	2000	2000
f44ab657b6ac3a63d752f8a5fe6ea9ef	1137110294	No	Fiber	2000	2000
77342378b6eaf5a650d4b2de829feaa1	1137110444	No	Fiber	2000	2000
18396a500229ec014bddd6d86ff5d50a	1137110416	No	Fiber	2000	2000
c7e27344abf126481d4d03b8a91153aa	1137110468	No	Fiber	2000	2000
9d4bf70a68faa3ed5060748545c9e33d	1137110399	No	Fiber	2000	2000
a9151e19b32f2340813155116f397fb9	1137110413	No	Fiber	2000	2000
9ff86bca1d9bea84d8692ab2b60b754c	1137115858	No	Fiber	2000	2000
3178387b7244cff5a8609e43863f053c	1137110434	No	Fiber	2000	2000
b747251017f77a00f97ada2a3f28d7a4	1137110491	No	Fiber	2000	2000
a8901131bdb170058b80ae1e08a2c035	1137110367	No	Fiber	2000	2000
6dc110326b590ad5515057cea0caea48	1137110376	No	Fiber	2000	2000
3c87a312e245cfdb484d32f4c4127057	1137110489	No	Fiber	2000	2000
18a1cf2984b883cbf1cf631ff388e756	1137110393	No	Fiber	2000	2000
9a6625e44f533a6595bca89f3be464cc	1137114603	No	Fiber	2000	2000
9f44057ec74795d9abe44a3dbe42f581	1137114601	No	Fiber	2000	2000
abb182737902234034f5e214563e7aac	1137114600	No	Fiber	2000	2000
6971b6c84e08e0967922a4f0ff536930	1137110414	No	Fiber	2000	2000
4daffeb164b7694cb1c3718f6fb35332	1137114604	No	Fiber	2000	2000
1fe021568e6247141e90281f0564986d	1137110427	No	Fiber	2000	2000
2ed600995704ad323ab8726d0312daee	1137114602	No	Fiber	2000	2000
24a364fbf627b0d527e4a252609da76c	1137110482	No	Fiber	2000	2000
a54a21ed42ea23573cd943bc48eb15e0	1137110432	No	Fiber	2000	2000
cffbeb92e5c599768e128c2bd9e2e355	1137115852	No	Fiber	2000	2000
ae4de72888f6824754884088adcc425c	1137114605	No	Fiber	2000	2000
61d57e7dbf2c5c9eecef5175e2816928	1137110457	No	Fiber	2000	2000
8a7a8b7790196e8d9e627dfc9c9e43cd	1137110383	No	Fiber	2000	2000
92ac0830a920ff6982249e93d5341d2c	1137110288	No	Fiber	2000	2000
de72382c2584f049fc1960231c4f36b0	1137110452	No	Fiber	2000	2000
a88a151e8dce6395946981f591945990	1137128345	No	Fiber	2000	2000
ce66030f8e27827b36f895434fab9cdc	1137110430	No	Fiber	2000	2000
dac112c9abdf7aec8098b91d69cc09d2	1137110451	No	Fiber	2000	2000
9758eea1390882d89793fb670f2a7bc4	1137128340	No	Fiber	2000	2000
122cffc394961b2ea0098a14c4cf2f41	1137110440	No	Fiber	2000	2000
6e51ac465456f92f803143603d13f21e	1137110417	No	Fiber	2000	2000
68954cc3dd6aa9981b82f35da4d010c9	1137110471	No	Fiber	2000	2000
8f758074cebec77ea55969d568f19e46	1137110421	No	Fiber	2000	2000
b796575959d7ad1636475b597ad9c2f2	1137110424	No	Fiber	2000	2000
1de19f50e79c68ccf35ba41b883c2080	1137110437	No	Fiber	2000	2000
b957a29fab1af162ed53b93ebc9dd8c8	1137110463	No	Fiber	2000	2000
4dbaa494a4ac79bd6604e032c30cc57a	1137128338	No	Fiber	2000	2000
1a5114d901e6277ec3001d877c735eac	1137110401	No	Fiber	2000	2000
2e3c9ceb68c321e51afc688f4ea46c94	1137110420	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
9f6ef16f1c379e33304191bedf9073d9	1137110299	No	Fiber	2000	2000
a20f55fa3efffbd9a5a6dc03d19a6ab8	1137115906	No	Fiber	2000	2000
4d2351db48eacd8b6f5a166837ed1a66	1137110429	No	Fiber	2000	2000
055ca5fee081857bfe096540e3d6e7db	1137110397	No	Fiber	2000	2000
b26e26a85b9db001517b3f66d4dcb6dc	1137127890	No	Fiber	2000	2000
ad887aa0dad05ec111439eaf2acd01db	1137110386	No	Fiber	2000	2000
e380558102fff547f7f76279bf1a7712	1137110435	No	Fiber	2000	2000
4c03c92c9dcb19232cb07b3688bb146c	1137110449	No	Fiber	2000	2000
68b6972334de731594b7b2b6ab2a546e	1137114599	No	Fiber	2000	2000
bdad430ebbbb3e2871c333e9829d96b3	1137110363	No	Fiber	2000	2000
c4c404ed067286cb9fb87e95adaa29ea	1137110392	No	Fiber	2000	2000
26ec7b956aa86914ce9e28d0cc5b22c9	1137110398	No	Fiber	2000	2000
e2668fd0a7b936b84d7b050690b1fa5e	1384723518	No	Fiber	2000	2000
e8144275dfcb8cc49600c476d2a22719	1137110409	No	Fiber	2000	2000
e125340b01e2663d79a1544060dd0785	1137110467	No	Fiber	2000	2000
732e3b4d5f759ecf3a758193f695f68d	1137110404	No	Fiber	2000	2000
78a0af968ebcff1e5c020cab61cce89e	1137110412	No	Fiber	2000	2000
ced06a338be10ec1f748fe0ccaaa0d5d	1137110426	No	Fiber	2000	2000
1de1c095f2fb7ca1134bb913b4d7fdcb	1137110370	No	Fiber	2000	2000
2c4f857ed58031a813388b38888e57b1	1137128391	No	Fiber	2000	2000
1065d7493f8730804a0b14fe7e4667e3	1137110396	No	Fiber	2000	2000
cec6b5895e7364eae7624606cf851c9b	1137110442	No	Fiber	2000	2000
0004e0a1680e98cc20104cda57b04207	1137110405	No	Fiber	2000	2000
20e3d7d8a6c87f489b828a404fc6dc44	1137110464	No	Fiber	2000	2000
62a0c3534cdc37e7f0938055697ca3bf	1137110486	No	Fiber	2000	2000
95cc32e664dda8e5f57813de35d2ac0d	1137110485	No	Fiber	2000	2000
efd25dbd7df734beb1fa99cf0a01744c	1137115861	No	Fiber	2000	2000
33253618fde5c62aeea96a3aa385baf1	1137115853	No	Fiber	2000	2000
ee74f7121c7f109f2dd02976f3942bb0	1137110443	No	Fiber	2000	2000
10573a589c8470ad3a8c617db278decb	1137128343	No	Fiber	2000	2000
cbf77164c980f784f998021ee6d0dea4	1137110361	No	Fiber	2000	2000
ba0745b4318bf5ba6bf00c541a8a7c71	1137110487	No	Fiber	2000	2000
9d1d2eaa863618e0be44b94b98596900	1137110375	No	Fiber	2000	2000
3b8e91be472722fee6ec1f3c771d8603	1137110289	No	Fiber	2000	2000
3b61f816734e797816c69296c7aa1d89	1137110418	No	Fiber	2000	2000
5f6ad6a6b1d3f2737fd6d54574946da7	1137110461	No	Fiber	2000	2000
2c7e20c1731c06e2d5c8190c5385fabf	1137110359	No	Fiber	2000	2000
eed84d83cf57d880ae980ae530d04099	1137110366	No	Fiber	2000	2000
6065b03ae10034a15fdbea8ad7f07dbc	1137110465	No	Fiber	2000	2000
c8e34ad9465701abbbdd8816b096f458	1137110431	No	Fiber	2000	2000
2b7e9ef96670f0e4251f9f5cb60e2ff2	1137110415	No	Fiber	2000	2000
bf966b497871f8855ea0350cbcbf758c	1137110371	No	Fiber	2000	2000
7e07a79153cbfe4f0b01b3fe1cd4aa5b	1137110419	No	Fiber	2000	2000
2e782b685ccf7a70bf09f6a4e4f0bbba	1137110433	No	Fiber	2000	2000
71f0095770b4155449b6e8f818cd1cc8	1137110462	No	Fiber	2000	2000
8e0efc0cbf2d6d0a63c422121f14b88f	1137110454	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
4a21153dc33797644b0005a3b0c595fa	1137110408	No	Fiber	2000	2000
6e5a303ea6e37f3bfcac97eaf699fa9b	1137110422	No	Fiber	2000	2000
12e8697082d32e3a6d715161d92ab975	1137110400	No	Fiber	2000	2000
75e18b05def7058c57d5aea7b6e6a145	1137110446	No	Fiber	2000	2000
2dcedbd297c0442a83a14d2f4d5d70ce	1137110387	No	Fiber	2000	2000
22d206f06813f6b1bf015b83fb24ea5d	1137110481	No	Fiber	2000	2000
ce377cdd94a49fd753cbd4fd638daebd	1137110466	No	Fiber	2000	2000
f3106955aef66bd298a12fdb77090bb5	1137110458	No	Fiber	2000	2000
80e441904af21c54a1ec43d55a6036c6	1137110297	No	Fiber	2000	2000
ff987b73c0a5b7e5b2174bd7f2e4f421	1137110411	No	Fiber	2000	2000
bf13bd333437acc166d8759aca3c4f23	1137110410	No	Fiber	2000	2000
d201c0da8613f9b4176f936c1194946c	1137110423	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 33 – Budget for Project Area IBO-888

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$35,588.00	$12,374.00	$23,214.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$12,916.00	$4,491.00	$8,425.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$105,408.00	$36,617.00	$68,791.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$31,255.00	$10,857.00	$20,398.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$6,097.00	$2,118.00	$3,979.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$94,200.00	$0.00	$94,200.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$4,724.00	$1,641.00	$3,083.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$15,000.00	$5,215.00	$9,785.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$1,845.00	$642.00	$1,203.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$3,207.00	$1,115.00	$2,092.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$44,400.00	$0.00	$44,400.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$1,385.00	$482.00	$903.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$34,108.00	$11,848.00	$22,260.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Pole Attachments	Pole Make Ready Costs	Professional Services	$30,475.00	$10,586.00	$19,889.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$1,841.00	$640.00	$1,201.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$3,564.00	$1,239.00	$2,325.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$120,104.00	$41,722.00	$78,382.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$6,750.00	$2,345.00	$4,405.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$396.00	$138.00	$258.00
Permitting Costs	Permitting Costs	Professional Services	$28,891.00	$10,036.00	$18,855.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 33 – Disbursement Schedule for Project Area IBO-888

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 33 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-888

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 33 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 34 –Subaward Conditions and Statement of Work for Project Area IBO-890

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$1,007,998.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$1,007,998.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$1,007,998.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 34 - Specific Award Conditions for Project Area IBO-890.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[65.88%]; [$1,946,624.00]
Total Project Cost = (subaward funds + match)	$2,954,622.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$1,007,998.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-890 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 34**. The Project Area is depicted in the map in **Appendix A of this Exhibit 34**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 34**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $1,946,624.00, which is 65.88% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 65.88% for a total match of $1,946,624.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 34** in the area depicted in **Appendix A of this Exhibit 34**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 34**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 34 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 34;
- Appendix A to this Exhibit 34 – Map of Project Area IBO-890;
- Appendix C to this Exhibit 34 – Budget for Project Area IBO-890;
- Appendix E to this Exhibit 34 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-890;
- Appendix F to this Exhibit 34 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 34 – Project Area
- Paragraph 5.B(2) of Exhibit 34 – Project Locations
- Paragraph 5.B(3) of Exhibit 34 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 34 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 34 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 34 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 34 – Access to Service
- Paragraph 5.B(5)e of Exhibit 34 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 34 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 34 – Map of Project Area IBO-890

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-890

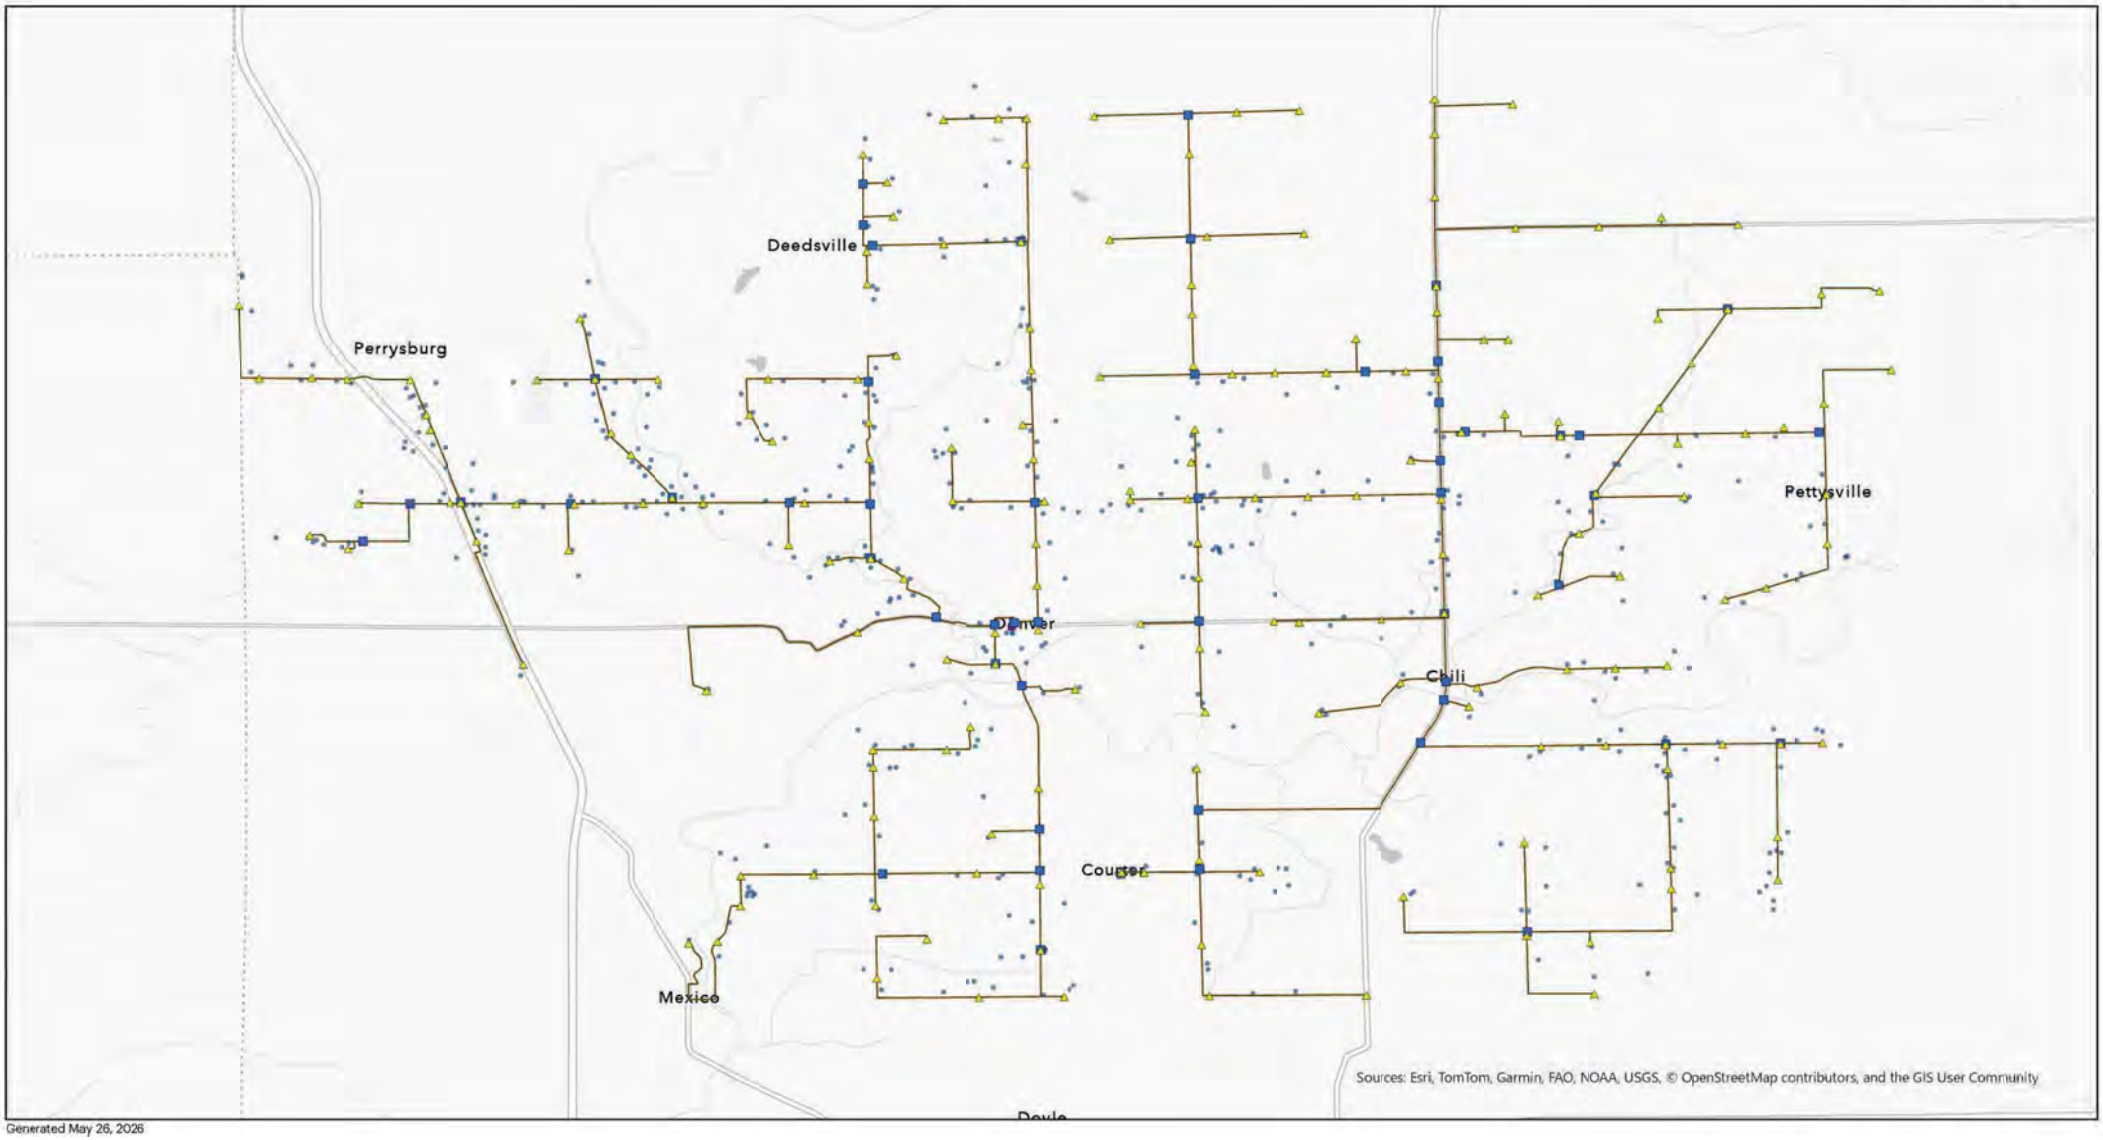

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 34 – List of Locations in Project Area IBO-890

Brightspeed IBO-890 Location List

460 locations

ID	Location ID	Is CAI	Technology	Upload	Download
0a9c990ad3b11347b74c5afc95d3d335	1286933227	No	Fiber	2000	2000
560ea4e2f866c7aae1a6436eb25ba6bd	1286924288	No	Fiber	2000	2000
ea3868d60739122215ce56d0bfd8449f	1286924603	No	Fiber	2000	2000
4494db7a11a989a93cd4670ad15e9ce0	1413416603	No	Fiber	2000	2000
0144bd52568883932644e519e4679de0	1286925578	No	Fiber	2000	2000
c71d43a399ab355db92e98b70bad5261	1286924738	No	Fiber	2000	2000
75c6006976f66b42ebfb85ac4406a61b	1286925989	No	Fiber	2000	2000
8d888630a4c8553b81f43b35f9c4bfe2	1286924280	No	Fiber	2000	2000
72e5ec821ca70643df4077b31899080f	1286926409	No	Fiber	2000	2000
1f255375057a5d79926ce167224b1f71	1286928555	No	Fiber	2000	2000
f98e70738d9d3b9766b19b0a5a2f97e3	1286923890	No	Fiber	2000	2000
66b50a4cbabbe45ae702164f35a7486b	1286925970	No	Fiber	2000	2000
acf99634056685a73b47db16ee207da9	1413416501	No	Fiber	2000	2000
10379324635c0d0fe4fcdd87217933e0	1286924613	No	Fiber	2000	2000
1d8207fe5960dd4f85654c770ba4f92e	1286924158	No	Fiber	2000	2000
617cf05b3c626e2e6e6d4110d8d236dc	1286924249	No	Fiber	2000	2000
9a33369a2c2d4563e9fa8daeb05a7296	1286924261	No	Fiber	2000	2000
7b87fb075538688ff2182b90eca50006	1286928403	No	Fiber	2000	2000
30b3837f1d66464399ba47d702a57691	1286924254	No	Fiber	2000	2000
0eedc7570440eb5f6d52142bfb977655	1286923715	No	Fiber	2000	2000
f966e136fedb446fd83429d898e0e41d	1286924174	No	Fiber	2000	2000
50716dfd397c0092fe0b312291b97705	1286924443	No	Fiber	2000	2000
5d6a909195620718 55b980d4f1cc4126	1286936758	No	Fiber	2000	2000
08340e92506ad1825925313c15e2ca26	1286924266	No	Fiber	2000	2000
49b4df5e85cbb5ef1356a1120d5e834a	1413416502	No	Fiber	2000	2000
a7a36a0cc44fce032fb4f105e69f07ec	1286923718	No	Fiber	2000	2000
238d5cd2420a0231c5a4433da5a709c4	1286933200	No	Fiber	2000	2000
0048051e2f28702c4c3fb4dce25b75f6	1286924141	No	Fiber	2000	2000
7b909febd1e45c62c7065ad2d969d20f	1286924340	No	Fiber	2000	2000
6870a2fc2345bb0403c5bb0bb27b766f	1286928885	No	Fiber	2000	2000
00b496e13a7d652ebca5f6f633af8170	1286923820	No	Fiber	2000	2000
4ebe9e1cfbcb767c185cb0f893bb9a03	1286923743	No	Fiber	2000	2000
c17054586f0f7bdf33e98b2db54ba03b	1286933222	No	Fiber	2000	2000
dd8e6f1c430a65ccbb700082bfa21b6d	1286923815	No	Fiber	2000	2000
43429960629abb84dded781fcf2183f0	1385111602	No	Fiber	2000	2000
b1bd75d6dd8052691fb5d2038a402bcf	1286925622	No	Fiber	2000	2000
6f089eaaeea6c39662f9aa0e4456b4d8	1286924609	No	Fiber	2000	2000
da4d7af84821ceb977ae84820354274e	1286924134	No	Fiber	2000	2000
1e3208ac016a4a20cd3c5a5d8644b91a	1286924688	No	Fiber	2000	2000
5a9645b58412516f4fc6bc5fb10e2cba	1286923831	No	Fiber	2000	2000
72418408277d34b265c8b3180ac2a137	1286936612	No	Fiber	2000	2000
4dcc08f716fd4a2c5c4cf059c5e07a3c	1286933220	No	Fiber	2000	2000
385a3cffe644313dcd27b6c534358f4a	1286923750	No	Fiber	2000	2000
d7a1a24cf614578edd8ea3216afab08c	1286924268	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
b93a47e0296cc7b48026605859c41b2e	1286924285	No	Fiber	2000	2000
c4334e129b0bd43e33c2644bfa784c50	1286933218	No	Fiber	2000	2000
1ec18464e010a0fb1255450f32f44f76	1286928619	No	Fiber	2000	2000
883329b8fafac36e9c8445e01951b5d4	1286924489	No	Fiber	2000	2000
7799aeb61ae1dcee2ac99cb3fe8996dc	1286923760	No	Fiber	2000	2000
f293ef74c67fa54d3d584c4eec97999d	1286924213	No	Fiber	2000	2000
8f830e3758fb18aae67a4460bd8ff68c	1286933223	No	Fiber	2000	2000
7d644f3fe9ff899d55ec50086cbeaf6d	1286933266	No	Fiber	2000	2000
ec054b2fa860f27208e953334c8930c5	1286924135	No	Fiber	2000	2000
710faba4ccba6587b7ad04fd8c009f1f	1286928896	No	Fiber	2000	2000
455d99b4cdbad588d62c270c87f5a92f	1286924262	No	Fiber	2000	2000
bcf399af6be8b07f7aa03c460ecf78fb	1413416596	No	Fiber	2000	2000
696361c555b318d322e49dbbc94195a6	1286925112	No	Fiber	2000	2000
635a035f567b118706968ea6ea283180	1286924277	No	Fiber	2000	2000
7709c5ac181ac5539cfcdf4c26a25f22	1286928878	No	Fiber	2000	2000
7d4c322b337b8ffb0466ef4bc891f53a	1286924444	No	Fiber	2000	2000
d482c34d6a1e34acd231788f7b974b1f	1286924736	No	Fiber	2000	2000
4c57419d0d316cbb9a0d180691cb88f5	1286924275	No	Fiber	2000	2000
969d62cbfc7cc8291e69c581811ea383	1286923900	No	Fiber	2000	2000
ef350c0fe475c8499260078cc7de15d3	1286924295	No	Fiber	2000	2000
f19b0bf55fcb85bd30608ed620c42d27	1286928235	No	Fiber	2000	2000
9bf9145d2e258d9a6aa42eb04b30f9c9	1286923819	No	Fiber	2000	2000
b473e9d30bce899c32ad9e64dbc9bff5	1286928883	No	Fiber	2000	2000
4f9073e3e5414afb29602b784e4b76f0	1286936593	No	Fiber	2000	2000
d3c5c774260f6f68d7eecee74d1eb859	1286924441	No	Fiber	2000	2000
dd306debf5bc19cf70676b5c369fc392	1286924335	No	Fiber	2000	2000
922e46672f7a92053e1bbcd81413ddd3	1286923830	No	Fiber	2000	2000
25f75d17b7a2af5fd35061abd24cc7f1	1286923719	No	Fiber	2000	2000
c29a6b97d38e4904c57e9d7cc6857aa4	1286924293	No	Fiber	2000	2000
6e7e04a37785c8f4ba81d5b67779ac01	1286926030	No	Fiber	2000	2000
18ab7287604efb44e500ff7837b1e76e	1286924291	No	Fiber	2000	2000
ca27323b41f40c8cedeafa1c1d8cbbc4	1286928413	No	Fiber	2000	2000
beadda148088f24d8554ab63e03efd65	1286928234	No	Fiber	2000	2000
fbdb1385898e5c6708626c4418dc755b	1413416606	No	Fiber	2000	2000
9ffad3a61cd59ce20be2fc93332d90d4	1286926093	No	Fiber	2000	2000
1537ac446451e53297677c23e4bb0efa	1286928162	No	Fiber	2000	2000
f9d28167ddeb718bbe3334df5af3e1e4	1286925101	No	Fiber	2000	2000
eab22e2b8135bfb75b226c25870db27a	1286924185	No	Fiber	2000	2000
1b871e706eb524b564adb7b1ef2186e4	1286924133	No	Fiber	2000	2000
d44fa97b030f96792b011ce8b5741280	1385117827	No	Fiber	2000	2000
80dfadab74335acb70a1a389f00f5dbd	1286928157	No	Fiber	2000	2000
5a6011ef9e81012ecd3456bb0b07ac20	1286923813	No	Fiber	2000	2000
f29ffaa67d087e076d82777b6fccbe0b	1286923738	No	Fiber	2000	2000
1c7cdd581dab74869a2e47c90d161b4b	1286924610	No	Fiber	2000	2000
00b0d69c6ab640d8379e7b843525a667	1286924276	No	Fiber	2000	2000
1766ed69d102e61cf789737d500636b2	1286923766	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a19431932ea866b4758b6371db1b05bc	1286924142	No	Fiber	2000	2000
fd94ce845f259023225dc29925783b07	1385111484	No	Fiber	2000	2000
a79ac2390aaa16ddd5c0d4cdcc09ecac	1385111530	No	Fiber	2000	2000
f9987e34475cb257e7e314709dddf0cd	1385111503	No	Fiber	2000	2000
5d69e483cf07ba8e8d010f2f5e4a5b4f	1286924056	No	Fiber	2000	2000
4f949872218ea368370eab4a12035be7	1286923731	No	Fiber	2000	2000
037fbd2be498d637bf0d429198182051	1286924299	No	Fiber	2000	2000
2a77f35eb59b30690fe780cdb7c5afa9	1286924612	No	Fiber	2000	2000
2b1bad9e3b1a06b70562325e6fd8e104	1286924635	No	Fiber	2000	2000
4af2af93981b47baa02f9fc47d96f0fe	1286923762	No	Fiber	2000	2000
2bb0a4e428fc85d19d322a3e18bfbb67	1286928156	No	Fiber	2000	2000
a018f22050f44319a364333f1723662d	1286928888	No	Fiber	2000	2000
82d4999c622823b3951b46b54bafc1ce	1286928889	No	Fiber	2000	2000
821be8fa39b4f7ed446b66cea10d5ab1	1286936581	No	Fiber	2000	2000
265ea32f5eebb98eb93dacf875524da6	1286924766	No	Fiber	2000	2000
9a4a601e8598d6cbbc8e7c4d8c7c38e5	1286923844	No	Fiber	2000	2000
9511670ee049d6e3a4a28d7dc23e7610	1286926105	No	Fiber	2000	2000
e7b7858b9cd5ded8bf14873d51077128	1286924139	No	Fiber	2000	2000
b59d4b62db5d8c4618707065bb660167	1286923939	No	Fiber	2000	2000
70ed9a51383a31bf6a9a3169b9329d17	1286924263	No	Fiber	2000	2000
a713ba3be00676ccb290ffa440de5a88	1286924044	No	Fiber	2000	2000
1afc7c47641f9751112d4f2435b8d99b	1286924173	No	Fiber	2000	2000
9d6f505bf8a64051d31a43107ab5dcd8	1286936550	No	Fiber	2000	2000
581cb087773aae9dd4f382b2bd779b2a	1286924025	No	Fiber	2000	2000
204853ac35d89bf95a911760081561b1	1286924255	No	Fiber	2000	2000
9e6586646b56e3b7d07f280eff641766	1286923739	No	Fiber	2000	2000
39e61a81a80b14ab8f7f9b63dfcb2cca	1286928163	No	Fiber	2000	2000
e8982af7ebae570a09fa95d44f43633c	1286928409	No	Fiber	2000	2000
7d6aac836957c533d211e3e4a8879d46	1286928586	No	Fiber	2000	2000
91830a18c9ac62e767c7406d1782ef40	1286923717	No	Fiber	2000	2000
e491117c9d03faf823b7c3482f9feefc	1286924461	No	Fiber	2000	2000
6fb53d7d8d2a825f2c87cf7a562d86f9	1286925114	No	Fiber	2000	2000
e6e25897ea804973dc7815e5aaf8a959	1286924767	No	Fiber	2000	2000
52014b9ee7910bbf385621deaab836bd	1286923899	No	Fiber	2000	2000
b792e7b6520c752e577b4a497e30d389	1286928422	No	Fiber	2000	2000
154c6d586cc6a624b6d6c45d17384133	1286926344	No	Fiber	2000	2000
604110e86c8925ae2a63cd4c25a1c910	1286928887	No	Fiber	2000	2000
c470882afbd179606f934b0fe8eed32b	1286923741	No	Fiber	2000	2000
b1f38e77cef3e8fb21110fda02367fcf	1286924341	No	Fiber	2000	2000
d4a1e05767b343b2d15ca169eb7ff1d6	1286924272	No	Fiber	2000	2000
9c4b69bcb742185cd62f26c459813fa8	1286928072	No	Fiber	2000	2000
dcc61f31274a8e92de057135a73ca88e	1286925592	No	Fiber	2000	2000
44cf142419fba833ec391abadbb95174	1286924160	No	Fiber	2000	2000
0ad0b1b783809e75dc953577c5ee3d8b	1286923729	No	Fiber	2000	2000
78f6c1ded45d0bd6eb1416a3fcf21263	1286928890	No	Fiber	2000	2000
8a46b0b9ef6139334c776e9556a16506	1385117826	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
41385d015bae72e77998db9caeb885c7	1286928075	No	Fiber	2000	2000
a3eb3abc52066c91dff9901f5de05c0e	1286928153	No	Fiber	2000	2000
56bae527b65a2eed310b5ee228159f61	1286924735	No	Fiber	2000	2000
b263fe4f793d15df8d237bf5e307ef4a	1286924606	No	Fiber	2000	2000
e8133e06ccdf61338d6c55419bb46b48	1286925623	No	Fiber	2000	2000
4a887bebdb1d853e5f83692c43760c25	1413416605	No	Fiber	2000	2000
12e43da77f34fb5801fa634489963219	1286924727	No	Fiber	2000	2000
f13ec1e6cb7e576b34fdcf7847fb316f	1286926019	No	Fiber	2000	2000
843550d459f5054dd0c169958df4c7e7	1286924279	No	Fiber	2000	2000
08e771872dcb7352e1d83f82f5cf9053	1286936575	No	Fiber	2000	2000
99b1c2eb4405b4d49ff3087cb872afc8	1286933214	No	Fiber	2000	2000
b9e7270a9ad5faad245abefec6819d09	1286925110	No	Fiber	2000	2000
29ada462fc56b367b93ad92491c23b85	1286928881	No	Fiber	2000	2000
08cfd7ee422919878f97c1eab7a7deb6	1286933204	No	Fiber	2000	2000
cf34d70d1d297c4ab4ecc1c74db89855	1286923732	No	Fiber	2000	2000
89d46defed44013acacd79a427babd2a	1413416591	No	Fiber	2000	2000
08605a2e5fe37696569423ad2c241726	1286924041	No	Fiber	2000	2000
dd6089cd4fff647891dae964b02c175a	1286933209	No	Fiber	2000	2000
76081820d2b51d3c5bdac04c92e5aa03	1286937308	No	Fiber	2000	2000
b966d1b0e52bdae35c2004407a216012	1286924851	No	Fiber	2000	2000
cde1359949af244f9b09c15572f6db0a	1286924286	No	Fiber	2000	2000
fd24bc55c3ffc322f86a484dcf1fdda0	1286923848	No	Fiber	2000	2000
d79aeecb9a7370963b1d638af201e491	1286923834	No	Fiber	2000	2000
96e258d6e1faec7c80a5316ffc63172f	1286924259	No	Fiber	2000	2000
b3b1f97f663b59cb125ddebfd481499c	1413416600	No	Fiber	2000	2000
2f054fedf43810d647db7507399564e2	1286924503	No	Fiber	2000	2000
eafad0ae546f378942ba044cd2da453b	1286925571	No	Fiber	2000	2000
137d8cc0ce039edc9e0fb74d54c48fbe	1286923711	No	Fiber	2000	2000
d52438cb75f1c08ebbe22fb17418f05c	1286924459	No	Fiber	2000	2000
321bb4e2c2d92e2b5718398b40b37a11	1286928300	No	Fiber	2000	2000
7dd6d26785c68d929f074ee1a2aa1176	1413416595	No	Fiber	2000	2000
357f2df7afd5c8e3df516c1f2a396ba9	1286923712	No	Fiber	2000	2000
6bd18eff76c98719542b4d33e5a1796e	1286924257	No	Fiber	2000	2000
12b5b3116ea3c11fcad7786121615e39	1286923851	No	Fiber	2000	2000
9512590901cd6b05698858b9458c9f33	1286924615	No	Fiber	2000	2000
e9bc73136039987d294b28a3f446cc92	1286924269	No	Fiber	2000	2000
a857b2e2a606a75bdacdb98562cc91e9	1286923722	No	Fiber	2000	2000
7335e6e13ec536143a8a7d439276c920	1286928582	No	Fiber	2000	2000
3b341fb0cc3a5d5929589ac69d716e7b	1286923838	No	Fiber	2000	2000
07024f2a8ebaaf184ac267cbba48b2e8	1286928901	No	Fiber	2000	2000
f9644e817f66a4e292b9fcd25b498817	1286924137	No	Fiber	2000	2000
0b4d1f6664b4adcdcbdeb5ab0cf09c3b	1286925658	No	Fiber	2000	2000
3b7aa11c05c6108a2aabab4ec670437f	1286932227	No	Fiber	2000	2000
0d3151b67397e2f9d950181a5ce611a9	1286924730	No	Fiber	2000	2000
1b72b704e662beba59da6910b08e98fb	1286933212	No	Fiber	2000	2000
060054f1c0278e91ab3663a6790996eb	1286928295	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
92c6862878913f755154c89cfe95f31e	1286923746	No	Fiber	2000	2000
148e48f8956e45f75c4799a277dc9a16	1286928605	No	Fiber	2000	2000
9c8e0b70723ef2f28c82d15f0f796bf4	1286936603	No	Fiber	2000	2000
f821f8fa01aa2ce0d443e98c26068cc6	1286923817	No	Fiber	2000	2000
7192933e23526baf01e096a45bff2804	1286933215	No	Fiber	2000	2000
ab0dab944037e4b416f154bc53699448	1286923759	No	Fiber	2000	2000
757513223393b492bd83466c2ed62911	1286924026	No	Fiber	2000	2000
461bd83690c687714db03443b4d00513	1286923842	No	Fiber	2000	2000
f77edcaeab280a3f82e4f77eb4bd82d1	1286924049	No	Fiber	2000	2000
1bd7b359b3aa9261ae04f421152ee0dc	1286933260	No	Fiber	2000	2000
047eee06b862ec502cd6e42eb0458031	1286923853	No	Fiber	2000	2000
e10e899061a874090ce2a7d591beb6fb	1286937315	No	Fiber	2000	2000
3a09f06e647d6410d0529cf0d19209d7	1286923763	No	Fiber	2000	2000
656339349286bbe627d5d9d771de98c5	1286924264	No	Fiber	2000	2000
c2f567868d894c5bf5f9be6559f8bbbc	1286925124	No	Fiber	2000	2000
82ccd648cacbce6d132afa4487440ecc	1286923735	No	Fiber	2000	2000
a5fbeef505b3f92e466e6f15cf741b4c	1286928160	No	Fiber	2000	2000
af84107b446a7a323bea89ac338a8a3e	1286928197	No	Fiber	2000	2000
99847f954ac5145cb8e37de7d6bf6da0	1286924060	No	Fiber	2000	2000
e74f3f38bacafb9b3802109bf06d84a3	1286928900	No	Fiber	2000	2000
66e1871905ff48cb0402e62a1f71c346	1286933226	No	Fiber	2000	2000
6794378ecf74c051f89f956dd98842c9	1286923951	No	Fiber	2000	2000
a5f509eb813e92049889b581caf0ba42	1286924063	No	Fiber	2000	2000
a2066fdd4ac550f79a1a19de81a2bc51	1286924614	No	Fiber	2000	2000
cf7b922af13d49a1c9b85af87719cadf	1286923745	No	Fiber	2000	2000
d9ca4201f2f1b1d26998c27d52861bfc	1286928417	No	Fiber	2000	2000
2dd4b7e0f5cf9ae23219c38642baca44	1286923827	No	Fiber	2000	2000
11cea8e177e6d9f0198b4f2b599330d1	1286928876	No	Fiber	2000	2000
371d6928b57eb4986e807d6ef651c625	1286923963	No	Fiber	2000	2000
fdf11df73ba3183f721998a4613ffd77	1286925040	No	Fiber	2000	2000
b10846cb1820b7cb4a41210748767a6d	1286924140	No	Fiber	2000	2000
72ebb5f924381bcc8d5eba797af52b84	1286928552	No	Fiber	2000	2000
55988b120c317e80325dceb4d2d33c17	1286924516	No	Fiber	2000	2000
66b0c87cf84a974197f15fd82360e985	1286924607	No	Fiber	2000	2000
cd16c702eeeee74c0de59a8b39a87a55	1286923727	No	Fiber	2000	2000
e9c02a246fef6f92bc231bc703656f59	1286924674	No	Fiber	2000	2000
18d669603a2ba8d6d9658f8fd48670ab	1286923833	No	Fiber	2000	2000
50a44dc4f82fb6f08545bfefaabdc164	1286923758	No	Fiber	2000	2000
b9ab09deb1a4ed5357f09963371788f4	1286923767	No	Fiber	2000	2000
0ca8a2a031d99fc1510ccae56299a3ae	1286923765	No	Fiber	2000	2000
7a6881dd09984f1adbded6b000b39aa2	1286933219	No	Fiber	2000	2000
d97d440b6f81aa6362542cca05395e31	1286926095	No	Fiber	2000	2000
5ada091c3e62ba5acc2ea3d96f33be6b	1286924445	No	Fiber	2000	2000
a3786030ced361d8df450b6992c441c4	1286924061	No	Fiber	2000	2000
d46d9b29bb907e6414e4d45129ca8db3	1286924265	No	Fiber	2000	2000
8eea81bdd30e94d06323993895abb2f5	1286937296	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
550d57e7baf837cfa770ac9c5741fabd	1286924290	No	Fiber	2000	2000
874948b112018ba5f939ce161bd02e4b	1286928292	No	Fiber	2000	2000
1e34761a86d3ec8cb69ab85a3c3d3ede	1286924176	No	Fiber	2000	2000
285c1cd3d782d46f6d527f036b2fcd89	1286924663	No	Fiber	2000	2000
9f633442ec4590e397a2de4ca93cbd6b	1286924740	No	Fiber	2000	2000
58212d0284b4f91e30c31f007ecc5098	1286924446	No	Fiber	2000	2000
1afaeb1c91ca9bc4bcce1d9f0dc0fe24	1286924618	No	Fiber	2000	2000
33c1332e4c7b5448cece195a7d43d766	1286924703	No	Fiber	2000	2000
aabe574a9a94e0e7903860f120d8e962	1286924298	No	Fiber	2000	2000
1a356341eae16589a4d6233f760537a9	1286924284	No	Fiber	2000	2000
c9611f85bdff23216b0945dfb01f1740	1286923832	No	Fiber	2000	2000
43d001b033f46557d315c1bd1f2ed878	1286924729	No	Fiber	2000	2000
f0c790dbf9624054e516a932ea2c00e2	1286928218	No	Fiber	2000	2000
b151eb880c78f44eee8d08cc3febad0b	1286924372	No	Fiber	2000	2000
1370cb15800eff73fc6f4f6fae3bd13e	1385111538	No	Fiber	2000	2000
3988fa6079ef4106885c35e307bb4bff	1286928895	No	Fiber	2000	2000
c0c8ce931a24911e146b7934f54abd83	1286923901	No	Fiber	2000	2000
74e0b221cdbcf2dd5b237a11730fb78b	1286928903	No	Fiber	2000	2000
2b8d0e7e1cb87f1952e5d993c952d763	1286924365	No	Fiber	2000	2000
820e84fad900548ab0d9150ac0f8a612	1286924157	No	Fiber	2000	2000
8c58569aa8b6e2b06467738ce57c5135	1286928195	No	Fiber	2000	2000
90e0a71958b73bd7ec07387596a18002	1286937302	No	Fiber	2000	2000
e6e2a9a26d09326c15471795bbc8d830	1286924032	No	Fiber	2000	2000
a70f6166828da27bc3ccc297256c1046	1286925570	No	Fiber	2000	2000
3e04d2d7b13a6952c47a1f9eb595410f	1286925609	No	Fiber	2000	2000
29402fcc9ef3138606a5dbb68420914e	1286937306	No	Fiber	2000	2000
ccb76d9bccb2b2441e6ce86f5a1a6a2f	1286924058	No	Fiber	2000	2000
07ec68a257bcecb19724742b204dc189	1286928404	No	Fiber	2000	2000
2271374b2c56b13689a2eea8b088e12b	1286924734	No	Fiber	2000	2000
f518d0ef69f982b27b0be638747962fb	1286936607	No	Fiber	2000	2000
c787525ac224755ab933a6809007bc4e	1286923713	No	Fiber	2000	2000
624ac6817795c8794e76c0eafd38a032	1286924617	No	Fiber	2000	2000
060fd7b8cc4cf8c0ceac2729c4b2f8ba	1286924374	No	Fiber	2000	2000
78df7d18428778b60269b01e71c0381e	1286936596	No	Fiber	2000	2000
bd93e07d1953e6c065df92fed8618c2d	1286924686	No	Fiber	2000	2000
e59d9a6cb12b3fcd837524b504ad89de	1286924616	No	Fiber	2000	2000
40ed5d8edca4bd5a4b1e9efedc1a871a	1286923737	No	Fiber	2000	2000
1e0c1b5fc0f916a0762fd70d2c3aaf30	1286932230	No	Fiber	2000	2000
5b05c95bfa4f6856b377ab11edd6e271	1413416604	No	Fiber	2000	2000
d078b13b8292f04be77ba0aeaf1fa97d	1286924442	No	Fiber	2000	2000
20deba977488aaabef4b065e8731cdfa	1286924131	No	Fiber	2000	2000
b09641060a0bd9a88601dd43508cba2f	1286923721	No	Fiber	2000	2000
68c0d9aa9a1e6b6834f4595a9088455e	1286923747	No	Fiber	2000	2000
557b6995f7d4b79c836fc611059fdf72	1413416677	No	Fiber	2000	2000
c49f7d6a0e5ca5a914ce4ecae008eb2a	1286924611	No	Fiber	2000	2000
3c25d57a900dfa28043a2d35573ad548	1286923960	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
ebb30ab15f8107771e9bb7063b029cb7	1286933203	No	Fiber	2000	2000
8c7ba83c86ca590bad0e0ba19eacc4ce	1286928424	No	Fiber	2000	2000
26d24bf5a336c1a5e846fdb5befb627c	1286923752	No	Fiber	2000	2000
fd7c8b434739209f29eb7e28f653b43c	1385111618	No	Fiber	2000	2000
b6df8ff3bc53a9e566034512fb2a43c7	1286924065	No	Fiber	2000	2000
e7c8d020e7034cc84c5f0dd34fb71f09	1286923824	No	Fiber	2000	2000
67cc05e4dd69cf97ac6a200af48b9313	1286924162	No	Fiber	2000	2000
2d8ba99e8d7448dc65f14425d8e8ab26	1286924048	No	Fiber	2000	2000
d0285c426a189ec0ef991d38e0f60937	1286937298	No	Fiber	2000	2000
171b6dcebf048126739686e0bd91af36	1286923942	No	Fiber	2000	2000
093aaa9f13fb0bc277abd6ab1b3820cc	1286924847	No	Fiber	2000	2000
5dda644ac4305f631f533ee97fb19100	1286924605	No	Fiber	2000	2000
546a63941d4fc185ac46a7341661697b	1286923828	No	Fiber	2000	2000
721668a4fa2e7f9fedf5653c642a2aec	1286925032	No	Fiber	2000	2000
b73662472d622601ffd5dec74a0bbe40	1286923849	No	Fiber	2000	2000
70ce8875d6b0ef679cbe89bb94ff3b3f	1286925179	No	Fiber	2000	2000
1d71d3940d6b97c8375ab53a93cc1fdb	1286924260	No	Fiber	2000	2000
30f865c92e46d4c6863ab281deb6e8c5	1286932228	No	Fiber	2000	2000
5dff8cf03e1b38e047901aad03b06075	1286924725	No	Fiber	2000	2000
88d908e535ce1b4882dd06c12e00c909	1286923898	No	Fiber	2000	2000
126baf8feddb4bf9d629f130c877af9c	1413416592	No	Fiber	2000	2000
f458f3c1d022d386681425914097e1da	1286928408	No	Fiber	2000	2000
4e5dfe923d99d0ffdd581eb4f7968880	1286924178	No	Fiber	2000	2000
68761bbd16824a0ee197159061597e5e	1286923761	No	Fiber	2000	2000
8605abbe0c130d43f3b8f47abac112f5	1286924014	No	Fiber	2000	2000
3cb53c11abccab449dbfa3ae044ec145	1286924294	No	Fiber	2000	2000
993dc72ca69bd3a5aacd96fe8c38ffd4	1413416593	No	Fiber	2000	2000
2d25cba21bde7aa9fd156e0b8279d13d	1286928407	No	Fiber	2000	2000
83c8f25be1e4bc8b09fc7f5c599fcc0b	1286928421	No	Fiber	2000	2000
3c37c343d7ab5bc1ae099d2be30fd2f4	1286926037	No	Fiber	2000	2000
b8a4c51a8be40424f5eab0bece1ab9a8	1286925119	No	Fiber	2000	2000
59e4a112fe8e53acf1cbfefe4b4bcd31	1413416544	No	Fiber	2000	2000
7cdac9dd21a6687d4b006e340bb28d5a	1286925115	No	Fiber	2000	2000
4c7f64143beae5be72c1ebb9709db732	1286923894	No	Fiber	2000	2000
1a30c5a17f9635185980638f63c5dec5	1286928212	No	Fiber	2000	2000
30c40aa68095fd349285a5274c9efbae	1286923843	No	Fiber	2000	2000
771e1eaa429c1b65cf97cf8a214c5b4c	1286933198	No	Fiber	2000	2000
1c9e46960672b638c8e9dd2f77b493ec	1385111615	No	Fiber	2000	2000
e843e2d454ef3f9dd77e4b69df6675c5	1286924368	No	Fiber	2000	2000
3d777375e89c78c95204a2b0c76b1f23	1286923837	No	Fiber	2000	2000
a8112a8793f9cc38766adb7188dfc730	1286924532	No	Fiber	2000	2000
be4ec249470e1800ab67afcebc59c7f8	1286928879	No	Fiber	2000	2000
ac34b91fb98971cdaaf0e5ddfcebc621	1286936590	No	Fiber	2000	2000
e0fa217b3ed0c517b4a4cef68a1d9b69	1286924393	No	Fiber	2000	2000
626ea83ebef82eae74af78dd6071cc6e	1286928541	No	Fiber	2000	2000
9218dc32bc551dbf100ea11e087d4ff7	1286925608	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
4ccc2f4be595257f18f075b4abce4c8c	1286923895	No	Fiber	2000	2000
cefaf5bd850734c646eea77408454405	1286923829	No	Fiber	2000	2000
663c110cdd65eae07f1362c74363b272	1286928884	No	Fiber	2000	2000
d2ee6ce480d87ca46e29bbfba323a994	1286928891	No	Fiber	2000	2000
6e45047dfc47289474e0afd659a494ff	1286923714	No	Fiber	2000	2000
7fc2ec9f34f7c6f63305e498a3c7eb7f	1286933207	No	Fiber	2000	2000
0c1293f97440165c25f2c02218285fe8	1286924731	No	Fiber	2000	2000
adf6e1f6f23d111d983a4d4f4e9ac79e	1286928220	No	Fiber	2000	2000
70b7dd7e3901bb0decaa0014685533a7	1286923847	No	Fiber	2000	2000
2d6852199e00a214623a77af7e3ee4f6	1286924273	No	Fiber	2000	2000
ce9ef84f47e020c2e01fefe9a2d6631c	1286924723	No	Fiber	2000	2000
f2a70152cea7ba2ac13effd7ad16b6f6	1286924638	No	Fiber	2000	2000
2284ef200eeb0e154017af5cf5bd5e75	1286924066	No	Fiber	2000	2000
831f59f70e085902a9a9a41a989e4aa8	1286923740	No	Fiber	2000	2000
9eca19130ab85f3bc5f63c8b0a8d5db0	1286923840	No	Fiber	2000	2000
066232710b4643566bfd2b556514afb6	1286924659	No	Fiber	2000	2000
c44eda934138da76a44c2cbbf09393fc	1413416601	No	Fiber	2000	2000
7e3d44c31e6487fedef622dc0d0670fe	1286924175	No	Fiber	2000	2000
60538b83d334506e947772da3c703c01	1286923764	No	Fiber	2000	2000
0ef386ae64a9067f30c7a7298101359d	1286924460	No	Fiber	2000	2000
5c075d99aa7d588ad4ba3066544b3793	1286936587	No	Fiber	2000	2000
cc5ea493b7aeced26dd1e7ad21339d9f	1286928211	No	Fiber	2000	2000
f05e117f5875f968ca428387b21b9a4f	1286923816	No	Fiber	2000	2000
282eeebaec16a800e2c7c7ee8c6d4608	1286923841	No	Fiber	2000	2000
7c2bd0c9fed2a66db65ac905e206074b	1385111501	No	Fiber	2000	2000
0383a6cb67c70ce764bb831f751711d0	1286928875	No	Fiber	2000	2000
baf5d8e5c8c631ad3c0803153956570b	1286923751	No	Fiber	2000	2000
fd1f2e36a90960a3f15d3c9238067c6f	1286933205	No	Fiber	2000	2000
ff67c64cbc62702d655ad1021f4aa550	1286936661	No	Fiber	2000	2000
edad1caabf9ab0e529a95d94b7e19d5d	1286924130	No	Fiber	2000	2000
6e3472e59b8984e315d177fef276b4bc	1286924439	No	Fiber	2000	2000
c6995c5967b72a2ca7cc8fe01b0cbee2	1286928904	No	Fiber	2000	2000
0eef7dd8ccc82151c9a9c4bdbc5c1ee3	1286924594	No	Fiber	2000	2000
dc8fe035e46482d57332a1c89aa92606	1286936619	No	Fiber	2000	2000
8061b84e216b5259bc0e659bdc548812	1286924161	No	Fiber	2000	2000
3d366b8a8fbe36e320f448c607f07fa9	1286925574	No	Fiber	2000	2000
0fd4786063210660e0b3303ee57b41f7	1286924278	No	Fiber	2000	2000
3082455fb3c0f18fa2cbb2f86ef3413a	1286924763	No	Fiber	2000	2000
e5e3def830b56809b2c2042b9eae6e15	1286924018	No	Fiber	2000	2000
f15895b0e9fdbd656585c6bdddeb1702	1286928897	No	Fiber	2000	2000
171b065f635238e096447c70db10892c	1286924181	No	Fiber	2000	2000
1efdb9bba9fba66bcbb748281477fa43	1286928247	No	Fiber	2000	2000
a18bf0ee2f43239f5eeb2ebea38ea0d3	1286923725	No	Fiber	2000	2000
b32c704e93eef78673767e49446e0f01	1286924013	No	Fiber	2000	2000
2e8911736c7dcf0489c685fe81da5d57	1286933224	No	Fiber	2000	2000
b8e9093729ff559bd311111d5162ddd1	1286923748	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
8e8bc7fcfb91d9891707f0090c25fe70	1286924739	No	Fiber	2000	2000
fb265413682fbcd43744f836945d4e02	1413416594	No	Fiber	2000	2000
e76b33827348add40cb205efa7e1d391	1286924184	No	Fiber	2000	2000
637afa86221d5a54f580a92e8fd0ddaa	1286925605	No	Fiber	2000	2000
2a8175f52d7fe484949d37786f97f3d8	1286928877	No	Fiber	2000	2000
00a37a028a9421f5e85f8a08e6eb4b58	1385114620	No	Fiber	2000	2000
c8bb1bb06e43ba59abab13da2ee62a8d	1286933206	No	Fiber	2000	2000
1fc52bb9058dff72156b491423c773bc	1286928405	No	Fiber	2000	2000
d7c3635c99746b02f6d55d7c1579a514	1286925050	No	Fiber	2000	2000
b95fc1a02cb40c9889496f477a409d2f	1286937295	No	Fiber	2000	2000
a16562a4de359a036ad5c04e08c60049	1286928899	No	Fiber	2000	2000
95fe47f0115effd5f51593d771352817	1286924256	No	Fiber	2000	2000
5a3ef6c5986a5defabdd9a0f6aaca79a	1286928207	No	Fiber	2000	2000
20b8352abc861197bca842c0069ffb1c	1286924042	No	Fiber	2000	2000
3a8b3c647820d5c996dc3f1ab94b7970	1286937312	No	Fiber	2000	2000
a235d14c61ce7f6a9249ebc395179840	1286928167	No	Fiber	2000	2000
5aa2c69963e2d95b7ae474308c337139	1286936610	No	Fiber	2000	2000
8addc4b2ceab90c94c9094cb35520a6e	1286923903	No	Fiber	2000	2000
a58d65fbad5537e8203633f6420fad2c	1286924282	No	Fiber	2000	2000
b9740384270f3c8cd9c44953cfdf6d04	1286924520	No	Fiber	2000	2000
de161592dc8c4802454472f94d8a9214	1286924132	No	Fiber	2000	2000
125d1256fbd1d64876f26fb2c39b5d58	1286928617	No	Fiber	2000	2000
db7786452f75d590d7e48361e7131225	1286923825	No	Fiber	2000	2000
275b422d2954d43c8672d4d733b35280	1286923755	No	Fiber	2000	2000
4e7743de8f33a2a758465ce714c72ef3	1286928882	No	Fiber	2000	2000
89c5cd2afef3b52bd38808b201884335	1286937297	No	Fiber	2000	2000
5dffab847cf8f799b548595d08644e43	1286924604	No	Fiber	2000	2000
0f07dc5568423ef897ce7d1de1d0c232	1286923754	No	Fiber	2000	2000
078fe15b2033a93c318aa26debc9c7ec	1286923934	No	Fiber	2000	2000
06d914b3adcac9243aa78fc12e49b3c2	1286923744	No	Fiber	2000	2000
3a34da4378c07f397bc32b1a6899567b	1286925647	No	Fiber	2000	2000
c0425755a0e6b11651cab000046e45e7	1286936617	No	Fiber	2000	2000
9c6b5582b5b87588d3f6b0fea7491555	1286924009	No	Fiber	2000	2000
8914ee456f66f79b2602d711fd16566b	1385110809	No	Fiber	2000	2000
c86d5ab1f1896e420bd300b3733b7658	1286924377	No	Fiber	2000	2000
4b36cf369e39e2819214939baab42e6f	1286923959	No	Fiber	2000	2000
bad4e13bd041eafd6582aa194166aca2	1286933217	No	Fiber	2000	2000
929a49a0f4cab8bc4e95a885ca646503	1286924270	No	Fiber	2000	2000
19f9abb4a15475613f01f8df82e4308e	1286923896	No	Fiber	2000	2000
b833db9b6de0973ef21a74f6c4e390b0	1286925180	No	Fiber	2000	2000
9f689d88248eb709b42f1a6e481af6b6	1286928196	No	Fiber	2000	2000
dfbde712ae82765839a2bb7a8d58403b	1286923736	No	Fiber	2000	2000
a8d5f55f7092ae9bee0432b62f847138	1286924701	No	Fiber	2000	2000
e9c0bea8a36a8c88b84a9ff1f87902df	1286924292	No	Fiber	2000	2000
fa65fb3f1fb18279b20bc1a477e3e469	1286923723	No	Fiber	2000	2000
8e7909673faf0be1005eff1f18a59589	1385112595	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
6db7ee5c53c1abefc9753b833f646215	1286928415	No	Fiber	2000	2000
b6b9d6d15e4dcdac649530b2a511068c	1286924281	No	Fiber	2000	2000
5511197d29301ebb053aaf0a087aaa8c	1286926039	No	Fiber	2000	2000
3bcb68425510087d3d2b3170fd8c0704	1286924274	No	Fiber	2000	2000
2bff14e237643cacb12364592e15812b	1286928200	No	Fiber	2000	2000
b9f50102920af5e5555710dffbaa74a7	1286923897	No	Fiber	2000	2000
f3c60b7d0f3121543cc5aabcf827c48f	1286925178	No	Fiber	2000	2000
3a534846a6cc7ba2d497bd05e0e4d911	1286923936	No	Fiber	2000	2000
bedfd35add948983332694cb3c600e1e	1286924289	No	Fiber	2000	2000
7fa6b40e7bdc72da7879e1d72818b0c6	1286924283	No	Fiber	2000	2000
00f178e7d20f091c82d96bd9b98e1ac1	1286928151	No	Fiber	2000	2000
a4b6035f5c79340182727ec6f3b94d11	1286933288	No	Fiber	2000	2000
3055d8eb08ebbae8c91e55621a4068d6	1286924045	No	Fiber	2000	2000
d89518c614febf9cfa8f48ecfa7274ad	1286924726	No	Fiber	2000	2000
e5d109bd577e52203aa9820625d7fbe4	1286923836	No	Fiber	2000	2000
ef12e8e7e128e8a5315692e5097faf25	1286923720	No	Fiber	2000	2000
9bc258868699e99a89e6a063a0edf714	1385112598	No	Fiber	2000	2000
470c2a41f35d4987fd2967499ee78705	1286924010	No	Fiber	2000	2000
e080bb0f0c4bd1abd031a85511e1734a	1286928410	No	Fiber	2000	2000
3cd9b709c65e20ef5ce964696a86b42b	1286926353	No	Fiber	2000	2000
513f32d58138444dc6848c46d65d0c65	1286928894	No	Fiber	2000	2000
0b1865fbc8da405546ee027a0e57ba1d	1286924138	No	Fiber	2000	2000
61a90ea62fb8cb4e79dec14986d6944f	1286924332	No	Fiber	2000	2000
8df955350dea6330eb7e67192512f2bf	1286936760	No	Fiber	2000	2000
c068c7479d52ce51c215e341a01a45fd	1286923757	No	Fiber	2000	2000
b495edc0aa124b75d1abc78e4e8d8e94	1286923845	No	Fiber	2000	2000
61a12fb4b1e9aa7da6a3e22779aff320	1286923944	No	Fiber	2000	2000
85b7ebc473e41ebb13a7f7b1616296b1	1286923753	No	Fiber	2000	2000
eeca948bbf3a58b51ae4c6ca50208fb1	1286928223	No	Fiber	2000	2000
79d5430a738cf8819136858812480d07	1286924737	No	Fiber	2000	2000
fba3f93f2cf86db91736fd27b5be7fb2	1286928892	No	Fiber	2000	2000
16faecddbc2bdf8b10bae5f330ae2278	1286924031	No	Fiber	2000	2000
1c4970a729032692a5c7edf504412936	1286923728	No	Fiber	2000	2000
019d98d566975579ddf9dd450eec7471	1286937307	No	Fiber	2000	2000
0f15a277eecba39ce679e5eae8018a28	1286928213	No	Fiber	2000	2000
7759af7a334cc950c5ca02cb00256ac7	1286924764	No	Fiber	2000	2000
98ce9bea1d2713b2f5953b6e7b169975	1286928893	No	Fiber	2000	2000
02eefd44cbd6cdad0ab4fbdfd08f415c	1385118741	No	Fiber	2000	2000
e07f9dd5ca8c6f5b45974f485ef7bf0f	1286924150	No	Fiber	2000	2000
05fa1ce30689de9e127e128d241218d5	1286923756	No	Fiber	2000	2000
8a2bd3ea10fcb7ddda2eefc162ba85d8	1286933216	No	Fiber	2000	2000
5cbe3398befb2364f110de184ed06bba	1286923733	No	Fiber	2000	2000
0814fb880c5b4e383d6c103249691003	1286928880	No	Fiber	2000	2000
5b199ff7918f7ea6dc6009c4eeed8bcd	1286924182	No	Fiber	2000	2000
e68cd6a85a4cdcda8f83c932af0a9c79	1286924062	No	Fiber	2000	2000
37d4d13f1a87645037ac47df7209f854	1286923852	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
22f133fadc0b91ab90c492454a2be36d	1286925105	No	Fiber	2000	2000
875ac3b16fa87ae880fdb4978dd94189	1286924297	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 34 – Budget for Project Area IBO-890

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$33,768.00	$13,514.00	$20,254.00
Permitting Costs	Permitting Costs	Professional Services	$164,032.00	$65,646.00	$98,386.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$193,651.00	$77,500.00	$116,151.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$84,000.00	$33,611.00	$50,389.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$10,440.00	$4,177.00	$6,263.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$19,242.00	$7,699.00	$11,543.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$73,326.00	$29,340.00	$43,986.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$173,026.00	$69,246.00	$103,780.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$681,900.00	$272,899.00	$409,001.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$598,464.00	$239,507.00	$358,957.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$7,886.00	$3,156.00	$4,730.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$177,650.00	$71,096.00	$106,554.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$39,000.00	$15,608.00	$23,392.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT Installation labor	Installation of OLT in the central office	Construction Services	$2,232.00	$893.00	$1,339.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$296,416.00	$0.00	$296,416.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$26,809.00	$10,729.00	$16,080.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$20,790.00	$8,319.00	$12,471.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$202,054.00	$80,849.00	$121,205.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$139,416.00	$0.00	$139,416.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$10,520.00	$4,209.00	$6,311.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 34 – Disbursement Schedule for Project Area IBO-890

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 34 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-890

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 34 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 35 –Subaward Conditions and Statement of Work for Project Area IBO-964

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 35 - Specific Award Conditions for Project Area IBO-964.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$25,499.00]
Total Project Cost = (subaward funds + match)	$25,499.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-964 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 35**. The Project Area is depicted in the map in **Appendix A of this Exhibit 35**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 35**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $25,499.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $25,499.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 35** in the area depicted in **Appendix A of this Exhibit 35**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 35**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 35 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 35;
- Appendix A to this Exhibit 35 – Map of Project Area IBO-964;
- Appendix C to this Exhibit 35 – Budget for Project Area IBO-964;
- Appendix E to this Exhibit 35 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-964;
- Appendix F to this Exhibit 35 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 35 – Project Area
- Paragraph 5.B(2) of Exhibit 35 – Project Locations
- Paragraph 5.B(3) of Exhibit 35 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 35 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 35 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 35 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 35 – Access to Service
- Paragraph 5.B(5)e of Exhibit 35 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 35 – Wholesale Rate

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 35 – Map of Project Area IBO-964

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C


brightspeed

IBO-964

addr_point
central_office
dtap
oh_route
splice_closure
terminal
ug_route

N

0 0.150.31 0.62 Miles

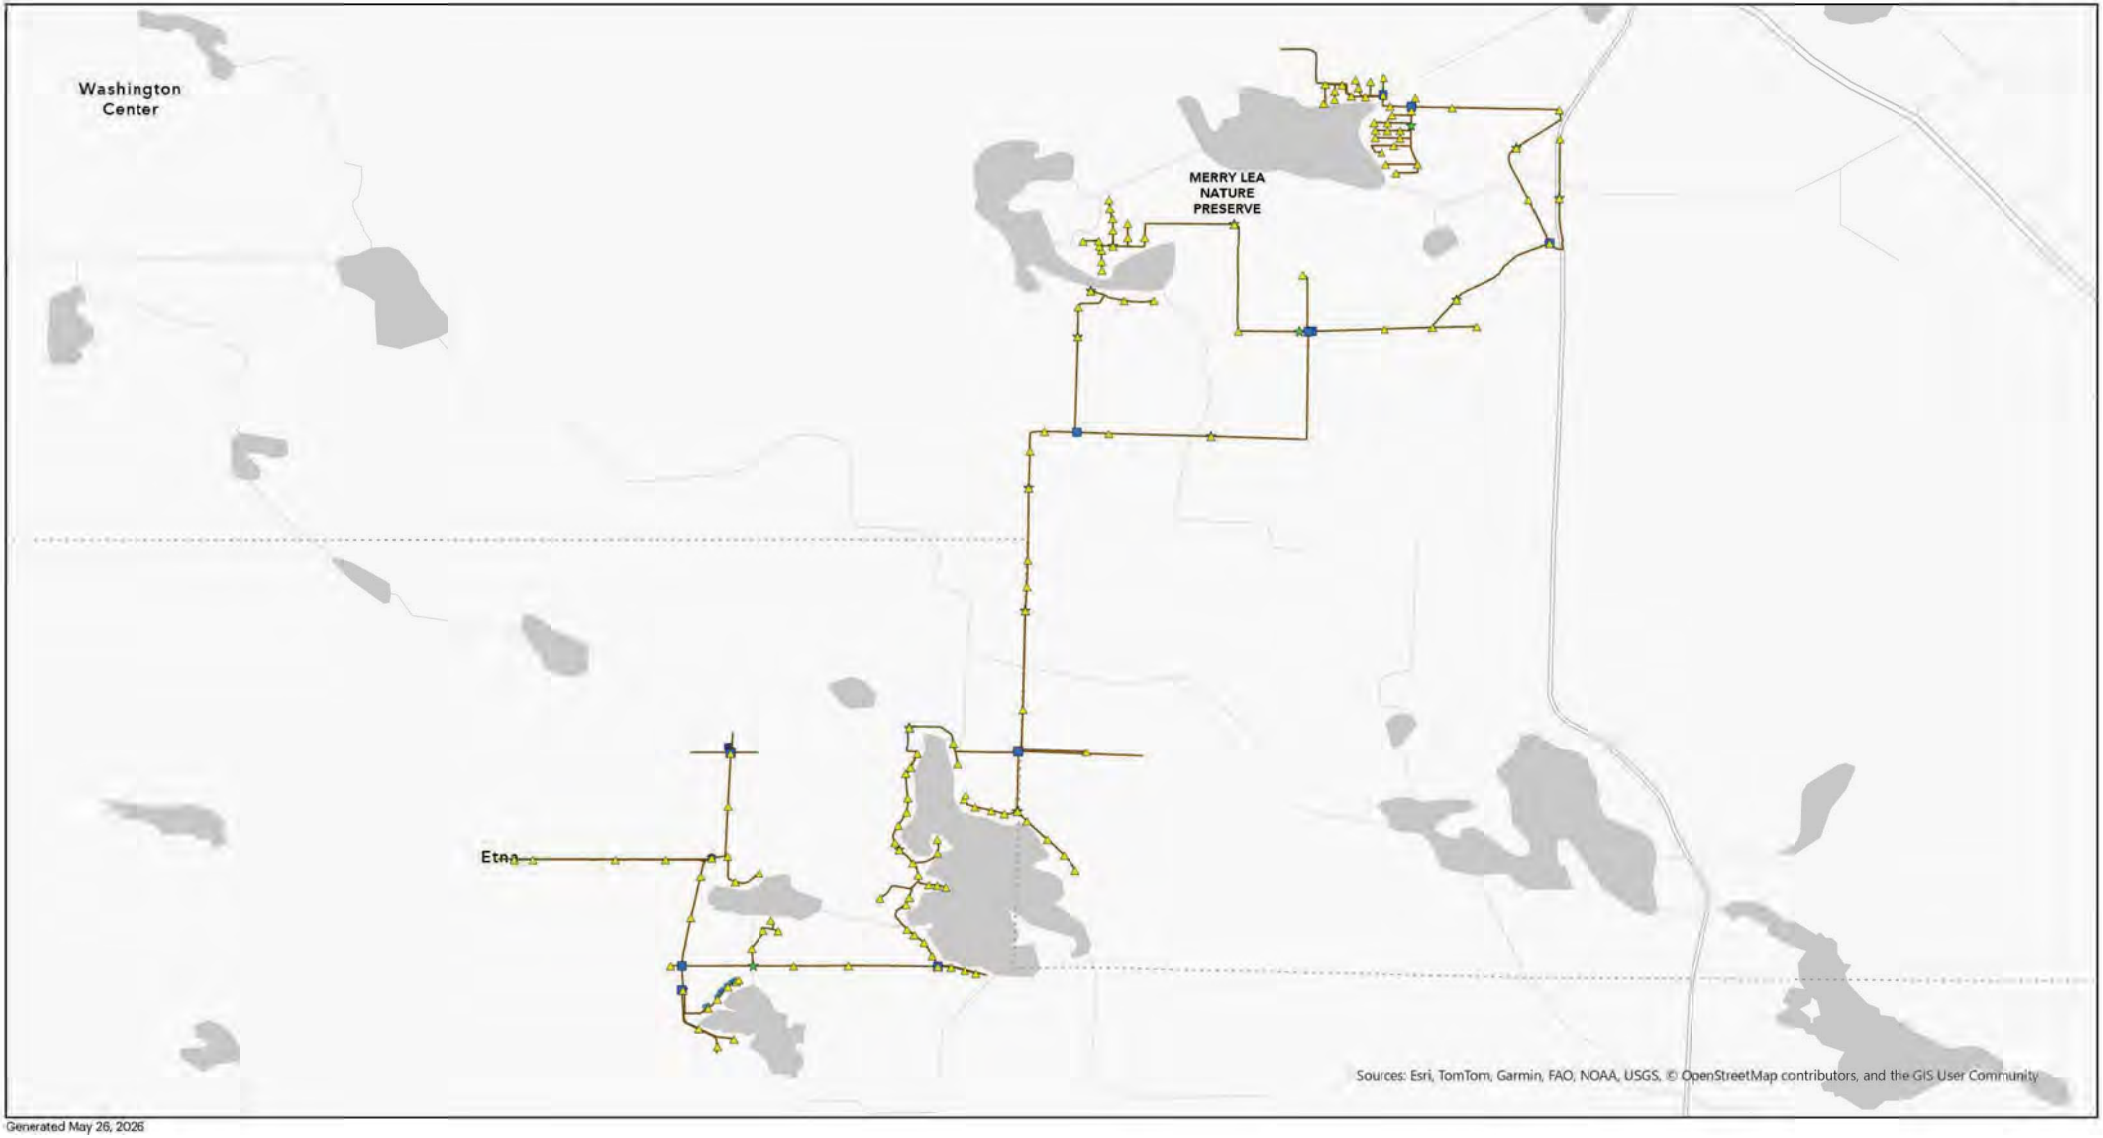

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 35 – List of Locations in Project Area IBO-964

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-964 Location List

10 locations

ID	Location ID	Is CAI	Technology	Upload	Download
4c84f58380c8428453b629f671c288a8	1037513700	No	Fiber	2000	2000
9b1d641b564327a01edd93b4b86b755a	1037513708	No	Fiber	2000	2000
e5229bf8f7636377820b3b4fc8c054bc	1037513704	No	Fiber	2000	2000
c01270e211304f62a68abb31d0324cbb	1037513706	No	Fiber	2000	2000
66043fcebaefb1aced496b1cd3c5c6f9	1037513707	No	Fiber	2000	2000
ac2d1ad50a9b9d2d5e9e1fd7236f7f1c	1037513705	No	Fiber	2000	2000
6b99c9f5adfa42b740b7c2a8bb514927	1037513701	No	Fiber	2000	2000
ded60ed7e614c41b58e3b1d9de4ea919	1037513709	No	Fiber	2000	2000
b6c594d2fe4a5ecb16713f6e2bcc2f20	1037513710	No	Fiber	2000	2000
733e08ca4b1e33ce1b007e600fa2200a	1037513696	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 35 – Budget for Project Area IBO-964

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Pole Attachments	Pole Make Ready Costs	Professional Services	$1,117.00	$0.00	$1,117.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$45.00	$0.00	$45.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$1,305.00	$0.00	$1,305.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$0.00	$0.00	$0.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$646.00	$0.00	$646.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$3,870.00	$0.00	$3,870.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$0.00	$0.00	$0.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$12.00	$0.00	$12.00
Permitting Costs	Permitting Costs	Professional Services	$1,059.00	$0.00	$1,059.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$1,250.00	$0.00	$1,250.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$6,280.00	$0.00	$6,280.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$4,404.00	$0.00	$4,404.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$937.00	$0.00	$937.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$2,960.00	$0.00	$2,960.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$0.00	$0.00	$0.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$474.00	$0.00	$474.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$1,140.00	$0.00	$1,140.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 35 – Disbursement Schedule for Project Area IBO-964

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 35 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-964

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 35 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 36 –Subaward Conditions and Statement of Work for Project Area IBO-914

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$58,764.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$58,764.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$58,764.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 36 - Specific Award Conditions for Project Area IBO-914.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[85.06%]; [$334,684.00]
Total Project Cost = (subaward funds + match)	$393,448.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$58,764.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-914 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 36**. The Project Area is depicted in the map in **Appendix A of this Exhibit 36**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 36**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $334,684.00, which is 85.06% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 85.06% for a total match of $334,684.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 36** in the area depicted in **Appendix A of this Exhibit 36**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 36**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 36 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 36;
- Appendix A to this Exhibit 36 – Map of Project Area IBO-914;
- Appendix C to this Exhibit 36 – Budget for Project Area IBO-914;
- Appendix E to this Exhibit 36 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-914;
- Appendix F to this Exhibit 36 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 36 – Project Area
- Paragraph 5.B(2) of Exhibit 36 – Project Locations
- Paragraph 5.B(3) of Exhibit 36 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 36 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 36 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 36 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 36 – Access to Service
- Paragraph 5.B(5)e of Exhibit 36 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 36 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 36 – Map of Project Area IBO-914

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-914

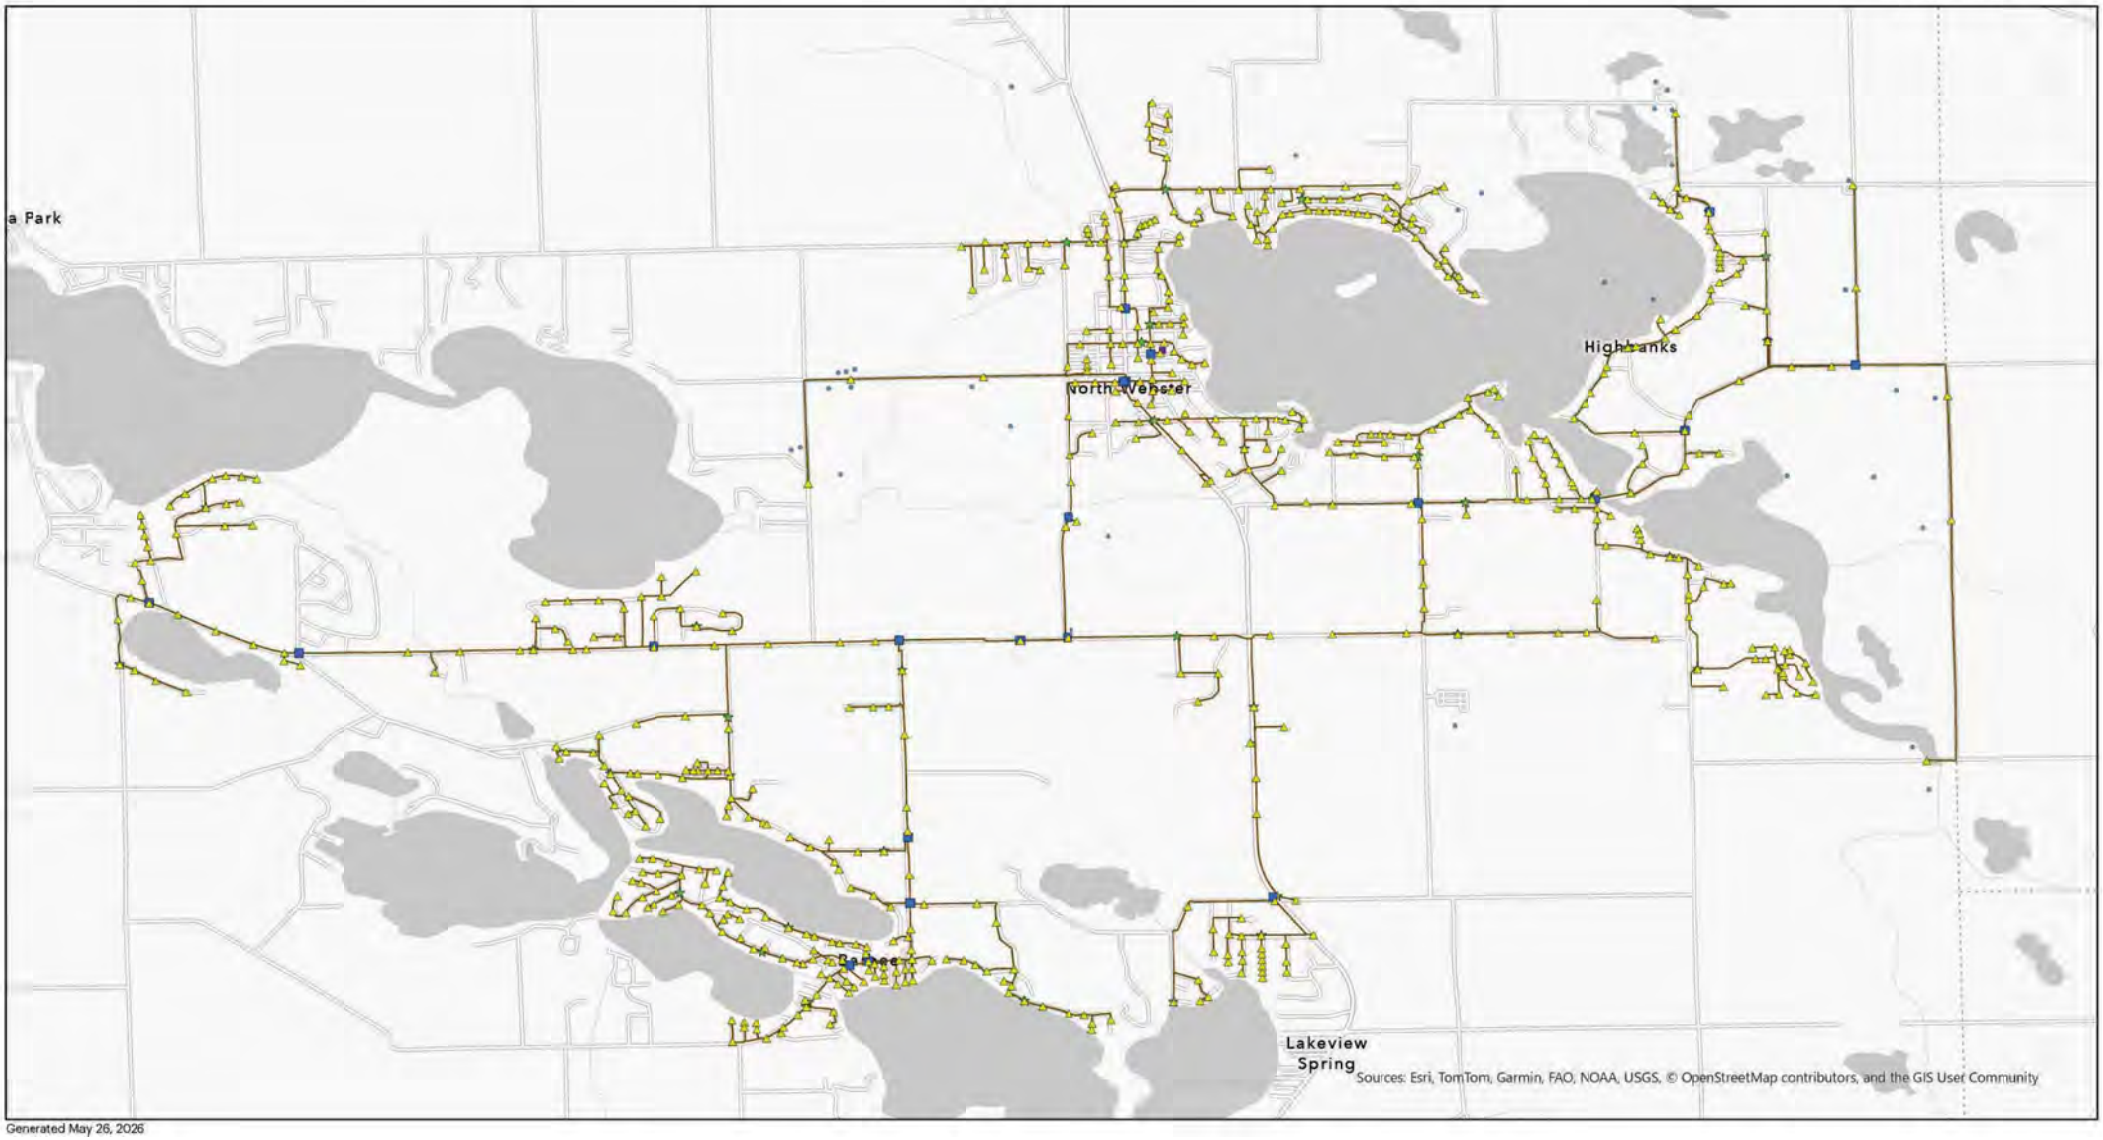

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 36 – List of Locations in Project Area IBO-914

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-914 Location List

33 locations

ID	Location ID	Is CAI	Technology	Upload	Download
8291f462df70c1e9a22f9a138e91ec71	1292811951	No	Fiber	2000	2000
9f1294a65de2a8bd28fbfecb9c4975af	1292811959	No	Fiber	2000	2000
9f3e5253d46c945601d8332ecd2e7b7d	1292813315	No	Fiber	2000	2000
4871845df1bc55b404e30db604dec5e4	1292811972	No	Fiber	2000	2000
5691b33b3da8097a440fe778bc2d168e	1385274165	No	Fiber	2000	2000
867c6cbf71d81ab3700e7be79ff176bf	1292815084	No	Fiber	2000	2000
75d70fe1f8b5256d096dbbd4a172260a	1385274465	No	Fiber	2000	2000
f7ab5de47255fb98d8528b5db0f8cb14	1292811948	No	Fiber	2000	2000
9acca9b247a6b0b8763abcbcbcb5dd39	1292811650	No	Fiber	2000	2000
7d8be6e11a70ddea390bdc954cd7c147	1292811977	No	Fiber	2000	2000
600f6ad0d1a6653ed6cf137e07f6ace9	1292811691	No	Fiber	2000	2000
4eba27e1a72c0856d4cc957d7bd364c6	1292811404	No	Fiber	2000	2000
4d262c368420aef9defc3934746cc328	1292811984	No	Fiber	2000	2000
c36946af1ea23dae80f27e5d07ad4691	1292813325	No	Fiber	2000	2000
b1da11583becc41873be153cd0cbd182	1292813542	No	Fiber	2000	2000
cc29b861a9107c913718a014fb8b46f5	1292813332	No	Fiber	2000	2000
48c5ee58cae7af3ba3f022183aa05727	1292811231	No	Fiber	2000	2000
0de30a143cb53259e4dc7b62a6a980b0	1292813321	No	Fiber	2000	2000
2bc341027b5bdbd64dd6ff40ddbd95ea	1292812514	No	Fiber	2000	2000
70e114787dd609d63f5fd57c3944fbee	1292848126	No	Fiber	2000	2000
b20f92293228e3a6694842cc50e18250	1385274162	No	Fiber	2000	2000
485cebf7b6786d1d89607f0f2f55d5de	1292812300	No	Fiber	2000	2000
f08ac4ebfddd62dc50fac4f6b54613a0	1385274506	No	Fiber	2000	2000
417ef8f89997cc3d957df0af98747b8d	1292811935	No	Fiber	2000	2000
d18213f08b4558b784bd25315bf75152	1292812294	No	Fiber	2000	2000
2613f8a382ce1f834e0833da52595cc4	1292811644	No	Fiber	2000	2000
559ca4b5e7887eefdcd976333a8c0441	1292813324	No	Fiber	2000	2000
3d2070490f7014862e383c899bada9f3	1292813134	No	Fiber	2000	2000
8ea667ee197dd8cefe58854e9f732400	1292812161	No	Fiber	2000	2000
fc9180d87211c554d027e60a2e882493	1292812156	No	Fiber	2000	2000
eb327b343b562e01905484579d700952	1292812310	No	Fiber	2000	2000
9fdf45af1a45058b95539fcaeae3f558	1292811930	No	Fiber	2000	2000
64d0438131fef8039855724c67b78f34	1292812154	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 36 – Budget for Project Area IBO-914

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$538.00	$88.00	$450.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$3,207.00	$525.00	$2,682.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$4,690.00	$767.00	$3,923.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$23,236.00	$0.00	$23,236.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$24,681.00	$4,037.00	$20,644.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$4,227.00	$691.00	$3,536.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$5,250.00	$859.00	$4,391.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$1,578.00	$258.00	$1,320.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$85,374.00	$13,964.00	$71,410.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$25,365.00	$4,149.00	$21,216.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$12,000.00	$1,963.00	$10,037.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$1,485.00	$243.00	$1,242.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$2,970.00	$486.00	$2,484.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$28,822.00	$4,716.00	$24,106.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$10,460.00	$1,711.00	$8,749.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$10,952.00	$0.00	$10,952.00
Permitting Costs	Permitting Costs	Professional Services	$23,398.00	$3,827.00	$19,571.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$27,623.00	$4,518.00	$23,105.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$324.00	$53.00	$271.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$97,268.00	$15,909.00	$81,359.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 36 – Disbursement Schedule for Project Area IBO-914

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 36 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-914

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 36 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 37 –Subaward Conditions and Statement of Work for Project Area IBO-1112

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 37 - Specific Award Conditions for Project Area IBO-1112.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$81,575.00]
Total Project Cost = (subaward funds + match)	$81,575.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-1112 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 37**. The Project Area is depicted in the map in **Appendix A of this Exhibit 37**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 37**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $81,575.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $81,575.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 37** in the area depicted in **Appendix A of this Exhibit 37**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 37**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 37 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 37;
- Appendix A to this Exhibit 37 – Map of Project Area IBO-1112;
- Appendix C to this Exhibit 37 – Budget for Project Area IBO-1112;
- Appendix E to this Exhibit 37 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1112;
- Appendix F to this Exhibit 37 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 37 – Project Area
- Paragraph 5.B(2) of Exhibit 37 – Project Locations
- Paragraph 5.B(3) of Exhibit 37 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 37 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 37 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 37 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 37 – Access to Service
- Paragraph 5.B(5)e of Exhibit 37 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 37 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 37 – Map of Project Area IBO-1112

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-1112

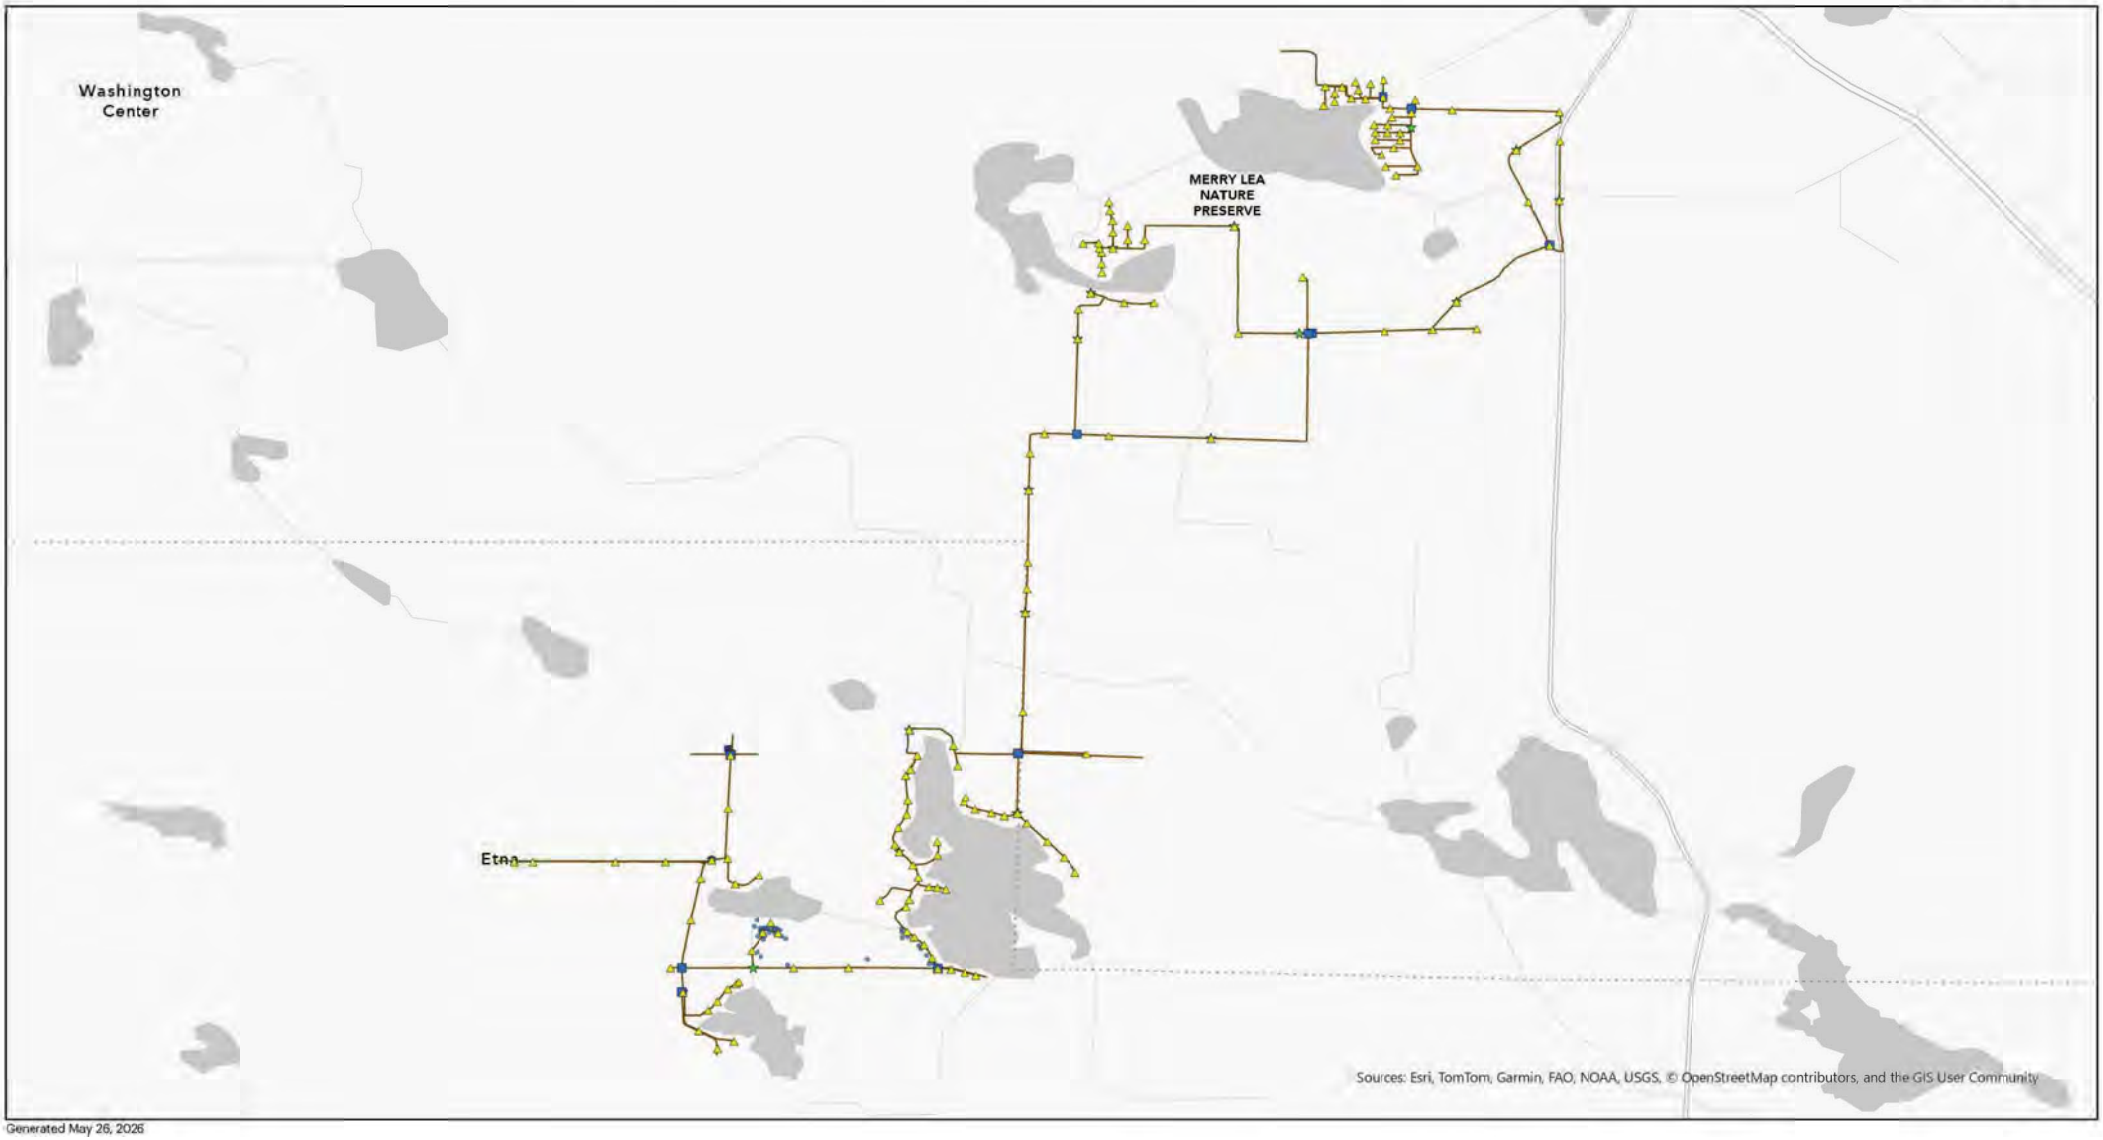

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 37 – List of Locations in Project Area IBO-1112

Brightspeed IBO-1112 Location List

34 locations

ID	Location ID	Is CAI	Technology	Upload	Download
736be3239e332b13cf7ad3d7b8895fd0	1037513615	No	Fiber	2000	2000
d33ccbba5ad385898371df1f54fde8cf	1037513556	No	Fiber	2000	2000
439bf91e6b2bfd1ab894536c97c292b3	1037513571	No	Fiber	2000	2000
4755c03089f18e3bc0ea468feffb1765	1037513130	No	Fiber	2000	2000
cde42183c507168068cc5478868b874c	1037513621	No	Fiber	2000	2000
898b509a01c381dcbc4ca3d39bf1fb0f	1037513627	No	Fiber	2000	2000
47d633d05f4a7e1ccdde076ccf466dd0	1037513620	No	Fiber	2000	2000
3177752585a44a0cd0e151025ef23796	1037513604	No	Fiber	2000	2000
9af7b003e2a03a5ac71f01037e8a4d4a	1037513624	No	Fiber	2000	2000
8837755b1109d4b0420a7217eab348e1	1037513622	No	Fiber	2000	2000
ff2126a45cb75aa0308ca3adf83718a9	1037513625	No	Fiber	2000	2000
608ba6e6a109113d84d1f8512059a965	1037513528	No	Fiber	2000	2000
b8f5ae9904b57824854dad420ec51b79	1037527589	No	Fiber	2000	2000
5d70a323f6afa8539dd12d752029cdd9	1037513626	No	Fiber	2000	2000
261afffa3656c60f4303f6caf9701af0	1037532173	No	Fiber	2000	2000
e141e93467dbc366d11372c2e74a0f91	1037513616	No	Fiber	2000	2000
6dc6822bb37620cc962b47c65326b475	1037513623	No	Fiber	2000	2000
c0b8ac3c8f8f5c2c95ef7e037c8e53cd	1037513453	No	Fiber	2000	2000
f38d376f7fed0db7f8fd5fef4734e3b8	1037513618	No	Fiber	2000	2000
413353816ba6736bcf2ad2853b5667b1	1037513455	No	Fiber	2000	2000
cbac2d1d6bd479469a13b03cba5dd50b	1037513628	No	Fiber	2000	2000
f19c61bde65d43b52b1832b66f2f74b6	1037513425	No	Fiber	2000	2000
36ca5561fef293df219612bb0e1ff984	1037513447	No	Fiber	2000	2000
a29a82420f8e089a727633d5146ceb29	1037513469	No	Fiber	2000	2000
7bf508a4798fd9607a34454a2a796b55	1037513440	No	Fiber	2000	2000
29d8d0cc5a020a0f9d09e99809b12e9b	1037513442	No	Fiber	2000	2000
7cb6b224552041d44c1f1e7db0420483	1037513617	No	Fiber	2000	2000
a1550b051f2436b97dc8689ffd227660	1037513446	No	Fiber	2000	2000
f47e30cb1437dfe97fa78a400e0d3c72	1037513448	No	Fiber	2000	2000
1c8affd7adc9393bc54a791d7fa177ec	1037513444	No	Fiber	2000	2000
a46920b1f772f4b5d3c4ae958dc33c61	1037527590	No	Fiber	2000	2000
fe0378f61127ae77601e7d779c328b59	1037513609	No	Fiber	2000	2000
502fe38ae7f6ffed4845b2a4e2c3c8dc	1037513443	No	Fiber	2000	2000
89a9db9c908ee3f90dcb27c7a54c7aa9	1037513439	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 37 – Budget for Project Area IBO-1112

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$13,336.00	$0.00	$13,336.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$10,360.00	$0.00	$10,360.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$686.00	$0.00	$686.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$3,787.00	$0.00	$3,787.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$297.00	$0.00	$297.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$225.00	$0.00	$225.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$263.00	$0.00	$263.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$3,383.00	$0.00	$3,383.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$684.00	$0.00	$684.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$3,515.00	$0.00	$3,515.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$469.00	$0.00	$469.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$21,980.00	$0.00	$21,980.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$3,951.00	$0.00	$3,951.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$1,434.00	$0.00	$1,434.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$750.00	$0.00	$750.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$48.00	$0.00	$48.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$11,700.00	$0.00	$11,700.00
Permitting Costs	Permitting Costs	Professional Services	$3,207.00	$0.00	$3,207.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$1,500.00	$0.00	$1,500.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 37 – Disbursement Schedule for Project Area IBO-1112

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 37 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1112

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 37 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 38 –Subaward Conditions and Statement of Work for Project Area IBO-963

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$883,657.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$883,657.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$883,657.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 38 - Specific Award Conditions for Project Area IBO-963.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[51.63%]; [$943,253.00]
Total Project Cost = (subaward funds + match)	$1,826,910.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$883,657.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-963 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 38**. The Project Area is depicted in the map in **Appendix A of this Exhibit 38**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 38**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $943,253.00, which is 51.63% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 51.63% for a total match of $943,253.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 38** in the area depicted in **Appendix A of this Exhibit 38**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 38**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 38 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 38;
- Appendix A to this Exhibit 38 – Map of Project Area IBO-963;
- Appendix C to this Exhibit 38 – Budget for Project Area IBO-963;
- Appendix E to this Exhibit 38 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-963;
- Appendix F to this Exhibit 38 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 38 – Project Area
- Paragraph 5.B(2) of Exhibit 38 – Project Locations
- Paragraph 5.B(3) of Exhibit 38 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 38 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 38 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 38 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 38 – Access to Service
- Paragraph 5.B(5)e of Exhibit 38 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 38 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 38 – Map of Project Area IBO-963

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-963

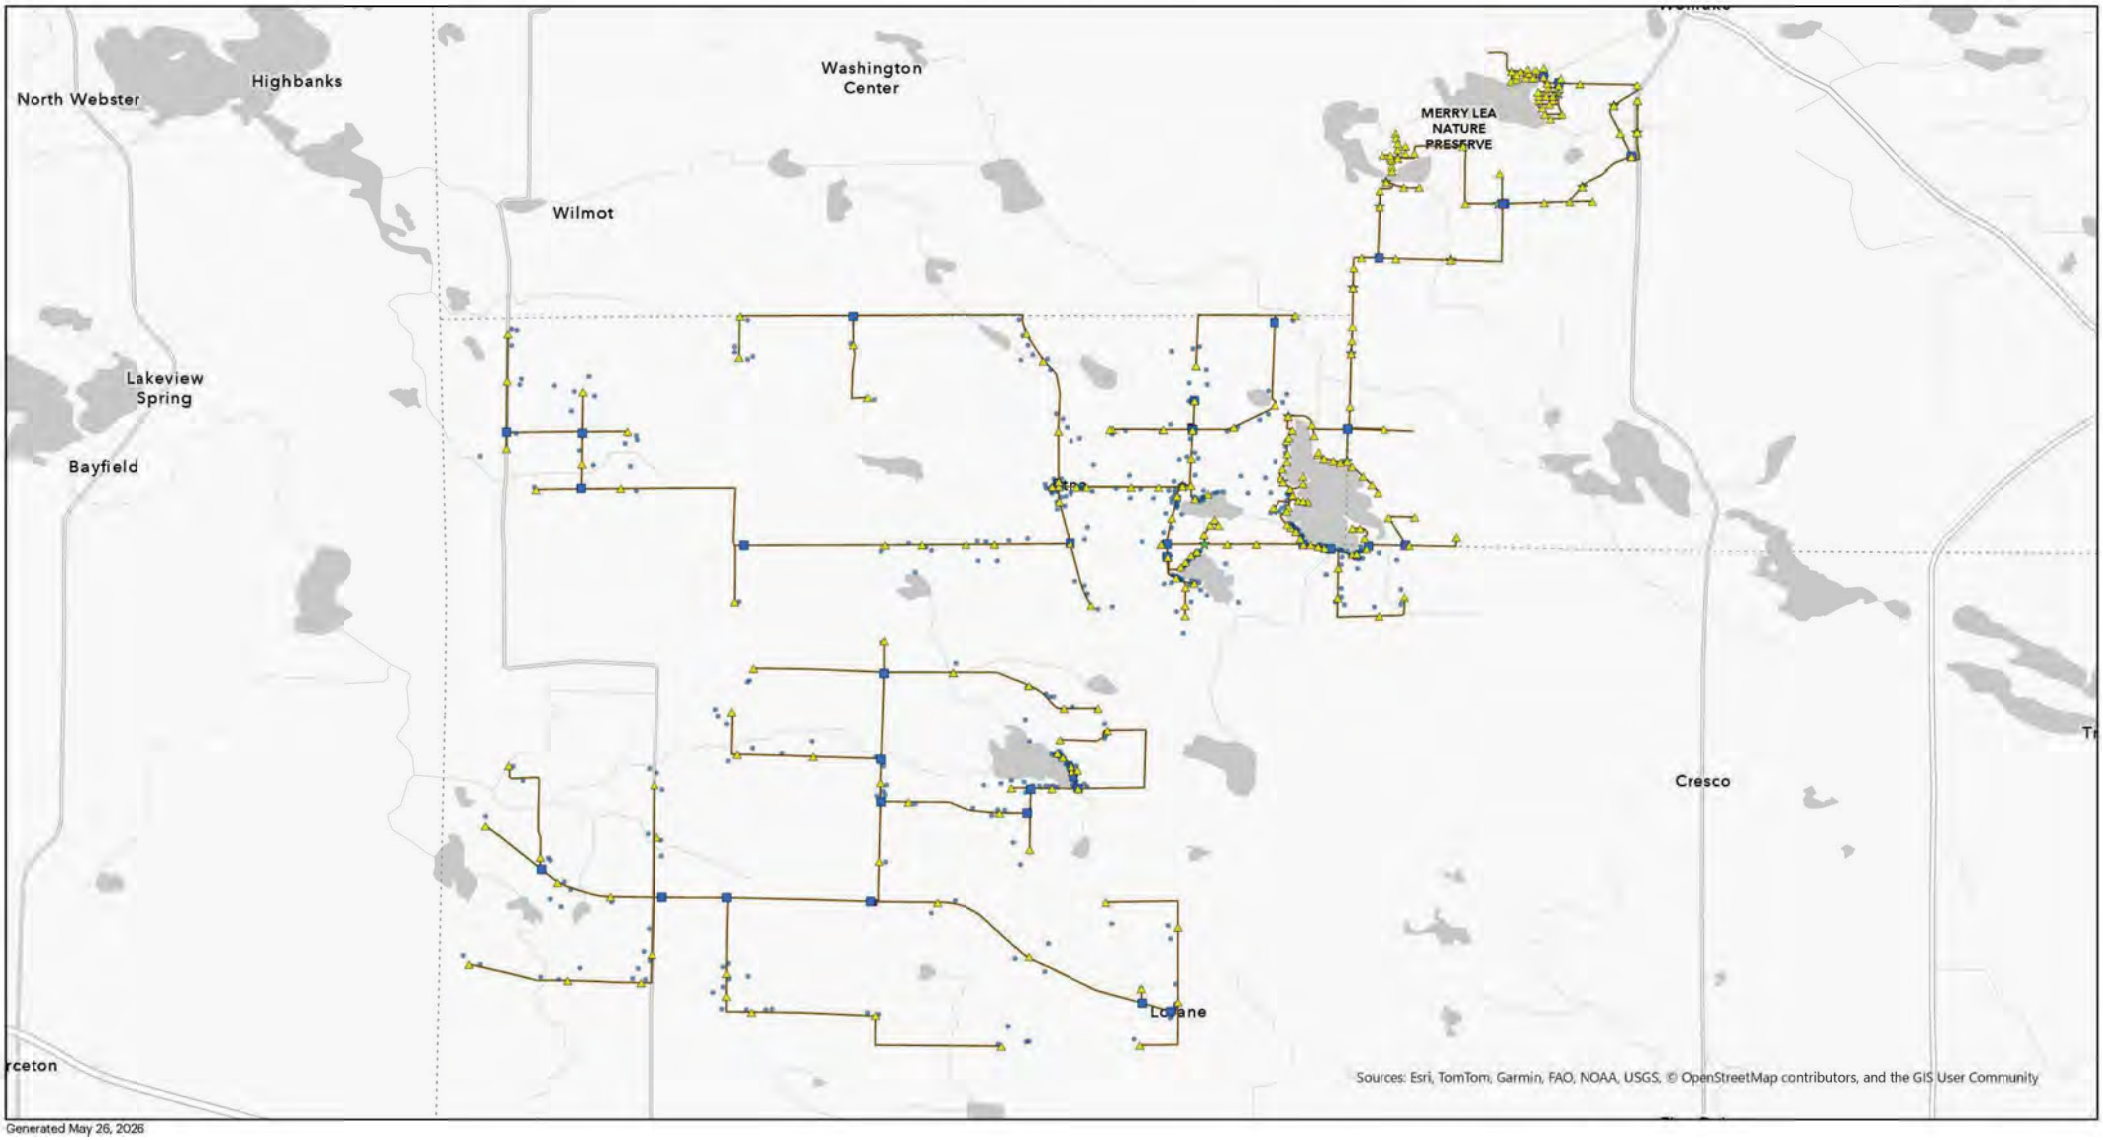

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 38 – List of Locations in Project Area IBO-963

Brightspeed IBO-963 Location List

396 locations

ID	Location ID	Is CAI	Technology	Upload	Download
c11a246b134e64913ec3de39b552a4cd	1037514109	No	Fiber	2000	2000
ed3987c0b6753b875b8ffa2df3bed8df	1037513449	No	Fiber	2000	2000
10f0a1943cd51d75326389607414d07b	1037514182	No	Fiber	2000	2000
6050a159a838c0c11e0e5281d9d19a51	1037513388	No	Fiber	2000	2000
b64d73349d717b1398ab1ca150798182	1037513474	No	Fiber	2000	2000
82894707d23cbabebcd542bbbeffa991	1037514271	No	Fiber	2000	2000
138b30a37bb8b80d5d049c72fb88da07	1037513610	No	Fiber	2000	2000
3d20d87c3d1641d2f0b287656f623fca	1037513636	No	Fiber	2000	2000
467af1e810164d3806198ab92f5ec037	1037515052	No	Fiber	2000	2000
c02a067c330d7d4ce92b23509ad2cc3c	1037513827	No	Fiber	2000	2000
5d2ce571d5d5831b3cec61e551bef2c5	1037513728	No	Fiber	2000	2000
2c81a56f29adac9e49274b2b4617e4c8	1037513682	No	Fiber	2000	2000
ffa7046876732199d6dbf9b4f5815d2a	1037513160	No	Fiber	2000	2000
4371647d42da7c78ced735731a0d8cd5	1037513693	No	Fiber	2000	2000
1ea22bfa5c2b7d9b5cf28c879bd2cefa	1037515018	No	Fiber	2000	2000
8b8a241ac265ae9147609855679a8643	1037513683	No	Fiber	2000	2000
30e6ab85a397047344fd430ce5f89ad5	1037513429	No	Fiber	2000	2000
723edadc216b01af1e367fcb05d7ad7e	1037513224	No	Fiber	2000	2000
e77b8e9fbab734a3e1654ab7a9bb7418	1037513931	No	Fiber	2000	2000
8e0758f39fa66053cc847e21093a3c44	1037513345	No	Fiber	2000	2000
4a6a1cfbd5b846f36619e28ccdccf1f8	1037513251	No	Fiber	2000	2000
48175d9ad19fb73438cdd83eb4865274	1037513476	No	Fiber	2000	2000
1cafa3584ff8f2820067fb2ea313f235	1037514191	No	Fiber	2000	2000
609d86109068bc5cf2073986d73c2276	1037513790	No	Fiber	2000	2000
ce8d1d58ce5102b1d33b93ef3fd44879	1037514066	No	Fiber	2000	2000
f2b5d5ebbd4666d46fa611ae1eaca261	1037515027	No	Fiber	2000	2000
2e2ef29d091b05a2548b98778fb7534c	1037513454	No	Fiber	2000	2000
b8c005991452f76abf21576bffaadebb	1037513882	No	Fiber	2000	2000
0724933c32a9f82a1a641401e7e13767	1037513464	No	Fiber	2000	2000
23ccff899d03cba658cc731194616fad	1037514138	No	Fiber	2000	2000
2c6ca924b79e0891c35eaefab1a1caa0	1037513273	No	Fiber	2000	2000
239a18ad59519b3fbc6e99cadb94a371	1037527934	No	Fiber	2000	2000
f15d08d94e977848df70f2a538a12178	1037513263	No	Fiber	2000	2000
7399790b81df730361b7e7fd40617b84	1037513285	No	Fiber	2000	2000
f751de718f2e3b14ab48557b0ba2eff9	1037514148	No	Fiber	2000	2000
4fb8e209e4d8895e6740806c9b150bec	1037513366	No	Fiber	2000	2000
c53c6aa621fc3a6d419b499b1d597efd	1037513330	No	Fiber	2000	2000
64318a009c2ab106038ee017232e3cea	1037514121	No	Fiber	2000	2000
c330eafe6b113fc5d000d5662c7c9a14	1037513404	No	Fiber	2000	2000
b0a28d641a20d87d41e0053745efc3ee	1037513365	No	Fiber	2000	2000
81b04ccec36de26a6d06217d6004056b	1037513896	No	Fiber	2000	2000
9e0eeeea55321877ab59956c956a2206	1037514133	No	Fiber	2000	2000
294b070d52fe8e4a3b33d00d52c21022	1037514273	No	Fiber	2000	2000
f4dcbaeaae9329688b9e4334dc9356cf	1037513312	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
2bd586c1a39bf2423d0a00c440e5e168	1037513856	No	Fiber	2000	2000
4079fcd4aac38859eb5b08a32a276170	1413434944	No	Fiber	2000	2000
3de4620ebc8daa8cbb1706ee815a3cf5	1037515014	No	Fiber	2000	2000
8ccc4965ab729c7976f12253f3be4085	1037513327	No	Fiber	2000	2000
24ba366eb96db876d76352cecac87364	1037513369	No	Fiber	2000	2000
0906329eef374f4f55f291d2068fe021	1037513403	No	Fiber	2000	2000
533451e923c1e8b8ad8bda75bd6a30a4	1037513834	No	Fiber	2000	2000
bd31378cdbd8c65156931a98c711891a	1037513689	No	Fiber	2000	2000
b843aff5cccb12c8279356011271fee0	1037533685	No	Fiber	2000	2000
5c60c31bc4b6faaa91530d99bde12457	1037515008	No	Fiber	2000	2000
7eae0f353af30c110f1a57421a146d52	1037513397	No	Fiber	2000	2000
344ff9b528e00d787e442009aab4c1e3	1037513269	No	Fiber	2000	2000
91c0485b36079bf03f4df5f6d9d85286	1037513333	No	Fiber	2000	2000
2f92a794b6edc9cd474fd7ba646a9e4a	1037513336	No	Fiber	2000	2000
9170b2fb4207183a1154d6b4cdba853f	1037513346	No	Fiber	2000	2000
ffa442ad5becb89f5b50c0365a1f50b4	1037514161	No	Fiber	2000	2000
19a8454e054b0df84694d78e2e68dac0	1037514196	No	Fiber	2000	2000
9203ceb4afb2a5429c88690e41f29ca8	1037513697	No	Fiber	2000	2000
53534e78fa7a4046d489c964f8a72884	1037513389	No	Fiber	2000	2000
6b08b9a9e9a1a9e93e7fd63ec0a0e667	1037513677	No	Fiber	2000	2000
946c08d35fb32144076e73065bde5cba	1037513718	No	Fiber	2000	2000
8b71a64153cb76c99488f83ff414a911	1037513360	No	Fiber	2000	2000
4b220a21e42b24b6d9741e84c5171f09	1037513721	No	Fiber	2000	2000
576654ac61fe804a3ca436e51c045a3f	1037527587	No	Fiber	2000	2000
a6df4c86b360dcd0acb6898d3c1f97d3	1037513904	No	Fiber	2000	2000
46b81690db7a7bba2550bc8be9e40aa0	1037513434	No	Fiber	2000	2000
271e390c5484e2e9a8563e9156566017	1037513654	No	Fiber	2000	2000
36de4e9d323de97b3ff3c31e86386d26	1037513363	No	Fiber	2000	2000
480a09c494b545feef9941f3c1c0a1b6	1037513798	No	Fiber	2000	2000
9b258c7bf7c463d4ea53619f265a8066	1037527765	No	Fiber	2000	2000
5e80bc7bb3b3e9d8fea7d5ba918987cc	1037513341	No	Fiber	2000	2000
157169e0d722f4d8e0354311d09315ba	1037527918	No	Fiber	2000	2000
cf3de73f9d629482f8ff72ffeb938acd	1037513450	No	Fiber	2000	2000
f87f09b156bb0560a3ab64610c03b9bb	1037513392	No	Fiber	2000	2000
4688ce17603aefae1559cdc70b4443d8	1037513876	No	Fiber	2000	2000
90eecd066bd5e6f786bb43d6dbfd6a83	1037515047	No	Fiber	2000	2000
a815756c756a77c258a2fa3db1513ded	1037513863	No	Fiber	2000	2000
49e3cb211cd9191c86013634e4ebb4bd	1037513125	No	Fiber	2000	2000
541152205f36b5061d626b77225a2868	1037513245	No	Fiber	2000	2000
e158dad4b050e7f41caa59089c313650	1037513351	No	Fiber	2000	2000
e83a0422f1a52b7c7643f219557b2006	1037533684	No	Fiber	2000	2000
b6d030f25535cec0051031008de7373f	1037513713	No	Fiber	2000	2000
f82a4bd9ef446d5640e992878c169be8	1037513724	No	Fiber	2000	2000
1dbfb54c7c0a7fd61cdde4e17282e011	1037528289	No	Fiber	2000	2000
636423584bce7881e9241cdaefa3565c	1037513673	No	Fiber	2000	2000
1ff6b1be8091b2080010e98f618c5429	1037513888	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a7839a3096d364dd46bb972f04fa03d9	1037513854	No	Fiber	2000	2000
d66381653bc410a6a91079f99b87bdd2	1037514073	No	Fiber	2000	2000
1aa83afade04e4d8d3bbc3e312031441	1037514132	No	Fiber	2000	2000
0c9086c2c3f4878395bbc6da5591da1a	1037513972	No	Fiber	2000	2000
51b58965fca1dcc0180be63d086e6d9e	1037513637	No	Fiber	2000	2000
b4269230883aade4e72c50a173ae84dc	1037533201	No	Fiber	2000	2000
eb2ee3178d43aff87c1af3675c9ce2be	1037514179	No	Fiber	2000	2000
ad24c6d1b0b1f45b8fb0ad8dc5f5982a	1037513695	No	Fiber	2000	2000
78faa75381486a3fb860003f1e94556f	1037514190	No	Fiber	2000	2000
9948c307b222a57f134f63214076371f	1037513246	No	Fiber	2000	2000
7a38baab81bf548c29d2e9f880e7b4aa	1037513829	No	Fiber	2000	2000
031a399fa0d47c44f0fe18f1fbe48c53	1037513295	No	Fiber	2000	2000
0737bbc52c94cbbe68308764c5f8dcc8	1037514255	No	Fiber	2000	2000
73e9b63f26b824afc6e383d3b29198d2	1037515046	No	Fiber	2000	2000
bf07df528440f54bbc4d51fcc4ad1bc6	1037514163	No	Fiber	2000	2000
6661e36370a57468d6bec41af2bf68a4	1037513910	No	Fiber	2000	2000
78ea7958701c3a305684bb1be5d65681	1037513691	No	Fiber	2000	2000
4e000d5c161dca50e238ab88179c3488	1037513652	No	Fiber	2000	2000
d072f4e301bf5e5c927ee8c50faf8b43	1037515025	No	Fiber	2000	2000
e3c710a1ea3036010be2507c302b2c45	1037513879	No	Fiber	2000	2000
388e3baa25d395e7a6b40761d5dca228	1037513204	No	Fiber	2000	2000
433d54524d1c11bdc5cc2e86ab9a06fe	1037513674	No	Fiber	2000	2000
e296f45baa6daef4d42b0c4fdf1c1c2b	1037513377	No	Fiber	2000	2000
b85714261401c56771972cf200edcf5f	1037513477	No	Fiber	2000	2000
c960e2aae67bdf314ef8db45b03bc4f7	1037513690	No	Fiber	2000	2000
f2eb5b4f1a75b4e63d3a16229cca79cb	1037513433	No	Fiber	2000	2000
ebe070868e1f126a79917d881720746f	1037513815	No	Fiber	2000	2000
ee7bc46d72d29e918540b85d90842578	1037513816	No	Fiber	2000	2000
407cb31a9f8cfd77dadf958c42af2bb9	1037514060	No	Fiber	2000	2000
8d0c924f323708123c96930309fb5cad	1037513399	No	Fiber	2000	2000
81c36ebf7ffc389a5addd07f00ce9ba1	1037527585	No	Fiber	2000	2000
e69b651a81bb44c674a695ba0c58f36c	1037513350	No	Fiber	2000	2000
468fdab267387ee29f33686499b42ad5	1037513349	No	Fiber	2000	2000
977e715ace5620f28b479e4350cd2481	1037513373	No	Fiber	2000	2000
57e36d632d2e2f914cadeeef66384aab	1037513395	No	Fiber	2000	2000
1a563fd269e16a9bd94ff70f24a8ab53	1037513889	No	Fiber	2000	2000
abe6871db8966c33663ff098e7b08f46	1037513281	No	Fiber	2000	2000
9d43648b5c4da7d856258cd77f0bf2a9	1037513859	No	Fiber	2000	2000
4a2d5ba0daead727d4811951412122cf	1037514103	No	Fiber	2000	2000
8b8250f538e3d4e1e0ba052b6bb742cc	1037515031	No	Fiber	2000	2000
a44152bf8883576dbfc927c94673629b	1037513261	No	Fiber	2000	2000
fc831028aa3425d2e4fab90b18fe6563	1037514149	No	Fiber	2000	2000
47d2190aa9ea184a37eee1633c58b9fa	1037514095	No	Fiber	2000	2000
7fe0588cdb57717c64bba85edca9b1c2	1037513284	No	Fiber	2000	2000
9d2b6b327ce5b51fa40b8b9d7ab9fdad	1037514192	No	Fiber	2000	2000
2aa28801ae266ba45e204e5aa31011f1	1037513878	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
deff11774efdbc4f5ece0449c33900ea	1037513875	No	Fiber	2000	2000
9f71926928fc6a705175d4f28d1386b3	1037513289	No	Fiber	2000	2000
82006f5cbc7fafa74ada6430f5ffada5	1037513820	No	Fiber	2000	2000
d60e8077b007e5e295547d38fc74f0ae	1037514195	No	Fiber	2000	2000
6495e5b6cdd51d6d6dc56988355cdaea	1037513339	No	Fiber	2000	2000
1ab7fc01e6096c2540b42f1e377c12ba	1037513653	No	Fiber	2000	2000
b4ac5dd907065908eb938cfad883317d	1037513862	No	Fiber	2000	2000
471ce0407122fb8ce3e3074b1b2dae0f	1037514134	No	Fiber	2000	2000
31c7f8020dfe5a800dcf5c60db99b906	1037513386	No	Fiber	2000	2000
131262b7993df04707c0166284bdc975	1037513288	No	Fiber	2000	2000
ad5e2282764f174079a57a1cbcdab995	1037513463	No	Fiber	2000	2000
35cdf6f0411fe033c3bc2e3fe80415be	1037513656	No	Fiber	2000	2000
4e887bd994189c6ecde9950a4d69caf0	1037514270	No	Fiber	2000	2000
1f3bf8a8ead14e67b89c5e548e364deb	1037513316	No	Fiber	2000	2000
7039ea533d98d346d3f40c0c120f850d	1037514141	No	Fiber	2000	2000
9cefc6244863e822f94fcfab8388bdaa	1037515059	No	Fiber	2000	2000
f499caca221566b46ee1858cda2c92c0	1037515026	No	Fiber	2000	2000
e9c4ed90f689f0ed57b5e4d1f0575f88	1037513337	No	Fiber	2000	2000
228f21a0074217f90a5883bce344544d	1037513655	No	Fiber	2000	2000
2a466339102f75183d959c49e3eb6efa	1037528086	No	Fiber	2000	2000
38f36af768781d7ce0ab10c6ea299a41	1037532174	No	Fiber	2000	2000
93a26bbacf3ebad955fc473cdada98e3	1037513460	No	Fiber	2000	2000
a6a89a109458122aa27f9518a61d9ee6	1037513462	No	Fiber	2000	2000
b7e95098ce13bfb36a73076eddcb2f3c	1037513825	No	Fiber	2000	2000
f286c877b623c85d2b4fcbbe535b51fc	1037513471	No	Fiber	2000	2000
65fa465fb86ee806b09c0e08772d9531	1037515030	No	Fiber	2000	2000
b0ca7c0890600fe0dae0f401bdb58a0b	1037514205	No	Fiber	2000	2000
3858e12375b29ed2b3d44b5823d9f634	1037513711	No	Fiber	2000	2000
41d45076451014226f443e2963b90b63	1037513808	No	Fiber	2000	2000
447280166062cc1834cac92e906a9954	1037513680	No	Fiber	2000	2000
7793d337f61c6b1fcbffc5f9ac4bf65d	1037513632	No	Fiber	2000	2000
8458bebb34d085b5b0c45470d6b3db00	1037514075	No	Fiber	2000	2000
6edff0c453b9a90cd00de01b57cef0b3	1037513902	No	Fiber	2000	2000
db10889e1d621a5972142f3a7e89de56	1037513234	No	Fiber	2000	2000
a6a39ebe3646fc36b6ce3d655791f6cc	1037515012	No	Fiber	2000	2000
df83b36723cbc598acaa88a2641ee53a	1037513187	No	Fiber	2000	2000
ea5e8c37e3d3d1077e77f6ffba568e47	1037513396	No	Fiber	2000	2000
f2724027fabd723e0fb60b193e2f034a	1037513871	No	Fiber	2000	2000
e6d44af8c19ed7b91bd077cf5ba6c3d0	1037513329	No	Fiber	2000	2000
a39b5d21ff7b52289d477ae149e41cc1	1037513550	No	Fiber	2000	2000
a216d8f71d9e8df09a2fcf1a64c6df61	1037514068	No	Fiber	2000	2000
5d59a570dc719e2102abca0a95151747	1037513662	No	Fiber	2000	2000
6662848777f4e27b2bbe7cd908f752b1	1037513335	No	Fiber	2000	2000
ca09f9b8cf6063cb6750d2cf8c68f9e7	1037513611	No	Fiber	2000	2000
6e9a9b66ac737020da26b31fd5914fd9	1037513318	No	Fiber	2000	2000
64b4e9170a854a68b75d864cfdce8924	1037514254	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
a8a603e3713c6e16c3c81f647ed38840	1037513257	No	Fiber	2000	2000
97b09b046771cb94eabbcea05c8eaefb	1037513886	No	Fiber	2000	2000
c9d2cdf1c7b429603bfa55db8b7ee102	1037513678	No	Fiber	2000	2000
c2d44dd5a45cf240647c5ef832fda30c	1037513343	No	Fiber	2000	2000
d6a91e57637396c959245b4df34c3e19	1037514101	No	Fiber	2000	2000
6809d8f1749c6c2111dae97bddaa560a	1037513869	No	Fiber	2000	2000
70af09e01c4dfe2ad03504a3b0459e70	1037514079	No	Fiber	2000	2000
37e7cd872c45ed79630642f3099761b2	1037514160	No	Fiber	2000	2000
963a52431ad3400a4b99fcff068c9c99	1037513635	No	Fiber	2000	2000
097c27740706d1611824d53f3a75a00d	1037513681	No	Fiber	2000	2000
abeda899e951ff8da72201eba794f659	1037513799	No	Fiber	2000	2000
d030a4c0b2ccbce6af7e6e8e64e637a5	1037513358	No	Fiber	2000	2000
ce87bf9a377a621cd6a76d8c955fbcc1	1037513633	No	Fiber	2000	2000
d0553ef2039d2dee03c08455b5c01bc3	1037513891	No	Fiber	2000	2000
a8643dd99f7e5f6ad872aa5328766f2f	1037513920	No	Fiber	2000	2000
575a3753f9b6524446128e893d9ba43a	1037513262	No	Fiber	2000	2000
0dcbcf5e352c1223e2ce417696431552	1037513238	No	Fiber	2000	2000
cb87eff1e9d1ad6188393c49560998e2	1037513385	No	Fiber	2000	2000
4aa8b79d579c38ef4f3c1da95361195d	1037513906	No	Fiber	2000	2000
30d09ead56d60e09efa5316fb442a7a2	1037513353	No	Fiber	2000	2000
7cf36856581e3e6688f9d40b5206e979	1037515033	No	Fiber	2000	2000
0c3ad8465232fac1652f752e6d4ea35b	1037513855	No	Fiber	2000	2000
03496221c4f4538ae741e7814e8858e8	1037514263	No	Fiber	2000	2000
907c4b2e367f3ff374456b6b61326b8b	1037514107	No	Fiber	2000	2000
1648d04494ea873b98dbf1fb160a8b3b	1037513249	No	Fiber	2000	2000
a483b64c6a67ce4daf9c4bacbf5aaa9f	1037515029	No	Fiber	2000	2000
564ce0156f13a06e9d5974336bd435dc	1037513657	No	Fiber	2000	2000
7534a37d296d0d9088c3bacd6a1acc44	1037513647	No	Fiber	2000	2000
b167a3bdf7c9cb0eac0f3543a3cef183	1037513672	No	Fiber	2000	2000
11c70fdcecc92997e4e935a4bcf422b9	1037513607	No	Fiber	2000	2000
32f815915421a879b0020e30d9c51750	1037513665	No	Fiber	2000	2000
a5b4debd9f873990bb3a4ee3628bc975	1037514055	No	Fiber	2000	2000
71ab302256fd39db37d4554485485882	1037513887	No	Fiber	2000	2000
624e64e9641402151de228eafd0097b0	1037513293	No	Fiber	2000	2000
16d7a44061bd8320b1fc6727c6097b28	1037513907	No	Fiber	2000	2000
5a26a80332392c5d42df1e37454c18bb	1037513364	No	Fiber	2000	2000
915436e37229cf54220ae141c883e79f	1037513826	No	Fiber	2000	2000
5c6d9e12a052768d040fd82ff07171c7	1037514012	No	Fiber	2000	2000
ca1a3697736417376994ce09e8119f2d	1037514164	No	Fiber	2000	2000
9e7b59d489023a95a0a5e04a482d4a91	1037513452	No	Fiber	2000	2000
8a5a7ef4ee76c7947f4ef8fed9729a3c	1037513905	No	Fiber	2000	2000
ceab1987cd332265c53f7c87a37385a5	1037513338	No	Fiber	2000	2000
0a6e56e9797ea8738af6e9f54322151d	1037513874	No	Fiber	2000	2000
988cc109996d6d0e750a4b9a7026e4d1	1037513548	No	Fiber	2000	2000
9f721ebbe483156d7d75411a824c070e	1037513670	No	Fiber	2000	2000
2330b053aa3ebee76a380dce6c4fb3f9	1037513437	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
af5d87cd930ff78db68afabacbcfddeb	1037513274	No	Fiber	2000	2000
f5ae0307291f9b1bab97b2406e8a9661	1037513694	No	Fiber	2000	2000
2666b56e3f4730ba9e30f3748fdfd4cf	1037513660	No	Fiber	2000	2000
fd7dc23de8a1eac5e34c0e7520b7042c	1037513835	No	Fiber	2000	2000
abfb08e8f2e910a57d3afbfc588d668e	1037514085	No	Fiber	2000	2000
af7f4fd22fad0f9d3e6395f7519d8e55	1037533712	No	Fiber	2000	2000
5b80dbd778f1384a672b7c2d0f1744dd	1037527927	No	Fiber	2000	2000
bf43098e2af95b8268daefd55b017028	1037513659	No	Fiber	2000	2000
e0aef490aaf170135aced3225b41f761	1037513631	No	Fiber	2000	2000
712ba620aaec6b7f74d34e30a68f69cf	1037513242	No	Fiber	2000	2000
e5f3f702fd64a0d68ca08e276c530f6b	1037513802	No	Fiber	2000	2000
11ef4fecc1326163e0f1c57992018d43	1037513541	No	Fiber	2000	2000
3adea8598b50b1202c9421820f2684b2	1037513317	No	Fiber	2000	2000
782710d7ca2573d491664d3b5c8e6ba7	1037513432	No	Fiber	2000	2000
92aaa06b29aa91b5b3f034380aba38ec	1037513248	No	Fiber	2000	2000
b0ee9c1b15af01c5c1f00269543a3c25	1037513763	No	Fiber	2000	2000
61c4bd309d86fec2b7c47fb1fe0020cb	1037513605	No	Fiber	2000	2000
8e0091993f3650798c48459c34c19bdb	1037514146	No	Fiber	2000	2000
982c827b123550df602d1fb1d3156d56	1037515032	No	Fiber	2000	2000
e972a55c6a06d256ad8bb57cd52de3f2	1037513286	No	Fiber	2000	2000
b1d8df3c1ec5b3cea9e30beb3ffc6670	1037533487	No	Fiber	2000	2000
d0e9d7570e66d71bb2be87254784776c	1037513545	No	Fiber	2000	2000
d326a9d0f29d23ecee1e7c5f6129f240	1037513549	No	Fiber	2000	2000
fb0de98dba2b514acb8cbd175a33a982	1037515015	No	Fiber	2000	2000
7bb2c8a4a45dd645ee98ce45122d1d75	1037513247	No	Fiber	2000	2000
a5d8b51078cbd60dffc2a98690c26914	1037514150	No	Fiber	2000	2000
029d17a3d26d85779083fff72ab5a975	1037513235	No	Fiber	2000	2000
1708df24ea0d8c17d9f13c6992fbbc5c	1037515017	No	Fiber	2000	2000
a461bc0b7e2e51287f0d9510b2bf250d	1037514143	No	Fiber	2000	2000
277048f9255b781c03aae88631160b9c	1037514145	No	Fiber	2000	2000
cf9c9ff50aa443797d2279a66815899b	1451745525	No	Fiber	2000	2000
9b330588a838950dbd35d75512da2ce8	1037513698	No	Fiber	2000	2000
ba0201f698b7a6fd8a26cb54935fee13	1037513813	No	Fiber	2000	2000
fbe55e69fc9a760ad94d7b2f54a0ed2e	1037513210	No	Fiber	2000	2000
076ca0f7b8d83f63aa09e2155095fd8e	1037514074	No	Fiber	2000	2000
fb0b5a9ca6fecb12e41e85d0050bd2dd	1037513663	No	Fiber	2000	2000
ecb4f5aabc7be30288aa2bd63cefe093	1037513857	No	Fiber	2000	2000
cd9a74e63afed4d7929d9751f1bedcb4	1037513546	No	Fiber	2000	2000
093cca7f140ba9616a17039bb648349d	1037513391	No	Fiber	2000	2000
821e98540c5901819413c2f0a268c9b8	1037513676	No	Fiber	2000	2000
71077263d10b44b0c979be6aedc12e6e	1037513687	No	Fiber	2000	2000
d840bf7b04052646b17e5485ab9519ad	1037527935	No	Fiber	2000	2000
d5548f2a07bdf86acf74a6c76117f767	1037514120	No	Fiber	2000	2000
2354abc93a7d4866b1d5f36d47b6403e	1037513554	No	Fiber	2000	2000
9bf12c86e028b296a7ef53163bca674e	1037513872	No	Fiber	2000	2000
3a1d650936262127ff04bc1ff0c6c40a	1037513236	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
14c7f8ae09a33990d3f0977bfe165fb7	1037513867	No	Fiber	2000	2000
71539b3330f4bb98ae2cefbd4e334965	1037513893	No	Fiber	2000	2000
234080cbeb39342c6946a138c8299729	1037514140	No	Fiber	2000	2000
b118991c36ffd1b76b34c39796edbc86	1037513309	No	Fiber	2000	2000
8b8e00328ba37e0eb907cce16a14c275	1037513276	No	Fiber	2000	2000
27917460b972322776d4fec4dfa345a7	1037513417	No	Fiber	2000	2000
6d13313e6c31183a93aa9529c39b870d	1037513730	No	Fiber	2000	2000
84bf03d0903972fbe2e0dfe983c63fad	1037513473	No	Fiber	2000	2000
2100b67f4aa2163b938f142d279fb73d	1037513357	No	Fiber	2000	2000
10ac967316463b4ecfa116de168f073a	1037513371	No	Fiber	2000	2000
750b0b2211309c1b7b38d576cd722c0a	1037513394	No	Fiber	2000	2000
e7165a0789bbb4d1120f849d2655af08	1037513911	No	Fiber	2000	2000
cfb5c69e913107191da5af7d75f67a05	1037513606	No	Fiber	2000	2000
b9a3929f552d1a3622b6f47b5a2f2ba3	1037513675	No	Fiber	2000	2000
f51d352e72bcab6d3ce151a8317db52d	1037513720	No	Fiber	2000	2000
e3ead362f24d0752da4b11a37b16503b	1037513686	No	Fiber	2000	2000
f31d07f78cd4fa4e4d7831f1ae27d4fe	1037513370	No	Fiber	2000	2000
831ca343469398445c2172b688564f43	1037513376	No	Fiber	2000	2000
9baae1b52c40ba3e91ba1f025ccb16dc	1037513372	No	Fiber	2000	2000
bdd86e02183ae9c8f2ced917f9397775	1037513608	No	Fiber	2000	2000
7b6d529c41314c4ee543758347e745dd	1037515028	No	Fiber	2000	2000
6a48a3de8d460c8059720351a3f27b7d	1037514093	No	Fiber	2000	2000
f7ef01d9f633e1ed1e37db2f481a8fac	1037513368	No	Fiber	2000	2000
bef538fb32005a4e0a0bef1126a50860	1037513679	No	Fiber	2000	2000
94de51912872a1166f97e6c55a7ec114	1037513340	No	Fiber	2000	2000
9840f3b8f659aa402afff36194a8b246	1037513641	No	Fiber	2000	2000
9809632f7848c90440d7a3ea4107028b	1037513211	No	Fiber	2000	2000
317966ce278fe80a39c215e3de25ae80	1037513776	No	Fiber	2000	2000
512de413bca849ce47c8417c7f851e8b	1037513841	No	Fiber	2000	2000
23460cf5bc96b84cdd05014ebde67786	1037533217	No	Fiber	2000	2000
ddbe9a68de15731fd42b1f09062ab49a	1037515056	No	Fiber	2000	2000
996827650c166d0a5074abf46ccb4524	1037514105	No	Fiber	2000	2000
a36dbd4b2b52190d91f93d5d0095f8bc	1037513465	No	Fiber	2000	2000
d060a4ad0bdf980dfba9b2c48632d023	1037513332	No	Fiber	2000	2000
69803c8285babe363835890b173241bd	1037513688	No	Fiber	2000	2000
da0534200abdcd2d972971aa3920c2f6	1037513684	No	Fiber	2000	2000
439a191a351b061e75dd6ababedb5ac0	1037513458	No	Fiber	2000	2000
7e3db1eefdf9c5aeb63b07de8ef3839b	1037513431	No	Fiber	2000	2000
f32fa2956f3b82eda451bf65ae3fd6f6	1037513282	No	Fiber	2000	2000
daa9dbca3c1391ad85963a268182c0cb	1037513362	No	Fiber	2000	2000
870af187032a603bc7f615bc7bfc6912	1037513408	No	Fiber	2000	2000
95586936ec91b5e0ba4ec2dbae74b255	1037514110	No	Fiber	2000	2000
867612cd7380e3fffe96b927f51d3aa2	1037513383	No	Fiber	2000	2000
0ddca20b4507ad6bd868b82662e254a4	1037515053	No	Fiber	2000	2000
faac65bf808937656170eeddf8364eda	1037513052	No	Fiber	2000	2000
875e065f460d12f2dbcbef95ccb2dbfd	1037514071	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
7f2b6d7994d305f2c9333a6519b24728	1037513614	No	Fiber	2000	2000
f48f638c458f95ea87771118ddcb9936	1037514058	No	Fiber	2000	2000
96723c37f8a931297d5672c8a79c6b32	1037513304	No	Fiber	2000	2000
b2448b5d1a937a4af613fe615a24e6e1	1037513055	No	Fiber	2000	2000
a4a2be8e301acce21e4265bf7e5edcb3	1037513612	No	Fiber	2000	2000
8c527fd38cd110903c228786a76b2f26	1037513791	No	Fiber	2000	2000
f2f395d625486d7c85fce0e53a877328	1037513401	No	Fiber	2000	2000
b68e0d0a70f85f40cc55590dc5dffddd	1037513214	No	Fiber	2000	2000
bfe3a00125b65d3f8eddefc4c492e6ad	1037513367	No	Fiber	2000	2000
440dd5ac88627273cebe0a5f9a25fafe	1037513272	No	Fiber	2000	2000
4f2d0920935077ddc9712162b349400d	1037513011	No	Fiber	2000	2000
b4bf41d15a8e878b40cd9f0da02089b1	1037513348	No	Fiber	2000	2000
c0306b037a44eade1ed632d0e44eddb6	1037513831	No	Fiber	2000	2000
bad1694a09ecef26372e9eb9aa495ac7	1037513205	No	Fiber	2000	2000
34f06bb11c8b8d868dd3e451d1744605	1037513359	No	Fiber	2000	2000
9b1313c21fd0aa3bd7fdb204d1f87698	1037513280	No	Fiber	2000	2000
2b06d2ba65cbd59f05762775e7475865	1037513603	No	Fiber	2000	2000
c128e84243bce0cffc3228d9608c5fae	1037513669	No	Fiber	2000	2000
b61ab4114eb54d9be2de0fd9f55f60e1	1037513374	No	Fiber	2000	2000
d995cab94563b81ff74c3f95f905c8d2	1037513860	No	Fiber	2000	2000
3a4bb81ea3df8b722e4c0326898c1ad7	1037513661	No	Fiber	2000	2000
94e7e409cab1c894a5f42e2fc15c5424	1037513271	No	Fiber	2000	2000
39c2642158c3082d4c78876e9c32744b	1037513664	No	Fiber	2000	2000
691eb4deaaca4238b76a81dc6f131fb9	1037514119	No	Fiber	2000	2000
c2cbfcd36b042ddd364e9ff88ca7d1bd	1037514186	No	Fiber	2000	2000
ef6213ead0133c8ad3f0b23684482824	1037514062	No	Fiber	2000	2000
dfee1ff7ac8210a02a65ecbab8067130	1037513699	No	Fiber	2000	2000
768c736dbacfcf8669fb82c1fca97c7a	1037514135	No	Fiber	2000	2000
24f73bfa03d49563cbe3b3eddc373f98	1385268469	No	Fiber	2000	2000
ab9a05e08a4ece4a02c6944c83712028	1037513400	No	Fiber	2000	2000
761f1f9ab2e3ce0d6a15251fd556f803	1037515050	No	Fiber	2000	2000
ae5c30817c02625123486ca72ceaf33d	1037514123	No	Fiber	2000	2000
5254d3369b625a43964f4899b4a79930	1037515057	No	Fiber	2000	2000
10b0da2702b8e3a117aa3b506fb0a0eb	1037513930	No	Fiber	2000	2000
68e8ffdbcafe1bffed8d02cf6435e0f7	1037513342	No	Fiber	2000	2000
8b84fd46109be41651fef488df1978a3	1037513375	No	Fiber	2000	2000
164283f1057ff112b82647660ce4d085	1037513894	No	Fiber	2000	2000
67d4928a40e67fa1072357716fff39f1	1037513809	No	Fiber	2000	2000
3f2b9dc8c456aa88c4df4196bef823bf	1037513667	No	Fiber	2000	2000
fc496c61ef51a8b02f4124867128f5da	1037513658	No	Fiber	2000	2000
a1d794b4e4099cebfe81b6e0c301c6c0	1037513468	No	Fiber	2000	2000
1aee849837308ad49c35ba41991206ed	1037514114	No	Fiber	2000	2000
2eb7b3a6e8f7d9bf0ebf779194d24d3b	1037513850	No	Fiber	2000	2000
6d1b2e715f0dd815cd93ea4074a69e25	1037513870	No	Fiber	2000	2000
a8589ca5efa29b66ae1a3aa63ff214d5	1037513315	No	Fiber	2000	2000
25c2f17904e3630c3752fee03b26f328	1037513387	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
dcf747dab5ad73670ff6ed5356e22237	1037513466	No	Fiber	2000	2000
20bf6eb8e07a5b3a0ff355aa4d1be857	1037513303	No	Fiber	2000	2000
7600ff1f44459b997e94185aeccd1110	1037513313	No	Fiber	2000	2000
bb48e65c897fdad7dc1bfe589d1db84e	1037513208	No	Fiber	2000	2000
1d82f7adbfe5179dc7dd2a75ac4ab554	1037514156	No	Fiber	2000	2000
248c9249ac97bb3fd6ba78a7ace39279	1037513467	No	Fiber	2000	2000
47d11f7e8fbd8ae993855c2e8c21ca89	1037513897	No	Fiber	2000	2000
2c4983069617b54bd5d305f3db93be5e	1451745877	No	Fiber	2000	2000
202b4981206f9f4fea8d56651f5d9406	1037514172	No	Fiber	2000	2000
24e66fc0494976e47b62d9ba2ac78a6c	1037527967	No	Fiber	2000	2000
bb46481a0230b0729d33fb4567996f55	1037513866	No	Fiber	2000	2000
93e4f50416162835f988bece8eb573f6	1037513712	No	Fiber	2000	2000
07764fa912afa47789b9d0e2792a794b	1037513836	No	Fiber	2000	2000
30856c298b1e25ce19da0ca36d794b0b	1037513402	No	Fiber	2000	2000
57d26e228c39078e842e8d256d3b19c1	1037513861	No	Fiber	2000	2000
6621be8518f8662baa9a01078da142a2	1413434945	No	Fiber	2000	2000
8624631fc1f1e57eae0383875f59d28a	1037513877	No	Fiber	2000	2000
9876098c48b6f2878bcbf354fb55edea	1037515058	No	Fiber	2000	2000
305e2b1be4f2a943cc884158251712f9	1037513436	No	Fiber	2000	2000
21c1d1a686574227a73a7dde9a5c31d9	1037513419	No	Fiber	2000	2000
7d99c6948bce7df4dd6a33a080e2d7e0	1037513613	No	Fiber	2000	2000
d79fdeeca63ff0a3cfc67f0730ed93fc	1037513451	No	Fiber	2000	2000
8d145a4adb0cee1123c6c0b31a5af90a	1037533218	No	Fiber	2000	2000
1e99b65e26550f0c57c514720d641386	1037513692	No	Fiber	2000	2000
eaf78a2ee57e54609c8175810d7cddeb	1037513903	No	Fiber	2000	2000
98eb14dfc750e228ae98dcd941290fb7	1037513461	No	Fiber	2000	2000
a0af12a5e04c45d6010944a84e1d951b	1037513873	No	Fiber	2000	2000
b63dadeeb694b3cfe1ce0093b308f1f5	1037533713	No	Fiber	2000	2000
a3851f13306c8db2dddfb2a562e7063a	1037514154	No	Fiber	2000	2000
1d43448572f55bba1b626a7ef5b57452	1037513243	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 38 – Budget for Project Area IBO-963

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT Installation labor	Installation of OLT in the central office	Construction Services	$1,284.00	$780.00	$504.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$22,500.00	$13,676.00	$8,824.00
Permitting Costs	Permitting Costs	Professional Services	$94,679.00	$57,548.00	$37,131.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$111,775.00	$67,940.00	$43,835.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$99,871.00	$60,704.00	$39,167.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$393,592.00	$239,235.00	$154,357.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$345,438.00	$209,965.00	$135,473.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$42,324.00	$25,714.00	$16,610.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$116,625.00	$70,857.00	$45,768.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$119,288.00	$0.00	$119,288.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$6,049.00	$3,675.00	$2,374.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$12,177.00	$7,398.00	$4,779.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$19,229.00	$11,688.00	$7,541.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$253,712.00	$0.00	$253,712.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$15,783.00	$9,594.00	$6,189.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$102,505.00	$62,305.00	$40,200.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$48,000.00	$29,163.00	$18,837.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$6,030.00	$3,664.00	$2,366.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$10,690.00	$6,495.00	$4,195.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$5,359.00	$3,256.00	$2,103.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 38 – Disbursement Schedule for Project Area IBO-963

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 38 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-963

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 38 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 39 –Subaward Conditions and Statement of Work for Project Area IBO-893

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$1,330,169.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$1,330,169.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$1,330,169.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 39 - Specific Award Conditions for Project Area IBO-893.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[53.61%]; [$1,537,103.00]
Total Project Cost = (subaward funds + match)	$2,867,272.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$1,330,169.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-893 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 39**. The Project Area is depicted in the map in **Appendix A of this Exhibit 39**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 39**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $1,537,103.00, which is 53.61% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 53.61% for a total match of $1,537,103.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 39** in the area depicted in **Appendix A of this Exhibit 39**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 39**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 39 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 39;
- Appendix A to this Exhibit 39 – Map of Project Area IBO-893;
- Appendix C to this Exhibit 39 – Budget for Project Area IBO-893;
- Appendix E to this Exhibit 39 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-893;
- Appendix F to this Exhibit 39 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 39 – Project Area
- Paragraph 5.B(2) of Exhibit 39 – Project Locations
- Paragraph 5.B(3) of Exhibit 39 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 39 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 39 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 39 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 39 – Access to Service
- Paragraph 5.B(5)e of Exhibit 39 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 39 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 39 – Map of Project Area IBO-893

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-893

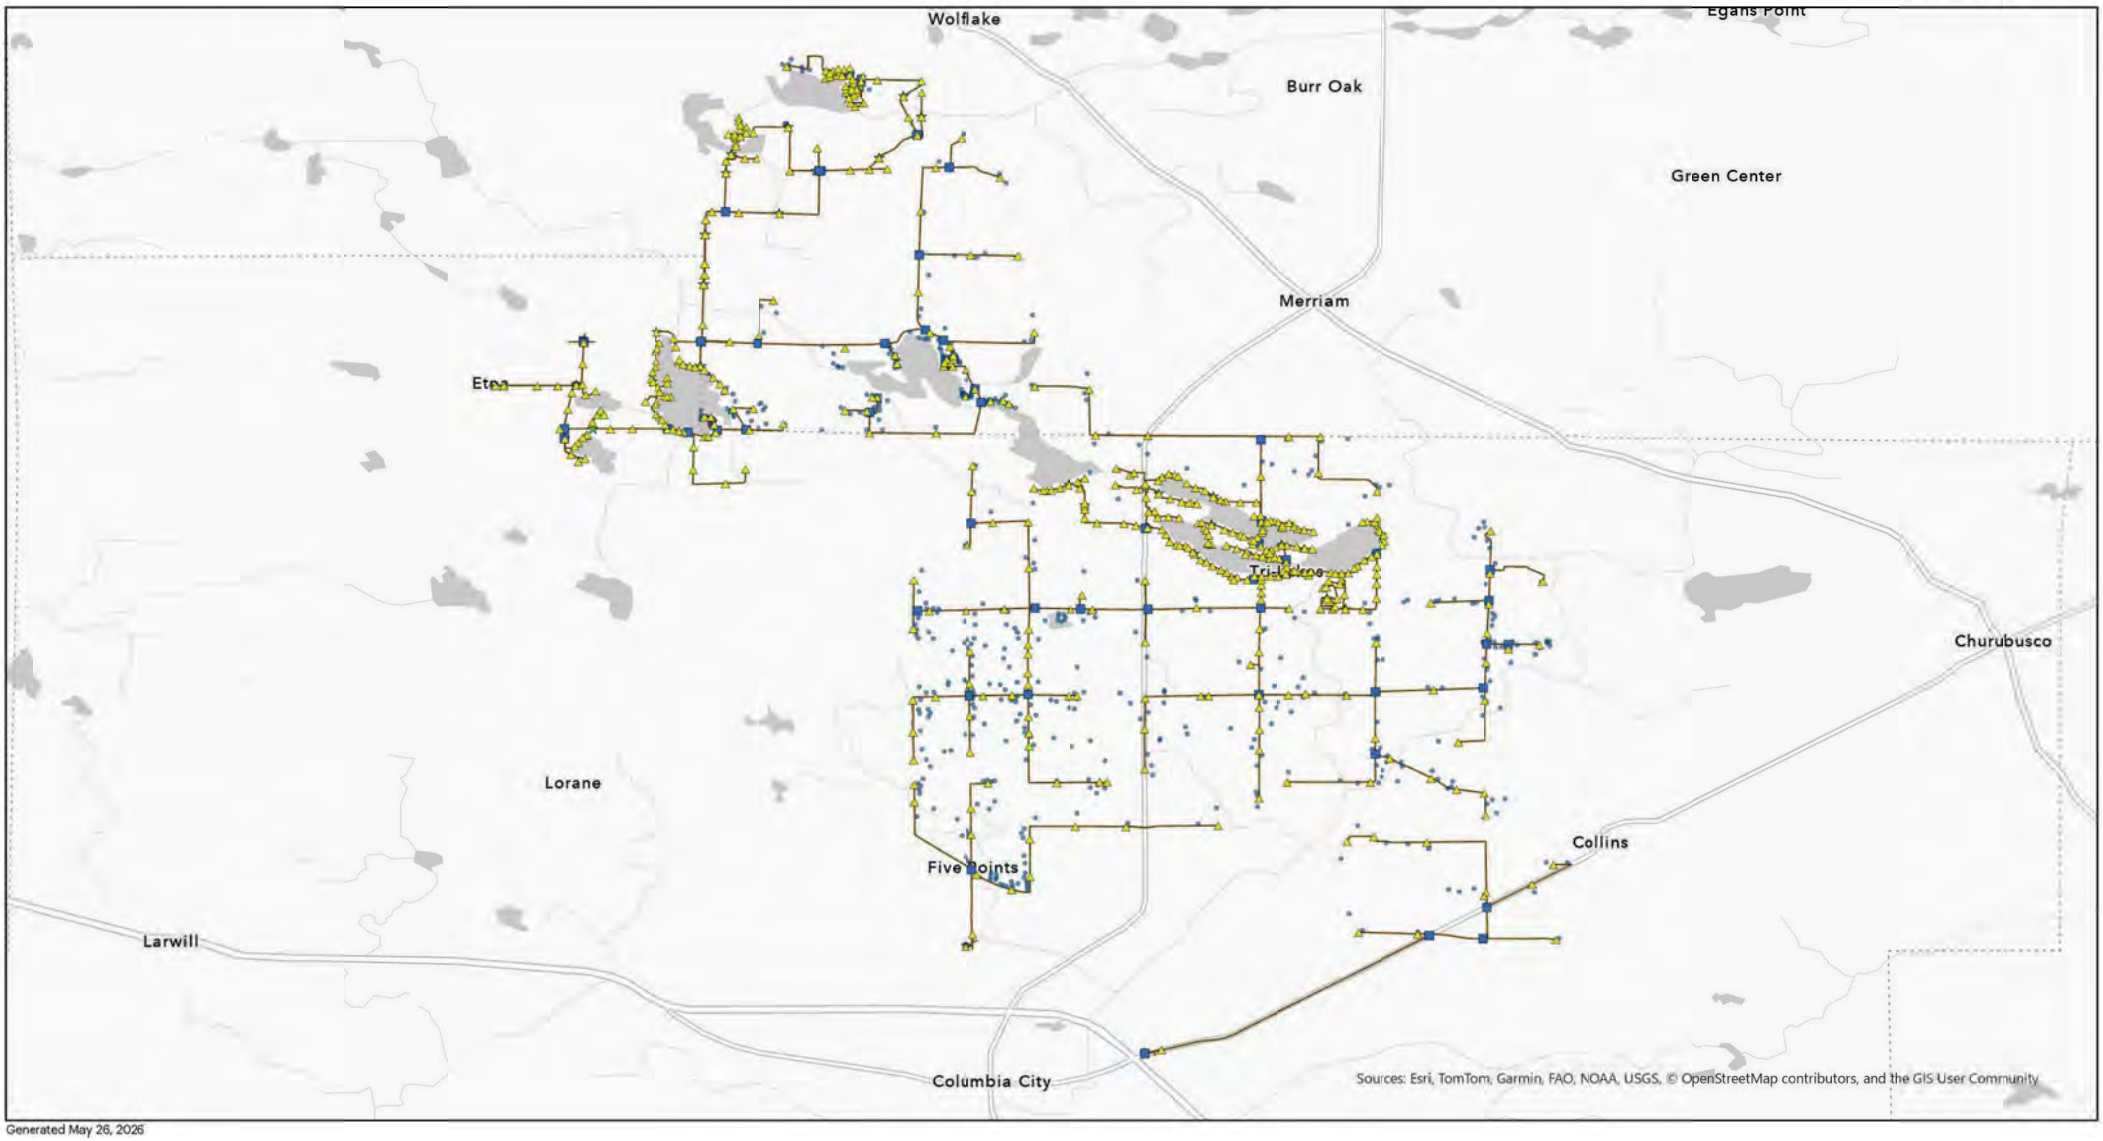

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 39 – List of Locations in Project Area IBO-893

Brightspeed IBO-893 Location List

545 locations

ID	Location ID	Is CAI	Technology	Upload	Download
91a9569dd12744f8fc63482e3d708632	1145362667	No	Fiber	2000	2000
10741679f569a57ce7e57a6b1e70cab6	1037516178	No	Fiber	2000	2000
22e556b3f3f2b415e6324c60cbfacf14	1037516166	No	Fiber	2000	2000
9487de327723a7e5f4d0cc48962453f4	1385445647	No	Fiber	2000	2000
5ae70a9825f08fe4ca9fa6146fd00ecf	1145362723	No	Fiber	2000	2000
baac2f2f5d421d82665922fe8d5b0518	1037515879	No	Fiber	2000	2000
3340368dc389f15aaa75557ef9529284	1145362590	No	Fiber	2000	2000
706fd922caca850717a8d65ac50a7d0c	1145362438	No	Fiber	2000	2000
bff42c0a9bcda6733956b0dd7b203450	1145362537	No	Fiber	2000	2000
0d376f8b17c5be9ebc5def2391c92214	1145362686	No	Fiber	2000	2000
cff1c0c2657833c92e1006e0b3d06e56	1145355448	No	Fiber	2000	2000
52ded3203f18eaf2263f086a86733360	1037515868	No	Fiber	2000	2000
aa211fef41e5bf3563335b4a5ddfcbc9	1037516338	No	Fiber	2000	2000
d8c2955e59b507a740fb24c5c33493a8	1037514597	No	Fiber	2000	2000
ee0759b0178fd28e48d0f5ed49eefd7b	1145362684	No	Fiber	2000	2000
67cd3d504e935070c87fba8c00e88114	1037516144	No	Fiber	2000	2000
3cfdf275f859b8d9d1970eb1bcd971f9	1037516927	No	Fiber	2000	2000
28a0cd3ee13908aa08bf06ada197e71d	1145362732	No	Fiber	2000	2000
15091e76b36f1811572ff6d3721391fe	1037518442	No	Fiber	2000	2000
7afee5da9c5f629c3c984f69c8a26849	1037515905	No	Fiber	2000	2000
675e62dd6a3fa73fb5837ed40a7615f4	1145362521	No	Fiber	2000	2000
a49b5bb9205f6a2556ccab48885ed73d	1145362533	No	Fiber	2000	2000
feac59bd4421d180a4d6a62e734773b8	1037516108	No	Fiber	2000	2000
bc10cf8b4d6ad8e740ce5e0b30df6c24	1037518849	No	Fiber	2000	2000
c87f1b25d87c967e397867f1c7f83243	1037518432	No	Fiber	2000	2000
a12d7219289788b3d8bab96095d50fb0	1037516170	No	Fiber	2000	2000
89061b07b03ef51c9469aa357c0d827e	1145362777	No	Fiber	2000	2000
109fa91f8af345c9126cb8cda5f65f1b	1145362682	No	Fiber	2000	2000
97bf9e25a2a8f09a450587474e174102	1037515984	No	Fiber	2000	2000
107d9acd7f5010a6cbdcf8716c269ca9	1037515986	No	Fiber	2000	2000
ed0b64c2197741a810101371dea310db	1145362361	No	Fiber	2000	2000
5baed805969234d49cbc1fbf09ff90b8	1145362721	No	Fiber	2000	2000
e33b18124fa22c4b7c44917538b9eb96	1037515862	No	Fiber	2000	2000
908f3d823fd71ea44b3d7fbc8e63dc1f	1145362494	No	Fiber	2000	2000
f91bbfc04cf3a82d866ca783291664b3	1037516533	No	Fiber	2000	2000
bd7f6188a2c801fb1651894e1bf2aafc	1037515918	No	Fiber	2000	2000
258b8f6a688da7f3deceb6ac1e9f58a5	1037518810	No	Fiber	2000	2000
88de7b37da087cc40be7320b30230983	1037516283	No	Fiber	2000	2000
98ceae78bb654ffed8da3fe0ba909a5a	1037516452	No	Fiber	2000	2000
dee936e51512b958d5c702bee662978e	1037516211	No	Fiber	2000	2000
31f789ba2d48c9eaed25ca41ff82f501	1037516929	No	Fiber	2000	2000
b0fd811162ae7c2b3bae61d2b3fefcd2	1145355318	No	Fiber	2000	2000
59f796c78e05707d34d79d86cc418a84	1037518791	No	Fiber	2000	2000
1c0025fbb0825391faaa8d6b36e7b02b	1037516097	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
eb793635c03f469359f5bc1c2f003b90	1413434885	No	Fiber	2000	2000
4ba6f6dc0d84dfcc5bfac9803c6ff22c	1037515096	No	Fiber	2000	2000
e89821c6f78ba61868bfc3645959d222	1037516165	No	Fiber	2000	2000
7be6bcdf2a9de86ef75d656dbd72b068	1037516004	No	Fiber	2000	2000
4655c86b499662fe1d964252436f77ee	1037518473	No	Fiber	2000	2000
46ba06c0d66ff68a26ce2bdbc9bed6af	1037515115	No	Fiber	2000	2000
b8dc94d3e47a0d54277be260d6dcf547	1037516523	No	Fiber	2000	2000
08d7251ec0e951093dac5ba23fbbf6dc	1037516217	No	Fiber	2000	2000
c172c70e122d1a566237c7e55bfe4c2d	1145356162	No	Fiber	2000	2000
e0e77dad77ecbadcc64b22cff3e0ad11	1145362498	No	Fiber	2000	2000
b0dcf98930a49d409345d20edabdb562	1037515926	No	Fiber	2000	2000
015a9443e491614511474d4b106c3829	1145362340	No	Fiber	2000	2000
8297862250909ec5f699b6cdebf4e0d2	1145362745	No	Fiber	2000	2000
06aa2322e2ced4b95fe012c5a97436e5	1037515981	No	Fiber	2000	2000
50e5f98d11873abcf31d76216d62cfac	1037514590	No	Fiber	2000	2000
e9508176a774472d014ea7e7f82b401d	1145362690	No	Fiber	2000	2000
539d5e60f0208e3735b8146188b37d01	1145362675	No	Fiber	2000	2000
5aa3181547a699930a8563ab5740d5c0	1037516307	No	Fiber	2000	2000
38de0b30be551f34388997357d685d33	1037516214	No	Fiber	2000	2000
fb9efeb41d42b98026d4f0409059a57e	1145355965	No	Fiber	2000	2000
2b3f2cea2247b889c32343db9e00c155	1037516011	No	Fiber	2000	2000
3afdb9cdd1fcf1823bf5a04ef1b6b748	1145362536	No	Fiber	2000	2000
cbb45e4a43abc89304e17b04f01d1a98	1037516530	No	Fiber	2000	2000
52d1df1cc4c44c63f0a01a550967aa56	1037516181	No	Fiber	2000	2000
102ab21e87cd781814c522b20eeaf64e	1037516261	No	Fiber	2000	2000
e4b4abed972dc9075748f36279489a92	1037518463	No	Fiber	2000	2000
c237b350c8c4e048bcba53ade075aa29	1037518461	No	Fiber	2000	2000
0fe5484226558d50b909441c1e0863f4	1037516095	No	Fiber	2000	2000
746fbc27c9a671607534068761a5f160	1037515989	No	Fiber	2000	2000
f2c88c61826e5967a65521b310199b72	1037515996	No	Fiber	2000	2000
13831d2acc8b65ebf5f26dfcee81068a	1037516518	No	Fiber	2000	2000
b7a10b21a3af3fd7428f13ad0884de82	1145362390	No	Fiber	2000	2000
e55bb6b025be19f4bba14237621338d3	1037516132	No	Fiber	2000	2000
9bed8d420190c16a643877c5c91052f4	1037515913	No	Fiber	2000	2000
ed92e5b4fdf4ef0e0603b7bdc1e52eb8	1037518424	No	Fiber	2000	2000
dd2c482ca40fbbd522fe935dc872566f	1037516193	No	Fiber	2000	2000
e5cbd7826a51a1564e3e1bbf87fb152f	1145362709	No	Fiber	2000	2000
c4a83be306640d315da4d38e96114da2	1037514576	No	Fiber	2000	2000
dae61e3362708b44f0c708486e7aeffa	1037516091	No	Fiber	2000	2000
214aa47de0c47ca36bc8ff64cf7cdbc2	1145356294	No	Fiber	2000	2000
04b5a8fd0e7d7539530c3d3985f28e85	1145355298	No	Fiber	2000	2000
d96823cec0d25acdc3f0a58e333d9c04	1037515941	No	Fiber	2000	2000
8792e70981dbfee0bf7c8e3cf918512c	1037515966	No	Fiber	2000	2000
6f892ec7c56369fca74040426945e787	1037516180	No	Fiber	2000	2000
92bf76df618e70854db0676e69932298	1145362437	No	Fiber	2000	2000
9ffe3e2bb9bf034360fb675d2043f437	1145362609	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
508c455f5e77614b3da066d5e242b2d4	1145356166	No	Fiber	2000	2000
158c1dc129144f6e74615bd36ee7db4b	1037516598	No	Fiber	2000	2000
a53e8066caf6d14e7313ed025a93b36d	1037518475	No	Fiber	2000	2000
b93361c24c281bb674a52de7c5724766	1037516310	No	Fiber	2000	2000
f81e2359452111907b5ebbc8ac9be249	1145362717	No	Fiber	2000	2000
9d1a962412dafc296b3857d1b0ff62e1	1037516199	No	Fiber	2000	2000
439e8c9f0b4921405ba9c68aa20c3afd	1037516185	No	Fiber	2000	2000
5ac6faaded3a44a8b89c7515e552223f	1037515978	No	Fiber	2000	2000
f21fa99aee98d41f385a744b15fa89fe	1145362699	No	Fiber	2000	2000
90517ed9cd9f95f2fcc19b70beb3cadb	1037516282	No	Fiber	2000	2000
3839a99a0ee43d11a1a388e4c129ff5b	1037516525	No	Fiber	2000	2000
297eb187f26540470be92f7bc72bdc05	1037518451	No	Fiber	2000	2000
526488fa53642d466b2902e2d8ddd862	1145362362	No	Fiber	2000	2000
3979ad2072fc04d9f9b8014ba23afce4	1145354555	No	Fiber	2000	2000
b74fb70508372c7d93dbaf198defecf9	1145362666	No	Fiber	2000	2000
eeee39957c98bef6c067de6bb159427c	1145362461	No	Fiber	2000	2000
067a88bd1132bf6527625fad864b4d4f	1145362711	No	Fiber	2000	2000
113a391bb665aa7cbda6d455b2d53b5a	1037515851	No	Fiber	2000	2000
e19f6ae4cb70c96959ae5db4fc5a818a	1145356034	No	Fiber	2000	2000
e6a8bfb27ee265e993a0441553f29fb0	1037515908	No	Fiber	2000	2000
231d5b9076d5e1ae0e0dc23c9908841d	1037518440	No	Fiber	2000	2000
91df3da007016cf4eede7ba86992436c	1037518455	No	Fiber	2000	2000
a9ad13f8a8f265f8babb10df68695d4c	1145356085	No	Fiber	2000	2000
785d1e6ef23c333e76a987b41872d495	1145356157	No	Fiber	2000	2000
9f49d47af99a14921d617b0c62adfe44	1037515940	No	Fiber	2000	2000
1045102a8166d80cf3c692397bdd636b	1145356295	No	Fiber	2000	2000
b64fe5c0db8d5a678c74b2b3df3da1a2	1037516177	No	Fiber	2000	2000
73a54c4089c5e29b61be80f379ba7743	1037515857	No	Fiber	2000	2000
920a8708615dcfd7d35996861016f3e5	1145355130	No	Fiber	2000	2000
44ca2f019fe61259d25df6c80743fc20	1037515994	No	Fiber	2000	2000
98efa0d3d61d43e92db1b65d14bd7e9f	1145362434	No	Fiber	2000	2000
450dda600787264f46c73038c36e2d84	1145362481	No	Fiber	2000	2000
da4b051768a37a169480df546e475f8c	1145362519	No	Fiber	2000	2000
406dcdee5d9b1a5fcb54d0998d902dc9	1037515095	No	Fiber	2000	2000
45aed3e9ac67aa7f96b2a29148732ec9	1145356060	No	Fiber	2000	2000
f8225b7fcb8235edc7ae7ef52121f429	1037518467	No	Fiber	2000	2000
4c3c208b674c51394d7aa0d0f324a468	1145362504	No	Fiber	2000	2000
5709929fd9512c9dfdbe30e10e561a25	1037516012	No	Fiber	2000	2000
bf83f17b05259633b9ba04d7bfc184be	1037516210	No	Fiber	2000	2000
9837643aedfce5aabf660d6bac6d8c29	1145356165	No	Fiber	2000	2000
c6ba1f2f7dfc45d44960339bdf780175	1037516015	No	Fiber	2000	2000
c0ef05aa1902e04317f0c1cdfb40affb	1145362389	No	Fiber	2000	2000
6fc3b38cd5e5e445b7f6cffb8972484a	1145356087	No	Fiber	2000	2000
1f7fdde1842e2f6b0db8829f339a4555	1037515923	No	Fiber	2000	2000
5f3dd776e4411b6c906cbfd4b255d397	1145362572	No	Fiber	2000	2000
ef4e36ae92d18b990be504aab8cdce41	1037515854	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
ac64eb772520daab39d58bd7871ed034	1037516192	No	Fiber	2000	2000
92e42d33b1aa379aa9b7eb713315b697	1037514927	No	Fiber	2000	2000
3f887b10eed404d04f3d3701a9bd5ddb	1037516058	No	Fiber	2000	2000
661cde7775bccb9c19c1509188899318	1037516268	No	Fiber	2000	2000
436a512ece6e114ae972d63f8c1d9c45	1145356090	No	Fiber	2000	2000
20ca8ca5e8ddf07c771066f1f65763c0	1145362546	No	Fiber	2000	2000
b70f4a67c261884b7b52d407b358e323	1037518437	No	Fiber	2000	2000
b63d4998f7665c64c530297006f0a02d	1037515891	No	Fiber	2000	2000
82741874441080f923252d8eb73fadc4	1145355831	No	Fiber	2000	2000
e56dfc57133b813ddddf45d783f82b63	1145362621	No	Fiber	2000	2000
cf71ad4a1ebc38af8f990bfc13e3137f	1037514588	No	Fiber	2000	2000
32d009eca55879001fd9983a043dbe8a	1037515972	No	Fiber	2000	2000
0303955d54e42f9bbe676e749d3b6c2d	1037516173	No	Fiber	2000	2000
bc0d28ff9ecd6d609060b6990a59f986	1145362693	No	Fiber	2000	2000
8694c46702cbc7b142f8eaadee40d84a	1145362534	No	Fiber	2000	2000
2ffaee76b6afbd5704447db130656f80	1037518429	No	Fiber	2000	2000
62151acf110daa3306add1d7f4e85cdf	1037516932	No	Fiber	2000	2000
83159ec494b94c52a6b30516db0befb1	1037516171	No	Fiber	2000	2000
0e00c7c9fd377fa3e5d80b63e33c572f	1037515982	No	Fiber	2000	2000
60738470f571c0b3999f70695a4a5501	1037518444	No	Fiber	2000	2000
cd8b521ae803942c855cdff093ef0487	1145362617	No	Fiber	2000	2000
5119f411647bbc18a6ba06ea1acadcd0	1385266640	No	Fiber	2000	2000
f7aa38d9070ce913be05839407358ae0	1037516512	No	Fiber	2000	2000
978222dbe666dcf1ffdbf8ee2fb8375f	1037518443	No	Fiber	2000	2000
4383d7ea513b43c61f52ff4fe9317e0d	1037515954	No	Fiber	2000	2000
27c8aef029da7d3e55a9414f6fc8229c	1145362540	No	Fiber	2000	2000
3126a60a155ff8e8d6d22dc222c7b79a	1037515135	No	Fiber	2000	2000
fdfc178013a6666311f9713e5d47bbec	1413434969	No	Fiber	2000	2000
e460e49d365a66cb7ec0ec315db9ee38	1037515861	No	Fiber	2000	2000
682caed717f121a35a8a1ee497cc1067	1037515182	No	Fiber	2000	2000
653173f0622aff3d98ff38ac5838aea5	1037516099	No	Fiber	2000	2000
938639a01dc696863b965bb406e2fb18	1037514706	No	Fiber	2000	2000
aed2d057efa43d20e77206963f009e28	1145362626	No	Fiber	2000	2000
94fdda1809b8bb65f7cf1ec08f94a513	1145355334	No	Fiber	2000	2000
a527f3bed241bed28fc50dfda6625969	1145362492	No	Fiber	2000	2000
40ee5008877d07693a6d08dbdeb5c835	1037516005	No	Fiber	2000	2000
845bd26732c10fd62dd157447757f01d	1037515988	No	Fiber	2000	2000
e934ff2bd16e648d54c13fd870d8b858	1037516010	No	Fiber	2000	2000
973e8400a73eeae9e27a2c4ac972dc29	1037516212	No	Fiber	2000	2000
6ad922d1adcb2fe0bb9397c6d31beadb	1037515970	No	Fiber	2000	2000
bb4c5f5ee0d6dab3eddcc461a10d4ca6	1037527517	No	Fiber	2000	2000
a65cae8e078080eb53b1c13f8e7b6d34	1145362585	No	Fiber	2000	2000
501dd7d463aead3e88f47bda2cbc7cf9	1385264558	No	Fiber	2000	2000
1a47938799d3c4e6c210653fd17c8aeb	1037516333	No	Fiber	2000	2000
f225df8320f38bb62aab1fac368b1786	1145362671	No	Fiber	2000	2000
f21712fe4168f427ff387fcc794a4cd5	1385443780	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
ac536accf4cc741c0775e62eabcc1a56	1145362528	No	Fiber	2000	2000
632ca4ca0d010b8e052f874b6844af26	1037515975	No	Fiber	2000	2000
00a20318087be9fe5eab521c654e1c28	1037515869	No	Fiber	2000	2000
ca7422df52795897b653979f781130a0	1037516013	No	Fiber	2000	2000
227f2d2cf4443cd868820980cc3804d1	1037513014	No	Fiber	2000	2000
225332501aac3eb607e8135c8f7452d7	1037518447	No	Fiber	2000	2000
836eea2adda27f0c6cf975a0a6b308cf	1037518434	No	Fiber	2000	2000
2eaefe0fea3ec0d7969da720a56cd197	1037516930	No	Fiber	2000	2000
68933b86dcab440bb400f545e20a40fb	1037515942	No	Fiber	2000	2000
8b0abec85cb30c0054df8add2067cd90	1037515943	No	Fiber	2000	2000
423f1753842cb4adbf9b745a11329593	1145362349	No	Fiber	2000	2000
28374fafdc87ef9fb4bca9081a129025	1145362729	No	Fiber	2000	2000
0db7dde4baf946e386c2319802d84135	1037516295	No	Fiber	2000	2000
55a37dbf189cf5254a6011fdf8a19d47	1145356062	No	Fiber	2000	2000
e63575a0a7a473daf522d119fe6702bc	1037527625	No	Fiber	2000	2000
52509d4cf9ff24a982d1ac3e2ca342ab	1037516115	No	Fiber	2000	2000
86f1721ec556caabe223cfbcb397b7e7	1037516509	No	Fiber	2000	2000
0b5e31e6d83d5f28fde16b28a1b57fb7	1037516203	No	Fiber	2000	2000
687779527c4b98b7c7bb67a1a5997e70	1037516316	No	Fiber	2000	2000
d3edb65ba713518ca546d181fcd20094	1037518464	No	Fiber	2000	2000
213d039313860aabfed61e3b1fd3c42e	1145362731	No	Fiber	2000	2000
d2ef8804caeb616bc14d1990bf9123ba	1037515089	No	Fiber	2000	2000
3c5acb23caedd642c3b39aa73c798c18	1037516330	No	Fiber	2000	2000
844e7cb0fb7aa62b6a359b79385a9632	1037516284	No	Fiber	2000	2000
0698505b33791a361a81652833b856b0	1145362433	No	Fiber	2000	2000
4481069a4c8bf523c5f7a9c9d49e299b	1037514702	No	Fiber	2000	2000
8ef2aabb2e176201cf75bc341059cea2	1037515866	No	Fiber	2000	2000
e6e71fa8380b89c6cd908e106948d840	1037518438	No	Fiber	2000	2000
61e6ea2a24783f7d6db2bfe4bc842dd6	1037516510	No	Fiber	2000	2000
3a828a763662c83186727fa1da2baae0	1145356292	No	Fiber	2000	2000
05baa45b40a45709f7eff8cdc9f44237	1037516933	No	Fiber	2000	2000
ae9d277990c771374810e5389416c1d8	1037515863	No	Fiber	2000	2000
9ab44c206e67bb27449560b5d049d993	1037518449	No	Fiber	2000	2000
359c1ddc1af577d7ec7ae1a9f0112d89	1145362706	No	Fiber	2000	2000
6bfca41877b1c57795ef7d587cb0f1b1	1145362703	No	Fiber	2000	2000
ab14f1cef9d24d807557bd05ee96cdb9	1145362616	No	Fiber	2000	2000
21a5fa502b5b9e952f6793c229630761	1145362633	No	Fiber	2000	2000
d41cd77348bd69e01ed49fb884d259ea	1037527594	No	Fiber	2000	2000
c6a0cb404e2fad9de92b69607f821bec	1037516092	No	Fiber	2000	2000
25f851973440e1ae70e261cb64cc38d6	1037514826	No	Fiber	2000	2000
a99cbbeb5c397e99e9f8137752cc893a	1037516260	No	Fiber	2000	2000
592dc3167b798a48267abf189f0ecfb2	1037516111	No	Fiber	2000	2000
b175b9ffcdc0f43b7515efe0a574c235	1145362506	No	Fiber	2000	2000
a8d0250fda674419dc7ed5657d8bb8b7	1037515101	No	Fiber	2000	2000
bb111ab2707c309e7cd9b18e32c3c885	1037516190	No	Fiber	2000	2000
1f10573dc3809202ba38be29fa37f623	1037527649	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
52a5513d9d49217d601aabd2ed00e74f	1037516123	No	Fiber	2000	2000
cb13e5648ae6aba6b0eb4b01086af77b	1037516152	No	Fiber	2000	2000
05a395bf65a41b165e9be6392ac96acd	1037518472	No	Fiber	2000	2000
e3ae040be92119f3e9b4b00e5c4622a7	1037516109	No	Fiber	2000	2000
761249272b390282b7784444f45bbe19	1037515909	No	Fiber	2000	2000
5c7d504b50ec758feb731da293a17bd6	1037516016	No	Fiber	2000	2000
34a3a948b33a970b28ebd3b22b022d69	1145362505	No	Fiber	2000	2000
2b9a5eb0b11a31b4fc28c69c801e9f82	1037518460	No	Fiber	2000	2000
cb34eb691634b1b9a74b619dbf02f1aa	1037516172	No	Fiber	2000	2000
30ebba48ddf4340c60dcb1b23b9e1f20	1037514598	No	Fiber	2000	2000
3e363cb657b286788908fab22b9df26d	1037516971	No	Fiber	2000	2000
9c90e0f864d0106ce017b8156c2f18e5	1145355122	No	Fiber	2000	2000
91d7eb4d4260a5b10cbbd8b4eb66c26e	1145362273	No	Fiber	2000	2000
7f0f6f2f2448bd6913c7d0b0994c04ac	1037518469	No	Fiber	2000	2000
1947f7cb2c20362e8adc45e0bef82fdb	1037515895	No	Fiber	2000	2000
07008dbb4710b6c6eee790ba4f6fbd06	1145362713	No	Fiber	2000	2000
99dafd91dd6d32846949a7e948fbbeb0	1037515094	No	Fiber	2000	2000
915873ed9eb39eb13c95e3991487a28d	1037516184	No	Fiber	2000	2000
19bbf58f1aab85926082fed07aefacca	1037516117	No	Fiber	2000	2000
8ba8ea7923141c34d49f4e02f7e00d1a	1145362763	No	Fiber	2000	2000
8b720050c74371e4a01ee6bd3127c9f3	1037515995	No	Fiber	2000	2000
7807d6322cdf0812a5c7bf74be315bab	1145362700	No	Fiber	2000	2000
9a0d45bd137aa2ac86866ad5325577c3	1145362385	No	Fiber	2000	2000
965f66d6d5a1c8bfbee4a6a8de371080	1037515883	No	Fiber	2000	2000
053d8c781749ad9a24ba5b4fe5a2b0e5	1145362726	No	Fiber	2000	2000
b7dda1c08b81c588501521849936c6b7	1037514932	No	Fiber	2000	2000
8f1ab084a9c03af0e142d61e8f423480	1145362687	No	Fiber	2000	2000
3c1b5a988383814a0c7b3e90b5929e65	1145362685	No	Fiber	2000	2000
2f8a4856424804b02ffe64af3f7f574d	1037515882	No	Fiber	2000	2000
cfacfbf368d4a130978b15ae1e828551	1037527938	No	Fiber	2000	2000
5c494fadc1c5ca4808024226943751d4	1037527928	No	Fiber	2000	2000
ef1ba729ae4a0aefb1cfce4af487a60c	1145356158	No	Fiber	2000	2000
abdf602f41c4e0778e1dd790a9e80049	1145355453	No	Fiber	2000	2000
bd41e1b80150bdcd20093a1f5c8f051d	1145355389	No	Fiber	2000	2000
785a8a54a8425f382735be11c751b599	1037515945	No	Fiber	2000	2000
87dbd7ff014cb93a0a9a20882b52c16a	1385266641	No	Fiber	2000	2000
16da540cbe46a8058f755f3ddf72d7b1	1145362676	No	Fiber	2000	2000
6e1d8872d0128ffc46c5283f1fe611b2	1037516008	No	Fiber	2000	2000
d9b2be48e8c23280ee12a68a5a5e9260	1037518459	No	Fiber	2000	2000
d79637e9f938b00f206fa05b5c27fd22	1145362727	No	Fiber	2000	2000
fe5bfb294c960452df5ca46e4bdb35b8	1037518807	No	Fiber	2000	2000
675da8e75ca25b3ec3c8bb5e36e6a419	1037516207	No	Fiber	2000	2000
e21e9044fc1d4dcdaaea2d6790caddb0	1145362395	No	Fiber	2000	2000
2fc1c9244769d4c4f41dc9fc48408e06	1037516204	No	Fiber	2000	2000
855f870f49525c3f05a38ca85d0308cb	1037516196	No	Fiber	2000	2000
bbdd3b2adf23bb46b6ba176c25ba54ce	1413418468	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
413b9f96f699d5490d35a5edf17fa045	1145362742	No	Fiber	2000	2000
68b2871c81d4ae1e185fdb4388c0edad	1037513015	No	Fiber	2000	2000
393eb429c93e1bfe3661d70a801812b3	1145362668	No	Fiber	2000	2000
343c57df2414cd2a0d733d446bd4dcfa	1037515932	No	Fiber	2000	2000
fc6b4ac0e8f3de31b8524865fb3fa34b	1037515973	No	Fiber	2000	2000
175986be0ac2af7d9b0a604d6ff1eff7	1037518480	No	Fiber	2000	2000
2d2594ea0c453bc99bca7c93e7574cf8	1145356163	No	Fiber	2000	2000
eea6d32f09b606cd0c9c8da54777b026	1037518867	No	Fiber	2000	2000
e7e51a92c5f38a5c90d1f344bea4d9fd	1037518804	No	Fiber	2000	2000
0c1356264e93759f095d518cea74588a	1037515967	No	Fiber	2000	2000
ed446e8a9f2b65de3efa849c9f712a1b	1037516521	No	Fiber	2000	2000
7a29c94660cde247d1cc8209f9ae96ce	1145355829	No	Fiber	2000	2000
f4b90594dfbb1c5fb36f78bcacea3ea1	1037516443	No	Fiber	2000	2000
b5ef5024ff79cd3ba68f5aee065c913c	1145362532	No	Fiber	2000	2000
688715ae26357751896158 34e42a6e1e	1037518792	No	Fiber	2000	2000
16a4ae2bce2a6fd3f2f35ea59528c29f	1145356154	No	Fiber	2000	2000
88f2837c2330580a24d91467412b071e	1145362606	No	Fiber	2000	2000
0bd9ee7878b1c9fc9e96e92c73254cc5	1037516254	No	Fiber	2000	2000
b734c4a601fa3b7a0f1ea4c00d7571d2	1145362509	No	Fiber	2000	2000
0189e8c509c97234c87c8800c7c8ee48	1037513077	No	Fiber	2000	2000
1edeca9bf93f8b0bba535c751019f773	1037516209	No	Fiber	2000	2000
aac8f1a1b2a2a2719954aa9ae39ea8df	1037515944	No	Fiber	2000	2000
13a408e3ea0ef58ca1fc0f54fda02175	1145362746	No	Fiber	2000	2000
7f10a7dc866097d69689da1ca4cbfc13	1037516328	No	Fiber	2000	2000
85246e298b12ef50a64ec6ffd47367fb	1145356168	No	Fiber	2000	2000
410674c7409b93265101a7502e9f6369	1037516093	No	Fiber	2000	2000
7bfe08a3773db3a2672433e3b00a8ed2	1145354551	No	Fiber	2000	2000
208639034c2901ab381ef9586c667b43	1145362747	No	Fiber	2000	2000
ab7c9cd6c1051b4ff5a714032d58970f	1145362708	No	Fiber	2000	2000
9f1e96094633afd28158dfa4b6517e17	1037514593	No	Fiber	2000	2000
7e6d7c3833b950e1c3ae933b576f2076	1037518818	No	Fiber	2000	2000
55c85b4fd04435d3fca1fb83a19c8e9a	1037515977	No	Fiber	2000	2000
19cd7cdab55d598e052926cb905d770a	1145362724	No	Fiber	2000	2000
6b0bc7f285787ccafe7aaf7aa3e23bb3	1037516102	No	Fiber	2000	2000
e646f6944c5496c37f3ed00fb4d2f3ec	1037515924	No	Fiber	2000	2000
d85b01567684c3b1cba13c739dfba48e	1037514817	No	Fiber	2000	2000
20a7aed45a59ffcc434ab99f42e84715	1037516128	No	Fiber	2000	2000
86412f7f534ca774e151f0e980485b96	1145362482	No	Fiber	2000	2000
605630097e8b682516cc22f8158ad46c	1037514577	No	Fiber	2000	2000
7281a1e72b7b81eea4be22a801133d2a	1037515116	No	Fiber	2000	2000
c02b3b747eae2dcff90f8561beea30c6	1037514637	No	Fiber	2000	2000
4a1632ba33ddf484eb08bda1865fa9c7	1037516189	No	Fiber	2000	2000
0168bf4ab7d7dc990157cb1bce679c9b	1037515125	No	Fiber	2000	2000
4df4532f5d50986a8e931f5dfccdd7ae	1037516153	No	Fiber	2000	2000
2f6002b20dfb5fb1f91995e7d97d3302	1037516938	No	Fiber	2000	2000
4c15d26b0e32063c205d43d68a2bb644	1037516161	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
6c7717ec631ac413a4de6f253e6a6e0b	1037516119	No	Fiber	2000	2000
628d053e124f68fb958144fb4376bc98	1037527772	No	Fiber	2000	2000
7e0219d9f16f5e65be5cecf2462ea94c	1145362371	No	Fiber	2000	2000
047316f2ee89f0f24f57fdeba1a2c63a	1037514856	No	Fiber	2000	2000
a5c7628e685137a83aa40ef58825521d	1037515976	No	Fiber	2000	2000
cd3f7552e12a0d17cb12e3f0c940f403	1037516309	No	Fiber	2000	2000
27f460e5727a5074760bea40d66c594b	1037516515	No	Fiber	2000	2000
7b098d37f3abee7680c09b5622163e65	1145362336	No	Fiber	2000	2000
648d6638bb88124f9bc72e1d4e89bcfe	1037516151	No	Fiber	2000	2000
6c967d7022404520ab380ad345e1f386	1145362436	No	Fiber	2000	2000
b850ba513e02c546cb4cb7ba6847661a	1037515127	No	Fiber	2000	2000
689e5150766ff925a58d30faab867c92	1037514672	No	Fiber	2000	2000
4410f66472ce511b622340485b3ee369	1037518454	No	Fiber	2000	2000
227862bd8db13bcf8a069ea12962519c	1037516313	No	Fiber	2000	2000
9592064f4f42c51173ce0c931093516c	1145362683	No	Fiber	2000	2000
be68c4b0d82a370efc329a4a554f66c3	1037516532	No	Fiber	2000	2000
26c8f47f60c44e9e2ca645d60d0cd7ab	1145362367	No	Fiber	2000	2000
02a6d9d780fd4b3e2e5122804e08bdea	1037518433	No	Fiber	2000	2000
9c8d71f01573cc7f4e32183d88725329	1145353628	No	Fiber	2000	2000
82c76763f36a1be923fafd8f39674048	1037516511	No	Fiber	2000	2000
ee67dd0783d158da761947c0a71e8a55	1145362584	No	Fiber	2000	2000
d72980bba0471a1c7d24ce005adbe181	1145355835	No	Fiber	2000	2000
145fa54b1a3c0be18526373038b8e588	1037515911	No	Fiber	2000	2000
2850ec28cdce71977a797a58fc13689f	1145362375	No	Fiber	2000	2000
dcc9261391a0e34c5e99116b06295818	1037516528	No	Fiber	2000	2000
086eb7a0bf78ccdab56142d62c27022f	1037516285	No	Fiber	2000	2000
46cbd62eb6107e82719079e3662b4696	1145362447	No	Fiber	2000	2000
8d61109deed94abf41fb5724d38ec006	1037527599	No	Fiber	2000	2000
539902aef45b973da5a7316994a7a354	1145362499	No	Fiber	2000	2000
b507ccb0d6f5fa66c8afefe1aa51ead4	1145355959	No	Fiber	2000	2000
cdc944cc90df829a2b20040ee441689d	1037515983	No	Fiber	2000	2000
8ff44580b6c20b67bf0352a5fcfd4ac6	1037516329	No	Fiber	2000	2000
3ecce43d71c7ecf15704061a3952e8e7	1037518458	No	Fiber	2000	2000
0bbe03b145b95b9d74a72b550e4683e7	1037515865	No	Fiber	2000	2000
abd16b7fa5e3f151a0cb137260e71571	1037527948	No	Fiber	2000	2000
c3cce9c904b7811b81983b4e6276194f	1037516121	No	Fiber	2000	2000
0e43ee3657fe7b16fa86c49a3ead41dd	1037516186	No	Fiber	2000	2000
e4f13b93d266ffa0add3eb852f997cf1	1145362698	No	Fiber	2000	2000
7e5144094bd2c65f16229da418551b6c	1145362771	No	Fiber	2000	2000
7353a6f9d90ac28a3028a3b11478a071	1145362485	No	Fiber	2000	2000
8f95da5bc1281827a045b883ddef927a	1145362599	No	Fiber	2000	2000
5d7b97cb8adc290f4c3a7beecde3eb3c	1037516168	No	Fiber	2000	2000
d86482db29c065c72c2bfcb97d62c072	1037514638	No	Fiber	2000	2000
0ce6c1ccaed8f0b4a89e9c042ba2ac88	1037515987	No	Fiber	2000	2000
aeaa66896a59c8e396b1851a3f5628a2	1145356052	No	Fiber	2000	2000
fe96509f3a8b0cdf036d2eb33d3201ff	1037516322	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
cf87f9af02c6e5a119597f2c4f5a0241	1037515979	No	Fiber	2000	2000
991fb91a1a348e56d36363f33c25e6b8	1037516267	No	Fiber	2000	2000
02b51b53dd2a31923bc80f6ac03bcf58	1145362525	No	Fiber	2000	2000
de210f304e23192212533ab9b6c59b98	1037515960	No	Fiber	2000	2000
d7fc6a6f899b3264c16cbd251503c537	1145362520	No	Fiber	2000	2000
bdd780122dc6644b06e9d38ded0fc5fb	1037518799	No	Fiber	2000	2000
8886e76a864cb7964c33efe7bcf2eb3c	1385267532	No	Fiber	2000	2000
bff3f20d649269548aaee6036f05e1d3	1037516934	No	Fiber	2000	2000
2bb376fe762acbefe905efb085f60882	1037516972	No	Fiber	2000	2000
677362fa473844373131371dbafa8e81	1037518450	No	Fiber	2000	2000
1a55323f1802239822712fadd9ed62aa	1037516311	No	Fiber	2000	2000
faa8868fb20c82ad097aa224142d1759	1145356463	No	Fiber	2000	2000
499140ae135a7bf1f324698603f4611d	1145362772	No	Fiber	2000	2000
aaeb536d0e0fafb517bee87ee6a0e1e7	1037518848	No	Fiber	2000	2000
f6ab79845cdbacae5e15215d206b2714	1145362692	No	Fiber	2000	2000
5c87cbfd224ab64c89653fc244543553	1037518817	No	Fiber	2000	2000
c03dc952d75895750bcbbf0399118e9b	1145356167	No	Fiber	2000	2000
8085041a43d9725e565d327346e7c45a	1037516198	No	Fiber	2000	2000
58007ee37dbb3e303d5a728784a6bf31	1037518476	No	Fiber	2000	2000
0d6fa06ed27f93ff3faa72d27301db74	1145362338	No	Fiber	2000	2000
f9437302ca43b33ceb7686605a951062	1037518808	No	Fiber	2000	2000
b243a0b24da20a0c9fc8e56d7b7c52b9	1145362518	No	Fiber	2000	2000
4271b7058a9f8abf2cfb22edaba95bec	1037516235	No	Fiber	2000	2000
76fe78cf0ace51e7bf86158690ffccfb	1037516122	No	Fiber	2000	2000
223594b359377cb64cf783041331cdd3	1145362632	No	Fiber	2000	2000
37538335ebd7cca19ab6a7f947e5bcf0	1145355299	No	Fiber	2000	2000
ecc97dfea65ced709b9b4141258295c0	1037516320	No	Fiber	2000	2000
bf5fd9711ec497925c60935a40de6e1a	1037518492	No	Fiber	2000	2000
bda87a8b8c05da40184308dca86763a1	1037516017	No	Fiber	2000	2000
e27fac72f0d52093cd0256f20d4c7a5d	1145355822	No	Fiber	2000	2000
cfa660b4813a4385f323c69102f3f057	1037518439	No	Fiber	2000	2000
38efb4ac8132a5a38c551fda02427b42	1145362522	No	Fiber	2000	2000
ba41115235d74c35051bdf4a027c4e77	1145362669	No	Fiber	2000	2000
f55eb96259d5f71988de3a881336dbbf	1037516939	No	Fiber	2000	2000
6cedff59298b00e28c1e05d5450bd918	1145356141	No	Fiber	2000	2000
fa0047a76fec0d3739e801240f68c7a9	1037515991	No	Fiber	2000	2000
3c5537e26f64d63df51c6e53a56dac13	1037518430	No	Fiber	2000	2000
35b90c57aa8a1345febfcc39ded47ce3	1145356164	No	Fiber	2000	2000
02677d6bc75c31a1c8aa5b218cdfcd2f	1145362620	No	Fiber	2000	2000
de9b88aaf1fe80df28c6039322007762	1037516529	No	Fiber	2000	2000
8b8c6402d4f57e3e35c0eebd42eb1184	1145362774	No	Fiber	2000	2000
758cb27494876c2597858cfea44448e4	1145362697	No	Fiber	2000	2000
ab345b021bc2c4b746ba720dc66fe091	1145362513	No	Fiber	2000	2000
80d82ba09fe17699016dac067933b69e	1037516104	No	Fiber	2000	2000
00a9de70868f407c84b047a722cb5a29	1037516147	No	Fiber	2000	2000
f6cd5026ed96c6639e8c0c07ea30dd77	1145362531	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
262cb916a2002eec29cf08290f4f5a99	1037516969	No	Fiber	2000	2000
acae68f835700a1776c28677c76a6b2a	1145362733	No	Fiber	2000	2000
d93f8cbe7968ae419e97b86cd680945d	1037513124	No	Fiber	2000	2000
95654d5632735db141a58e70cc8834d6	1037518435	No	Fiber	2000	2000
2d58a33736b5a39bcbd1643f905e3d57	1145355074	No	Fiber	2000	2000
b52dfca5916e2b0391c42e5742267ec9	1037518478	No	Fiber	2000	2000
088808bab96b8b12768bfb21a0f60e49	1145362715	No	Fiber	2000	2000
3fd1bdd806c1378774f5ce59ebe10435	1037515867	No	Fiber	2000	2000
dbb1379b49b069c30cbda177ad09877c	1037516237	No	Fiber	2000	2000
cb28ed6c911f3707b0dbe84a5f3332ed	1037515919	No	Fiber	2000	2000
ab042d477c0dc39811f43567380f3a18	1145356071	No	Fiber	2000	2000
79cb9189ef0d92cd8ea0d8ca184ea37f	1037516926	No	Fiber	2000	2000
eec0229d3cb29753825ccffd3664ed0c	1037516236	No	Fiber	2000	2000
cf190df8fba13ebd9b6bc3bc0f329185	1145362610	No	Fiber	2000	2000
de1f406f0b4b5b800c67c872cd6b0d30	1037516116	No	Fiber	2000	2000
e24a1fcccd176f5195ea13cc114ecef6	1145362670	No	Fiber	2000	2000
307fa6bbd283c287ed4204ba3851cb70	1037515112	No	Fiber	2000	2000
c084929842463e2082c1adfa58ec4bd4	1037518819	No	Fiber	2000	2000
1ad1cd0c2c168bc064cbfc3a1ecf9b7a	1037516331	No	Fiber	2000	2000
e622bd9f68a6f53f267c7cdee1fddcda	1145355333	No	Fiber	2000	2000
4959e0de87698f3df70e6a2539042cc4	1037518468	No	Fiber	2000	2000
9d34c2cee6af40bd2242c5269ccff9a0	1037516096	No	Fiber	2000	2000
dbbddd0449533f46a4b04bac85445b7a	1145362594	No	Fiber	2000	2000
7d5bfc153bf74a165d13f3919d8a856a	1145362712	No	Fiber	2000	2000
b2a284c72494d784aa7efd55e622befc	1037516208	No	Fiber	2000	2000
58f8468f9e01656cc772e5c4e9c8d012	1037515864	No	Fiber	2000	2000
938fdf3e1221f0d9b6f37247c3078471	1145356153	No	Fiber	2000	2000
855453f7da18983df28abc85dbba3507	1037516156	No	Fiber	2000	2000
2b6fe4b78d8ae085ec6cf03721d329fc	1037516138	No	Fiber	2000	2000
f20656e9cdeae797b74582181c34ad74	1145356055	No	Fiber	2000	2000
4b702639b92459ada84aac3c93bbc3c5	1145362627	No	Fiber	2000	2000
04d950ca98bfc572289b505925bcdcdc	1145355352	No	Fiber	2000	2000
654219e75c3bda53e2faedde43791671	1037514596	No	Fiber	2000	2000
ee137fbc3fd916abd1aa6cabab7fac7d	1037515877	No	Fiber	2000	2000
102362cd24626fdb7a315e7193c55691	1037516149	No	Fiber	2000	2000
5a28e9d5c6c6185a7edf861446b13e0f	1413434968	No	Fiber	2000	2000
33445717f24dce6bb5bc46617e859286	1037516014	No	Fiber	2000	2000
cd7bf624f8b837c303d80d570f082288	1145356080	No	Fiber	2000	2000
eecb545ac6525ea5dde9364cbccb641a	1145362502	No	Fiber	2000	2000
cf7bbe48e76cba08092d8b652bdd8de9	1037518814	No	Fiber	2000	2000
53a26986bce3263f89e20f1f56a98db7	1037518448	No	Fiber	2000	2000
ae508010617a18340201900c0e7d0146	1145362778	No	Fiber	2000	2000
52b23e426555df454ad68b4f00aef385	1037516197	No	Fiber	2000	2000
2677c70f6fa44382382e2171b6f59ec5	1037515993	No	Fiber	2000	2000
f57307d568d98c2945431b7fe4f67927	1037516000	No	Fiber	2000	2000
cb860aac44b862f0782142040a483921	1037515971	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
c6d5999d3af8b16e3338f20965237ed0	1145362773	No	Fiber	2000	2000
4054a918aa802dfa9c5ae3ffe637ec94	1145362503	No	Fiber	2000	2000
6e2e5b847025aeb4606a069f4301957a	1037516089	No	Fiber	2000	2000
7716a38aedded2c9ffa50154ec53f5e0	1037516157	No	Fiber	2000	2000
2cce3919a4fdd699f84919ad8c6d9870	1037516179	No	Fiber	2000	2000
2d6b6ee9d3c356a2d34b61a9fd8a4d38	1037518477	No	Fiber	2000	2000
4370eae6e213f317c14e7f8f2c1aae7e	1037516106	No	Fiber	2000	2000
a7078b34f1af68ed67eb8631bb7e8c25	1145362368	No	Fiber	2000	2000
f1b5f5244aba9ae14c1ea27904867f6c	1145362619	No	Fiber	2000	2000
20e583b18ed4b5c947ef228da32b4122	1037515916	No	Fiber	2000	2000
f91d35c5077ef3586e298b0daf2d8526	1037514810	No	Fiber	2000	2000
57512e3b25349e712251c7df9551e0f1	1037516527	No	Fiber	2000	2000
12ba022b6bc2740ab94464046626eba1	1145354569	No	Fiber	2000	2000
479235a5a364702d49a05e3414f5da20	1037516514	No	Fiber	2000	2000
0e359e7f8f5a274cc909bc3edf2fe61b	1145362635	No	Fiber	2000	2000
fd72377f2583b183040e92df2fa48520	1037516205	No	Fiber	2000	2000
9523fecb0c1bd3086df2efe849d7951d	1037515165	No	Fiber	2000	2000
257f49f46c5e211873ea97a5f58d67bf	1145356053	No	Fiber	2000	2000
4bcf1a0aa37073187b150dbaa372e3e8	1037516234	No	Fiber	2000	2000
4bd3b6b504c1a997b6389eb97321f2df	1037514811	No	Fiber	2000	2000
3bc722b6410e4015a7c9d54444aa5902	1037518847	No	Fiber	2000	2000
5296e1b34744cc9584101f10e083b275	1145362596	No	Fiber	2000	2000
c6b93fd8573de86ff5bfe8a0673083ea	1145356155	No	Fiber	2000	2000
a092d18a7bab272365ba597e49c1e8ae	1037515852	No	Fiber	2000	2000
113088d42811c753435dfc8160caab2a	1145362695	No	Fiber	2000	2000
d5c168d9566b3e614366f8570b47fa58	1145362508	No	Fiber	2000	2000
1bf3ab3ff17a54b7a16ea821caa38ca4	1145362529	No	Fiber	2000	2000
11d36b35375f39d301e7ea71384e05c2	1037516169	No	Fiber	2000	2000
51a3983c3beafe118bc5e506384c7294	1145362618	No	Fiber	2000	2000
795a9f6c180f032594089032811b4fa2	1037515992	No	Fiber	2000	2000
6b6d7ba96d79894bd7d297b5a0c003cb	1037518479	No	Fiber	2000	2000
f2946b1fdad6e8608fa75cf7c80cc515	1037518452	No	Fiber	2000	2000
bb3165b728a812eb8b01b6eb0cac5792	1037514581	No	Fiber	2000	2000
291ef7464043e7a63308dfd5783daafb	1037527771	No	Fiber	2000	2000
95253e54693d4cf1ac58a7a6f278bc87	1145355828	No	Fiber	2000	2000
813d46a6d54a73c0235cf5f5b9779082	1145356033	No	Fiber	2000	2000
0a6d5f1b19c37224060fb9e3c6791176	1037515640	No	Fiber	2000	2000
2a250198459f3a06e9af0b697e8991c1	1037518431	No	Fiber	2000	2000
a5cb97df30d538b20b575c8bd48f690a	1145356175	No	Fiber	2000	2000
c05b8ed342b097cc18c1cfcf9c4907ed	1037516923	No	Fiber	2000	2000
3144f773a3e95812ed06bb091f8eb7bb	1037516146	No	Fiber	2000	2000
0b002765f151fa3c1c79d6184d869b7e	1037516183	No	Fiber	2000	2000
a446cce6b324a4a4bed5f4ef861f5a3b	1145362507	No	Fiber	2000	2000
dd0d17b885766de6ff3a24bd154241cb	1037516113	No	Fiber	2000	2000
92acf3ba8382b5e1505ccfb94760d31c	1037515999	No	Fiber	2000	2000
2df27a42bd18613f9225047eca4bb161	1413434967	No	Fiber	2000	2000

ID	Location ID	Is CAI	Technology	Upload	Download
6cf31513e41e125001bf2c4d89f6f77c	1145362401	No	Fiber	2000	2000
bba204e0448a52b57df369da230e24c0	1413434886	No	Fiber	2000	2000
f1cba8df27228f0ff6cea2d3a591c920	1037516191	No	Fiber	2000	2000
07d04eb7eea1a255e4ad1aa8e2f09b73	1145356035	No	Fiber	2000	2000
db44138d32e3b9a20660ae1d7d841386	1037515114	No	Fiber	2000	2000
839b8f4c4e45fe8a23ff8932992f53e0	1385443999	No	Fiber	2000	2000
b35465bffaa9de4c9a3a2e179c687c00	1145355294	No	Fiber	2000	2000
27d98b04a1c909ecfd43fe531550f2a2	1145362490	No	Fiber	2000	2000
504c7c0e65d26fa335cc3acbd0c6d842	1037516298	No	Fiber	2000	2000
006bebd50d26c1c0081166845aecbab4	1037516206	No	Fiber	2000	2000
88d4b8f960c3aac798c500d48660ce2e	1037515896	No	Fiber	2000	2000
e895310cb3872ca7f51be66979f64dca	1145362704	No	Fiber	2000	2000
102ee23fd3d0b13450604b05cd0246e3	1037515856	No	Fiber	2000	2000
23f98049d665e8c9a6c54c176ef69546	1037515980	No	Fiber	2000	2000
ac59d91193cb418a401b0bedfaf75312	1145356159	No	Fiber	2000	2000
b95050fd1f2fe9bb17caee6e4c74417c	1145356156	No	Fiber	2000	2000
23db95318934797bad95ebfa97f4b9c0	1145362530	No	Fiber	2000	2000
7801b1bb12849f532b73238f630ee5d5	1037516150	No	Fiber	2000	2000
5f9a47fad41055f6433adc50a192695e	1037516990	No	Fiber	2000	2000
d28e7ed2a836589a5a3b527d16e4c3db	1037516936	No	Fiber	2000	2000
150a39befda5fa837d805a261f31780c	1145355850	No	Fiber	2000	2000
6c19c6d7ca9d974ac5dabce2acd83eb8	1037518802	No	Fiber	2000	2000
ada0eb2e574b95eb2b030ce2f3bc5b7a	1145362689	No	Fiber	2000	2000
f7874352693f19b9d289a54c1e4edb54	1037516120	No	Fiber	2000	2000
fcf5ad3743e633314e6c92790df3f65a	1037516296	No	Fiber	2000	2000
434c189d2acb15fd1724a2742c19f663	1037518860	No	Fiber	2000	2000
50392bd3d5200810eef170effc9ed17b	1037516090	No	Fiber	2000	2000
0b6b7d9c68ad83b48789405907fc34ac	1037516002	No	Fiber	2000	2000
8490afe7e69e8ba26d9a3957280fe795	1037516224	No	Fiber	2000	2000
a8238ecf27e8bf59782ac04e9e341764	1037518798	No	Fiber	2000	2000
b1193b6e05f2db231a52769f92759a4e	1037516094	No	Fiber	2000	2000
9dc56ec9db203b82b1349a6639562963	1145356160	No	Fiber	2000	2000
34fc5c814ed9683faad28e4a502fcb22	1037518470	No	Fiber	2000	2000
aaf69eb4c145b533645c6cac80c950d4	1037518493	No	Fiber	2000	2000
15336772bd4046bd9cd8aec24b7a92a5	1145362500	No	Fiber	2000	2000
a0a88878a2ebafea26a9480abd85b183	1037516989	No	Fiber	2000	2000
1e22bd8f4ee1d30ba5e012b91c70173b	1037516297	No	Fiber	2000	2000
87e830060fc04b23e2a75525a9c5dba9	1145362526	No	Fiber	2000	2000
00334ddd9e4b4495deef3ce94dfc6a05	1145362674	No	Fiber	2000	2000
45150e1462d56eb04f04e8c86703ccd0	1037516110	No	Fiber	2000	2000
ca2744db295294dac2f4db0a82af5adc	1145362448	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 39 – Budget for Project Area IBO-893

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$637,000.00	$360,122.00	$276,878.00
Permitting Costs	Permitting Costs	Professional Services	$153,230.00	$86,627.00	$66,603.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$164,576.00	$0.00	$164,576.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$36,750.00	$20,776.00	$15,974.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$559,062.00	$316,060.00	$243,002.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$165,965.00	$93,827.00	$72,138.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$9,731.00	$5,501.00	$4,230.00
Corning Fiber Terminals-Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$19,602.00	$11,081.00	$8,521.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$188,749.00	$106,697.00	$82,052.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$68,498.00	$38,721.00	$29,777.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$2,088.00	$1,180.00	$908.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$180,899.00	$102,270.00	$78,629.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$161,633.00	$91,378.00	$70,255.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$9,765.00	$5,520.00	$4,245.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$17,104.00	$9,669.00	$7,435.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$8,575.00	$4,848.00	$3,727.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$31,423.00	$17,765.00	$13,658.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$349,796.00	$0.00	$349,796.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$24,826.00	$14,035.00	$10,791.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$78,000.00	$44,092.00	$33,908.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 39 – Disbursement Schedule for Project Area IBO-893

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 39 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-893

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 39 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 40 –Subaward Conditions and Statement of Work for Project Area IBO-1085

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 40 - Specific Award Conditions for Project Area IBO-1085.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$103,764.00]
Total Project Cost = (subaward funds + match)	$103,764.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-1085 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 40**. The Project Area is depicted in the map in **Appendix A of this Exhibit 40**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 40**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $103,764.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $103,764.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 40** in the area depicted in **Appendix A of this Exhibit 40**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 40**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 40 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 40;
- Appendix A to this Exhibit 40 – Map of Project Area IBO-1085;
- Appendix C to this Exhibit 40 – Budget for Project Area IBO-1085;
- Appendix E to this Exhibit 40 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1085;
- Appendix F to this Exhibit 40 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 40 – Project Area
- Paragraph 5.B(2) of Exhibit 40 – Project Locations
- Paragraph 5.B(3) of Exhibit 40 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 40 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 40 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 40 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 40 – Access to Service
- Paragraph 5.B(5)e of Exhibit 40 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 40 – Wholesale Rate

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 40 – Map of Project Area IBO-1085

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C


brightspeed

IBO-1085

addr_point
central_office
dtap
oh_route
splice_closure
terminal
ug_route

N

0 0.150.31 0.62 Miles

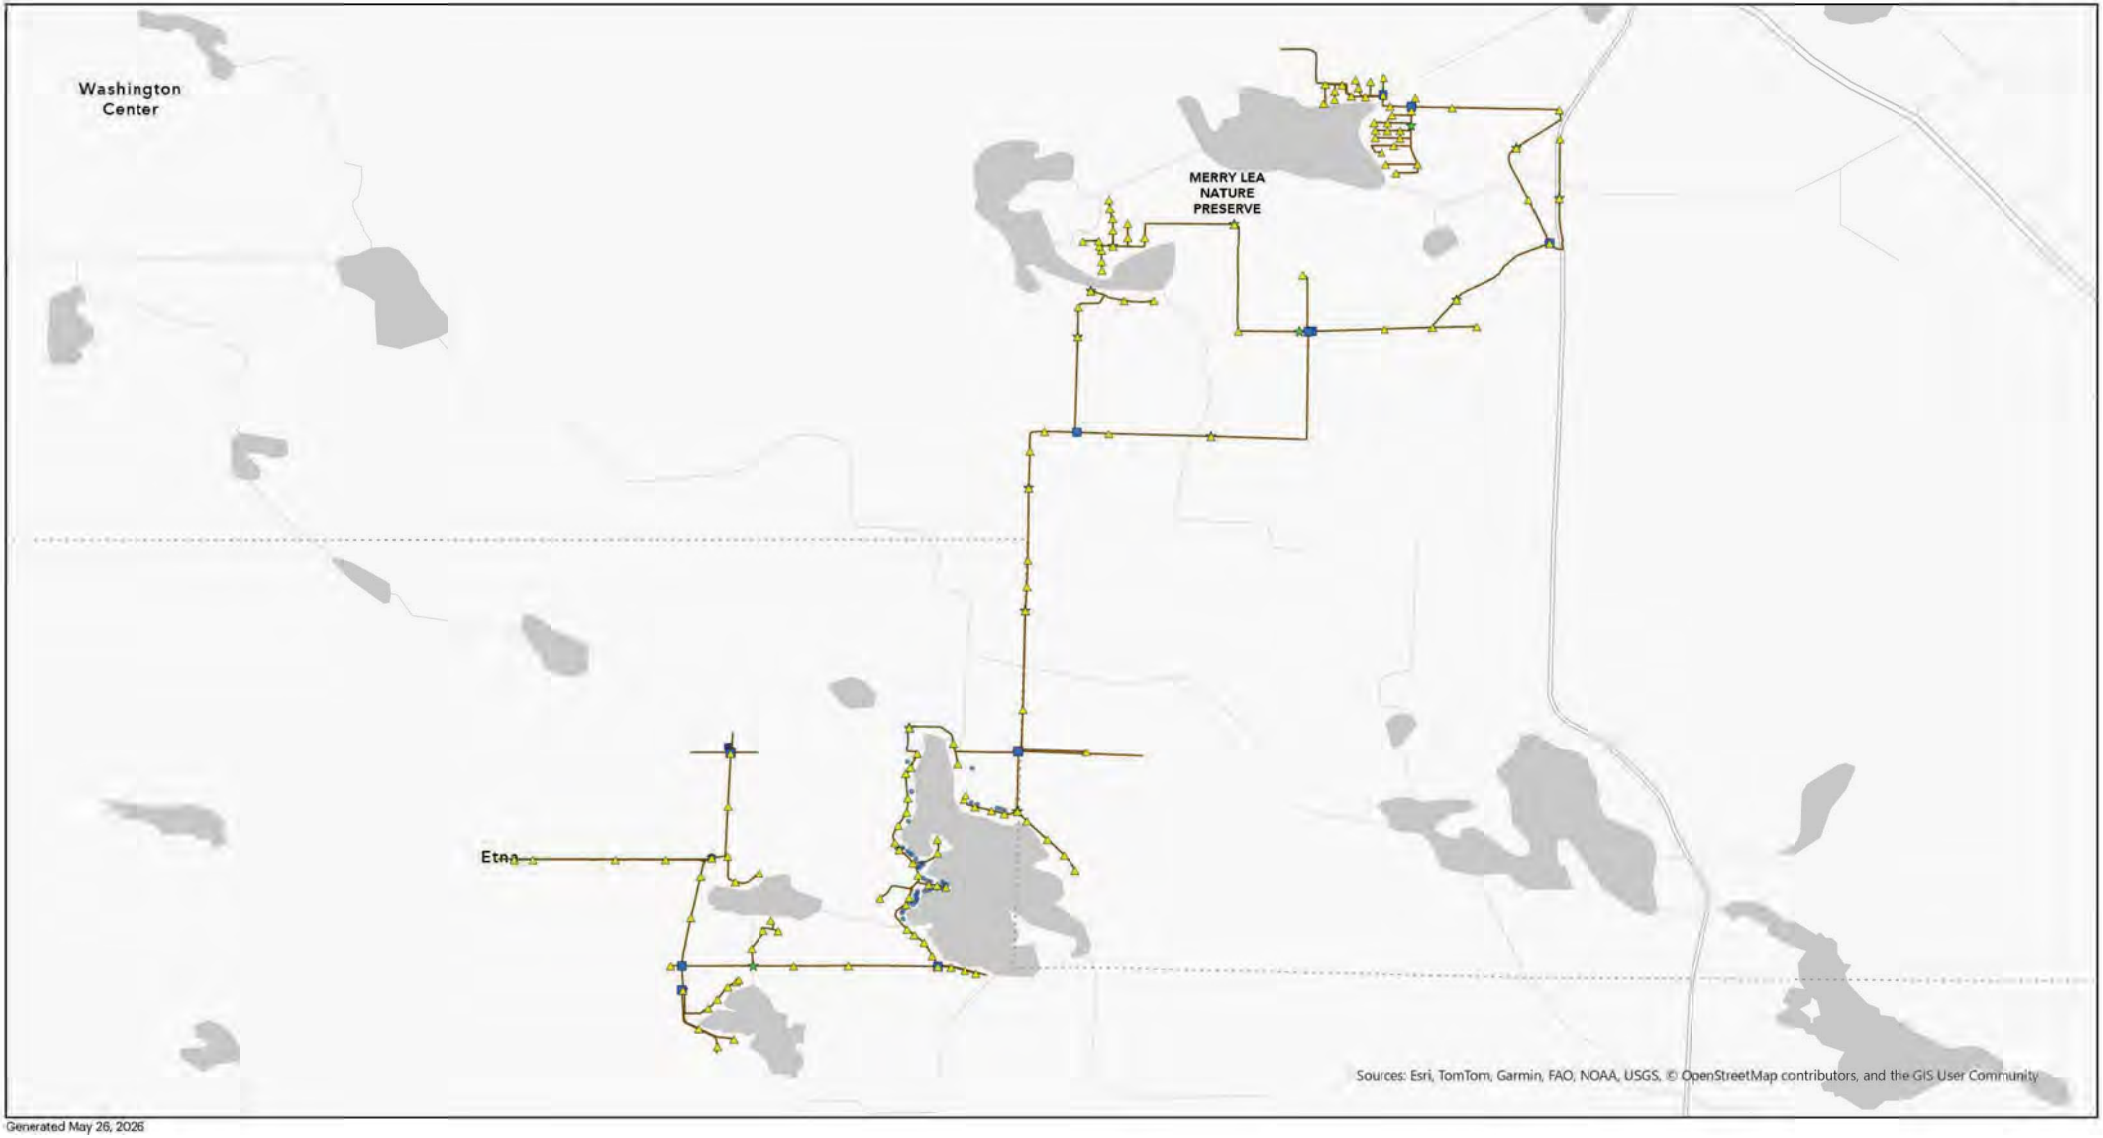

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 40 – List of Locations in Project Area IBO-1085

Brightspeed IBO-1085 Location List

43 locations

ID	Location ID	Is CAI	Technology	Upload	Download
8b53ed62500fa0e7daa8275c5f0391fd	1037513579	No	Fiber	2000	2000
5ac0db1ffd74b633cd347df29ea249e6	1037513563	No	Fiber	2000	2000
8db061e77d374f469c2b1036abdae749	1037513583	No	Fiber	2000	2000
e8101bd8e99184bb90c9fe1f848f9ff2	1037513567	No	Fiber	2000	2000
b141e7a457d659183c4be716540fc06b	1037513525	No	Fiber	2000	2000
486d166a2761f9f48b7acb396f252dc7	1037533657	No	Fiber	2000	2000
57359f94373795824b06737586228a75	1037513552	No	Fiber	2000	2000
bf11303471c72726e5a123c67a4ca4e0	1037513557	No	Fiber	2000	2000
8333166822b1211b6a4bae6c9ffa62f7	1037513526	No	Fiber	2000	2000
b3e883e87e80f780de0715ba074c4545	1037513581	No	Fiber	2000	2000
a93876c081cedb330bb8b47f962e956f	1037533575	No	Fiber	2000	2000
be1e3e69ac0256f70855d5cf85448d1c	1037513602	No	Fiber	2000	2000
a7d1691d2ad024e28e7ae3846372cb4b	1037513586	No	Fiber	2000	2000
554b0fbe0744924d1df917db22caf7f8	1037513569	No	Fiber	2000	2000
476c28854d40ba4213336b53f87dc4aa	1037513551	No	Fiber	2000	2000
fa5d77b42ab13b66c1101fb6ad521cbd	1037513584	No	Fiber	2000	2000
bed46d2c9eda0d75cb1bb6f665daef13	1037513499	No	Fiber	2000	2000
00f55127e8b3914a3c98307d6c05f204	1037513565	No	Fiber	2000	2000
7216a24fb8b7f9aded4a1a5849f85d1c	1037513577	No	Fiber	2000	2000
98c1bd49696e70eef89115eee8871d53	1037513406	No	Fiber	2000	2000
8f7c1582e85ac017857f82081ee4fa3a	1037513573	No	Fiber	2000	2000
c93865422286f458bde59133b8d55328	1037513555	No	Fiber	2000	2000
6cbf02843aa13eb105c73cac790ed649	1037513580	No	Fiber	2000	2000
363042d82e3ba485c6dd13d45cb13563	1037513475	No	Fiber	2000	2000
e3627ba0b856f5379508904f99e6c452	1037513561	No	Fiber	2000	2000
0246234870bcc96879754983d0ab4425	1037513566	No	Fiber	2000	2000
cb507187775e1d2c25b3180b5dde081c	1037513585	No	Fiber	2000	2000
5364d2fc968cd50370623fed5c767563	1037513520	No	Fiber	2000	2000
8b5304238be1908ad6b9e9ee05feefa7	1037513544	No	Fiber	2000	2000
033512ade470a98ecc6f6f21198b95d7	1037513521	No	Fiber	2000	2000
f8785d617ba5541cc096befd2204c6d9	1037513572	No	Fiber	2000	2000
332eb78fca96ce82699e23afeb120c00	1037513589	No	Fiber	2000	2000
b22e3ea035c9a040b54926f2713f1370	1037513522	No	Fiber	2000	2000
fce5099b6afd64c3b2c0d13ea474c882	1037513488	No	Fiber	2000	2000
471af83e5ac918853d3fa8ccbb45a0be	1037513560	No	Fiber	2000	2000
713a2c976b2aac17a03193b9f4b71967	1037513562	No	Fiber	2000	2000
fe7c1164c56c731a4508faee02b9c42d	1037513564	No	Fiber	2000	2000
46448cf0a297717746683b75f3776185	1037513559	No	Fiber	2000	2000
7cebd29d5cdfcea313013757cadf3f6d	1037513568	No	Fiber	2000	2000
5717164984632950af5f27ac252d812b	1037513553	No	Fiber	2000	2000
44580200ebf3fc61861ff3c08ad79de8	1037513500	No	Fiber	2000	2000
ae356bba1ee494da8227cf60fab5a9ce	1037513558	No	Fiber	2000	2000
0e163dd30cb002ac3b09ecba22da8179	1037513587	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 40 – Budget for Project Area IBO-1085

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$750.00	$0.00	$750.00
Permitting Costs	Permitting Costs	Professional Services	$4,171.00	$0.00	$4,171.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$1,238.00	$0.00	$1,238.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$60.00	$0.00	$60.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$4,925.00	$0.00	$4,925.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$938.00	$0.00	$938.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$27,004.00	$0.00	$27,004.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$791.00	$0.00	$791.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$1,500.00	$0.00	$1,500.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$263.00	$0.00	$263.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$594.00	$0.00	$594.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$5,138.00	$0.00	$5,138.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$1,866.00	$0.00	$1,866.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$17,340.00	$0.00	$17,340.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$15,228.00	$0.00	$15,228.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$4,560.00	$0.00	$4,560.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$4,400.00	$0.00	$4,400.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$270.00	$0.00	$270.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$12,728.00	$0.00	$12,728.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 40 – Disbursement Schedule for Project Area IBO-1085

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 40 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1085

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 40 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 41 –Subaward Conditions and Statement of Work for Project Area IBO-935

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 41 - Specific Award Conditions for Project Area IBO-935.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$68,237.00]
Total Project Cost = (subaward funds + match)	$68,237.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-935 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 41**. The Project Area is depicted in the map in **Appendix A of this Exhibit 41**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 41**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $68,237.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $68,237.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 41** in the area depicted in **Appendix A of this Exhibit 41**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 41**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 41 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 41;
- Appendix A to this Exhibit 41 – Map of Project Area IBO-935;
- Appendix C to this Exhibit 41 – Budget for Project Area IBO-935;
- Appendix E to this Exhibit 41 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-935;
- Appendix F to this Exhibit 41 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 41 – Project Area
- Paragraph 5.B(2) of Exhibit 41 – Project Locations
- Paragraph 5.B(3) of Exhibit 41 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 41 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 41 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 41 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 41 – Access to Service
- Paragraph 5.B(5)e of Exhibit 41 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 41 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 41 – Map of Project Area IBO-935

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-935

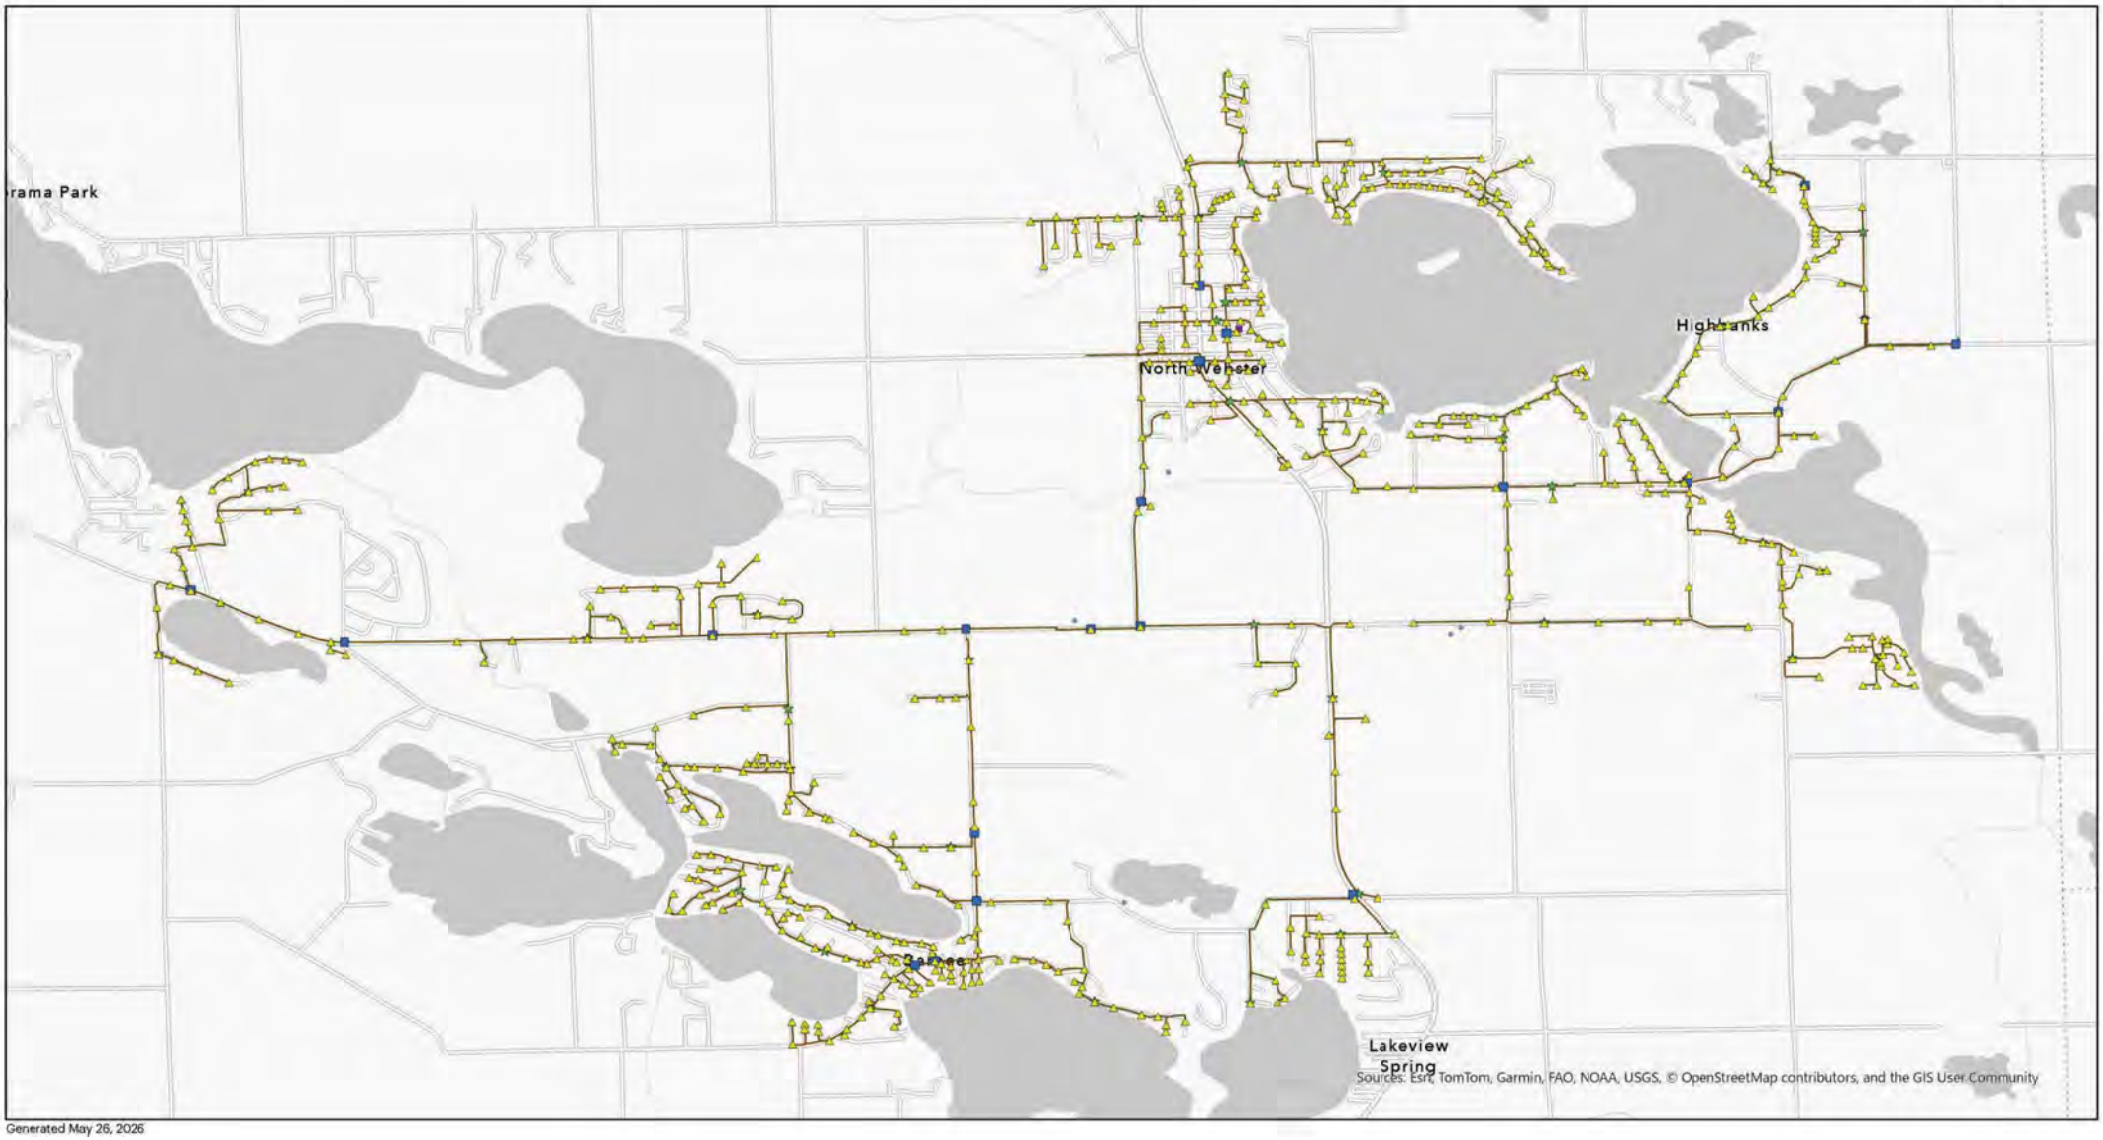

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 41 – List of Locations in Project Area IBO-935

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-935 Location List

5 locations

ID	Location ID	Is CAI	Technology	Upload	Download
1beacd5b69981db9d4565895afff7867	1292802131	No	Fiber	2000	2000
628b01230f453df058aa16140af1b6ba	1292811649	No	Fiber	2000	2000
d19c081a0aaca8f3e4f45226dc0c8f36	1292812043	No	Fiber	2000	2000
4db9a27e3fa0c0820d7fe189ba858f6a	1292802220	No	Fiber	2000	2000
f7593cd5dccbb60f7bf0e10e84049998	1292802224	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 41 – Budget for Project Area IBO-935

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$263.00	$0.00	$263.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$594.00	$0.00	$594.00
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$5,104.00	$0.00	$5,104.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$1,852.00	$0.00	$1,852.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$1,480.00	$0.00	$1,480.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$1,230.00	$0.00	$1,230.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$938.00	$0.00	$938.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$3,140.00	$0.00	$3,140.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$750.00	$0.00	$750.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$60.00	$0.00	$60.00
Permitting Costs	Permitting Costs	Professional Services	$4,143.00	$0.00	$4,143.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$4,891.00	$0.00	$4,891.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$4,370.00	$0.00	$4,370.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$843.00	$0.00	$843.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$1,500.00	$0.00	$1,500.00
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$270.00	$0.00	$270.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$17,224.00	$0.00	$17,224.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$15,120.00	$0.00	$15,120.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$4,465.00	$0.00	$4,465.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 41 – Disbursement Schedule for Project Area IBO-935

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 41 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-935

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 41 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 42 –Subaward Conditions and Statement of Work for Project Area IBO-1030

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$21,249.00]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$21,249.00]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$21,249.00]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 42 - Specific Award Conditions for Project Area IBO-1030.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[58.88%]; [$30,426.00]
Total Project Cost = (subaward funds + match)	$51,675.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$21,249.00** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-1030 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 42**. The Project Area is depicted in the map in **Appendix A of this Exhibit 42**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 42**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $30,426.00, which is 58.88% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 58.88% for a total match of $30,426.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 42** in the area depicted in **Appendix A of this Exhibit 42**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 42**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 42 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 42;
- Appendix A to this Exhibit 42 – Map of Project Area IBO-1030;
- Appendix C to this Exhibit 42 – Budget for Project Area IBO-1030;
- Appendix E to this Exhibit 42 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1030;
- Appendix F to this Exhibit 42 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

The Subgrantee shall provide quarterly updates to the IBO on the status of its milestone progress under this Paragraph 13.C.

D. Unanticipated Discoveries.
Burial sites, human remains, and funerary objects are subject to the requirements of all applicable Federal, Tribal, state, and local laws and protocols, such as the Native American Graves Protection and Repatriation Act (NAGPRA), in addition to Section 106 of the NHPA. Subgrantee must notify the IBO and NTIA of inadvertent discoveries and potential impacts to these resources and identify and follow all applicable laws or protocols. Subgrantee should have an archaeologist who meets the Secretary of the Interior's Professional Qualification Standards monitor ground disturbance for grant funded activities proposed in the vicinity of National Register eligible archaeological sites and suspected or known burials. If any potential archeological resources or buried human remains are discovered during construction, the Subgrantee must immediately stop work in that area, secure that area, and keep information about the discovery confidential, except to notify the IBO and NTIA and the interested SHPO, THPO, and potentially affected Tribes. Such construction activities may then only continue with the written approval of NTIA.

14. Deployment Scope Changes and Budget Modification.

Post-award changes shall be handled as set forth in Section 23 of the Grant Agreement and in accordance with then-current BEAD Program rules or guidance.

15. Access to Subgrantee's Records.

The Subgrantee acknowledges and agrees that the IBO has the right to collect any Project-related information from the Subgrantee or its subcontractors related to budgets, expenses, receipts, financial reports, and deployment milestones as set forth in more detail in the Grant Agreement.

16. Updated NTIA Guidance and Requirements.

The Subgrantee acknowledges and agrees that the IBO retains the right to update provisions of the Grant Agreement to align with updated NTIA guidance and requirements via a written amendment signed by the Subgrantee and the IBO.

17. Survival.

A. Any provision of this Grant Agreement that would reasonably be expected to be complied with or performed after the expiration or termination of this Grant Agreement shall survive the expiration or termination of this Grant Agreement and continue until the end of the Federal Interest Period.

B. The Subgrantee acknowledges and agrees that some terms shall remain an ongoing obligation of the Subgrantee through the Federal Interest Period. These ongoing terms include, but are not limited to, the following provisions:
   - Paragraph 17 of Attachment A – Affordability and Low-Cost Plans
   - Paragraph 32 of Attachment A – Encumbrances
   - Paragraph 33 of Attachment A – Recordation of the Federal Interest in BEAD – funded Property

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Paragraph 43.C of Attachment A – Exceptions and Clarifications to 2 CFR 200.313 - Equipment
- Paragraph 5.B(1) of Exhibit 42 – Project Area
- Paragraph 5.B(2) of Exhibit 42 – Project Locations
- Paragraph 5.B(3) of Exhibit 42 – Network Capabilities
- Paragraph 5.B(4)b of Exhibit 42 – Conduit Access Points
- Paragraph 5.B(4)c of Exhibit 42 – Covered Purchases
- Paragraph 5.B(5)a of Exhibit 42 – Low-Cost Plans
- Paragraph 5.B(5)b of Exhibit 42 – Access to Service
- Paragraph 5.B(5)e of Exhibit 42 – Cybersecurity and SCRM
- Paragraph 5.B(5)f of Exhibit 42 – Wholesale Rate


Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix A to Exhibit 42 – Map of Project Area IBO-1030

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

brightspeed

IBO-1030

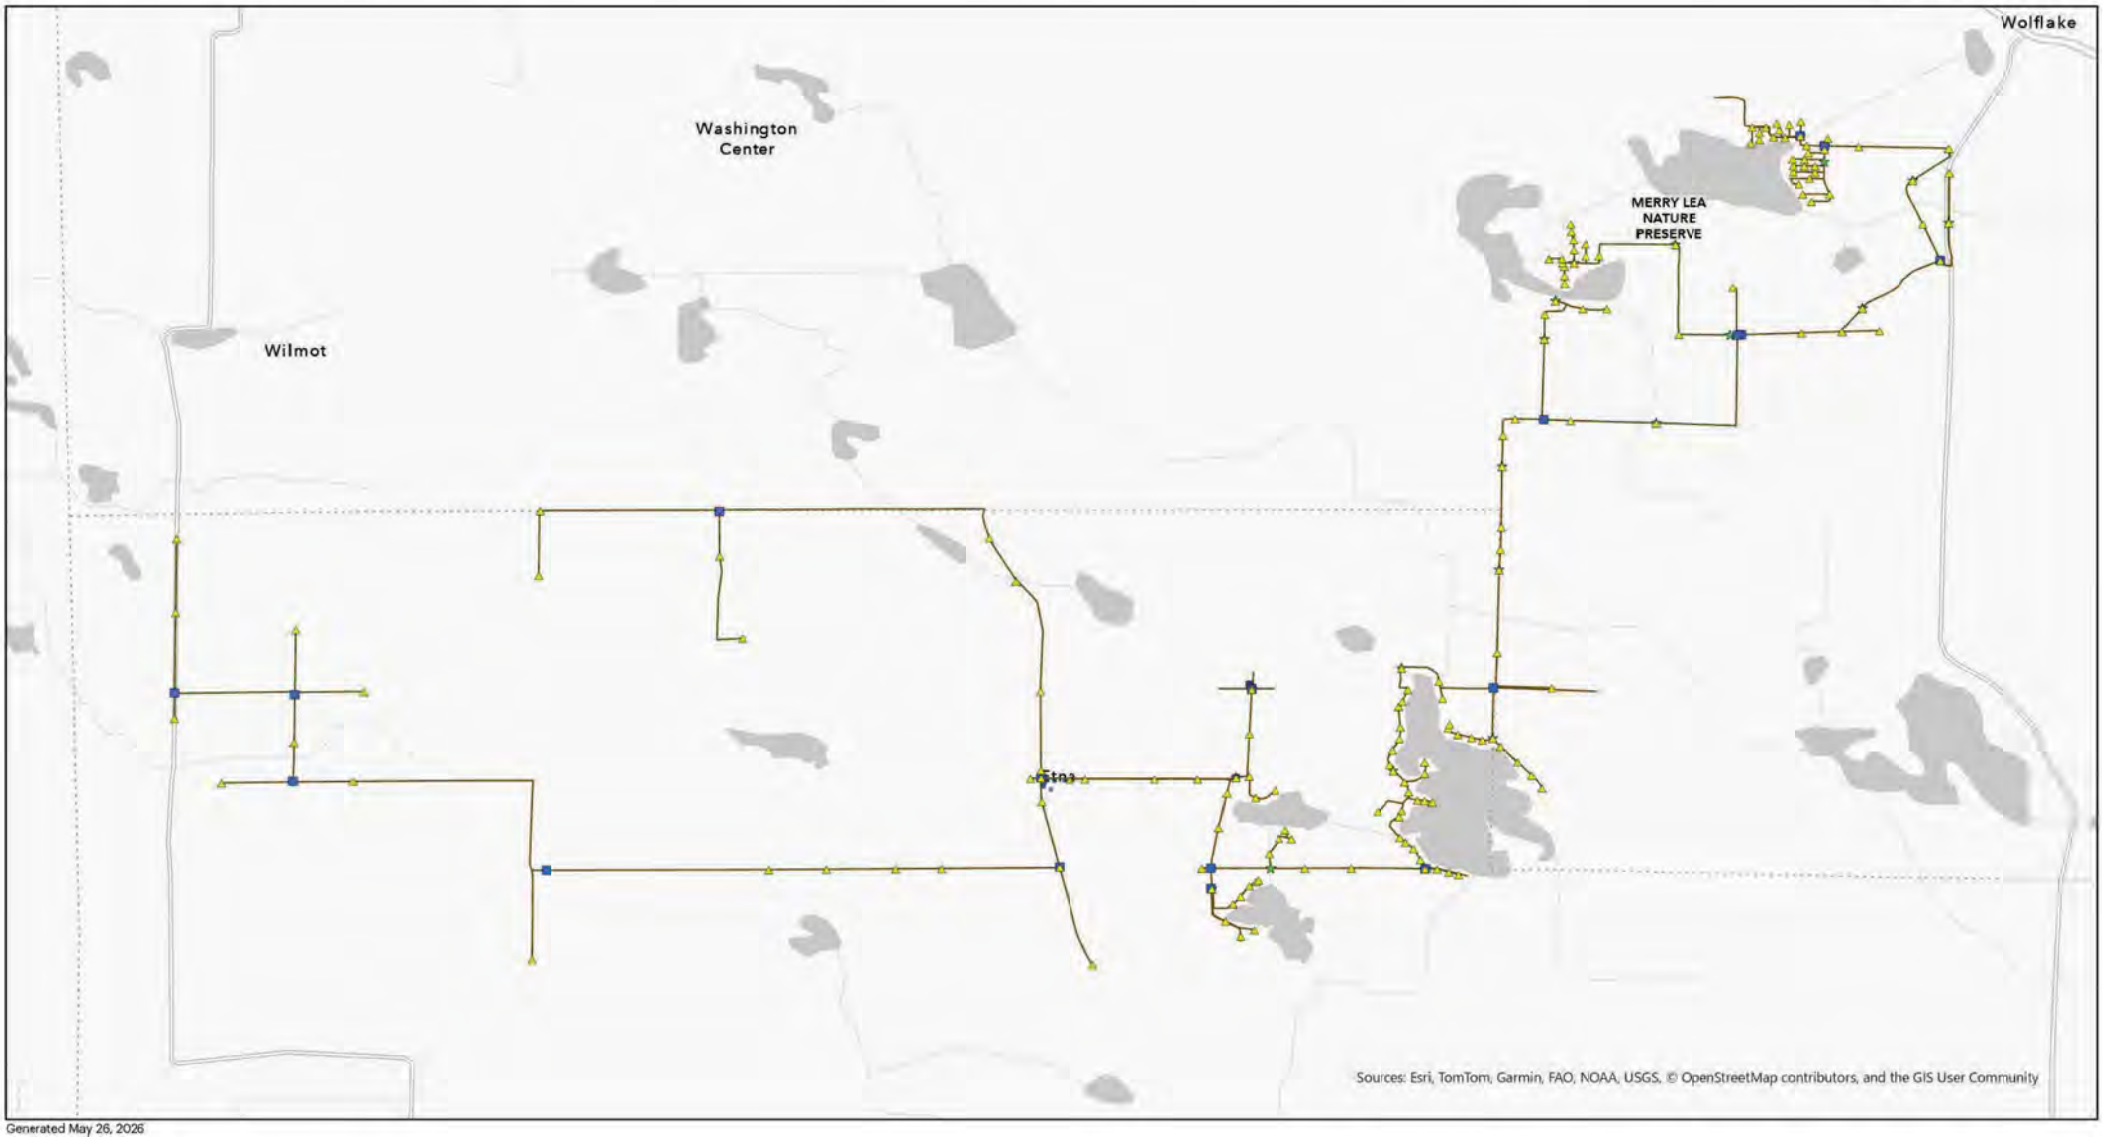

Generated May 26, 2026

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix B to Exhibit 42 – List of Locations in Project Area IBO-1030

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Brightspeed IBO-1030 Location List

8 locations

ID	Location ID	Is CAI	Technology	Upload	Download
8459c2e9b40b712e239c7329817be781	1037513185	No	Fiber	2000	2000
34a7676e70423af5e813fdbb80e705a3	1037513354	No	Fiber	2000	2000
964654d71877b7a59eb2730be8f11c98	1037513184	No	Fiber	2000	2000
998095b5a4312316e8a1270c4be0bdca	1037513186	No	Fiber	2000	2000
3598aed2865370ac225eb2a3f5751ddc	1037513355	No	Fiber	2000	2000
0d34d515c67e7e12471d8c864e4f11f5	1037533466	No	Fiber	2000	2000
495cd024d02f1d96e4b7129d4f9aca5a	1037513398	No	Fiber	2000	2000
82facd3966c922bb8bc48f73b12e47db	1037533465	No	Fiber	2000	2000

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix C to Exhibit 42 – Budget for Project Area IBO-1030

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
Corning 144F Armored Fiber Cable- Material	Fiber cable used to connect the terminals back to the central office	Outside Plant, Towers, and Poles	$3,553.00	$1,705.00	$1,848.00
Feeder Fiber Buried Installation Labor	Installation of all burried fiber underground	Construction Services	$10,530.00	$5,052.00	$5,478.00
Transport Calix ASM hardware	Calix transport ASM equipt for connecting OLT to wide area network	Other Allowable Costs	$1,500.00	$720.00	$780.00
Feeder Splicing Labor	Splicing labor costs for individual fiber connections	Construction Services	$3,135.00	$1,504.00	$1,631.00
Terminal Installation & splicing Labor	Labor costs for terminal installation and associated splicing	Construction Services	$469.00	$225.00	$244.00
Customer Connect Costs Labor	Labor costs for subscriber fiber drop installation	Construction Services	$5,024.00	$0.00	$5,024.00
Pole Attachments	Pole Make Ready Costs	Professional Services	$3,042.00	$1,460.00	$1,582.00
Conduit- Material	Conduit used for burried fiber	Outside Plant, Towers, and Poles	$1,290.00	$619.00	$671.00
Corning 2178 Splice Cases- Material	Splice cases manufactured, used for connections in network	Outside Plant, Towers, and Poles	$263.00	$126.00	$137.00
Feeder Fiber Aerial Installation Labor	Installation of all Aerial fiber on poles	Construction Services	$11,992.00	$5,754.00	$6,238.00
Transport installation Labor	Installation of network transport hardware like the ASM	Construction Services	$750.00	$360.00	$390.00
OLT Installation labor	Installation of OLT in the central office	Construction Services	$36.00	$17.00	$19.00
Corning Fiber Terminals- Material	8, 4 or 2 port fiber terminals, used for customer ONT connections	Outside Plant, Towers, and Poles	$297.00	$143.00	$154.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Cost Item	Description	Category	Total Cost	Grant Funds Requested	Match Funds
OLT hardware- Calix Optical Line Terminal Shelf	Calix OLT for servicing all subscriber traffic	Other Allowable Costs	$180.00	$86.00	$94.00
Handholes- Material	Handholes for in ground equipment	Outside Plant, Towers, and Poles	$0.00	$0.00	$0.00
Permitting Costs	Permitting Costs	Professional Services	$2,884.00	$1,384.00	$1,500.00
Engineering Design / Design Verification	Engineering Design Labor Costs	Professional Services	$3,405.00	$1,634.00	$1,771.00
Ancillary Costs	Contingencies for costs like tree trimming, Rock	Contingency Funds	$515.00	$247.00	$268.00
Customer Connect Costs-Material	Material costs for subscriber drop and equipment installation	Other Allowable Costs	$2,368.00	$0.00	$2,368.00
Ancillary Costs	Contingencies for costs like fiber cable reel waste	Contingency Funds	$442.00	$213.00	$229.00

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix D to Exhibit 42 – Disbursement Schedule for Project Area IBO-1030

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
0.5. Full execution of the Grant Agreement.	5%	5%
1. Complete EHP Reviews and demonstrate compliance with all applicable environmental laws: • Complete any and all review(s) required under the National Environmental Policy Act of 1969 (42U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the IBO, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA; • Complete reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, *et seq.*) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes; • Complete consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, *et seq.*), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, *et seq.*), as applicable; and • Demonstrate compliance with all other applicable Federal, state, and local environmental laws and regulations;	5%	10%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestones Subgrantee must submit a disbursement request no less than every 6 months	**Disbursement (% of Subaward)**	**Cumulative Disbursement (% of Subaward)**
2. Complete a high-level design for the Project so that Subgrantee can apply for necessary permits.	15%	25%
3. Serve 10% of Project Locations.	10%	35%
4. Serve 35% of Project Locations.	15%	50%
5. Serve 50% of Project Locations.	15%	65%
6. Serve 65% of Project Locations.	10%	75%
7. Serve 90% of Project Locations.	15%	90%
8. Serve **100%** of Project Locations. AND Complete Final Inspection and Project Closeout requirements.	10%	100%

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix E to Exhibit 42 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-1030

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Milestone	Planned Date to Submit	Actual Date Submitted	Date Accepted	Notes
Categorical Exclusion Review	4/1/2026			
Conduct Endangered Species Act (ESA) Section 7 obligations. This includes the use of the Information for Planning and Consultation (IPaC) tool and other relevant consultations	5/1/2026			
Conduct National Historic Preservation Act (NHPA) Section 106 Process. This includes any consultations required by Federal law, such as State Historic Preservation Office (SHPO)	5/1/2026			
Federal Agency Permits				
Bureau of Land Management (BLM) ROW Authorization				
Forest Service (FS) Special Uses				
Clean Water Act Section (CWA) 404 / Rivers and Harbors Act (RHA) Section 10 - General Permit				
Less Common Permits				
National Park Service (NPS) ROW				
U.S. Fish & Wildlife Service (USFWS) Special Uses Permit/ROW				
Army Corps of Engineers (USACE) Section 408				
Clean Water Act Section 401				
Bureau of Indian Affairs (BIA) ROW				
Bureau of Reclamation (BOR) ROW Authorization				
State Permits (This list includes the most common state permits but is not exhaustive. Please add rows for any additional permits as needed.)				
Use and Occupancy Permit (Fiber Optic on Freeways)	6/1/2026			
Railroad Crossing Permits	6/1/2026			
Utility Pole Attachment Permit	6/1/2026			
Local Permits (Please add rows to list the permit type, if applicable.)				
Private Authorizations (Please add rows to list the permit type, if applicable.)				

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Appendix F to Exhibit 42 – Form of Attestation to Accompany Disbursement Request

I, [Officer Name], in my capacity as the [Title] of [Subgrantee], and not personally, hereby certify that the information regarding the matching funds provided by [Subgrantee] in connection with [Subgrantee]'s BEAD subaward provided herewith is complete and accurate, to the best of my knowledge.

_____

[Officer Name]

[Title], [Subgrantee]

[Date]

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Exhibit 43 –Subaward Conditions and Statement of Work for Project Area IBO-996

1. General Information.

General Information	
2 CFR 200.332(a)(1) Federal Award Identification.	
(i) Subrecipient name (which must match the name associated with its unique entity identifier);	[Brightspeed (Connect Holding LLC)]
(ii) Subrecipient's unique entity identifier;	UEI Number or CAGE Code: JWYXBY1U3ML3
(iii) Federal Award Identification Number (FAIN);	18-20-B297; UEI Number: LK34C47QFQC5
(iv) Federal Award Date;	11/15/2022
(v) Subaward Period of Performance Start and End Date;	Four years from Effective Date ("ED")
(vi) Subaward Budget Period Start and End Date;	Effective Date through Four years from ED
(vii) Amount of Federal Funds Obligated by this action by the pass-through entity to the Subrecipient (subaward funds);	[$0]
(viii) Total Amount of Federal Funds Obligated to the subrecipient by the pass-through entity including the current obligation (subaward funds);	[$0]
(ix) Total Amount of the Federal Award committed to the Subrecipient by the pass-through entity (subaward funds);	[$0]
(x) Federal Award project description, as required to be responsive to the Federal Funding Accountability and Transparency Act (FFATA);	This project will utilize a Federal Award to build broadband infrastructure for unserved and underserved locations. Subrecipient will deploy and install broadband to BEAD eligible locations in Appendix B in accordance with the terms and milestones set forth in this Exhibit 43 - Specific Award Conditions for Project Area IBO-996.
(xi) Name of Federal awarding agency, pass-through entity, and contact information for awarding official of the Pass- through entity;	Federal Awarding Agency: United States Department of Commerce National Telecommunications Information Administration Pass-Through Entity: Indiana Broadband Office Pass-Through Entity Contact Information: Megan Minor, Chief Broadband Officer email: MeMinor@iot.in.gov phone: 317-509-4363

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(xii) Assistance Listing Number and Title;	Assistance Listing Number and Title: 11.035 – Broadband Equity, Access, and Deployment Program
(xiii) Identification of whether the award is R&D; and	This award does not support research and development (R&D).
(xiv) Indirect cost rate for the Federal Award (including if the de minimis rate is charged per §200.414 Indirect (F&A) costs).	N/A
Match percentage and Match amount	[100.00%]; [$18,193.00]
Total Project Cost = (subaward funds + match)	$18,193.00

2. **Subaward Amount.** The IBO will provide the Subgrantee with subaward funds in the amount of **$0** ("Subgrant Funds" or "Subaward Amount") to deliver and maintain broadband to Project Area IBO-996 ("Deployment Project") in accordance with applicable law and the State and federal conditions applicable to the BEAD Award and this Agreement. *Project Area* means the area designated by the Subgrantee in which Subgrantee will construct a broadband network to provide reliable broadband to residents and businesses listed in **Appendix B of this Exhibit 43**. The Project Area is depicted in the map in **Appendix A of this Exhibit 43**, attached hereto and incorporated herein.

3. **Fixed Amount Subaward and Milestone Payment Schedule.**
   A. This Subaward is issued as a Fixed Amount Subaward per 2 CFR 200.333. As such, the Subgrantee shall be responsible for all Project costs that exceed the amount of the Subgrant Funds. In the event the available Subgrant Funds are insufficient to satisfy all Project costs, the Subgrantee shall be responsible for fulfilling all of its obligations under the Grant Agreement.

   B. Record Keeping. Although there is no routine monitoring of the actual costs incurred by the Subgrantee under this Subaward, the Subgrantee must keep records of actual costs incurred and abide by the record retention requirements contained in 2 CFR 200.334 through 200.338 as well as the responsibilities of making records available for review during an audit.

   C. The IBO will disburse Subaward Funds after the Subgrantee's completion and verification of each milestone event detailed in **Appendix D of this Exhibit 43**, attached hereto and incorporated herein. Subgrantee will report on match expenditures as part of the disbursement request. For the avoidance of doubt, the level of match is not a precondition to reimbursement. The IBO may, at its reasonable discretion and for monitoring purposes only, request evidence of actual costs. Subgrantee further acknowledges that match shall be provided at the same general rate as the federal share and material failure to do so is a material breach of this Agreement. If, in the course of such monitoring activities, (a) the IBO identifies substantial misalignment between actual costs incurred by the Subgrantee and a reasonable estimate of actual costs for a particular milestone event and (b) Subgrantee cannot demonstrate that such misalignment is likely to be rectified by the completion of the Project, then the IBO may

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

restrict payment to actual costs incurred in connection with any milestone disbursement request made under the Grant Agreement.

D. Conditions Precedent to First Disbursement. The IBO shall not disburse any Subaward Funds prior to the Subgrantee's completion of Environmental and Historic Preservation ("EHP") reviews, EHP consultations and compliance with applicable environmental laws and regulations as detailed in Paragraph 8.A of Attachment A to the Grant Agreement.

4. Match Details.

A. The Subgrantee has budgeted a match in the amount of $18,193.00, which is 100.00% of the Total Project Cost. Notwithstanding anything to the contrary in the Grant Agreement, the Subgrantee's shall provide matching funds of at least 25% of the Total Project Cost. Before Subgrantee makes a change to its total approved match amount, Subgrantee shall request prior written approval from the IBO pursuant to 2 CFR 200.308(f)(7).

B. The Subgrantee's match (or cost share) toward the Total Project Cost shall be from the following sources[1], and in the amounts and percentages below:
   (1) Brightspeed (Connect Holding LLC)/Private Funds; cash match at 100.00% for a total match of $18,193.00.

C. Verification of Match. Upon the completion of a project milestone and submission of a disbursement request related to the completion of such milestone, the Subgrantee shall provide a report showing the amount of matching funds expended as of the date of such disbursement request ***along with a legally binding attestation***, substantially in the form attached hereto as Appendix F. The report shall contain records verifying the match amount and shall include, as applicable, the source, amount, quantity, time, and delivery of each match service. For the avoidance of doubt and acknowledging Subgrantee's obligation set forth in Section 4.A above, Subgrant Funds shall be earned and payable upon achievement of the relevant milestone set forth in Appendix D.

D.
   (1) Cash Match. Examples of records verifying cash matches include:
      - Bank or financial statement, showing available and expended funding.
      - Receipts from disbursements.
   (2) In-Kind Match. Examples of records verifying in-kind matches include:
      - For volunteer services where the rate must not exceed fair market value, use federal tools such as the Bureau of Labor Statistics to determine wage rate information. To the extent feasible, record time as an organization would for paid labor, such as timesheets and timecards.
      - For reduced rates from consultants and other individuals, compare current charges against standard or set labor category rates.

[1] Match can be provided from the following sources: the Subgrantee; the Eligible Entity; Philanthropic Organization; Federal Regional Commission or Authority; Unit of Local Government; For-Profit Company; Utility Company; Regional Planning; Government Organization; Non-Profit Organization; Cooperative; or any combination of the above.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- For facility in-kind matches, verify the amount against current mortgage statements or rental rates.

E. The Subgrantee agrees to abide by the cost sharing/match requirements of 2 CFR 200.306 by ensuring its matches are:
   (1) Verifiable from the records submitted to the IBO;
   (2) Not included as contribution for another Federal Award;
   (3) Necessary and reasonable to accomplish project or program objectives;
   (4) Allowable under subpart E of CFR 200.306;
   (5) Not paid by the federal government under another Federal Award, except where the federal statute authorizing a program specifically provides that federal funds made available for such program can be applied to matching or cost sharing requirements of other federal programs. *See* the IIJA provision providing for such exceptions under 47 USC § 1702(h)(3)(B)(iii) and Section III.B.1 of the BEAD NOFO; and
   (6) In conformance to other provisions of 2 CFR 200.306, as applicable.

F. The Subgrantee shall retain records associated with its match towards the project cost through the life of the Subaward, grant closeout and records retention period set forth in 2 CFR 200.334 and Section 8.A of the Grant Agreement.

5. Scope of Work.

A. Project Description.
   (1) Grantee must, no later than four (4) years after receiving the Subaward, create a fully-functioning, commercially serviceable broadband network within the Project Area that meets all Project Completion Standards.
   (2) The Subgrantee, in deploying broadband infrastructure, must do the following:
      a. Acquire such Equipment as is necessary to install, create, and maintain the broadband network, and to construct and install its related facilities[2];
      b. Design, install, construct, test, maintain, and operate its broadband network; and
      c. Acquire all necessary real property interests or access rights to real property for the purpose of installing its transmission lines.

B. Project Completion Standards. The Subgrantee agrees and warrants that, upon completion of the Project as described in this Paragraph 5.A(1), the broadband network will comply with the following:
   (1) Project Area. The broadband network will provide broadband to the locations listed in **Appendix B of this Exhibit 43** in the area depicted in **Appendix A of this Exhibit 43**.
   (2) Locations Served in the Project Area. The network will service each of the residential and business locations (broadband serviceable location or BSL) listed in **Appendix B of this Exhibit 43**, attached hereto and incorporated herein (the "Project Locations"). The Subgrantee agrees that, upon completion, the network will serve the comprehensive list of Project Locations (whether residential or business) located within the Project Area at the service speeds specified below. Any modifications must be approved in writing by both parties. A Project Location is considered "served" if the Subgrantee can initiate service through a routine installation within ten (10)

[2] Facilities means a place or building used to construct, maintain, or operate a broadband network.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

business days of a request with no extraordinary monetary charges or delays attributable to the extension of Subgrantee's network. The Subgrantee may charge standard installation fees to subscribers on the BEAD-funded network but may not require subscribers to make modifications to their own or surrounding property or charge fees for the same in connection with installation of broadband services funded by this Subaward.

(3) Network Capabilities. Pursuant to 47 U.S.C. § 1702(g)(1)(A), the Subgrantee shall ensure that every Funded Network meets the criteria related to speed and latency and network outages outlined in the NOFO. *See* NOFO IV.C.2.a. and in the Performance Measures for BEAD Last Mile Networks Policy Notice[3] (an any future amendments).

a. Speed and Latency.

i. Broadband networks shall deliver broadband service to each of the Project Locations served with speeds of not less than one hundred (100) Mbps for downloads and twenty (20) Mbps for uploads. In addition, ninety-five percent (95%) of latency measurements during testing windows must fall at or below one hundred (100) milliseconds round trip time.

ii. Connections to Eligible Community Anchor Institutions, as defined in the BEAD NOFO, shall be capable of delivering service at speeds not less than one (1) Gigabit per second for uploads. The Subgrantee shall ensure that such connections can be used to provide business service data.[4]

iii. Subgrantees must demonstrate continued compliance with these standards by performing speed and latency tests from the subscriber premises of an active subscriber to a remote test server at an end-point consistent with the requirements for a Commission-designated IXP (FCC Designated Internet exchange point).[5]

b. Reliability and Resilience. The Subgrantee shall establish risk management plans that account for technology infrastructure reliability and resilience, including safeguards against natural disasters (e.g., wildfires, flooding, tornadoes, hurricanes, etc.), as applicable, as well as cybersecurity and SCRM best practices[6] that incorporate strategies for mitigating risks associated with natural disasters. The plans should reflect best practices and demonstrate preparedness for physical and digital disruptions.

c. Network Outages. The network's outages should not exceed, on average, forty-eight (48) hours over any three hundred sixty-five (365) day period except in the case of natural disasters or other force majeure occurrence. The Subgrantee shall ensure a prospective network is designed to meet this requirement. Developing a comprehensive outage management plan that includes preventive maintenance schedules, metrics for measuring outages, quick response teams for outage resolution, and clear communication channels for informing subscribers about

[3] At https://broadbandusa.ntia.gov/sites/default/files/2025-09/Performance_Measures_Policy_Notice.pdf

[4] The term "business data service" refers to the dedicated point-to-point transmission of data at certain guaranteed speeds and service levels using high-capacity connections. *See Business Data Services in an Internet Protocol Environment et al.*, WC Docket No. 16-143 *et al.*, Report and Order, 32 FCC Rcd 3459, 3463 para. 6 (2017).

[5] *See Performance Measures Reconsideration Order*, 34 FCC Rcd at 10114-16, paras. 17-19.

[6] *See*, e.g., National Institute of Standards and Technology Framework for Improving Critical Infrastructure Cybersecurity, *Cybersecurity Supply Chain Risk Management Practices for Systems and Organizations,* NIST 800-161 Rev.1 and *Key Practices in Cyber Supply Chain Risk Management: Observations from Industry,* NIST IR 8276.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

outages and expected restoration times will meet this requirement. As applicable, the Subgrantee shall develop network designs that meet IBO metrics for measuring outages once the network is operational.

(4) Deployment Requirements.

a. Deployment Deadline. The Subgrantee must deploy broadband networks and start service to each prospective subscriber that desires it no later than four (4) years after the effective date of this Agreement.

b. Conduit Access Points. Any Project that involves laying fiber-optic cables or conduit underground or along a roadway must include interspersed conduit access points at regular and short intervals.

c. Covered Purchases. When deploying broadband networks, the Subgrantee may not purchase covered communications equipment[7] or support the People's Republic of China through purchasing fiber optic cable and optical transmission equipment manufactured there.

(5) Service Obligations.

a. Low-Cost Plans. The Subgrantee must offer at least one Low-Cost Broadband Service Option that is consistent with BEAD Program requirements ("LCSO") The LCSO must be made available to eligible subscribers[8] for the useful life of the network asset (i.e., the Federal Interest Period, which is ten (10) years after the year in which the subgrant for a project has been closed out or in the case of LEOs, a ten (10) year period of performance). The NTIA or the IBO may take corrective action, as set forth in Section 21 of this Grant Agreement, including recoupment of Subaward Funds from the Subgrantee, for non-compliance with the statutory low-cost plan requirement.

The Subgrantee's definition of a LCSO must detail:

i. All recurring charges to the subscriber, as well as any non-recurring costs or fees to the subscriber;

ii. The plan's basic service characteristics (download and upload speeds and latency; the LCSO must be at least 100/20 Mbps and <100ms latency);

iii. The plan's price and, as applicable, how the price will change over time;

iv. Whether the Subgrantee will define Eligible Subscriber more broadly than the RPN.

b. Access to Service. The Subgrantee shall provide access to broadband service to each subscriber served by the project that desires broadband service on terms and conditions that are reasonable and non-discriminatory.

i. The Subgrantee shall be able to initiate service at standard installation charges within ten (10) business days of a request from any prospective subscriber at a Project Location in the Project Area.

ii. For Low Earth orbit (LEO) Projects, the Subgrantee is required to provide all necessary consumer premises equipment (CPE) at no cost as part of the standard installation for each new subscriber at the BEAD-funded Location throughout the period of performance. This obligation is limited to no more than three (3) CPE per Location during the Period of Performance. If the Subgrantee plans to send CPE to the subscriber to self-install or use a third-

[7] Covered communications equipment or services are defined in section 9 of the Secure and Trusted Communications Networks Act of 2019 (47 U.S.C. 1608).

[8] Eligible Subscriber means any household seeking to subscribe to broadband internet access service that is eligible for the FCC's Lifeline Program. Lifeline eligibility criteria are defined in 47 CFR 54.409.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

party installer, the Subgrantee shall ensure the subscriber receive the CPE within ten (10) days.

c. Use of Funds. The Subgrantee shall use Subaward Funds in an equitable and nondiscriminatory manner. The Subgrantee further acknowledges and agrees that the IBO may recover Subaward Funds and/or terminate the Grant Agreement in the event of the Subgrantee's nonperformance as detailed in Section 21 of the Grant Agreement.

d. Public Notice.
   i. Once the broadband network has been deployed, the Subgrantee shall provide public notice, online and through other means, of that fact to the locations and areas to which broadband service has been provided and share the public notice with the IBO; and
   ii. The Subgrantee shall conduct public awareness campaigns in broadband network service areas to increase broadband adoption by highlighting the value and benefits of broadband internet access.

e. Cybersecurity and Supply Chain Risk Management. The Subgrantee shall comply with the Cybersecurity and Supply Chain Risk Management (SCRM) requirements detailed in Paragraph 22 of Exhibit A to the Grant Agreement.

f. Wholesale Rate. If the Subgrantee is no longer able to provide broadband service to the Project Locations covered by the Subaward at any time, the Subgrantee shall sell the network capacity at a reasonable, wholesale rate on a nondiscriminatory basis to other broadband service providers or public sector entities.

6. Reporting.

Subgrantee shall, for the duration of the Subaward, submit the reports discussed below.

After the conclusion of the period of performance, Subgrantee shall submit all reports consistent with 2 CFR 200.344.

The IBO may not make any changes to the requirements contemplated below, except as a result of (a) Subgrantee's nonperformance or (b) changes in BEAD Program rules or other applicable federal or state laws or regulations.

A. Semiannual Report.

The Subgrantee shall submit to the IBO a semiannual report on a semiannual basis for the periods ending June 30 and December 31. The Semiannual Report must be submitted no later than fifteen (15) days following the end of each reporting period. The Subgrantee must maintain sufficient records to substantiate all information below upon request. Each semiannual report shall:

(1) Describe each type of project carried out using the Subaward and the duration of the Subaward;

(2) Include a list of addresses or locations (including the Broadband Serviceable Location Fabric established under 47 U.S.C. 642(b)(1)(B)) that constitute the service locations that will be served by the broadband infrastructure to be constructed;

(3) Identify new locations served within each project area at the relevant reporting intervals, and service taken (if applicable);

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

(4) Identify whether each address or location described is residential, commercial, or a community anchor institution;
(5) Describe the types of facilities that have been constructed and installed;
(6) Describe the peak and off-peak actual speeds of the broadband service being offered;
(7) Describe the maximum advertised speed of the broadband service being offered;
(8) Describe the non-promotional prices, including any associated fees, charged for different tiers of broadband service being offered;
(9) Include any other data that would be required to comply with the data and mapping collection standards of the Commission under section 1.7004 of title 47, Code of Federal Regulations, or any successor regulation, for broadband infrastructure projects;
(10) Include Form SF-425 (Real Property Status Report) that meets the requirements described in DOC ST&Cs, Section A.01 for Real Property Status Reports;
(11) Describe delays in broadband-related projects that Subgrantee attributes to a state or local prohibition on using its preferred construction technique;
(12) Describe delays in broadband-related projects that Subgrantee attributes to state and/or local authorities failing to follow FCC rules regarding pole attachment timelines, rates, terms, and conditions for access to municipally owned poles and conduit for broadband projects;
(13) Identify Federal, State or local permit requests submitted;
(14) Detail Subgrant Funds and matching funds expended, in a manner consistent with the requirements of Paragraph 52.A of the General Terms and Conditions for the BEAD Program;
(15) Comply with any other reasonable reporting requirements determined by the IBO to meet the reporting requirements established by the Assistant Secretary; and
(16) Certify that the information in the report is accurate.

B. Close-Out Performance Report.
Final Performance Report. The Subgrantee must submit a final Performance Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance[9].

C. Financial Report.
The Subgrantee shall submit to the IBO a Performance Report on a semiannual basis for the periods ending March 31 and September 30. The Financial Report must be submitted no later than fifteen (15) calendar days following the end of each reporting period.
(1) The Subgrantee shall submit a Form SF-425 (Federal Financial Report) that meets the requirements described in the DOC ST&Cs, Section A.01 for Financial Reports.
(2) Final Financial Report. The Subgrantee must submit a final Financial Report to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance.

[9] *See* Section A.01.b.3 DOC ST&C.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

7. Project Monitoring.

A. Monitoring Activities. The IBO will monitor the Subgrantee's overall performance to ensure that the goals and objectives of the Subaward are achieved. Monitoring activities may consist of site visits, desk reviews and performance/financial report reviews.

B. Monitoring Plan. The monitoring plan will consist of:
   (1) Quarterly progress check-in meetings with the Subgrantee;
   (2) Review of Subgrantee's Financial and Performance reports that are required by the NTIA, the Grant Agreement, or any applicable laws and regulations;
   (3) Review of Subgrantee's audit results;
   (4) Site visits, if deemed necessary by the IBO and upon advance written notice to the Subgrantee; and
   (5) Review to ensure Subgrantee's compliance with applicable laws, the terms of the Grant Agreement and BEAD Program requirements.

C. The State may, pursuant to 2 CFR 200.332 and 200.208, change its monitoring plan, procedures or requirements at any time during the term of this Grant Agreement, including, but not limited to placing specific award conditions on this Subaward.

D. Corrective Action and Compliance Oversight. The IBO will take corrective action on all significant developments that negatively affect the Subaward. Significant developments include Single Audit findings related to the Subaward, other audit findings, site visits, and written notifications from a subrecipient of adverse conditions which will impact the Subgrantee's ability to meet the milestones or the objectives of this Subaward. When significant developments negatively impact the Subaward, the Subgrantee shall provide the IBO with information on its plan for corrective action and any assistance needed to resolve the situation.
   (1) Any corrective action plan under this Paragraph 7.D will:
      i. Identify the specific noncompliance or deficiency;
      ii. Define clear resolution steps and timelines;
      iii. Outline documentation required for remediation;
      iv. Establish consequences for failure to comply, consistent with the enforcement provisions in 2 CFR 200.339.
   (2) The IBO will monitor corrective action plans closely through scheduled follow-ups and additional oversight activities. The Subgrantee will receive guidance and tailored support throughout the process to promote timely resolution and sustained compliance.

E. Final Inspection. The Subgrantee shall provide notice of completion of the broadband infrastructure project and other construction activities when all construction has been completed, the architect/engineer has conducted its own final inspection, and any deficiencies have been corrected. The IBO will schedule the final inspection. Representatives of the IBO, the architect/engineer and the Subgrantee must attend the final inspection for the project.

8. Project Closeout

A. Closeout will be conducted on the timelines and in the manner set forth in 2 CFR 200.344.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

B. The Subgrantee shall submit all reports (financial, performance, and other reports required by the Subaward) to the IBO no later than ninety (90) calendar days after the conclusion of the period of performance of the Subaward (or an earlier date as agreed upon by the IBO and Subgrantee).

C. The Subgrantee must liquidate all financial obligations incurred under this Subaward no later than ninety (90) calendar days after the conclusion of the period of performance of this Subaward (or an earlier date as agreed upon by IBO and Subgrantee).

D. The Subgrantee must promptly refund any unobligated funds that the IBO paid and that are not authorized to be retained. *See* OMB Circular A–129 and 2 CFR 200.346.

E. The Subgrantee must account for any "real property" and "equipment," in each case as defined in 2 CFR 200.1, acquired with Subaward Funds or received from the Federal Government in accordance with 2 CFR 200.310 through 200.313, 200.316 and 200.330.

F. Certification of Project Completion. The Subgrantee shall certify in writing to the IBO that the project was completed as agreed to in this Exhibit 43 to the Grant Agreement, or identify activities that were not completed, and that all expenditures were incurred in accordance with 2 CFR 200.403. If the required activities are completed in accordance with the terms and conditions of the Federal BEAD Requirements and this Grant Agreement, the Subgrantee is entitled to any unexpended funds.

9. Performance Bond.

A. Within sixty (60) days of entering into the Grant Agreement, the Subgrantee shall obtain a performance bond, which is acceptable in all aspects to the IBO and in a value of no less than 10% of the Subaward Amount.
B. If the Subgrantee fails to obtain a performance bond within sixty (60) days of entering into the Grant Agreement, this Subaward may be terminated.
C. The Subgrantee commits to maintain a performance bond in the amount of at least 10% of the Subaward Amount until it has demonstrated to the satisfaction of the IBO that it has completed the buildout of 100% of Project Locations or until the period of performance of the Subaward has ended, whichever occurs first.
D. The Subgrantee shall submit requests for payment of Subaward Funds no less frequently than every six months.

10. Project Personnel.

A. Both IBO and Subgrantee have designated the following persons to serve as Project Manager to support effective communication between the Parties to report on the work's progress.
   (1) For IBO: IBO Division Director (TBD); IndianaBroadband@iot.in.gov; phone: TBD
   (2) For Subgrantee: Marcy Mealy; marcy.mealy@brightspeed.com

B. Written notice shall be provided to personnel at the email addresses set forth in this Paragraph 10 in the event of any change in Project Personnel.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

11. Insurance.

A. Subgrantee must comply with the insurance requirements in 2 CFR 200.310. In addition, the Subgrantee and its contractors shall secure and keep in force during the term of the Grant Agreement the following insurance coverages or self-insurance where expressly permitted (as applicable) covering the Subgrantee for any and all claims of any nature which may in any manner arise out of or result from Subcontractor's performance under this Grant Agreement:

(1) Commercial general liability, including contractual coverage, and products or completed operations coverage (if applicable), with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence unless additional coverage is required by the State. The State is to be named as an additional insured on a primary, non-contributory basis for any liability arising directly or indirectly under or in connection with this Grant Agreement.

(2) Automobile liability for owned, non-owned, and hired autos with minimum liability limits not less than $700,000 per person and $5,000,000 per occurrence. The State is to be named as an additional insured on a primary, non-contributory basis.

(3) Errors and Omissions liability with minimum liability limits of $1,000,000 per claim and in the aggregate. Coverage for the benefit of the State shall continue for a period of two (2) years after the date of service provided under this Grant Agreement.

The Subgrantee may satisfy this requirement through a commercially issued insurance policy or through a formal program of self-insurance, provided that the Subgrantee maintains financial capacity to satisfy claims in amounts not less than the minimum limits required herein and agrees that such self-insurance shall provide protection to the State equivalent to the coverage otherwise required.

The Subgrantee shall remain fully responsible for all acts, errors, and omissions arising from services performed under this Grant Agreement and shall defend, indemnify, and hold harmless the State of Indiana and its BEAD Office from any claims, damages, or liabilities arising therefrom and shall remain in effect for the term of the Grant Agreement and continue for a period of two (2) years after the date of service provided under this Grant Agreement for the benefit of the State.

(4) Workers' Compensation insurance as required by state statute.

(5) Insurance Coverage reasonably sufficient to protect Grant funded property from theft, fire, vandalism, weather damage to materials, equipment, and the project itself during the build.

(6) Inland Marine Insurance reasonably sufficient to protect equipment acquired with Grant funds.

(7) Cyber Liability addressing risks associated with electronic transmissions, the internet, networks, and informational assets sufficient to satisfy the obligations under the Grant Agreement.
The Subgrantee shall maintain Cyber Liability insurance, or approved self-insurance shall, at all times, be maintained at levels sufficient to cover all reasonably foreseeable financial risks, losses, and liabilities identified or assessed in the

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Subgrantee's cybersecurity risk management plan and supply chain risk management (SCRM) plan.

Such coverage or financial responsibility shall address claims and costs arising from cybersecurity incidents affecting BEAD-funded infrastructure or services, that the Subgrantee is responsible and liable for pursuant to and in connection with the services agreed herein.

The limits of such insurance or self-insurance shall not be less than the minimum limits required under this Agreement and reasonably commensurate with the risks associated with the Subgrantee's cybersecurity obligations and operation of BEAD-funded broadband infrastructure.

Where the Subgrantee satisfies this requirement through self-insurance, the Subgrantee shall maintain financial capacity sufficient to satisfy claims arising from cyber incidents and shall remain fully responsible for all liabilities arising from its failure to comply with the cybersecurity and supply chain risk management requirements of this Agreement.

The Subgrantee's maintenance of cyber liability insurance or self-insurance shall not limit or reduce its indemnification obligations to the State of Indiana or the Indiana Broadband Office under this Agreement. The Subgrantee shall provide proof of such insurance coverage and self-insurance by tendering to the undersigned State representative (i) a certificate of insurance for all commercially procured coverages and (ii) the self-insurance certification and supporting documentation prior to the commencement of this Grant Agreement and proof of workers' compensation coverage meeting all statutory requirements of IC § 22-3-2.

B. The Subgrantee's insurance coverage must meet the following additional requirements:

(1) The insurer must have a certificate of authority or other appropriate authorization to operate in the state in which the policy was issued.
(2) Any deductible or self-insured retention amount or other similar obligation under the insurance policies shall be the sole obligation of the Subgrantee.
(3) The State will be defended, indemnified, and held harmless to the full extent of any coverage actually secured by the Subgrantee in excess of the minimum requirements set forth above. The duty to indemnify the State under this Grant Agreement t shall not be limited by the insurance required in this Grant Agreement.
(4) The insurance required in this Grant Agreement, through a policy or endorsement(s) or the self-insurance program, shall include a provision that the policy and endorsements may not be canceled or modified (or, in the case of self-insurance, that the self-insurance program may not be materially altered or discontinued) without thirty (30) days' prior written notice to the undersigned State agency.
(5) The Subgrantee waives and agrees to require their insurer to waive their rights of subrogation against the State of Indiana.

C. The Subgrantee shall furnish a certificate of insurance (or self-insurance certification) and all endorsements to the State before the commencement of this Grant Agreement.

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

Failure to provide insurance as required under this Grant Agreement may constitute a material breach of contract, entitling the State to immediately terminate this Grant Agreement.

Evidence of Self-Insurance. Prior to commencement of the Grant Agreement and annually thereafter (or upon the State's reasonable request), the Subgrantee shall deliver to the State a written certification signed by its Chief Financial Officer (or equivalent officer) confirming that it maintains sufficient balance sheet liquidity and financial resources to fully satisfy claims up to the limits set forth in (a) and (b) above. The certification shall be accompanied by the Subgrantee's most recent audited financial statements (or other evidence satisfactory to the State) demonstrating adequate liquidity and net worth.

The Subgrantee shall provide the State at least thirty (30) days' prior written notice of any material change to its self-insurance program or financial condition that could reasonably impair its ability to satisfy claims hereunder.

12. Conditions Precedent to Grant Agreement Execution.

Before the Effective Date of this Grant Agreement, the Subgrantee shall provide the following documents to the IBO:

- FFATA information from Paragraph 27 of Attachment A to the Grant Agreement;
- Certificate of Insurance and all endorsements;
- Letter of Credit with an opinion letter from legal counsel or Performance Bond;
- Cybersecurity Risk Management Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Supply Chain Risk Management (SCRM) Plan referenced in Paragraph 22 of Attachment A to the Grant Agreement;
- Match details listing the match source, type of match, percentage of Total Project Cost, and dollar amount as required in Paragraph 4.B of this Exhibit 43;
- Appendix A to this Exhibit 43 – Map of Project Area IBO-996;
- Appendix C to this Exhibit 43 – Budget for Project Area IBO-996;
- Appendix E to this Exhibit 43 – Environmental and Historic Preservation (EHP) Milestone Schedule for Project Area IBO-996;
- Appendix F to this Exhibit 43 – Form of Attestation to Accompany Disbursement Request;
- Byrd Anti-Lobbying Certification (Attachment C to the Grant Agreement); and
- Protecting the BEAD Program from Defaults Certification (Attachment D to the Grant Agreement). The NTIA may, at its discretion, publicly publish the signed certifications in Attachment D.

13. Specific Award Conditions – Environmental and Historic Preservation (EHP)/Permitting

A. Completion of Environmental Review.

The Subgrantee must comply with all applicable statutory environmental and historic preservation regulations and identify to the IBO and NTIA when a proposed infrastructure project may have potentially significant effects on the environment. The Subgrantee may not expend any federal BEAD funds other than for the limited

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

permissible activities identified in General Terms and Conditions for NTIA BEAD Program Funds Section 13.E prior to the following:

- The completion of any review required under the National Environmental Policy Act of 1969 (42 U.S.C. 4321, et seq.) (NEPA), and issuance by NTIA and the Grantee, as required, of a Categorical Exclusion (Cat Ex) determination, Record of Environmental Consideration (REC), Finding of No Significant Impact (FONSI), or Record of Decision (ROD) (hereinafter "decision documents") that meets the requirements of NEPA;

- The completion of reviews required under Section 106 of the National Historic Preservation Act of 1966 (54 U.S.C. 300101, et seq.) (NHPA), including any consultations required by Federal law, to include consultations with the State Historic Preservation Office (SHPO), and Federally recognized Native American tribes;

- The completion of consultations with the U.S. Fish and Wildlife Service (USFWS) or the National Marine Fisheries Service (NMFS), as applicable, under Section 7 of the Endangered Species Act (16 U.S.C. 1531, et seq.), and/or consultations with the U.S. Army Corps of Engineers (USACE) under Section 404 of the Clean Water Act (33 U.S.C. 1251, et seq.), as applicable; and

- Demonstration of compliance with all other applicable Federal, state, and local environmental laws and regulations.

Project implementation (site preparation, demolition, construction, ground disturbance, or any other project implementation activities) may not begin prior to the completion of the above activities. The Subgrantee must comply with all conditions placed on the grant funded activities as the result of environmental reviews and associated consultations as the result of NEPA or NHPA consultation or processes under other applicable laws — e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The allowable use of funds prior to beginning project implementation includes, but is not limited to, activities necessary for the completion of the following:

- Pre-construction planning, including collecting information necessary to complete environmental reviews;
- Applications for environmental permits;
- Studies including, but not limited to, Environmental Assessments (EA), wetland delineations, biological assessments, archaeological surveys, and other environmental reviews and analyses;
- Administrative costs;
- Pre-award application costs;
- Activities supporting consultations required under the NHPA, the Endangered Species Act, and the Clean Water Act;

Docusign Envelope ID: F6168E03-BAEE-825D-8099-20D4B6004A4C

- Limited, preliminary procurement, including the purchase or lease of equipment, or entering into binding contracts to do so; the purchase of applicable or conditional insurance; and/or funds used to secure land or building leases (including right-of-way easements).

If the Subgrantee undertakes unauthorized project activities in contravention of this Section, it proceeds at its own risk and may face de-obligation of funding.

B. Timely Provision of NEPA Documents and Permits.
The Subgrantee shall provide any information requested by the IBO or NTIA to support initial and ongoing compliance with environmental and historic preservation laws and regulations. Once consultation activities have been completed, the IBO will review all documentation and determine sufficiency. Projects with potentially significant impacts to environmental or historic resources may face de-obligation of funding if impacts cannot be mitigated.

The Subgrantee must comply with all conditions placed on the grant funded activities as the result of NEPA or NHPA consultation or processes under other applicable laws—e.g., mitigation requirements, best management practices, or other measures necessary to reduce environmental impacts.

The Subgrantee shall notify the IBO within 24 hours upon receipt of any notices of foreclosure; requests for additional consultation received from the SHPO, THPO, Tribal representative, USFWS, or other consulting party; or notices of noncompliance received from consulting authorities or regulatory agencies.

The Subgrantee must notify the IBO of any change to the approved project scope that has the potential for altering the nature or extent of environmental or cultural resources impacts. Projects with such potential will be re-evaluated for compliance with applicable regulatory requirements.

C. Milestone Schedule for NEPA and Permitting
Before executing this Grant Agreement, the Subgrantee must provide the IBO a draft milestone schedule identifying environmental review and permitting activities, dependencies, and deadlines and describing how the Subgrantee proposes to meet timing requirements including, as required:

- The completion of any statutorily required reviews and consultations including, but not limited to, Endangered Species Act Section 7 and National Historic Preservation Act Section 106;
- The completion of NEPA, including the submission of Environmental Assessments (EAs) or Environmental Impact Statements (EISs) if anticipated; and
- Anticipated dates for any necessary federal permit applications, including application acceptance and permit decisions.

The IBO may stipulate the format of the NEPA and Permitting milestone schedule and, upon review, request revisions to reflect statutorily driven sequencing requirements.
